CROSSWIND


HOLLANDSE KUST NOORD WIND PARK Project

BASE LOAD POWER HUB

Contract No. CW-I-WP4-2023-05

ROSETTI MARINO

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
123A90 - Cross Wind BLPH - Preliminary Lvl 4. Schedule - baseline issued 25.10.2024		800d	731d	31-May-23 A	28-Oct-25	31-May-23	14-Nov-25	2d
Milestones & Key Dates		731d	731d	31-May-23 A	28-Oct-25	31-May-23	14-Nov-25	2d
MIL-20	Contract Start Date	0d	0d	10-Jul-23 A		10-Jul-23		
MIL-10	Notification Tender Result	0d	0d	31-May-23 A		31-May-23		
MIL-30	Project Completion	0d	0d		28-Oct-25*		14-Nov-25	2d
Key Dates		703d	706d	22-Nov-23 A	28-Oct-25	07-Oct-23	30-Oct-25	2d
KD01	KD01 - HAZOP Workshop conducted and report issued - (Contract: 28.11.2023)	0d	0d	08-Dec-23 A		23-Dec-23		
KD02a	KD02a - 30% Model Review completed and report issued - (Contract: 15.11.2023)	0d	0d	22-Dec-23 A		15-Nov-23		
KD02b	KD02b - 60% Model Review completed and report issued - (Contract: 29.02.2024)	0d	0d	15-Jul-24 A		29-Feb-24		
KD02c	KD02c - 90% Model Review completed and report issued - (Contract: 13.06.2024)	0d	0d	25-Jul-24 A		20-Jun-24		
KD03	KD03 - Purchase Order of Desalination Unit issued (& accepted) - (Contract: 11.12.2023)	0d	0d	23-Feb-24 A		24-Jan-24		
KD04	KD04 - Purchase Order (1st batch) of Primary and Secondary Structural Steel issued (& accepted) - (Contract: 0	0d	0d	26-Jan-24 A		13-Dec-23		
KD05	KD05 - Primary Steel Construction Drawings AFC issued -(Contract: 27.12.2023)	0d	0d	22-Dec-23 A		27-Dec-23		
KD06	KD06 - Start of construction of steel structure - (Contract: 27.12.2023)	0d	0d	22-Nov-23 A		27-Dec-23		
KD07	KD07 - Purchase Order of Electrical Equipment (Main & Aux Trafo, HV&MV Switchgear) issued - (Contract: 01.(	0d	0d	21-Dec-23 A		07-Oct-23		
KD08	KD08 - Assembly of Steel Structure of Lower Deck (Primary and Secondary Steel) completed - (Contract: 29.03.2	0d	0d	16-Nov-24		29-Mar-24		348d
KD09	KD09 - Installation of Mechanical Equipment of Lower Deck completed - (Contract: 28.09.2024)	0d	0d	20-Nov-24		16-Oct-24		344d
KD10	KD10 - Mechanical Completion finished - (Contract: 07.12.2024)	0d	0d	21-Feb-25		07-Dec-24		251d
KD11	KD11 - Onshore Commissioning completed - (Contract: 02.04.2025)	0d	0d	19-Mar-25		02-Apr-25		225d
KD12	KD12 - Onshore Integrated Testing completed - (Contract: 01.05.2025)	0d	0d	29-Apr-25		02-May-25		184d
KD13	KD13 - Ready for Sail-away Certificate issued - (Contract: 16.05.2025)	0d	0d	16-May-25		16-May-25		101d
KD14	KD14 - CONTRACTOR Ready in All Respects to Commence Topsides Installation at the PROJECT SITE.	0d	0d	16-Jun-25		16-Jun-25		70d
KD15	KD15 - Topsides Installation completed - (Contract: 21.06.2025) - LD	0d	0d	19-Jun-25		21-Jun-25		18d
KD16	KD16 - HANDOVER CERTIFICATE for the whole PERMANENT WORK issued - (Contract: 01.08.2025)	0d	0d	30-Jul-25		01-Aug-25		2d
KD17	KD17 - Topsides As-Builts issued - (Contract: 15.09.2025)	0d	0d	13-Sep-25		15-Sep-25		47d
KD18	KD18 - COMPLETION - (Contract: 30.10.2025)	0d	0d	28-Oct-25		30-Oct-25		2d
Notification Mechanism (Assumption - As Early As Possible)		185d	185d	10-Jan-25	20-Aug-25	02-Sep-24	20-Aug-25	60d
Detail Engineering		406d	491d	02-Aug-23 A	20-Dec-24	10-Jul-23	05-Apr-24	215d
Payment Milestones		627d	722d	25-Jul-23 A	16-Jul-25	25-Jul-23	16-Jul-25	16d
Project Management		565d	580d	10-Jul-23 A	23-Oct-25	10-Jul-23	23-Oct-25	4d
Project Management		491d	489d	10-Jul-23 A	17-Jun-25	10-Jul-23	19-Jun-25	2d
Services to be provided to COMPANY		491d	491d	10-Jul-23 A	19-Jun-25	10-Jul-23	19-Jun-25	93d
Financial Guarantees		565d	565d	31-Jul-23 A	23-Oct-25	31-Jul-23	23-Oct-25	4d
Engineering		593d	593d	10-Jul-23 A	25-Jun-25	10-Jul-23	09-Jul-25	107d
Detail Engineering		519d	519d	10-Jul-23 A	25-Mar-25	10-Jul-23	18-Jan-25	181d
Engineering Follow-Up		400d	395d	02-Oct-23 A	25-Apr-25	25-Sep-23	25-Apr-25	38d
Engineering Support during Fabrication / Construction Engineering		430d	459d	23-Oct-23 A	02-May-25	28-Oct-23	02-Apr-25	33d
Engineering Load-Out, Transport & Installation		351d	424d	04-Dec-23 A	02-May-25	22-Jan-24	14-Feb-25	76d
As-Built Documentation		80d	80d	19-Mar-25	25-Jun-25	02-Apr-25	09-Jul-25	31d
Procurement		528d	461d	21-Aug-23 A	26-Feb-25	01-Aug-23	12-Feb-25	204d
Company Provided Items		156d	168d	01-Jun-24 A	17-Dec-24	30-Apr-24	15-Aug-24	22d
Electrolysers - CPI		91d	104d	15-Aug-24 A	17-Dec-24	15-Aug-24	15-Aug-24	22d
Fuell Cells - CPI		95d	109d	01-Jun-24 A	18-Sep-24 A	30-May-24	30-May-24	
BESS Battery - CPI		52d	52d	01-Jun-24 A	22-Jul-24 A	30-May-24	30-May-24	
ICCP - CPI		0d	0d	03-Jul-24 A	03-Jul-24 A	30-Apr-24	30-Apr-24	

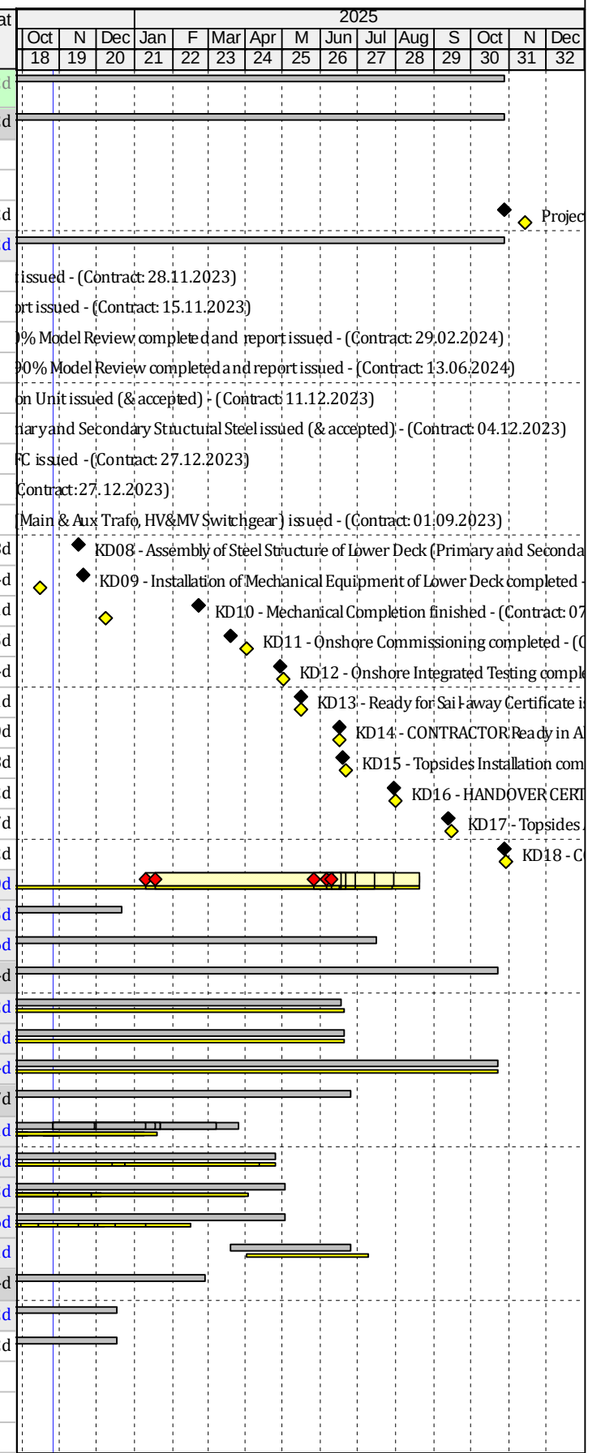

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
Milestone
summary
Notification Mechanism


Data Date: 25-Oct-24

CROSSWIND BLPH EPCI

Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Equipment		528d	425d	21-Aug-23 A	15-Jan-25	01-Aug-23	12-Feb-25	38d
H2 Storage Vessel		399d	363d	29-Aug-23 A	07-Nov-24	29-Aug-23	22-Nov-24	64d
Hydrogen Vent KO Drum		217d	259d	30-Nov-23 A	08-Oct-24 A	15-Jan-24	25-Oct-24	
Electro-Chlorination Unit		287d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	25-Aug-24	48d
Desalinisation Unit (SWRO)		282d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	24-Aug-24	48d
Ultra Filtration Unit		287d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	04-Aug-24	48d
UV Water Filter		282d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	04-Aug-24	48d
Sea Water Coarse Filter Package		282d	292d	15-Nov-23 A	31-Oct-24	12-Dec-23	16-Jul-24	48d
Fresh Water Pump		281d	291d	15-Nov-23 A	30-Oct-24	12-Dec-23	07-Apr-24	49d
Filtered Seawater Tank		296d	307d	27-Oct-23 A	31-Oct-24	20-Nov-23	29-Jul-24	48d
Fresh Water Tank		301d	307d	27-Oct-23 A	31-Oct-24	20-Nov-23	29-Jul-24	48d
Transformer Main 66/6.6kV		344d	291d	21-Aug-23 A	05-Aug-24 A	21-Aug-23	03-Nov-24	
Transformer Aux. 6.6/0.4kV		362d	287d	21-Aug-23 A	31-Jul-24 A	21-Aug-23	29-Oct-24	
Transformer 0,4/6,6kV630kVA		362d	286d	21-Aug-23 A	30-Jul-24 A	21-Aug-23	29-Oct-24	
Neutral earthing resistor		362d	311d	29-Aug-23 A	06-Sep-24 A	29-Aug-23	29-Oct-24	
HV Switchgear 66kV		443d	425d	21-Aug-23 A	15-Jan-25	02-Aug-23	01-Feb-25	36d
MV Switchgear 6.6kV		341d	293d	21-Aug-23 A	07-Aug-24 A	01-Aug-23	31-Aug-24	
Low Voltage Switchgear		355d	293d	21-Aug-23 A	07-Aug-24 A	01-Aug-23	17-Sep-24	
Solar farm in-feed power isolator panel		214d	234d	20-Dec-23 A	27-Sep-24 A	11-Dec-23	14-Jul-24	
Automation systems CCS-SIS & EMS		378d	359d	21-Aug-23 A	25-Oct-24 A	01-Aug-23	02-Sep-24	
Shelter for plant instrument room		208d	226d	03-Nov-23 A	02-Aug-24 A	14-Nov-23	29-Jul-24	
Shelter for LV switchgear room		210d	220d	03-Nov-23 A	26-Jul-24 A	14-Nov-23	24-Jul-24	
Shelter for HV switchgear room		206d	220d	03-Nov-23 A	26-Jul-24 A	14-Nov-23	24-Jul-24	
Shelter for AC UPS fitted with UPS system		209d	222d	03-Nov-23 A	29-Jul-24 A	14-Nov-23	24-Jul-24	
DC UPS panel board		249d	234d	23-Oct-23 A	01-Aug-24 A	18-Oct-23	16-Jul-24	
AC UPS for CCS, SIS field instruments		269d	293d	23-Oct-23 A	10-Oct-24 A	03-Nov-23	03-Aug-24	
AC UPS for PAGA/FGS/EMCS Rectifier		263d	291d	23-Oct-23 A	08-Oct-24 A	20-Nov-23	24-Aug-24	
Essential process load distribution panel		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
Process load distribution panel		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	11-Jul-24	
Distribution board for top deck lights		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
Distribution board for lower deck lights		215d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
Distribution board for stair tower lights		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
Distribution board for Relief valve platform lights		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
Distribution board for Emergency light		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
Telecom System		248d	288d	16-Oct-23 A	27-Sep-24 A	07-Dec-23	11-Oct-24	
Waste Water Tank		322d	274d	02-Nov-23 A	27-Sep-24 A	20-Oct-23	03-Oct-24	
Instrument Air Receiver		273d	307d	27-Oct-23 A	31-Oct-24	20-Oct-23	17-Sep-24	78d
Davit Crane		230d	286d	16-Jan-24 A	20-Dec-24	15-Jan-24	13-Sep-24	53d
Instrument Air Package		282d	307d	27-Oct-23 A	31-Oct-24	13-Oct-23	25-Sep-24	71d
Seawater Intake Pump		346d	247d	01-Mar-24 A	20-Dec-24	06-Nov-23	12-Feb-25	43d
Liferaft		145d	145d	08-Jul-24 A	27-Dec-24	09-Apr-24	16-Jul-24	51d
Hydrogen Vent		238d	247d	09-Feb-24 A	29-Nov-24	18-Oct-23	05-Sep-24	48d
Container 40' ISO for Water treatment system		278d	292d	15-Nov-23 A	31-Oct-24	14-Nov-23	29-Jul-24	72d
JB with disconnector for Temporary Generator		178d	111d	14-Jun-24 A	22-Oct-24 A	08-Jan-24	27-Jul-24	
SDV & BDV		261d	239d	15-Nov-23 A	30-Aug-24 A	14-Nov-23	01-Oct-24	
Actuated Control Valves		286d	291d	21-Nov-23 A	06-Nov-24	27-Nov-23	30-Sep-24	86d

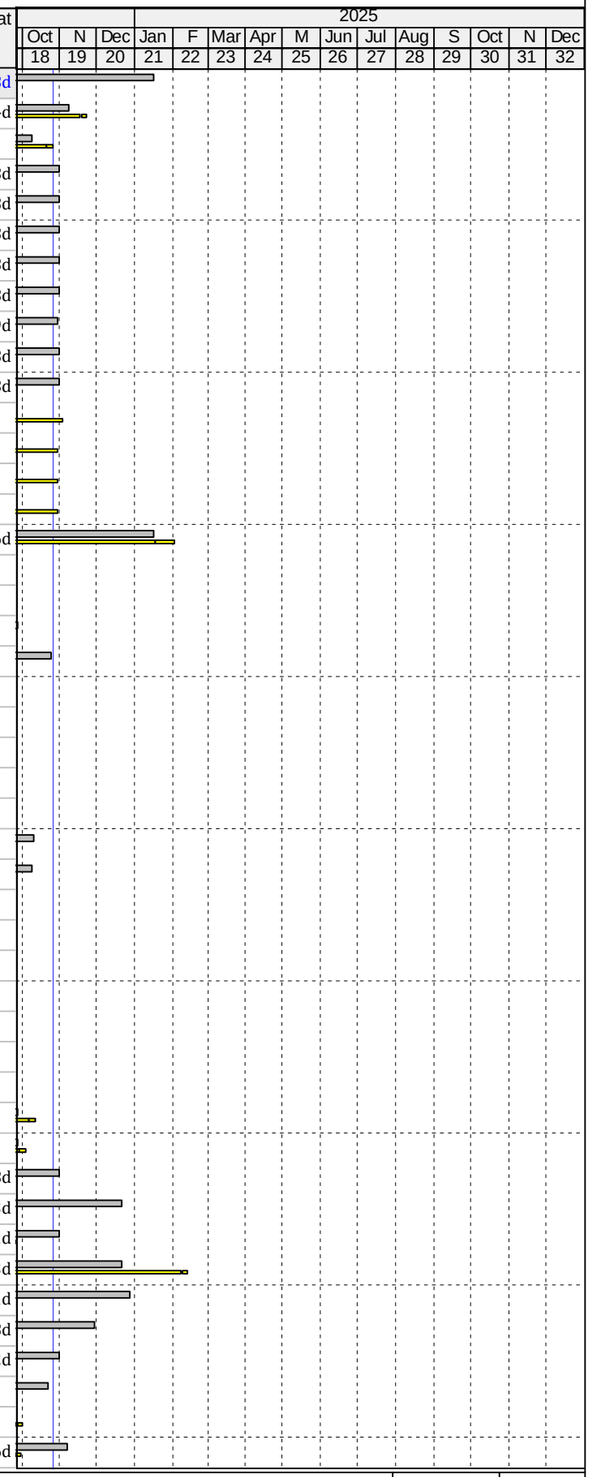

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
Milestone
summary
Notification Mechanism

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
	Pressure Safety Valves	213d	230d	12-Dec-23 A	14-Sep-24 A	27-Nov-23	30-Sep-24	
	Nav. Aids & anti collision system	225d	230d	26-Jan-24 A	25-Oct-24 A	04-Dec-23	11-Jul-24	
	Bulk Material - Steel	373d	421d	25-Aug-23 A	15-Jan-25	21-Sep-23	04-Nov-24	71d
	Primary Structures - Plate Girders	77d	133d	25-Aug-23 A	02-Feb-24 A	21-Sep-23	16-Dec-23	
	Primary Structures - Nodes	107d	25d	10-Oct-23 A	08-Nov-23 A	21-Sep-23	20-Dec-23	
	Primary Structures - Seamless Pipe (column)	97d	53d	26-Sep-23 A	27-Nov-23 A	30-Oct-23	29-Jan-24	
	Primary Structures - Rolled Pipe (column)	74d	53d	10-Oct-23 A	12-Dec-23 A	30-Oct-23	29-Jan-24	
	Primary Structures - Seamless Pipe (bracing)	97d	53d	26-Sep-23 A	27-Nov-23 A	30-Oct-23	29-Jan-24	
	Primary Structures - Rolled Pipe (bracing)	86d	41d	10-Oct-23 A	27-Nov-23 A	30-Oct-23	29-Jan-24	
	Transition Piece - Box Girders	199d	128d	21-Nov-23 A	26-Apr-24 A	10-Apr-24	04-Sep-24	
	Upper Grillage	89d	56d	09-Feb-24 A	16-Apr-24 A	16-Oct-23	14-Jan-24	
	Rigging Platform	87d	101d	13-May-24 A	08-Sep-24 A	13-May-24	08-Sep-24	
	Secondary Structures - Cones	43d	66d	30-Oct-23 A	21-Jan-24 A	30-Oct-23	21-Jan-24	
	Secondary Structures - Beams	116d	134d	26-Sep-23 A	06-Mar-24 A	30-Oct-23	21-Jan-24	
	Secondary Structures - Structural Plates	71d	26d	20-Nov-23 A	20-Dec-23 A	30-Oct-23	14-Jan-24	
	Secondary Structures - Racks	72d	39d	08-Jan-24 A	21-Feb-24 A	30-Oct-23	21-Jan-24	
	Caissons - Seamless Pipe and plates	98d	120d	12-Jun-24 A	30-Oct-24	10-May-24	25-Jul-24	32d
	Caissons - Cones	64d	66d	10-May-24 A	25-Jul-24 A	10-May-24	25-Jul-24	
	Caissons - Supports	98d	120d	12-Jun-24 A	30-Oct-24	10-May-24	25-Jul-24	31d
	Transition Piece - Rolled Pipe and plates	317d	128d	21-Nov-23 A	26-Apr-24 A	10-Apr-24	04-Sep-24	
	Transition Piece - Flange, cap, padeyes, bolts, stairs and door	283d	287d	21-Nov-23 A	31-Oct-24	10-Apr-24	25-Aug-24	4d
	Equipment Supports	76d	49d	22-Mar-24 A	22-May-24 A	30-Oct-23	29-Jan-24	
	Access Platform	64d	53d	13-Dec-23 A	16-Feb-24 A	30-Oct-23	29-Jan-24	
	Hatches	63d	73d	30-Oct-23 A	29-Jan-24 A	30-Oct-23	29-Jan-24	
	Lifting Padeyes	174d	25d	10-Oct-23 A	08-Nov-23 A	30-Oct-23	29-Jan-24	
	Walkways	128d	69d	13-Dec-23 A	06-Mar-24 A	30-Oct-23	29-Jan-24	
	Gratings	111d	113d	19-Jan-24 A	03-Jun-24 A	30-Oct-23	29-Jan-24	
	Handrails	68d	67d	17-Jan-24 A	05-Apr-24 A	30-Oct-23	21-Jan-24	
	Ladders	178d	30d	13-Dec-23 A	21-Jan-24 A	30-Oct-23	21-Jan-24	
	Stairs	78d	53d	13-Dec-23 A	16-Feb-24 A	30-Oct-23	21-Jan-24	
	Lower Grillage & Seafastening Beams	85d	333d	07-Dec-23 A	15-Jan-25	26-Jul-24	04-Nov-24	21d
	Bulk Material - Piping & Valves	259d	306d	28-Nov-23 A	01-Dec-24	14-Nov-23	21-Sep-24	65d
	Piping - Carbon Steel	124d	85d	08-Feb-24 A	21-May-24 A	08-Jan-24	25-May-24	
	Fittings & Flanges Carbon Steel	134d	132d	08-Feb-24 A	15-Jul-24 A	08-Jan-24	25-May-24	
	Forged Fittings - Carbon Steel	124d	116d	08-Jan-24 A	25-May-24 A	08-Jan-24	25-May-24	
	BW Fittings - Carbon Steel	141d	96d	08-Feb-24 A	03-Jun-24 A	08-Jan-24	25-May-24	
	Piping - Stainless Steel	155d	96d	08-Feb-24 A	03-Jun-24 A	08-Jan-24	07-Jun-24	
	Fittings & Flanges - Stainless Steel	155d	109d	08-Feb-24 A	18-Jun-24 A	08-Jan-24	07-Jun-24	
	Piping - Super Duplex	172d	96d	08-Feb-24 A	03-Jun-24 A	08-Jan-24	24-Jun-24	
	Fittings & Flanges Super Duplex	172d	153d	08-Feb-24 A	08-Aug-24 A	08-Jan-24	24-Jun-24	
	Forged Fittings - Super Duplex & SS	172d	136d	08-Feb-24 A	19-Jul-24 A	08-Jan-24	24-Jun-24	
	BW Fittings - Super Duplex & SS	172d	136d	08-Feb-24 A	19-Jul-24 A	08-Jan-24	24-Jun-24	
	Gaskets	170d	130d	08-Feb-24 A	12-Jul-24 A	26-Feb-24	14-Jul-24	
	Studs & Bolts	175d	165d	08-Feb-24 A	23-Aug-24 A	22-Jan-24	17-Jul-24	
	Manual Valves - Ball	258d	281d	28-Nov-23 A	01-Nov-24	14-Nov-23	21-Sep-24	63d
	Manual Valves - Check, Gate and Globe	259d	281d	28-Nov-23 A	31-Oct-24	14-Nov-23	21-Sep-24	90d

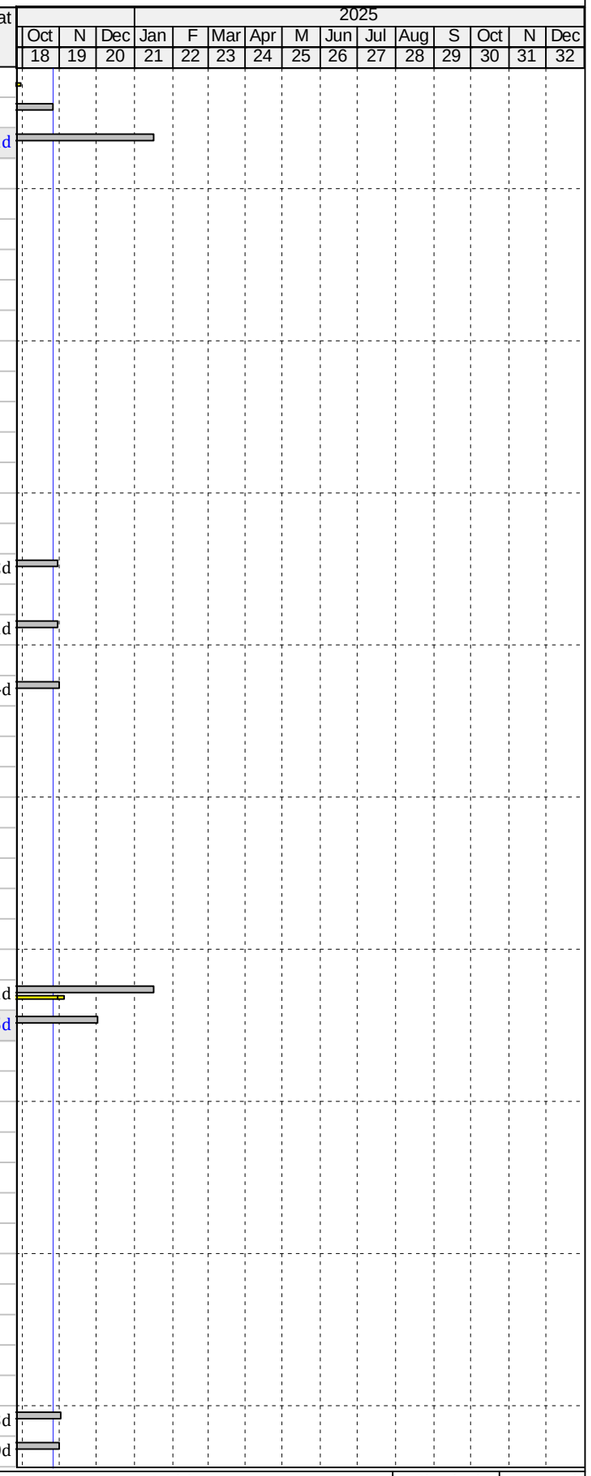


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
Milestone
summary
Notification Mechanism

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
	Manual Valves - DBB & SBB	239d	280d	28-Nov-23 A	30-Oct-24	14-Nov-23	21-Sep-24	64d
	Flame Arresters & Bird Screen	201d	187d	17-Jan-24 A	27-Aug-24 A	17-Jan-24	27-Aug-24	
	Y Strainers	171d	176d	08-Jan-24 A	03-Aug-24 A	08-Jan-24	03-Aug-24	
	Expansion Joints	117d	178d	20-Dec-23 A	23-Jul-24 A	20-Dec-23	23-Jul-24	
	Piping supports (incl. Spring Supports, if any)	126d	163d	23-May-24 A	01-Dec-24	29-Feb-24	09-Aug-24	43d
	Bulk Material - Electrical, Instrumentation, Control	317d	384d	20-Nov-23 A	26-Feb-25	10-Nov-23	27-Nov-24	204d
	Cable Trays and Ladder	85d	140d	15-Mar-24 A	30-Aug-24 A	15-Feb-24	01-Aug-24	
	Instrument & Telecom Cable Trays	150d	140d	15-Mar-24 A	30-Aug-24 A	05-Feb-24	22-Jul-24	
	Electrical HV Cables	277d	289d	15-Mar-24 A	26-Feb-25	31-Jan-24	04-Sep-24	3d
	Electrical MV Cables	165d	113d	15-Mar-24 A	29-Jul-24 A	31-Jan-24	04-Sep-24	
	Electrical LV Cables	150d	164d	15-Mar-24 A	27-Sep-24 A	06-Feb-24	16-Sep-24	
	Instrumental cables	183d	106d	25-Mar-24 A	30-Jul-24 A	21-Feb-24	24-Sep-24	
	Telecom cables	107d	81d	26-Apr-24 A	30-Jul-24 A	09-Feb-24	05-Oct-24	
	Earthing Cables	157d	113d	15-Mar-24 A	29-Jul-24 A	28-Dec-23	27-Aug-24	
	Earthing accessories	97d	177d	13-Mar-24 A	10-Oct-24 A	11-Jan-24	18-Jun-24	
	Heat Tracing	113d	111d	24-Jun-24 A	31-Oct-24	23-Jan-24	09-Aug-24	77d
	Cable Glands	122d	120d	15-Apr-24 A	04-Sep-24 A	15-Feb-24	01-Aug-24	
	Connections & Terminations	240d	172d	21-Feb-24 A	13-Sep-24 A	23-Feb-24	26-Aug-24	
	Junction Boxes	107d	182d	01-Mar-24 A	04-Oct-24 A	28-Dec-23	16-Jun-24	
	MCT	47d	99d	08-Mar-24 A	05-Jul-24 A	23-Feb-24	13-Jul-24	
	Instrument & Telecom MCT	114d	45d	15-May-24 A	05-Jul-24 A	09-Feb-24	28-Jun-24	
	Instrument Junction Boxes	226d	116d	15-Apr-24 A	30-Aug-24 A	27-Nov-23	13-Jul-24	
	Instrument Cable Glands & Accessories	232d	120d	15-Apr-24 A	04-Sep-24 A	15-Feb-24	09-Oct-24	
	Floor penetration for GIS & MV cables	57d	18d	20-Nov-23 A	11-Dec-23 A	10-Nov-23	10-Apr-24	
	Lighting Fixtures	121d	146d	22-Mar-24 A	13-Sep-24 A	28-Dec-23	31-Jul-24	
	Small Power Sockets	93d	182d	01-Mar-24 A	04-Oct-24 A	02-Jan-24	07-Aug-24	
	Pressure, Temperature and Diff. Pressure Level Transmitters	239d	173d	17-Jan-24 A	09-Aug-24 A	04-Jan-24	02-Oct-24	
	Radar Level Transmitters	167d	173d	17-Jan-24 A	09-Aug-24 A	04-Jan-24	02-Oct-24	
	Variable Area Flow Transmitters and Flow gauges	220d	199d	26-Feb-24 A	19-Oct-24 A	04-Jan-24	02-Oct-24	
	Ultrasonic Flow Transmitters	216d	237d	18-Mar-24 A	27-Dec-24	04-Jan-24	02-Oct-24	55d
	Flow Gauges	171d	201d	28-Feb-24 A	24-Oct-24 A	04-Jan-24	02-Oct-24	
	F&G Detectors	256d	198d	05-Feb-24 A	27-Sep-24 A	15-Dec-23	27-Nov-24	
	Dew Point Analyzer	187d	222d	04-Jan-24 A	25-Sep-24 A	04-Jan-24	30-Jul-24	
	Orifice	115d	132d	16-Jul-24 A	18-Dec-24	20-Dec-23	23-Sep-24	260d
	Tubing	157d	148d	27-Mar-24 A	20-Sep-24 A	09-Feb-24	20-Sep-24	
	E&I supports (incl. Bulk Material)	138d	93d	30-Jan-24 A	21-May-24 A	08-Jan-24	27-Jun-24	
	Bulk Material - Insulation & Coating	248d	293d	17-Nov-23 A	05-Nov-24	18-Dec-23	24-Aug-24	84d
	Painting for Structures	61d	100d	17-Nov-23 A	18-Mar-24 A	18-Dec-23	21-Feb-24	
	Painting for Piping	98d	42d	03-May-24 A	20-Jun-24 A	15-Mar-24	17-May-24	
	Insulation	136d	106d	03-Jul-24 A	05-Nov-24	15-Mar-24	24-Aug-24	84d
	All Other Material	366d	387d	13-Nov-23 A	22-Feb-25	30-Oct-23	28-Nov-24	4d
	Safety Signs	97d	99d	25-Oct-24 A	22-Feb-25	14-Jun-24	24-Oct-24	4d
	Safety Equipment	104d	127d	03-Jul-24 A	29-Nov-24	14-Jun-24	24-Oct-24	73d
	Firefighting Equipment	114d	127d	03-Jul-24 A	29-Nov-24	14-Jun-24	24-Oct-24	73d
	Nitrogen Generation Package and Nitrogen bottles - Option	274d	293d	15-Nov-23 A	02-Nov-24	30-Oct-23	28-Nov-24	67d
	Mechanical Handling – Monorail - Option	43d	51d	13-Nov-23 A	16-Jan-24 A	13-Nov-23	16-Jan-24	

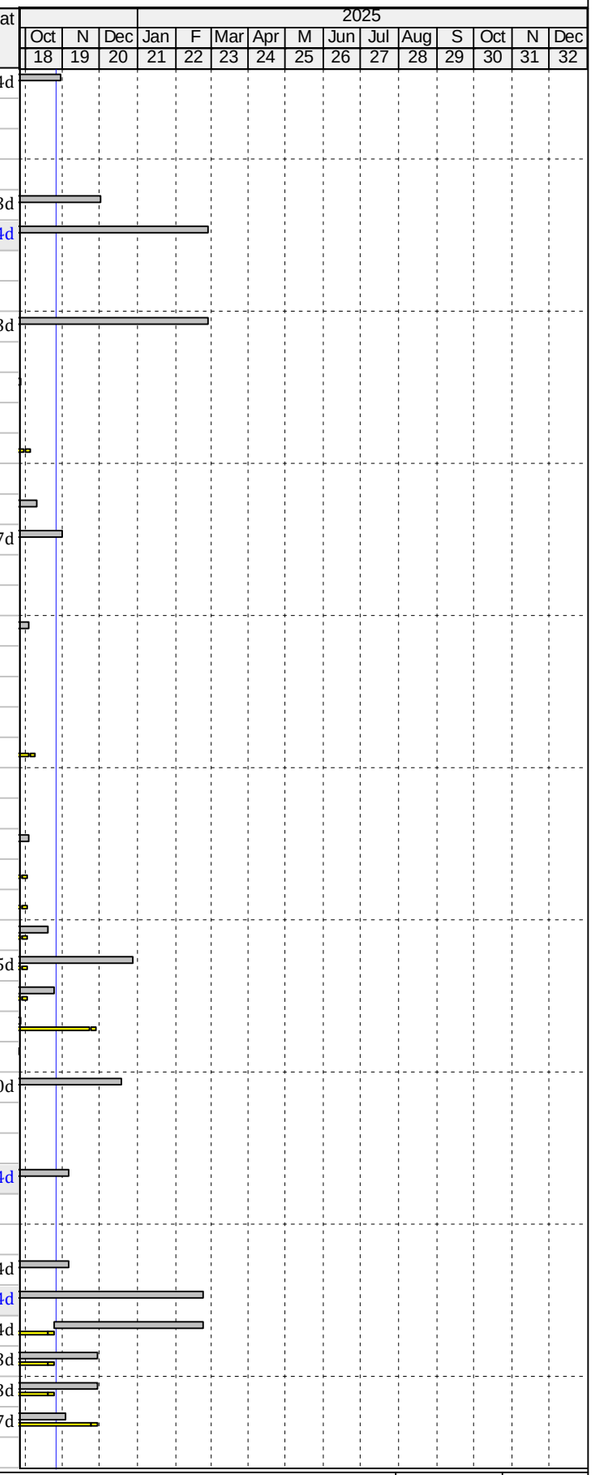

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

CROSSWIND


HOLLANDSE KUST NOORD WIND PARK Project

BASE LOAD POWER HUB

Contract No. CW-I-WP4-2023-05

ROSETTI MARINO

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Fabrication		435d	559d	10-Jul-23 A	16-May-25	27-Dec-23	16-May-25	141d
Onshore Fabrication		408d	511d	10-Jul-23 A	15-Mar-25	27-Dec-23	03-Apr-25	189d
Structural		386d	396d	22-Nov-23 A	14-Mar-25	27-Dec-23	19-Mar-25	190d
Piping		161d	208d	10-Jun-24 A	13-Feb-25	27-May-24	26-Nov-24	32d
MH SUMMARY - Mechanical		99d	101d	22-Jul-24 A	18-Nov-24	22-Jun-24	19-Sep-24	103d
Mechanical		138d	468d	10-Jul-23 A	24-Jan-25	30-Jul-24	04-Dec-24	45d
Electrical		187d	198d	22-Jul-24 A	15-Mar-25	27-Aug-24	03-Dec-24	6d
Instrumentation		152d	151d	22-Jul-24 A	20-Jan-25	27-Aug-24	03-Dec-24	236d
Telecommunication		57d	1d	23-Aug-24 A	23-Aug-24 A	03-Oct-24	19-Nov-24	
Safety		24d	24d	10-Feb-25	08-Mar-25	12-Oct-24	18-Nov-24	12d
Key Package Integration		233d	475d	10-Jul-23 A	01-Feb-25	18-Sep-24	03-Apr-25	121d
Mechanical Completion		172d	173d	23-Aug-24 A	18-Mar-25	11-Sep-24	28-Dec-24	91d
CON-FIN0904	Finalization - Electrical Mechanical Completion (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	60d	1d	23-Aug-24 A	23-Aug-24 A	28-Sep-24	07-Dec-24	
CON-FIN0902	Finalization - Equipment & Piping Mechanical Completion (DELETED AFTER REVISED SCHEDULE AUGUST 2(	60d	1d	23-Aug-24 A	23-Aug-24 A	28-Sep-24	07-Dec-24	
CON-FIN0906	Finalization - Instrumentation & Telecomm Mechanical Completion (DELETED AFTER REVISED SCHEDULE AU	60d	1d	23-Aug-24 A	23-Aug-24 A	17-Oct-24	28-Dec-24	
CON-FIN0910	Finalization - Painting and Insulation Mechanical Completion	40d	40d	31-Jan-25	18-Mar-25			4d
CON-FIN1100	Finalization - PRE-COMM - Leak Testing (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	10d	1d	23-Aug-24 A	23-Aug-24 A	27-Nov-24	07-Dec-24	
CON-FIN0920	Finalization - Safety Mechanical Completion	20d	20d	24-Feb-25	18-Mar-25			4d
CON-FIN0900	Finalization - Structural Mechanical Completion - Build (Arch+Struc+MCT+Cable Tray)	60d	60d	09-Dec-24	20-Feb-25	11-Sep-24	20-Nov-24	26d
Mechanical Completion - Transformer 0,4/6,6kV 630kVA		15d	15d	26-Oct-24	09-Nov-24			120d
Mechanical Completion - Transformer Aux. 6.6/0.4kV		15d	15d	26-Oct-24	09-Nov-24			120d
Mechanical Completion - Transformer Main 66/6.6kV		15d	15d	16-Nov-24	30-Nov-24			93d
Mechanical Completion - BESS Without Batteries		13d	13d	05-Nov-24	19-Nov-24			26d
Mechanical Completion - AC & DC UPS		10d	10d	26-Oct-24	04-Nov-24			64d
Mechanical Completion - BESS with Batteries		54d	54d	20-Nov-24	26-Jan-25			28d
Mechanical Completion - LV Switchboard 400V		10d	54d	09-Sep-24 A	01-Nov-24			50d
Mechanical Completion - HV/MV Switchboard 66kV/6.6kV		9d	9d	26-Oct-24	03-Nov-24			105d
Mechanical Completion - F&G - SIS -PCS		15d	15d	28-Oct-24	11-Nov-24			81d
Mechanical Completion - Fuel Cell System		15d	15d	10-Nov-24	24-Nov-24			96d
Mechanical Completion - ICSS		9d	9d	26-Oct-24	03-Nov-24			89d
Mechanical Completion - Small Power Sockets		18d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - Telecomm		9d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - H2 Storage Vessels		16d	16d	15-Nov-24	30-Nov-24			107d
Mechanical Completion - Lighting Fixtures		15d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - Trace Heating		15d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - Water treatment system		15d	15d	25-Nov-24	09-Dec-24			84d
Mechanical Completion - GIS		9d	9d	02-Feb-25	10-Feb-25			148d
Finalization		35d	35d	01-Apr-25	16-May-25	01-Apr-25	16-May-25	2d
Onshore Commissioning & Integrated Testing		326d	545d	10-Jul-23 A	29-Apr-25	07-Dec-24	02-May-25	155d
Construction		252d	292d	10-Jul-23 A	26-Apr-24 A			
Onshore Commissioning (Systems/Subsystems)		134d	149d	20-Sep-24 A	19-Mar-25	02-Apr-25	02-Apr-25	4d
Onshore Commissioning - MH SUMMARY/Baseline		226d	54d	21-Jun-24 A	23-Aug-24 A	07-Dec-24	01-Apr-25	
Onshore Testing		32d	32d	19-Mar-25	29-Apr-25	14-Mar-25	02-May-25	155d
Transpotation and Installation		10d	10d	05-May-25	15-May-25	05-May-25	15-May-25	2d
CON-FIN1050	Finalization - Load-Out & Sea-Fastening	10d	10d	05-May-25	15-May-25	05-May-25	15-May-25	2d

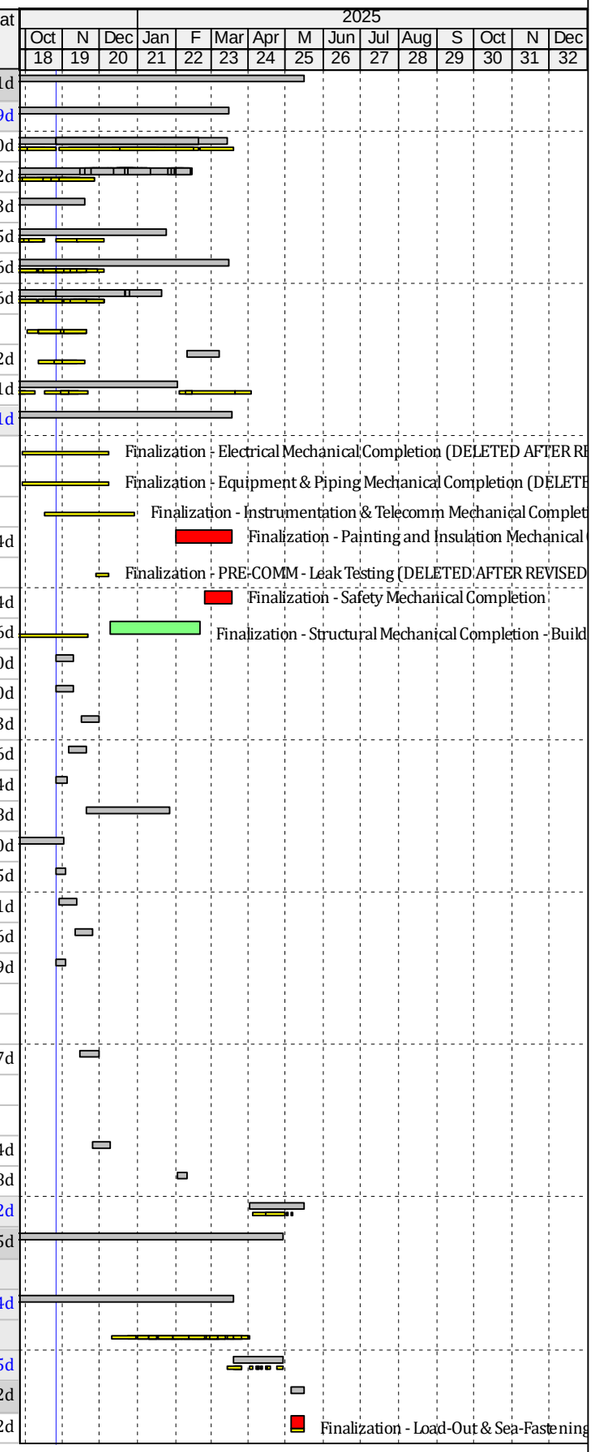

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
Milestone
summary
Notification Mechanism


Data Date: 25-Oct-24

CROSSWIND BLPH EPCI

Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-FIN1080	Finalization - Transition Piece Load-Out & Sea-Fastening	7d	7d	05-May-25	12-May-25	07-May-25	14-May-25	5d
Installation at Project Site		63d	63d	22-Apr-25	24-Jun-25	22-Apr-25	25-Jun-25	38d
Mob/Demob Vessel		63d	63d	22-Apr-25	24-Jun-25	22-Apr-25	25-Jun-25	38d
Installation Vessel + Support Vessel		56d	56d	24-Apr-25	19-Jun-25	24-Apr-25	20-Jun-25	2d
Offshore Hook-Up, Commissioning and Start-Up		41d	41d	19-Jun-25	30-Jul-25	21-Jun-25	01-Aug-25	2d
Hook-Up Activities		25d	25d	19-Jun-25	13-Jul-25	21-Jun-25	15-Jul-25	6d
Offshore Commissioning		40d	40d	20-Jun-25	30-Jul-25	22-Jun-25	01-Aug-25	2d
Start-Up		7d	7d	23-Jul-25	29-Jul-25	25-Jul-25	31-Jul-25	2d
Variation Orders		180d	189d	15-Apr-24 A	25-Nov-24			97d
Variation Orders		180d	189d	15-Apr-24 A	25-Nov-24			97d

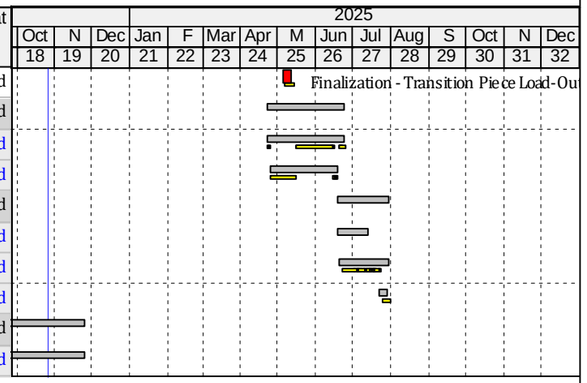

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
Milestone
summary
Notification Mechanism

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR
