CROSSWIND


HOLLANDSE KUST NOORD WIND PARK Project

BASE LOAD POWER HUB

Contract No. CW-I-WP4-2023-05

ROSETTI MARINO

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
123A90 - Cross Wind BLPH - Preliminary Lvl 4. Schedule - baseline issued 25.10.2024		800d	731d	31-May-23 A	28-Oct-25	31-May-23	14-Nov-25	2d
Milestones & Key Dates		731d	731d	31-May-23 A	28-Oct-25	31-May-23	14-Nov-25	2d
MIL-10	Notification Tender Result	0d	0d	31-May-23 A		31-May-23		
MIL-20	Contract Start Date	0d	0d	10-Jul-23 A		10-Jul-23		
MIL-30	Project Completion	0d	0d		28-Oct-25*		14-Nov-25	2d
Key Dates		703d	706d	22-Nov-23 A	28-Oct-25	07-Oct-23	30-Oct-25	2d
KD06	KD06 - Start of construction of steel structure - (Contract: 27.12.2023)	0d	0d	22-Nov-23 A		27-Dec-23		
KD01	KD01 - HAZOP Workshop conducted and report issued - (Contract: 28.11.2023)	0d	0d	08-Dec-23 A		23-Dec-23		
KD07	KD07 - Purchase Order of Electrical Equipment (Main & Aux Trafo, HV&MV Switchgear) issued - (Contract: 01.(	0d	0d	21-Dec-23 A		07-Oct-23		
KD05	KD05 - Primary Steel Construction Drawings AFC issued - (Contract: 27.12.2023)	0d	0d	22-Dec-23 A		27-Dec-23		
KD02a	KD02a - 30% Model Review completed and report issued - (Contract: 15.11.2023)	0d	0d	22-Dec-23 A		15-Nov-23		
KD04	KD04 - Purchase Order (1st batch) of Primary and Secondary Structural Steel issued (& accepted) - (Contract: 0	0d	0d	26-Jan-24 A		13-Dec-23		
KD03	KD03 - Purchase Order of Desalination Unit issued (& accepted) - (Contract: 11.12.2023)	0d	0d	23-Feb-24 A		24-Jan-24		
KD02b	KD02b - 60% Model Review completed and report issued - (Contract: 29.02.2024)	0d	0d	15-Jul-24 A		29-Feb-24		
KD02c	KD02c - 90% Model Review completed and report issued - (Contract: 13.06.2024)	0d	0d	25-Jul-24 A		20-Jun-24		
KD08	KD08 - Assembly of Steel Structure of Lower Deck (Primary and Secondary Steel) completed - (Contract: 29.03.2	0d	0d	16-Nov-24		29-Mar-24		348d
KD09	KD09 - Installation of Mechanical Equipment of Lower Deck completed - (Contract: 28.09.2024)	0d	0d	20-Nov-24		16-Oct-24		344d
KD10	KD10 - Mechanical Completion finished - (Contract: 07.12.2024)	0d	0d	21-Feb-25		07-Dec-24		251d
KD11	KD11 - Onshore Commissioning completed - (Contract: 02.04.2025)	0d	0d	19-Mar-25		02-Apr-25		225d
KD12	KD12 - Onshore Integrated Testing completed - (Contract: 01.05.2025)	0d	0d	29-Apr-25		02-May-25		184d
KD13	KD13 - Ready for Sail-away Certificate issued - (Contract: 16.05.2025)	0d	0d	16-May-25		16-May-25		101d
KD14	KD14 - CONTRACTOR Ready in All Respects to Commence Topsides Installation at the PROJECT SITE.	0d	0d	16-Jun-25		16-Jun-25		70d
KD15	KD15 - Topsides Installation completed - (Contract: 21.06.2025) - LD	0d	0d	19-Jun-25		21-Jun-25		18d
KD16	KD16 - HANDOVER CERTIFICATE for the whole PERMANENT WORK issued - (Contract: 01.08.2025)	0d	0d	30-Jul-25		01-Aug-25		2d
KD17	KD17 - Topsides As-Builts issued - (Contract: 15.09.2025)	0d	0d	13-Sep-25		15-Sep-25		47d
KD18	KD18 - COMPLETION - (Contract: 30.10.2025)	0d	0d	28-Oct-25		30-Oct-25		2d
Notification Mechanism (Assumption - As Early As Possible)		185d	185d	10-Jan-25	20-Aug-25	02-Sep-24	20-Aug-25	60d
NOTIF. MECH 3	Period 3 -10th January - (15.06.2025 -14.07.2025)	30d	30d	10-Jan-25*	14-Jul-25	10-Jan-25	14-Jul-25	107d
NOTIF. MECH 4	Period 4 - 150 days before Start of Period 3 - (15.06.2025 -29.06.2025)	15d	15d	17-Jan-25*	29-Jun-25	17-Jan-25	29-Jun-25	122d
NOTIF. MECH 5	Period 5 - 21 days before Start of Period 4 - (15.06.2025 -21.06.2025)	7d	7d	26-May-25*	21-Jun-25	26-May-25	21-Jun-25	130d
NOTIF. MECH 6	Period 6 - 10 days before Start of Period 5 - (15.06.2025 -17.06.2025)	3d	3d	05-Jun-25*	17-Jun-25	05-Jun-25	17-Jun-25	134d
NOTIF. MECH 7	Period 7 - 5 days before Start of Period 6 - (15.06.2025 -15.06.2025)	1d	1d	10-Jun-25*	10-Jun-25	10-Jun-25	16-Jun-25	136d
NOTIF. MECH 1	Period 1 - Effective Date - (15.06.2025 -20.08.2025)	66d	66d	16-Jun-25	20-Aug-25	16-Jun-25	20-Aug-25	70d
NOTIF. MECH 2	Period 2 -1st September 2024 - (15.06.2025 -29.07.2025)	45d	45d	16-Jun-25*	30-Jul-25	02-Sep-24	29-Jul-25	91d
Detail Engineering		406d	491d	02-Aug-23 A	20-Dec-24	10-Jul-23	05-Apr-24	215d
Contract Deliverables		406d	491d	02-Aug-23 A	20-Dec-24	10-Jul-23	05-Apr-24	215d
CDL-POS-1	Performance Bond Guarantee	0d	0d		02-Aug-23 A		31-Jul-23	
CDL-POS-3	Final format of Invoice	0d	0d		02-Aug-23 A		09-Aug-23	
CDL-POS-28	Procedures for Freight Handling and Shipment	0d	0d		04-Aug-23 A		08-Sep-23	
CDL-POS-47	WBS Structure	0d	0d		04-Aug-23 A		10-Jul-23	
CDL-POS-2	Cover Sheet - template	0d	0d		07-Aug-23 A		07-Aug-23	
CDL-POS-8	Focal Points for Information Technology	0d	0d		07-Aug-23 A		09-Aug-23	
CDL-POS-9	IT Plan	0d	0d		07-Aug-23 A		09-Aug-23	
CDL-POS-10	Information Risk Management Procedures	0d	0d		07-Aug-23 A		09-Aug-23	
CDL-POS-7	Document Control Procedure	0d	0d		09-Aug-23 A		09-Aug-23	

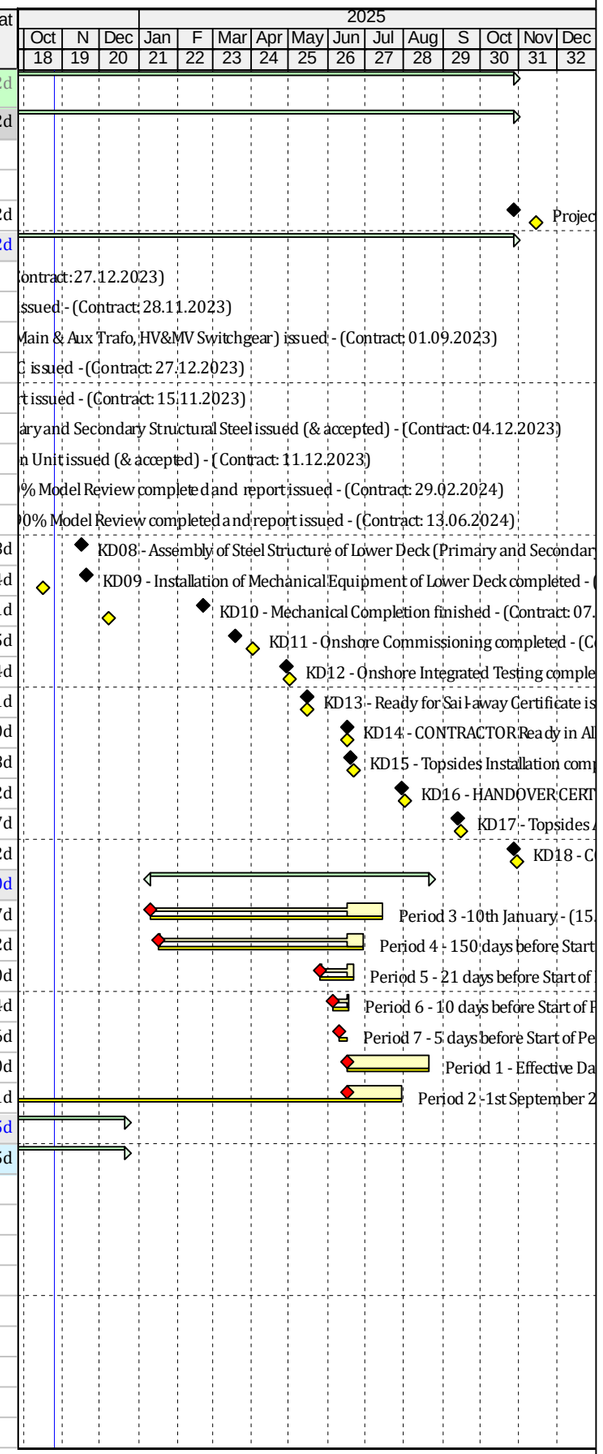

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Data Date: 25-Oct-24

CROSSWIND BLPH EPCI

Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CDL-POS-4	Project Controls Plan	0d	0d		11-Aug-23 A		09-Aug-23	
CDL-POS-6	EXECUTION PLAN	0d	0d		11-Aug-23 A		09-Aug-23	
CDL-POS-12	Schedule of Design Reviews, Studies and Workshops	0d	0d		11-Aug-23 A		09-Aug-23	
CDL-POS-13	Contract HSSE Plan	0d	0d		11-Aug-23 A		09-Aug-23	
CDL-POS-21	Digital Delivery Execution Plan	0d	0d		11-Aug-23 A		24-Aug-23	
CDL-POS-29	Materials Management Plan	0d	0d		11-Aug-23 A		08-Sep-23	
CDL-POS-14	Schedule of required dates for delivery of CPI	0d	0d		23-Aug-23 A		21-Aug-23	
CDL-POS-11	Key Performance Indicators	0d	0d		24-Aug-23 A		09-Aug-23	
CDL-POS-20	Weight Management and Weighing Procedure	0d	0d		24-Aug-23 A		24-Aug-23	
CDL-POS-15	Project Controls Plans Procedures	0d	0d		29-Aug-23 A		24-Aug-23	
CDL-POS-18	Master Deliverables Register	0d	0d		31-Aug-23 A		24-Aug-23	
CDL-POS-5	Baseline Schedule (L1,2,3)	0d	0d		01-Sep-23 A		09-Aug-23	
CDL-POS-32	Project Quality Plan, including any procedures	0d	0d		01-Sep-23 A		08-Sep-23	
CDL-POS-36	Contractor Audit Plan	0d	0d		04-Sep-23 A		08-Sep-23	
CDL-POS-33	Storage, Packing, Protection and Preservation Procedure	0d	0d		06-Sep-23 A		08-Sep-23	
CDL-POS-16	First Monthly Project Management Report	0d	0d		08-Sep-23 A		24-Aug-23	
CDL-POS-24	Information Quality Management Framework (IQMF)	0d	0d		08-Sep-23 A		08-Sep-23	
CDL-POS-25	Project Codes and Standards Report	0d	0d		08-Sep-23 A		08-Sep-23	
CDL-POS-27	Contracting and Procurement Plan	0d	0d		08-Sep-23 A		08-Sep-23	
CDL-POS-35	Criticiality Assessment	0d	0d		18-Sep-23 A		08-Sep-23	
CDL-POS-23	CPI Engineering Data Transfer Plan	0d	0d		19-Sep-23 A		24-Aug-23	
CDL-POS-46	Systems List and Systems Master Document	0d	0d		20-Sep-23 A		05-Apr-24	
CDL-POS-17	Baseline of quantities for key elements of the Scope (reimbursable)	0d	0d		27-Sep-23 A		24-Aug-23	
CDL-POS-39	Construction Execution Plan	0d	0d		13-Oct-23 A		08-Oct-23	
CDL-POS-31	Overall schedule for Offshore Phase	0d	0d		20-Oct-23 A		08-Sep-23	
CDL-POS-26	First Weight Report	0d	0d		09-Feb-24 A		08-Sep-23	
CDL-POS-41	SECE Information and Guidelines	0d	0d		22-Feb-24 A		08-Oct-23	
CDL-POS-37	Permits and Consents Workshop	0d	0d		04-Mar-24 A		08-Oct-23	
CDL-POS-38	Master Tag and Equipment Register - EIS Data	0d	0d		17-May-24 A		08-Oct-23	
CDL-POS-19	Fully detailed SAFOP	0d	0d		12-Jun-24 A		24-Aug-23	
CDL-POS-22	Lessons Learnt Workshop	0d	0d		25-Oct-24		24-Aug-23	269d
CDL-POS-30	Data Delivery Plan for CMMS	0d	0d		25-Oct-24		08-Sep-23	269d
CDL-POS-34	Repeated Failures Management Plan	0d	0d		25-Oct-24		08-Sep-23	269d
CDL-POS-40	Operations Readiness Plan	0d	0d		25-Oct-24		08-Oct-23	269d
CDL-POS-42	Commissioning and Handover Procedures - Index	0d	0d		25-Oct-24		07-Nov-23	124d
CDL-POS-43	Systemisation Workshop	0d	0d		25-Oct-24		07-Jan-24	73d
CDL-POS-44	Specialist Subcontractor Plan	0d	0d		25-Oct-24		07-Jan-24	124d
CDL-POS-45	Operating Philosophy	0d	0d		20-Dec-24		27-Jan-24	70d
Payment Milestones		627d	722d	25-Jul-23 A	16-Jul-25	25-Jul-23	16-Jul-25	16d
Additional Milestone Proposal		0d	26d	25-Jul-23 A	20-Aug-23 A	25-Jul-23	20-Aug-23	
PM-MIL-6	Mobilisation Project Management Team (Key Personnel)	0d	0d	25-Jul-23 A		25-Jul-23		
ING-MIL-7	Mobilisation Engineering Team (Key Personnel)	0d	0d	20-Aug-23 A		20-Aug-23		
FIN-MIL-1	Financial Securities Issued	0d	0d	20-Aug-23 A		20-Aug-23		
Project Management incl. Services for Company, Documentation, Insurances/Financial Guarantees		364d	429d	24-Aug-23 A	26-Oct-24	10-Aug-23	10-Oct-23	279d
PM-MIL-1	All 30 day deliverables issued	0d	0d	24-Aug-23 A		10-Aug-23		
PM-MIL-2	All 60 day deliverables issued	0d	0d	26-Oct-24		09-Sep-23		279d

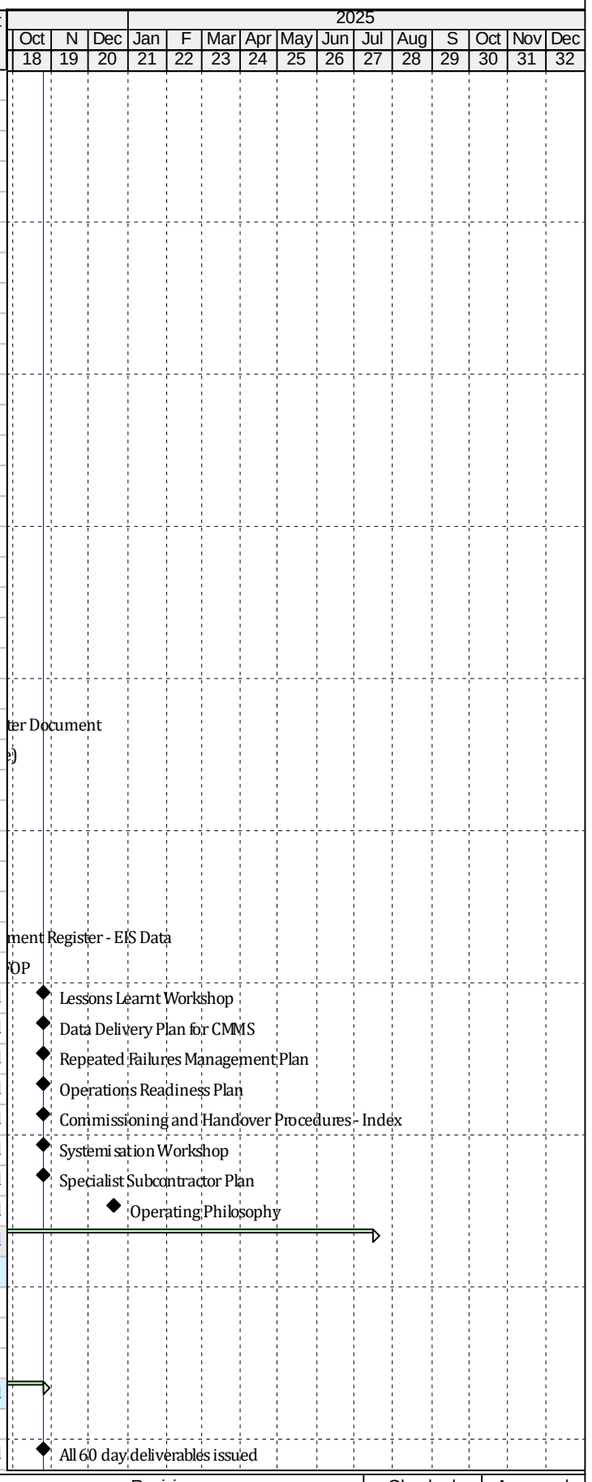


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PM-MIL-3	All 90 day deliverables issued	0d	0d	26-Oct-24		10-Oct-23		279d
BLPH Engineering		625d	720d	25-Jul-23 A	14-Jul-25	25-Jul-23	16-Jul-25	18d
ING-MIL-1	Kick off Meeting	0d	0d	25-Jul-23 A		25-Jul-23		
ING-MIL-4	All primary steel drawings issued AFC (Accepted for Construction) and accepted by COMPANY	0d	0d	21-Dec-23 A		27-Dec-23		
ING-MIL-8	30% Model Review completed and report issued and accepted by COMPANY	0d	0d	22-Dec-23 A		15-Nov-23		
ING-MIL-2	60% Model Review completed and report issued and accepted by COMPANY	0d	0d	12-Mar-24 A		29-Feb-24		
ING-MIL-5	90% Model Review completed and report issued and accepted by COMPANY	0d	0d	25-Jul-24 A		20-Jun-24		
ING-MIL-3	HAZOP conducted and all CONTRACTOR's actions closed and accepted by COMPANY	0d	0d	18-Oct-24 A		12-Jan-24		
ING-MIL-6	Delivery of Final Documentation Package before HANDOVER (As-built documentation issued) - Onshore	0d	0d	14-Jul-25		16-Jul-25		18d
BLPH Procurement; Materials and Equipment Supply - Issued Unpriced PO		406d	332d	08-Sep-23 A	05-Aug-24 A	11-Oct-23	10-Apr-24	
MAT-MIL-1	Purchase of Structural Steel [unpriced PO submitted]	0d	0d	08-Sep-23 A		31-Oct-23		
MAT-MIL-3	Other Equipment/Materials - [Transformer Main 66kV, Transformer Aux 6.6kV, HV Switchgear 66kV, MV Switcl	0d	0d	21-Dec-23 A		11-Oct-23		
MAT-MIL-5	Bulk Materials (Piping)	0d	0d	26-Apr-24 A		24-Feb-24		
MAT-MIL-2	Other Equipment/Materials - [H2 Vessel, Air Compressor Package, Davit Crane, Instrument Room, Electrical Roc	0d	0d	17-May-24 A		28-Feb-24		
MAT-MIL-7	Bulk Materials (E & I)	0d	0d	05-Aug-24 A		10-Apr-24		
BLPH Procurement; Materials and Equipment Supply - Delivery of Materials		546d	570d	22-Dec-23 A	14-Jul-25	17-Dec-23	16-Jul-25	18d
MAT-MIL-9	Structural Steel	0d	0d	22-Dec-23 A		17-Dec-23		
MAT-MIL-12	Other Equipment/Materials - [Instrument Room, Electrical Room LV and HV] - Delivery 3	0d	0d	30-Jul-24 A		30-Jul-24		
MAT-MIL-19	Bulk Materials (Piping)	0d	0d	01-Aug-24 A		25-Jun-24		
MAT-MIL-16	Other Equipment/Materials - [Transformer Main 66kV, Transformer Aux 6.6kV] - Delivery 7	0d	0d	31-Aug-24 A		04-Nov-24		
MAT-MIL-15	Other Equipment/Materials - [Control System CCS] - Delivery 6	0d	0d	18-Oct-24 A		03-Sep-24		
MAT-MIL-21	Bulk Materials (E & I)	0d	0d	26-Oct-24		27-Aug-24		279d
MAT-MIL-11	Other Equipment/Materials - [Air Compressor Package] - Delivery 2	0d	0d	01-Nov-24		26-Sep-24		273d
MAT-MIL-10	Other Equipment/Materials - [H2 Vessel] - Delivery 1	0d	0d	08-Nov-24		23-Nov-24		266d
MAT-MIL-13	Other Equipment/Materials - [Davit Crane] - Delivery 4	0d	0d	21-Dec-24		14-Sep-24		223d
MAT-MIL-14	Other Equipment/Materials - [HV Switchgear 66kV, MV Switchgear 6.6kV] - Delivery 5	0d	0d	16-Jan-25		01-Feb-25		197d
MAT-MIL-22	Delivery of Final Documentation Package before HANDOVER (As-built documentation issued) - Onshore	0d	0d	14-Jul-25		16-Jul-25		18d
Onshore Fabrication		119d	119d	19-Mar-25	16-Jul-25	28-Dec-24	16-Jul-25	16d
FAB-MIL-2	Mechanical Completion Certificate	0d	0d	19-Mar-25		28-Dec-24		135d
FAB-MIL-3	Ready for Sail-away Certificate Issued (Final Acceptance Test)	0d	0d	16-May-25		16-May-25		16d
FAB-MIL-4	Delivery of Final Documentation Package before HANDOVER (As-built documentation issued) - Onshore	0d	0d	16-Jul-25		16-Jul-25		16d
Onshore Pre-Commissioning and Commissioning, Onshore Integrated Testing		186d	186d	09-Jan-25	14-Jul-25	07-Dec-24	16-Jul-25	18d
COM-MIL-1	Leak Testing Complete	0d	0d	09-Jan-25		07-Dec-24		106d
COM-MIL-2	Onshore Commissioning Complete (Certificate issued)	0d	0d	19-Mar-25		02-Apr-25		37d
COM-MIL-3	Onshore Integrated Testing Complete (Certificate issued)	0d	0d	29-Apr-25		01-May-25		19d
COM-MIL-4	Delivery of Final Documentation Package before HANDOVER (As-built documentation issued) - Onshore	0d	0d	14-Jul-25		16-Jul-25		18d
BLPH Load Out, Transportation Readiness and Transport to Project Site		74d	74d	03-May-25	16-Jul-25	15-Feb-25	16-Jul-25	16d
T&I-MIL-1	All T&I Engineering deliverables issued and accepted by COMPANY	0d	0d	03-May-25		15-Feb-25		90d
T&I-MIL-2	Load out Certificate Signed off by MWS (PERMANENT WORK Loaded out)	0d	0d	16-May-25		16-May-25		77d
T&I-MIL-3	Ready for Sail-away Certificate Issued (Final Acceptance Test)	0d	0d	16-May-25		16-May-25		77d
T&I-MIL-4	Arrival of PERMANENT WORK at PROJECT SITE	0d	0d	16-Jun-25		16-Jun-25		46d
T&I-MIL-5	Completion of Heavy Lift Vessel MOBILISATION at PROJECT SITE	0d	0d	16-Jun-25		16-Jun-25		16d
T&I-MIL-6	Delivery of Final Documentation Package before HANDOVER (As-built documentation issued) - Offshore	0d	0d	16-Jul-25		16-Jul-25		16d
Project Management		565d	580d	10-Jul-23 A	23-Oct-25	10-Jul-23	23-Oct-25	4d
Project Management		491d	489d	10-Jul-23 A	17-Jun-25	10-Jul-23	19-Jun-25	2d
PROMAN1000	Project Management	491d	489d	10-Jul-23 A	17-Jun-25	10-Jul-23	19-Jun-25	2d

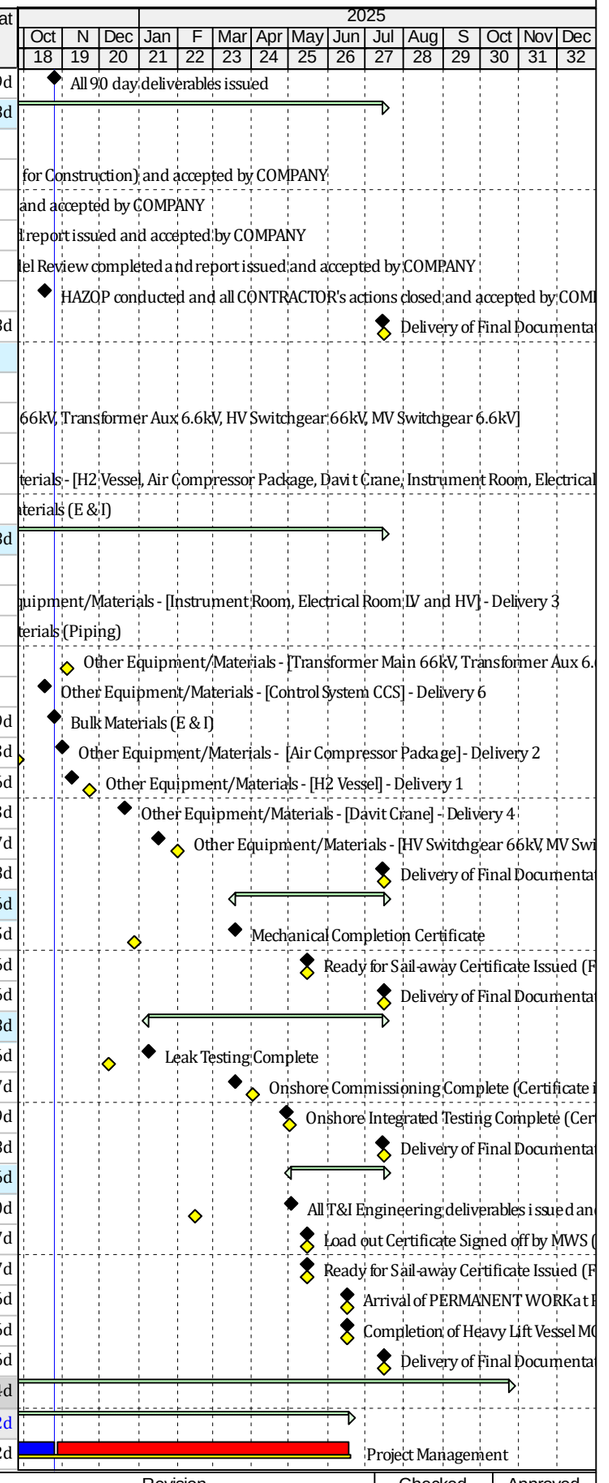


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Services to be provided to COMPANY		491d	491d	10-Jul-23 A	19-Jun-25	10-Jul-23	19-Jun-25	93d
PROMAN1010	Services to be provided to COMPANY	491d	491d	10-Jul-23 A	19-Jun-25	10-Jul-23	19-Jun-25	93d
Financial Guarantees		565d	565d	31-Jul-23 A	23-Oct-25	31-Jul-23	23-Oct-25	4d
PROMAN1020	Financial Guarantees	565d	565d	31-Jul-23 A	23-Oct-25	31-Jul-23	23-Oct-25	4d
Engineering		593d	593d	10-Jul-23 A	25-Jun-25	10-Jul-23	09-Jul-25	107d
Detail Engineering		519d	519d	10-Jul-23 A	25-Mar-25	10-Jul-23	18-Jan-25	181d
General		436d	415d	25-Aug-23 A	08-Jan-25	19-Sep-23	08-Jan-25	55d
ENG-MULTI-1020-A	Monthly Weight Report - IFA	15d	139d	25-Aug-23 A	09-Feb-24 A	19-Sep-23	05-Oct-23	
ENG-MULTI-1020-B	Monthly Weight Report - IFC	289d	250d	12-Mar-24 A	08-Jan-25	18-Oct-23	08-Jan-25	55d
ENG-MULTI-1030-A	Permit Management Plan - IFA	15d	15d	26-Oct-24	13-Nov-24	19-Sep-23	05-Oct-23	54d
ENG-MULTI-1000-A	Decommissioning and Abandonment Philosophy - IFA	20d	20d	11-Nov-24	03-Dec-24	30-Oct-23	22-Nov-23	54d
ENG-MULTI-1030-B	Permit Management Plan - IFC	10d	10d	22-Nov-24	03-Dec-24	18-Oct-23	28-Oct-23	54d
ENG-MULTI-1000-B	Decommissioning and Abandonment Philosophy - IFC	15d	15d	04-Dec-24	20-Dec-24	05-Dec-23	22-Dec-23	59d
Maintenance		112d	112d	26-Oct-24	11-Mar-25	06-Oct-23	24-Apr-24	54d
Issue For Approval		70d	70d	26-Oct-24	21-Jan-25	06-Oct-23	23-Mar-24	79d
ENG-OP&MAIN-1000-A	Operations Readiness Plan - IFA	15d	15d	26-Oct-24	13-Nov-24	23-Dec-23	13-Jan-24	82d
ENG-OP&MAIN-1070-A	Asset Register - IFA	15d	15d	26-Oct-24	13-Nov-24	17-Nov-23	04-Dec-23	72d
ENG-OP&MAIN-1140-A	Mechanical Handling - removal & replacement procedures - IFA	15d	15d	26-Oct-24	13-Nov-24	01-Feb-24	17-Feb-24	34d
ENG-OP&MAIN-1150-A	Mechanical Handling - Lifting equipment requisition and location list - IFA	15d	15d	26-Oct-24	13-Nov-24	01-Feb-24	17-Feb-24	34d
ENG-OP&MAIN-1130-A	FMECA for Key Equipment Items - IFA	15d	15d	11-Nov-24	27-Nov-24	30-Oct-23	16-Nov-23	54d
ENG-OP&MAIN-1030-A	Battery Limit Isolation Plan and Equipment Isolation Guideline - IFA	20d	20d	14-Nov-24	06-Dec-24	06-Oct-23	28-Oct-23	79d
ENG-OP&MAIN-1040-A	Operability and maintainability workshop report- IFA	15d	15d	14-Nov-24	30-Nov-24	05-Dec-23	22-Dec-23	72d
ENG-OP&MAIN-1160-A	Maintenance Schedule - IFA	15d	15d	14-Nov-24	30-Nov-24	19-Feb-24	06-Mar-24	34d
ENG-OP&MAIN-1180-A	Two-year operating spares list - IFA	15d	15d	02-Dec-24	18-Dec-24	07-Mar-24	23-Mar-24	34d
ENG-OP&MAIN-1090-A	Reliability Availability Maintainability (RAM) model - IFA	15d	15d	04-Dec-24	20-Dec-24	23-Nov-23	11-Dec-23	59d
ENG-OP&MAIN-1010-A	First fill list - IFA	15d	15d	07-Dec-24	24-Dec-24	19-Feb-24	06-Mar-24	82d
ENG-OP&MAIN-1100-A	Reliability Availability Maintainability (RAM) Study Report - IFA	10d	10d	21-Dec-24	04-Jan-25	12-Dec-23	22-Dec-23	59d
ENG-OP&MAIN-1120-A	Failure modes, effects, and criticality analysis (FMECA) - IFA	15d	15d	21-Dec-24	11-Jan-25	17-Nov-23	04-Dec-23	54d
ENG-OP&MAIN-1170-A	Project to Asset (P2A) Plan - IFA	15d	15d	03-Jan-25	21-Jan-25	07-Mar-24	23-Mar-24	79d
Issue For Construction		87d	87d	26-Nov-24	11-Mar-25	11-Nov-23	24-Apr-24	54d
ENG-OP&MAIN-1000-B	Operations Readiness Plan - IFC	10d	10d	26-Nov-24	06-Dec-24	26-Jan-24	06-Feb-24	82d
ENG-OP&MAIN-1070-B	Asset Register - IFC	10d	10d	26-Nov-24	06-Dec-24	18-Dec-23	30-Dec-23	81d
ENG-OP&MAIN-1030-B	Battery Limit Isolation Plan and Equipment Isolation Guideline - IFC	10d	10d	19-Dec-24	02-Jan-25	11-Nov-23	22-Nov-23	79d
ENG-OP&MAIN-1180-B	Two-year operating spares list - IFC	10d	10d	19-Dec-24	02-Jan-25	13-Apr-24	24-Apr-24	47d
ENG-OP&MAIN-1040-B	Operability and maintainability workshop report- IFC	10d	10d	21-Dec-24	04-Jan-25	09-Jan-24	19-Jan-24	59d
ENG-OP&MAIN-1010-B	First fill list - IFC	10d	10d	02-Jan-25	14-Jan-25	19-Mar-24	29-Mar-24	82d
ENG-OP&MAIN-1090-B	Reliability Availability Maintainability (RAM) model - IFC	15d	15d	07-Jan-25	23-Jan-25	23-Dec-23	13-Jan-24	64d
ENG-OP&MAIN-1100-B	Reliability Availability Maintainability (RAM) Study Report - IFC	10d	10d	07-Jan-25	17-Jan-25	20-Jan-24	31-Jan-24	59d
ENG-OP&MAIN-1130-B	FMECA for Key Equipment Items - IFC	10d	10d	18-Jan-25	29-Jan-25	01-Feb-24	12-Feb-24	59d
ENG-OP&MAIN-1120-B	Failure modes, effects, and criticality analysis (FMECA) - IFC	10d	10d	24-Jan-25	04-Feb-25	18-Dec-23	30-Dec-23	54d
ENG-OP&MAIN-1150-B	Mechanical Handling - Lifting equipment requisition and location list - IFC	10d	10d	30-Jan-25	10-Feb-25	01-Mar-24	12-Mar-24	59d
ENG-OP&MAIN-1140-B	Mechanical Handling - removal & replacement procedures - IFC	10d	10d	05-Feb-25	15-Feb-25	01-Mar-24	12-Mar-24	54d
ENG-OP&MAIN-1160-B	Maintenance Schedule - IFC	10d	10d	17-Feb-25	27-Feb-25	02-Apr-24	12-Apr-24	54d
ENG-OP&MAIN-1170-B	Project to Asset (P2A) Plan - IFC	10d	10d	28-Feb-25	11-Mar-25	13-Apr-24	24-Apr-24	54d
Materials		381d	342d	26-Aug-23 A	10-Oct-24 A	26-Aug-23	11-Dec-23	
Issue For Approval		361d	322d	26-Aug-23 A	17-Sep-24 A	26-Aug-23	16-Nov-23	

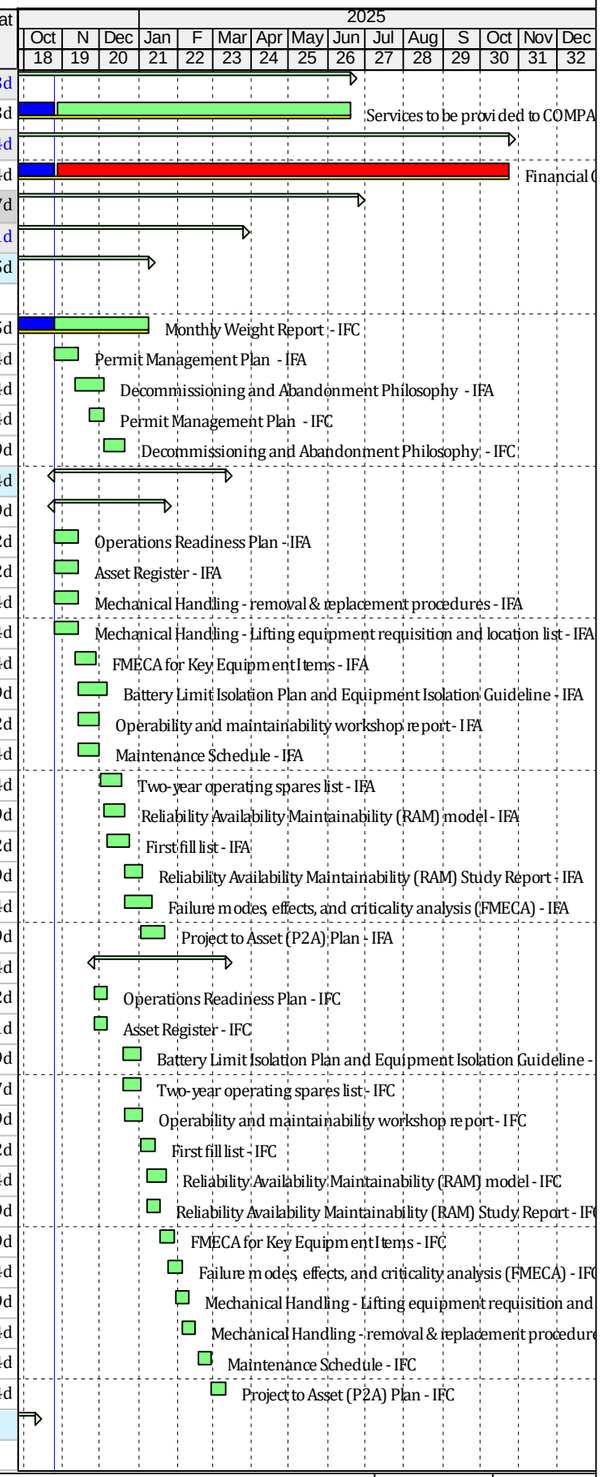

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-MAT&CORR-1100-A	Key Inspection Point Register - IFA - deleted	20d	20d	26-Aug-23 A	18-Sep-23 A	26-Aug-23	18-Sep-23	
ENG-MAT&CORR-1110-A	Materials Selection Report - IFA	15d	26d	30-Aug-23 A	28-Sep-23 A	30-Aug-23	15-Sep-23	
ENG-MAT&CORR-1000-A	Welding, PWHT and NDE Specification - IFA - to be deleted	25d	25d	01-Sep-23 A	29-Sep-23 A	01-Sep-23	29-Sep-23	
ENG-MAT&CORR-1060-A	Coating and Painting Specification - IFA	20d	26d	12-Sep-23 A	11-Oct-23 A	19-Sep-23	11-Oct-23	
ENG-MAT&CORR-1010-A	Welding, NDE, Fabrication, Inspection Procedure - IFA - to be deleted	15d	15d	30-Sep-23 A	17-Oct-23 A	30-Sep-23	17-Oct-23	
ENG-MAT&CORR-1080-A	Weld Repair Procedure - IFA - to be deleted	15d	15d	06-Oct-23 A	23-Oct-23 A	06-Oct-23	23-Oct-23	
ENG-MAT&CORR-1020-A	Corrosion Management Framework and Inspection Plan - IFA - deleted	14d	15d	12-Oct-23 A	28-Oct-23 A	12-Oct-23	28-Oct-23	
ENG-MAT&CORR-1030-A	Insulation Specification - IFA	15d	27d	20-Oct-23 A	21-Nov-23 A	30-Oct-23	16-Nov-23	
ENG-MAT&CORR-1090-A	Weld Repair Register - IFA - to be deleted	15d	15d	24-Oct-23 A	10-Nov-23 A	24-Oct-23	10-Nov-23	
ENG-MAT&CORR-1050-A	Positive Material Identification (PMI) Procedure - IFA	10d	109d	07-May-24 A	11-Sep-24 A	18-Oct-23	28-Oct-23	
ENG-MAT&CORR-1070-A	Coating Inspection Reports - IFA	15d	15d	31-Aug-24 A	17-Sep-24 A	30-Oct-23	16-Nov-23	
Issue For Construction		346d	302d	12-Oct-23 A	10-Oct-24 A	10-Oct-23	11-Dec-23	
ENG-MAT&CORR-1100-B	Key Inspection Point Register - IFC - deleted	15d	15d	12-Oct-23 A	28-Oct-23 A	12-Oct-23	28-Oct-23	
ENG-MAT&CORR-1110-B	Materials Selection Report - IFC	10d	258d	19-Oct-23 A	27-Aug-24 A	10-Oct-23	20-Oct-23	
ENG-MAT&CORR-1000-B	Welding, PWHT and NDE Specification - IFC - to be deleted	15d	27d	24-Oct-23 A	24-Nov-23 A	24-Oct-23	10-Nov-23	
ENG-MAT&CORR-1010-B	Welding, NDE, Fabrication, Inspection Procedure - IFC - to be deleted	10d	10d	06-Nov-23 A	16-Nov-23 A	06-Nov-23	16-Nov-23	
ENG-MAT&CORR-1060-B	Coating and Painting Specification - IFC	15d	52d	06-Nov-23 A	10-Jan-24 A	06-Nov-23	22-Nov-23	
ENG-MAT&CORR-1080-B	Weld Repair Procedure - IFC - to be deleted	10d	10d	06-Nov-23 A	16-Nov-23 A	06-Nov-23	16-Nov-23	
ENG-MAT&CORR-1020-B	Corrosion Management Framework and Inspection Plan - IFC - deleted	10d	10d	11-Nov-23 A	22-Nov-23 A	11-Nov-23	22-Nov-23	
ENG-MAT&CORR-1090-B	Weld Repair Register - IFC - to be deleted	10d	5d	20-Nov-23 A	24-Nov-23 A	23-Nov-23	04-Dec-23	
ENG-MAT&CORR-1030-B	Insulation Specification - IFC	10d	58d	18-Dec-23 A	27-Feb-24 A	29-Nov-23	11-Dec-23	
ENG-MAT&CORR-1070-B	Coating Inspection Reports - IFC	10d	10d	18-Sep-24 A	28-Sep-24 A	29-Nov-23	11-Dec-23	
ENG-MAT&CORR-1050-B	Positive Material Identification (PMI) Procedure - IFC	10d	10d	30-Sep-24 A	10-Oct-24 A	11-Nov-23	22-Nov-23	
Process Engineering		461d	461d	30-Aug-23 A	07-Mar-25	30-Aug-23	05-Oct-24	196d
ENGPROC1040	PROCESS FLOW DIAGRAMS, HEAT & MATERIAL BALANCE (IFR, IFA, IFC)	70d	73d	30-Aug-23 A	23-Nov-23 A	30-Aug-23	20-Nov-23	
ENGPROC1050	UTILITY FLOW DIAGRAMS, HEAT & MATERIAL BALANCE (IFR, IFA, IFC)	70d	73d	30-Aug-23 A	23-Nov-23 A	30-Aug-23	20-Nov-23	
ENGPROC1080	UTILITY P&I DIAGRAMS for HAZOP (IFH)	75d	82d	30-Aug-23 A	04-Dec-23 A	30-Aug-23	25-Nov-23	
ENGPROC1110	UTILITY P&I DIAGRAMS (IFR, IFA, IFC)	70d	73d	30-Aug-23 A	23-Nov-23 A	30-Aug-23	20-Nov-23	
ENGPROC1075	PROCESS P&I DIAGRAMS for HAZOP (IFH)	35d	39d	09-Sep-23 A	24-Oct-23 A	09-Sep-23	19-Oct-23	
ENGPROC1100	PROCESS P&I DIAGRAMS (IFR, IFA, IFC)	154d	343d	09-Sep-23 A	26-Oct-24	09-Sep-23	13-Mar-24	305d
ENGPROC1020	PROCESS DESIGN BASIS (IFR, IFA, IFC)	35d	41d	15-Sep-23 A	02-Nov-23 A	16-Sep-23	26-Oct-23	
ENGPROC1030	PROCESS PHILOSPOHY (IFR, IFA, IFC)	35d	41d	15-Sep-23 A	02-Nov-23 A	16-Sep-23	26-Oct-23	
ENGPROC1090	CAUSE & EFFECT DIAGRAM for HAZOP (IFH)	10d	20d	20-Oct-23 A	13-Nov-23 A	26-Oct-23	07-Nov-23	
ENGPROC1120	CAUSE & EFFECT DIAGRAM (IFR, IFA, IFC)	61d	127d	20-Oct-23 A	22-Mar-24 A	26-Oct-23	11-Jan-24	
ENGPROC1070	HYDRAULIC STUDY REPORT	155d	306d	23-Oct-23 A	26-Oct-24	10-Oct-23	25-Mar-24	305d
ENGPROC1130	LINE LIST (IFR, IFA, IFC)	115d	166d	23-Oct-23 A	14-May-24 A	26-Oct-23	25-Mar-24	
ENGPROC1060	PROCESS SIMULATION REPORT	35d	297d	03-Nov-23 A	26-Oct-24	06-Feb-24	13-Mar-24	305d
ENGPROC1150	OPERATING MANUAL & PROCEDURES	242d	406d	03-Nov-23 A	07-Mar-25	03-Nov-23	05-Oct-24	13d
ENGPROC1140	START-UP, NORMAL OPERATION, NORMAL & EMERGENCY SHUTDOWN PROCEDURE	81d	295d	06-Nov-23 A	26-Oct-24	08-Nov-23	15-Feb-24	305d
ENGPROC0000	CPI P&ID Input Frozen	0d	0d	26-Oct-24*		10-Oct-23		69d
Issue For Approval		437d	437d	30-Aug-23 A	07-Feb-25	30-Aug-23	31-Aug-24	17d
ENG-PROC-1030-A	BLPH PROCESS FLOW SCHEME FUEL CELL PACKAGE - IFA	15d	18d	30-Aug-23 A	19-Sep-23 A	30-Aug-23	15-Sep-23	
ENG-PROC-1040-A	BLPH UTILITY FLOW DIAGRAM VENT SYSTEMS - IFA	15d	18d	30-Aug-23 A	19-Sep-23 A	30-Aug-23	15-Sep-23	
ENG-PROC-1160-A	BLPH PROCESS FLOW SCHEME ELECTROLYSER AND HYDROGEN DRYING PACKAGE - IFA	15d	18d	30-Aug-23 A	19-Sep-23 A	30-Aug-23	15-Sep-23	
ENG-PROC-1170-A	BLPH PROCESS FLOW SCHEME HYDROGEN STORAGE - IFA	15d	18d	30-Aug-23 A	19-Sep-23 A	30-Aug-23	15-Sep-23	
ENG-PROC-1180-A	BLPH UTILITY FLOW DIAGRAM WATER TREATMENT PLANT - IFA	15d	18d	30-Aug-23 A	19-Sep-23 A	30-Aug-23	15-Sep-23	

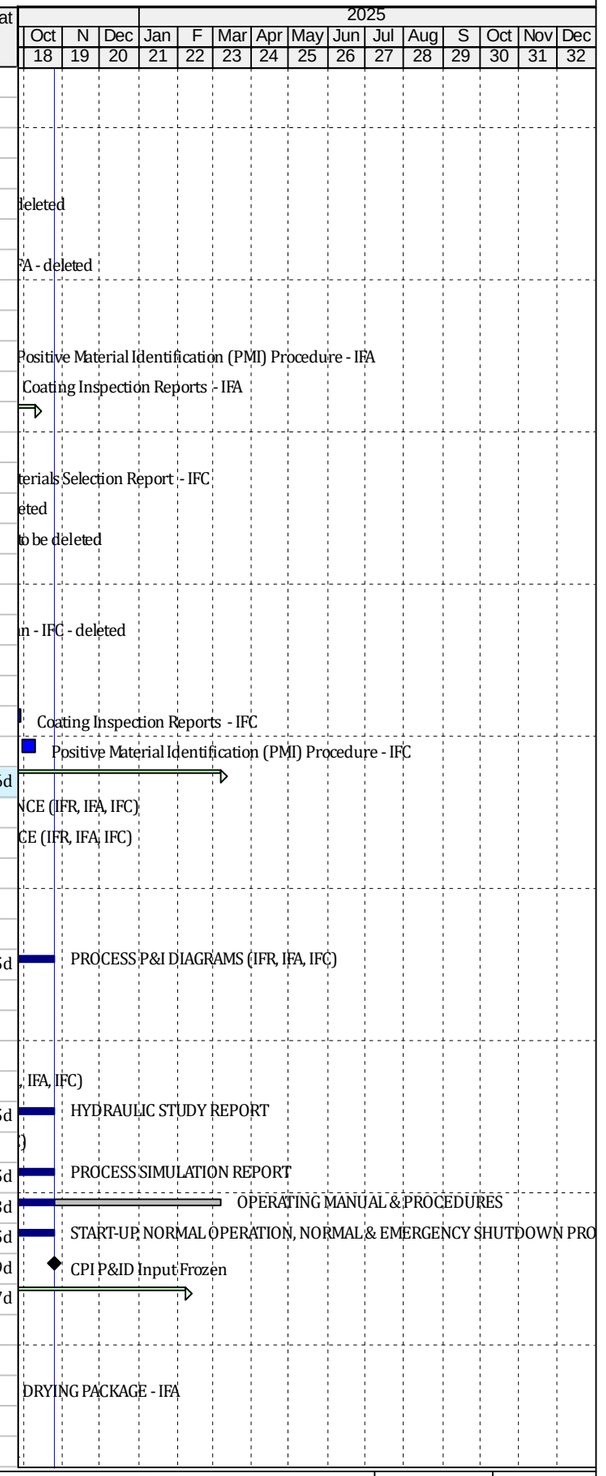

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-PROC-1190-A	BLPH PROCESS FLOW SCHEME ELECTROLYSER AND HYDROGEN DRYING PACKAGE - IFA	15d	18d	30-Aug-23 A	19-Sep-23 A	30-Aug-23	15-Sep-23	
ENG-PROC-1020-A	Heat & Mass Balance - IFA	11d	13d	04-Sep-23 A	18-Sep-23 A	04-Sep-23	15-Sep-23	
ENG-PROC-1200-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM GENERAL NOTES - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1210-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM PIPING SYMBOLOGY - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1220-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM ELECTROLYSER PACKAGE - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1230-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM FUEL CELL PACKAGE - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1240-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSELS HEADER (INLET) - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1250-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSELS HEADER (OUTLET) - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1260-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL A - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1270-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL B - IFA	35d	39d	09-Sep-23 A	24-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1280-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL C - IFA	35d	39d	09-Sep-23 A	24-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1290-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSELD - IFA	35d	39d	09-Sep-23 A	24-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1300-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL E - IFA	35d	39d	09-Sep-23 A	24-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1310-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL F - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1320-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM SEA-WATER INTAKE SYSTEM SHEET 1 - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1330-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM SEA-WATER INTAKE SYSTEM SHEET 2 - IFA	35d	39d	09-Sep-23 A	24-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1340-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER TREATMENT PLANT SHEET 1 - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1350-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER TREATMENT PLANT SHEET 2 - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1360-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER DISPOSAL SHEET 1 - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1370-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER DISPOSAL SHEET 2 - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1380-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM INSTRUMENT AIR PACKAGE - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1390-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN VENT HEADER - IFA	35d	38d	09-Sep-23 A	23-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1400-A	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN VENT DRUM - IFA	35d	39d	09-Sep-23 A	24-Oct-23 A	09-Sep-23	19-Oct-23	
ENG-PROC-1150-A	Process Design Philosophy (including Sparing, design P&T, Isolation PHY) - IFA	15d	16d	15-Sep-23 A	03-Oct-23 A	16-Sep-23	03-Oct-23	
ENG-PROC-1080-A	Equipment Sizing Philosophy and Calculations - IFA	24d	13d	02-Oct-23 A	16-Oct-23 A	16-Sep-23	13-Oct-23	
ENG-PROC-1000-A	Process Safety Cause & Effect Block Diagram - IFA	10d	20d	20-Oct-23 A	13-Nov-23 A	26-Oct-23	07-Nov-23	
ENG-PROC-1070-A	Insulation and Winterisation Philosophy - IFA	10d	7d	20-Oct-23 A	27-Oct-23 A	20-Oct-23	31-Oct-23	
ENG-PROC-1130-A	Process Safeguarding Flow Schemes (PSFS) - IFA	15d	29d	20-Oct-23 A	23-Nov-23 A	20-Oct-23	07-Nov-23	
ENG-PROC-1100-A	Process Line List - IFA	10d	16d	23-Oct-23 A	10-Nov-23 A	26-Oct-23	07-Nov-23	
ENG-PROC-1050-A	Relief, Vent and Blowdown Report - IFA	14d	29d	31-Oct-23 A	04-Dec-23 A	21-Oct-23	14-Nov-23	
ENG-PROC-1090-A	Line sizing report - IFA	15d	18d	31-Oct-23 A	21-Nov-23 A	20-Oct-23	07-Nov-23	
ENG-PROC-1120-A	Chemicals / Utility Consumption report - IFA	10d	56d	03-Nov-23 A	12-Jan-24 A	03-Nov-23	14-Nov-23	
ENG-PROC-1060-A	Process Control, Operation, Start-up and Shutdown Philosophy - IFA	20d	33d	06-Nov-23 A	14-Dec-23 A	08-Nov-23	30-Nov-23	
ENG-PROC-1110-A	Alarm & Trip Schedule - IFA - to be deleted	0d	17d	06-Nov-23 A	24-Nov-23 A	09-Sep-23	09-Sep-23	
ENG-PROC-1140-A	Identification of Process Safety Times - IFA - DELETED	10d	10d	12-Mar-24 A	22-Mar-24 A	12-Mar-24	22-Mar-24	
ENG-PROC-1010-A	Operations & Maintenance Manuals - IFA	19d	19d	17-Jan-25	07-Feb-25	02-Aug-24	31-Aug-24	13d
Issue For Construction		421d	430d	05-Oct-23 A	07-Mar-25	09-Sep-23	05-Oct-24	13d
ENG-PROC-1030-B	BLPH PROCESS FLOW SCHEME FUEL CELL PACKAGE - IFC	10d	42d	05-Oct-23 A	23-Nov-23 A	09-Nov-23	20-Nov-23	
ENG-PROC-1040-B	BLPH UTILITY FLOW DIAGRAM VENT SYSTEMS - IFC	10d	42d	05-Oct-23 A	23-Nov-23 A	09-Nov-23	20-Nov-23	
ENG-PROC-1160-B	BLPH PROCESS FLOW SCHEME ELECTROLYSER AND HYDROGEN DRYING PACKAGE - IFC	10d	42d	05-Oct-23 A	23-Nov-23 A	09-Nov-23	20-Nov-23	
ENG-PROC-1170-B	BLPH PROCESS FLOW SCHEME HYDROGEN STORAGE - IFC	10d	42d	05-Oct-23 A	23-Nov-23 A	09-Nov-23	20-Nov-23	
ENG-PROC-1190-B	BLPH PROCESS FLOW SCHEME ELECTROLYSER AND HYDROGEN DRYING PACKAGE - IFC	10d	42d	05-Oct-23 A	23-Nov-23 A	09-Nov-23	20-Nov-23	
ENG-PROC-1020-B	Heat & Mass Balance - IFC	15d	30d	06-Oct-23 A	10-Nov-23 A	21-Oct-23	08-Nov-23	
ENG-PROC-1180-B	BLPH UTILITY FLOW DIAGRAM WATER TREATMENT PLANT - IFC	10d	41d	06-Oct-23 A	23-Nov-23 A	09-Nov-23	20-Nov-23	
ENG-PROC-1150-B	Process Design Philosophy (including Sparing, design P&T, Isolation PHY) - IFC	10d	12d	19-Oct-23 A	02-Nov-23 A	16-Oct-23	26-Oct-23	
ENG-PROC-1200-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM GENERAL NOTES - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	

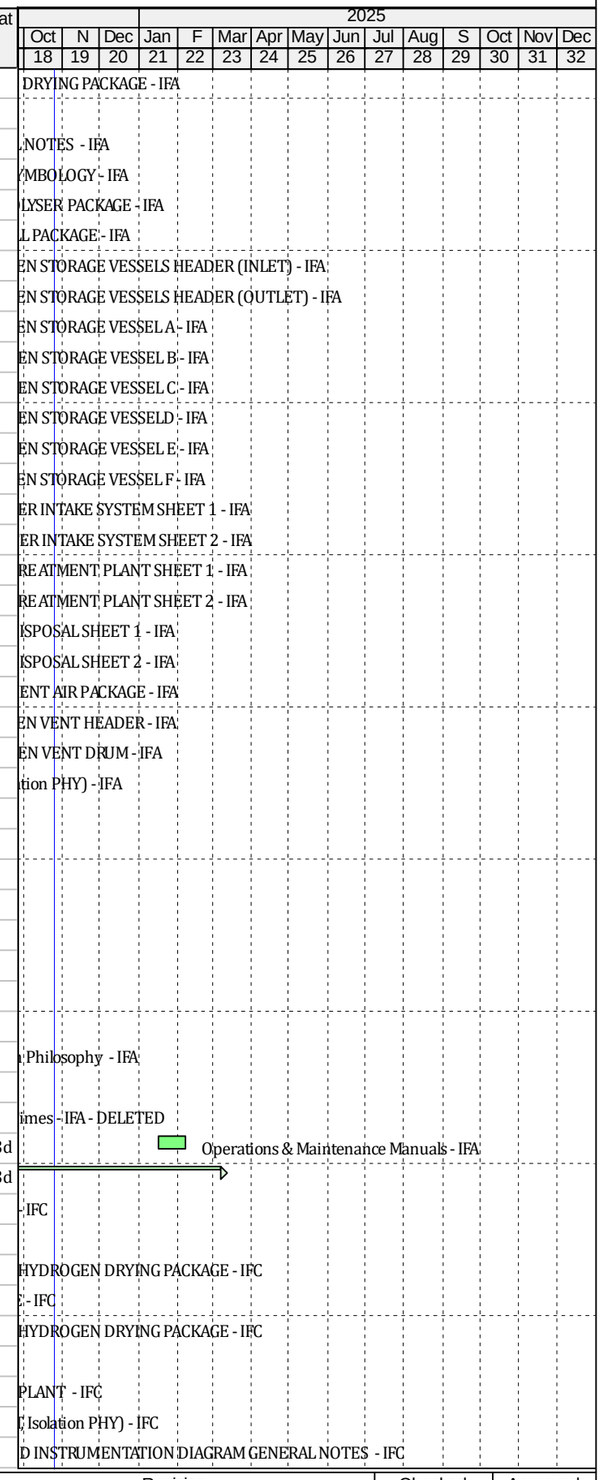

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-PROC-1210-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM PIPING SYMBOLOGY - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1220-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM ELECTROLYSER PACKAGE - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	06-Feb-24	02-Mar-24	
ENG-PROC-1230-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM FUEL CELL PACKAGE - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	06-Feb-24	02-Mar-24	
ENG-PROC-1240-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSELS HEADER (INLET) - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1250-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSELS HEADER (OUTLET) - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1260-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL A - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1270-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL B - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1280-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL C - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1290-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSELD - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1300-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL E - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1310-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN STORAGE VESSEL F - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1320-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM SEA-WATER INTAKE SYSTEM SHEET 1 - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1330-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM SEA-WATER INTAKE SYSTEM SHEET 2 - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1340-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER TREATMENT PLANT SHEET 1 - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1350-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER TREATMENT PLANT SHEET 2 - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1360-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER DISPOSAL SHEET 1 - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1370-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM WATER DISPOSAL SHEET 2 - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1380-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM INSTRUMENT AIR PACKAGE - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1390-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN VENT HEADER - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1400-B	BLPH PIPING AND INSTRUMENTATION DIAGRAM HYDROGEN VENT DRUM - IFC	23d	184d	03-Nov-23 A	14-Jun-24 A	16-Feb-24	13-Mar-24	
ENG-PROC-1080-B	Equipment Sizing Philosophy and Calculations - IFC	10d	88d	06-Nov-23 A	21-Feb-24 A	03-Nov-23	14-Nov-23	
ENG-PROC-1110-B	Alarm & Trip Schedule - IFC - to be deleted	0d	17d	06-Nov-23 A	24-Nov-23 A	09-Sep-23	09-Sep-23	
ENG-PROC-1070-B	Insulation and Winterisation Philosophy - IFC	10d	102d	13-Nov-23 A	15-Mar-24 A	02-Mar-24	13-Mar-24	
ENG-PROC-1100-B	Process Line List - IFC	15d	140d	23-Nov-23 A	14-May-24 A	08-Mar-24	25-Mar-24	
ENG-PROC-1000-B	Process Safety Cause & Effect Block Diagram - IFC	10d	78d	19-Dec-23 A	22-Mar-24 A	29-Dec-23	11-Jan-24	
ENG-PROC-1090-B	Line sizing report - IFC	10d	140d	19-Dec-23 A	07-Jun-24 A	14-Mar-24	25-Mar-24	
ENG-PROC-1050-B	Relief, Vent and Blowdown Report - IFC	10d	30d	03-Jan-24 A	07-Feb-24 A	08-Feb-24	19-Feb-24	
ENG-PROC-1130-B	Process Safeguarding Flow Schemes (PSFS) - IFC	10d	104d	26-Jan-24 A	30-May-24 A	18-Apr-24	30-Apr-24	
ENG-PROC-1060-B	Process Control, Operation, Start-up and Shutdown Philosophy - IFC	20d	127d	12-Feb-24 A	12-Jul-24 A	24-Jan-24	15-Feb-24	
ENG-PROC-1120-B	Chemicals / Utility Consumption report - IFC	10d	21d	12-Feb-24 A	06-Mar-24 A	20-Feb-24	01-Mar-24	
ENG-PROC-1140-B	Identification of Process Safety Times - IFC - DELETED	10d	10d	06-Apr-24 A	17-Apr-24 A	06-Apr-24	17-Apr-24	
ENG-PROC-1010-B	Operations & Maintenance Manuals - IFC	20d	20d	13-Feb-25	07-Mar-25	13-Sep-24	05-Oct-24	13d
Structural Engineering		472d	472d	04-Sep-23 A	25-Mar-25	04-Sep-23	19-Jul-24	181d
ENGSTR1060	TOPSIDE STRUCTURAL REPORTS & CALCULATIONS (IFR, IFA, IFC)	265d	324d	02-Oct-23 A	26-Oct-24	04-Sep-23	19-Jul-24	305d
ENGSTR1070	TOPSIDE PRIMARY STRUCTURAL DRAWINGS & DETAILS (IFR, IFA, IFC)	81d	69d	02-Oct-23 A	22-Dec-23 A	18-Sep-23	22-Dec-23	
ENGSTR1050	STRUCTURAL DESIGN PREMISES (IFR, IFA, IFC)	87d	129d	02-Oct-23 A	06-Mar-24 A	04-Sep-23	15-Dec-23	
ENGSTR1010	MR Issue - Primary Steel	0d	0d	13-Oct-23 A		03-Oct-23		
ENGSTR1080	TOPSIDE SECONDARY STRUCTURAL DRAWINGS & DETAILS (IFR, IFA, IFC)	70d	308d	20-Oct-23 A	26-Oct-24	28-Oct-23	24-Jan-24	305d
ENGSTR1090	TOPSIDE TERTIARY STRUCTURAL DRAWINGS & DETAILS (IFR, IFA, IFC)	176d	132d	20-Oct-23 A	28-Mar-24 A	28-Oct-23	31-May-24	
ENGSTR1030	IFC Issue - Primary Steel Construction Drawings	0d	0d	21-Dec-23 A		27-Dec-23		
ENGSTR1020	MR Issue - Secondary Steel	0d	0d	17-Jan-24 A		02-Dec-23		
ENGSTR1040	IFC Issue - Secondary Steel Construction Drawings	0d	0d	25-May-24 A		09-Jan-24		
Issue For Approval		413d	413d	04-Sep-23 A	15-Jan-25	04-Sep-23	23-May-24	78d
ENG-STR-1310-A	TOPSIDE - STANDARD DRAWINGS - BEAM CONNECTION TYPICAL DETAILS - IFA	35d	35d	04-Sep-23 A	13-Oct-23 A	04-Sep-23	13-Oct-23	
ENG-STR-1320-A	TOPSIDE - STANDARD DRAWINGS - BOX GIRDER & PLATE GIRDER TYPICAL DETAILS - IFA	35d	35d	04-Sep-23 A	13-Oct-23 A	04-Sep-23	13-Oct-23	
ENG-STR-1330-A	TOPSIDE - STANDARD DRAWINGS - TYPICAL SUPPORT FOR SKIDDED EQUIPMENT - IFA	35d	35d	04-Sep-23 A	13-Oct-23 A	04-Sep-23	13-Oct-23	

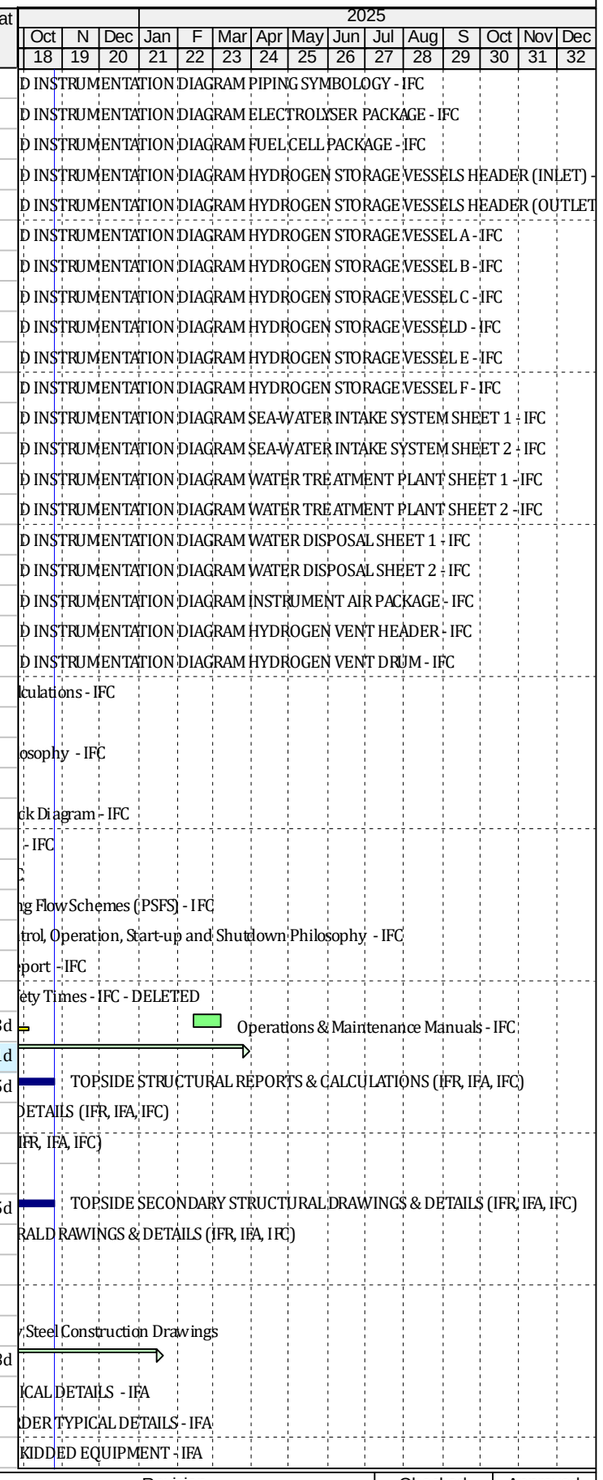

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-STR-1340-A	TOPSIDE - STANDARD DRAWINGS - TYPICAL SUPPORT FOR HORIZONTAL LARGE / HEAVY VESSELS - IFA	35d	35d	04-Sep-23 A	13-Oct-23 A	04-Sep-23	13-Oct-23	
ENG-STR-1350-A	TOPSIDE - STANDARD DRAWINGS - TYPICAL SUPPORT FOR VERTICAL LARGE / HEAVY VESSELS - IFA	35d	35d	04-Sep-23 A	13-Oct-23 A	04-Sep-23	13-Oct-23	
ENG-STR-1360-A	TOPSIDE - STANDARD DRAWINGS - TYPICAL DRAIN BOX AND DRAIN FUNNEL - IFA	35d	35d	04-Sep-23 A	13-Oct-23 A	04-Sep-23	13-Oct-23	
ENG-STR-1180-A	MATERIAL SPECIFICATION - IFA	47d	29d	07-Sep-23 A	10-Oct-23 A	07-Sep-23	31-Oct-23	
ENG-STR-1280-A	STANDARD DRAWINGS - TUBULAR JOINTS, STANDARD WELDING DETAILS - IFA	35d	32d	07-Sep-23 A	13-Oct-23 A	07-Sep-23	17-Oct-23	
ENG-STR-1290-A	STANDARD DRAWINGS - STANDARD BUTT WELD DETAILS - ACCESS FROM ONE SIDE - IFA	35d	32d	07-Sep-23 A	13-Oct-23 A	07-Sep-23	17-Oct-23	
ENG-STR-1300-A	STANDARD DRAWINGS - STANDARD BUTT WELD DETAILS - ACCESS FROM BOTH SIDES - IFA	35d	32d	07-Sep-23 A	13-Oct-23 A	07-Sep-23	17-Oct-23	
ENG-STR-1370-A	STANDARD DRAWINGS - TYPICAL HANDRAIL DETAILS - IFA	35d	32d	07-Sep-23 A	13-Oct-23 A	07-Sep-23	17-Oct-23	
ENG-STR-1380-A	STANDARD DRAWINGS - TYPICAL STAIRWAY DETAILS - IFA	35d	32d	07-Sep-23 A	13-Oct-23 A	07-Sep-23	17-Oct-23	
ENG-STR-1390-A	STANDARD DRAWINGS - TYPICAL SIDE ENTRY LADDER DETAILS - IFA	35d	32d	07-Sep-23 A	13-Oct-23 A	07-Sep-23	17-Oct-23	
ENG-STR-1400-A	STANDARD DRAWINGS - TYPICAL PLATING/GRATING AND PENETRATION DETAILS - IFA	35d	32d	07-Sep-23 A	13-Oct-23 A	07-Sep-23	17-Oct-23	
ENG-STR-1410-A	TOPSIDE PRIMARY STEEL - ELEVATION ROW A - IFA	35d	23d	18-Sep-23 A	13-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1420-A	TOPSIDE - PRIMARY STEEL - ELEVATION ROW B - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1430-A	TOPSIDE - PRIMARY STEEL - ELEVATION ROW C - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1450-A	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 2 - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1460-A	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 3 - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1470-A	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 4 - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1480-A	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 5 - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1490-A	TOPSIDE - PRIMARY STEEL - PLAN EL +23310 - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1500-A	TOPSIDE - PRIMARY STEEL - PLAN EL +30310 - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1510-A	TOPSIDE - PRIMARY JOINTS - PLAN AT EL +23310 TOS - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1520-A	TOPSIDE - PRIMARY JOINTS - PLAN AT EL +30310 TOS - IFA	35d	31d	18-Sep-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1780-A	TP - PRIMARY STEEL - ELEVATION ROW A - IFA	35d	46d	18-Sep-23 A	10-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1790-A	TP - PRIMARY STEEL - ELEVATION ROW B - IFA - deleted	35d	58d	18-Sep-23 A	24-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1800-A	TP - PRIMARY STEEL - ELEVATION ROW C - IFA - deleted	35d	58d	18-Sep-23 A	24-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1810-A	TP - PRIMARY STEEL - ELEVATION ROW 2 - IFA	35d	46d	18-Sep-23 A	10-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1820-A	TP - PRIMARY STEEL - ELEVATION ROW 4 - IFA - deleted	35d	58d	18-Sep-23 A	24-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1830-A	TP - PRIMARY STEEL - PLAN AT EL +17050 TOS (FLANGE CONNECTION) - IFA	35d	46d	18-Sep-23 A	10-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1840-A	TP - PRIMARY STEEL - PLAN AT EL +17300 TO +19242 TOS - IFA - deleted	35d	58d	18-Sep-23 A	24-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1850-A	TP - PRIMARY STEEL - PLAN AT EL +21710 TOS - IFA	35d	46d	18-Sep-23 A	10-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1860-A	TP - TOPSIDE SUPPORT POINTS - IFA	35d	46d	18-Sep-23 A	10-Nov-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1200-A	MTO - TOPSIDE - IFA	10d	20d	21-Sep-23 A	13-Oct-23 A	21-Sep-23	02-Oct-23	
ENG-STR-1530-A	TOPSIDE - PRIMARY JOINTS - PLAN AT EL +30310 TOS - CRANE PEDESTAL - IFA - deleted	35d	35d	23-Sep-23 A	03-Nov-23 A	23-Sep-23	03-Nov-23	
ENG-STR-1000-A	BLPH PLATFORM - IN-SERVICE ANALYSIS - IFA	62d	52d	02-Oct-23 A	01-Dec-23 A	04-Sep-23	15-Nov-23	
ENG-STR-1010-A	BLPH PLATFORM - LOAD-OUT ANALYSIS - IFA	107d	94d	02-Oct-23 A	25-Jan-24 A	02-Oct-23	09-Feb-24	
ENG-STR-1040-A	BLPH PLATFORM - LIFTING ANALYSIS - IFA	46d	80d	02-Oct-23 A	09-Jan-24 A	02-Oct-23	24-Nov-23	
ENG-STR-1170-A	STRUCTURAL DESIGN PREMISES - IFA	41d	17d	02-Oct-23 A	20-Oct-23 A	04-Sep-23	20-Oct-23	
ENG-STR-1240-A	3D GENERAL ARRANGEMENT - IFA	17d	165d	02-Oct-23 A	19-Apr-24 A	02-Oct-23	20-Oct-23	
ENG-STR-1250-A	DRAWINGS LIST - IFA	30d	165d	02-Oct-23 A	19-Apr-24 A	02-Oct-23	20-Oct-23	
ENG-STR-1260-A	STANDARD DRAWINGS - GENERAL NOTES - IFA	17d	11d	02-Oct-23 A	13-Oct-23 A	02-Oct-23	20-Oct-23	
ENG-STR-1270-A	STANDARD DRAWINGS - DETAILS OF TUBULAR JOINT CONNECTIONS - IFA	11d	11d	02-Oct-23 A	13-Oct-23 A	02-Oct-23	13-Oct-23	
ENG-STR-1440-A	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 1 - IFA	35d	19d	02-Oct-23 A	23-Oct-23 A	18-Sep-23	27-Oct-23	
ENG-STR-1550-A	TOPSIDE - LIFTING POINTS - GENERAL ARRANGEMENT - IFA	28d	19d	02-Oct-23 A	23-Oct-23 A	02-Oct-23	03-Nov-23	
ENG-STR-1870-A	TP - LIFTING POINTS - GENERAL ARRANGEMENT - IFA	36d	228d	02-Oct-23 A	04-Jul-24 A	29-Sep-23	10-Nov-23	
ENG-STR-1210-A	MTO - TOPSIDE - GRILLAGE & FASTENING - IFA	10d	328d	09-Oct-23 A	07-Nov-24	03-Oct-23	13-Oct-23	15d
ENG-STR-1230-A	MTO - TP - GRILLAGE & FASTENING - IFA	10d	363d	09-Oct-23 A	18-Dec-24	03-Oct-23	13-Oct-23	21d

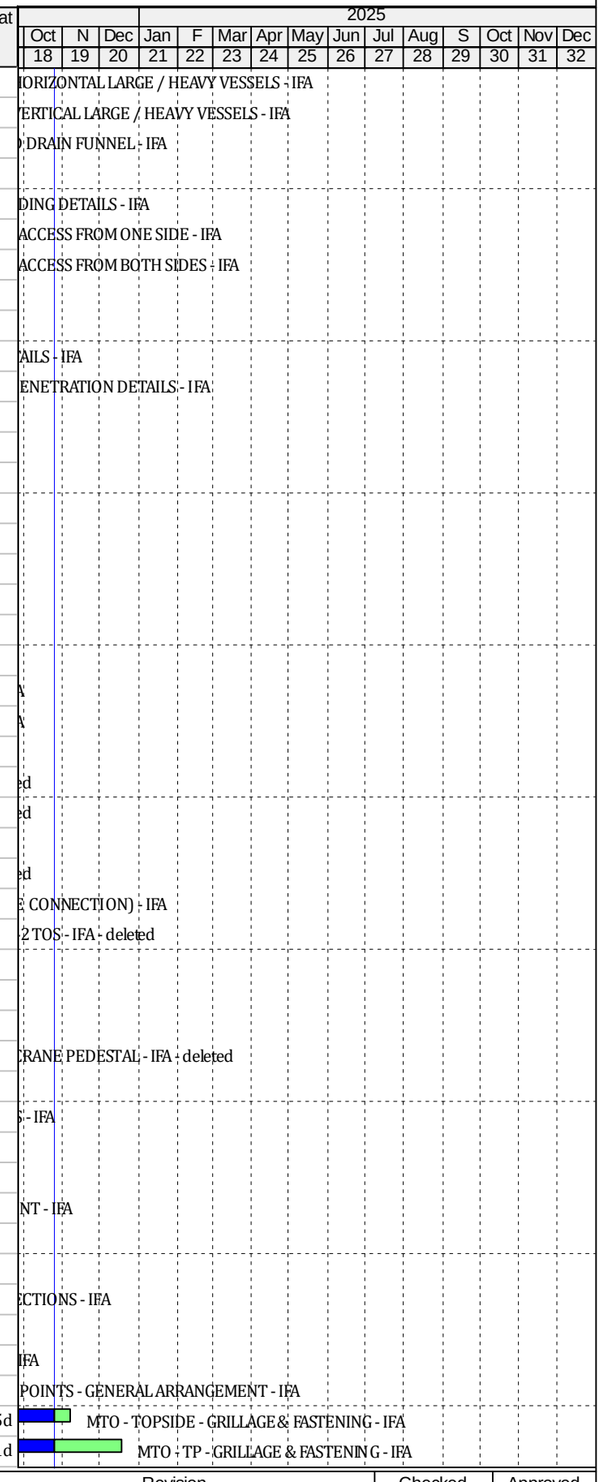

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-STR-1200-B	MTO - TOPSIDE - IFC	10d	15d	13-Oct-23 A	30-Oct-23 A	14-Oct-23	25-Oct-23	
ENG-STR-1020-A	BLPH PLATFORM - TRANSPORTATION ANALYSIS - IFA	45d	66d	20-Oct-23 A	11-Jan-24 A	16-Oct-23	07-Dec-23	
ENG-STR-1030-A	BLPH PLATFORM - TRANSPORTATION FATIGUE ANALYSIS - IFA	71d	309d	20-Oct-23 A	26-Oct-24	16-Oct-23	12-Jan-24	38d
ENG-STR-1190-A	FABRICATION SPECIFICATION - IFA	26d	149d	20-Oct-23 A	19-Apr-24 A	07-Sep-23	06-Oct-23	
ENG-STR-1560-A	TOPSIDE - LIFTING POINTS - DETAILS - IFA	28d	3d	20-Oct-23 A	23-Oct-23 A	02-Oct-23	03-Nov-23	
ENG-STR-1570-A	TOPSIDE - SECONDARY STEEL - PLAN AT EL 23310 TOS 30310 - IFA	29d	36d	20-Oct-23 A	01-Dec-23 A	28-Oct-23	01-Dec-23	
ENG-STR-1580-A	TOPSIDE - SECONDARY STEEL - PLAN +30310 TOP - IFA	29d	36d	20-Oct-23 A	01-Dec-23 A	28-Oct-23	01-Dec-23	
ENG-STR-1590-A	TOPSIDE - FLOORING - PLAN AT EL +23310 ??? - IFA	34d	43d	20-Oct-23 A	11-Dec-23 A	28-Oct-23	07-Dec-23	
ENG-STR-1600-A	TOPSIDE - FLOORING - PLAN AT EL +30310 ??? - IFA	34d	43d	20-Oct-23 A	11-Dec-23 A	28-Oct-23	07-Dec-23	
ENG-STR-1630-A	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFA	35d	84d	20-Oct-23 A	01-Feb-24 A	28-Oct-23	09-Dec-23	
ENG-STR-1690-A	TOPSIDE - EQUIPMENT SUPPORTS GENERAL ARRANGEMENT EL +23310 - IFA	35d	320d	20-Oct-23 A	09-Nov-24	28-Oct-23	09-Dec-23	104d
ENG-STR-1700-A	TOPSIDE - EQUIPMENT SUPPORTS GENERAL ARRANGEMENT EL +30310 - IFA	35d	320d	20-Oct-23 A	09-Nov-24	28-Oct-23	09-Dec-23	104d
ENG-STR-1670-A	TOPSIDE - TECHNICAL ROOM EL +23310 - IFA - deleted	35d	35d	28-Oct-23 A	09-Dec-23 A	28-Oct-23	09-Dec-23	
ENG-STR-1680-A	TOPSIDE - TECHNICAL ROOM EL +30310 - IFA - deleted	35d	35d	28-Oct-23 A	09-Dec-23 A	28-Oct-23	09-Dec-23	
ENG-STR-1220-A	MTO - TP - IFA	10d	8d	02-Nov-23 A	10-Nov-23 A	27-Mar-24	09-Apr-24	
ENG-STR-1220-B	MTO - TP - IFC	10d	10d	14-Nov-23 A	24-Nov-23 A	13-May-24	23-May-24	
ENG-STR-1540-A	TOPSIDE - TOPSIDE TO JACKET WELD CONNECTION DETAILS - IFA	34d	11d	20-Nov-23 A	01-Dec-23 A	25-Sep-23	03-Nov-23	
ENG-STR-1890-A	TP - TOPSIDE BOLTED CONNECTION DETAILS - IFA - deleted	27d	49d	27-Nov-23 A	27-Jan-24 A	27-Nov-23	27-Jan-24	
ENG-STR-1090-A	TP - TRANSPORTATION ANALYSIS - IFA	60d	71d	01-Dec-23 A	27-Feb-24 A	20-Nov-23	02-Feb-24	
ENG-STR-1100-A	TP - TRANSPORTATION FATIGUE ANALYSIS - IFA	60d	333d	01-Dec-23 A	09-Jan-25	20-Nov-23	02-Feb-24	19d
ENG-STR-1640-A	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFA	41d	22d	07-Jan-24 A	01-Feb-24 A	16-Mar-24	29-Apr-24	
ENG-STR-1650-A	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFA	41d	22d	07-Jan-24 A	01-Feb-24 A	16-Mar-24	29-Apr-24	
ENG-STR-1660-A	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFA	41d	22d	07-Jan-24 A	01-Feb-24 A	16-Mar-24	29-Apr-24	
ENG-STR-1900-A	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFA	30d	5d	08-Jan-24 A	12-Jan-24 A	18-Dec-23	31-Jan-24	
ENG-STR-1910-A	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFA	30d	5d	08-Jan-24 A	12-Jan-24 A	18-Dec-23	31-Jan-24	
ENG-STR-1920-A	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFA	30d	5d	08-Jan-24 A	12-Jan-24 A	18-Dec-23	31-Jan-24	
ENG-STR-1930-A	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFA	30d	5d	08-Jan-24 A	12-Jan-24 A	18-Dec-23	31-Jan-24	
ENG-STR-1110-A	TP - LIFTING ANALYSIS - IFA	20d	93d	26-Jan-24 A	17-May-24 A	27-Nov-23	19-Jan-24	
ENG-STR-1120-A	TP - JOINT CHECK DESIGN REPORT - IFA	32d	141d	26-Jan-24 A	12-Jul-24 A	27-Nov-23	02-Feb-24	
ENG-STR-1130-A	TP-MP FLANGE CONNECTION VERIFICATION - IFA	49d	98d	26-Jan-24 A	23-May-24 A	11-Dec-23	09-Feb-24	
ENG-STR-1880-A	TP - LIFTING POINTS - DETAILS - IFA	36d	134d	26-Jan-24 A	04-Jul-24 A	29-Sep-23	10-Nov-23	
ENG-STR-1940-A	CAISSONS ELEVATION - IFA	30d	190d	26-Jan-24 A	09-Sep-24 A	23-Dec-23	06-Feb-24	
ENG-STR-1950-A	CAISSONS DETAILS - IFA	30d	190d	26-Jan-24 A	09-Sep-24 A	23-Dec-23	06-Feb-24	
ENG-STR-1960-A	CAISSON DETAILS - IFA	30d	260d	26-Jan-24 A	30-Nov-24	23-Dec-23	06-Feb-24	72d
ENG-STR-1080-A	TP - LOAD-OUT ANALYSIS - IFA	18d	67d	31-Jan-24 A	19-Apr-24 A	08-Jan-24	23-Feb-24	
ENG-STR-1150-A	CAISSONS - TRANSPORTATION ANALYSIS - IFA	35d	141d	05-Feb-24 A	22-Jul-24 A	05-Feb-24	15-Mar-24	
ENG-STR-1620-A	TOPSIDE - MONORAILS - DETAILS - IFA	19d	13d	01-Mar-24 A	15-Mar-24 A	01-Mar-24	15-Mar-24	
ENG-STR-1730-A	TOPSIDE - PIPING & E&I PIPE RACKS EL+23310 - IFA - deleted	19d	13d	01-Mar-24 A	15-Mar-24 A	01-Mar-24	15-Mar-24	
ENG-STR-1740-A	TOPSIDE - PIPING & E&I PIPE RACKS EL+30310 - IFA - deleted	19d	13d	01-Mar-24 A	15-Mar-24 A	01-Mar-24	15-Mar-24	
ENG-STR-1770-A	TOPSIDE - TERTIARY STRUCTURES - IFA - deleted	13d	13d	01-Mar-24 A	15-Mar-24 A	01-Mar-24	15-Mar-24	
ENG-STR-1160-A	CAISSONS - LIFTING ANALYSIS - IFA - DELETED	41d	41d	11-Mar-24 A	30-Apr-24 A	11-Mar-24	30-Apr-24	
ENG-STR-1610-A	TOPSIDE - MONORAILS - PLANS - IFA - deleted	13d	13d	16-Mar-24 A	02-Apr-24 A	16-Mar-24	02-Apr-24	
ENG-STR-1050-A	BLPH PLATFORM - JOINT CHECK DESIGN REPORT - IFA	29d	26d	02-Apr-24 A	03-May-24 A	12-Feb-24	15-Mar-24	
ENG-STR-1060-A	BLPH PLATFORM - SECONDARY STRUCTURES DESIGN & CRANE PEDESTAL DESIGN REPORT - IFA	41d	20d	02-Apr-24 A	24-Apr-24 A	08-Jan-24	23-Feb-24	
ENG-STR-1070-A	BLPH PLATFORM - FE ANALYSES - IFA	29d	20d	02-Apr-24 A	24-Apr-24 A	04-Mar-24	29-Mar-24	
ENG-STR-1750-A	TOPSIDE - DRAIN SYSTEM - IFA	31d	9d	10-Apr-24 A	19-Apr-24 A	01-Feb-24	29-Feb-24	

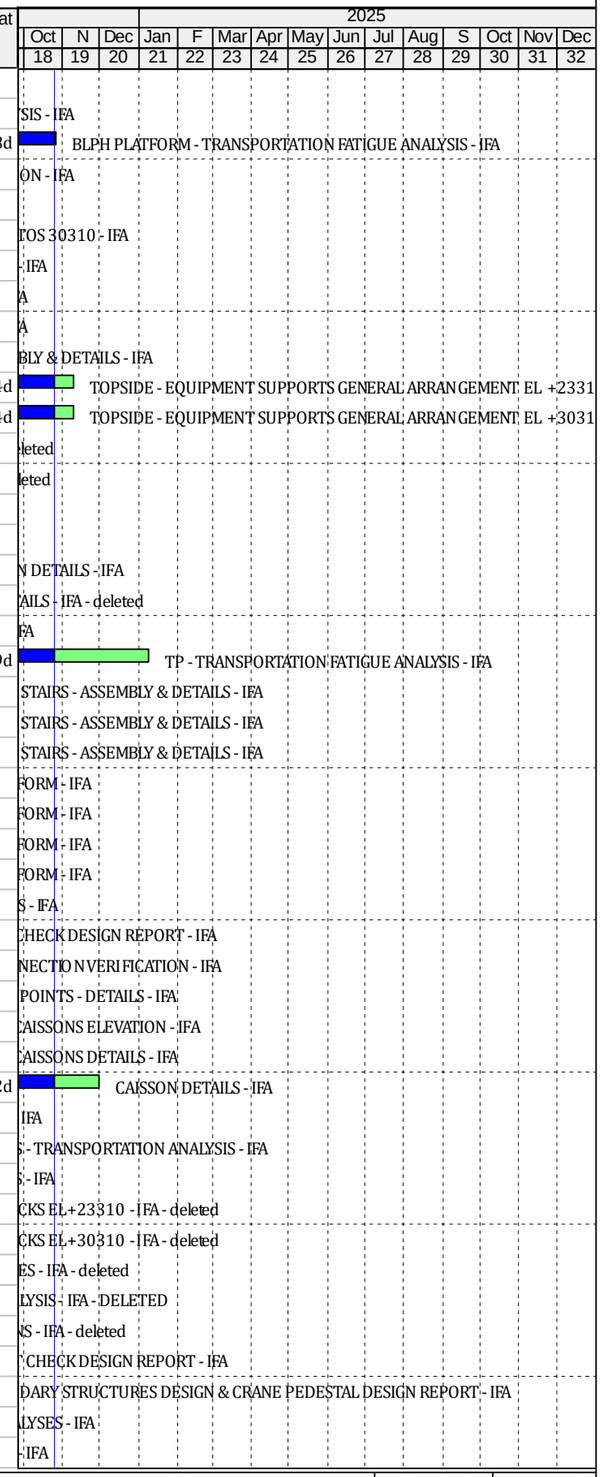


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-STR-1710-A	STORAGE VESSEL - PRIMARY STEEL - PLAN EL +2 - IFA	31d	13d	03-May-24 A	17-May-24 A	01-Feb-24	29-Feb-24	
ENG-STR-1720-A	STORAGE VESSEL - PRIMARY STEEL - PLAN EL +3 - IFA	31d	13d	03-May-24 A	17-May-24 A	01-Feb-24	29-Feb-24	
ENG-STR-1140-A	CAISSONS - LOAD-OUT ANALYSIS - IFA	35d	35d	26-Oct-24	06-Dec-24	05-Feb-24	15-Mar-24	47d
ENG-STR-1760-A	TOPSIDE - IDENTIFICATION PANEL - IFA	31d	31d	26-Oct-24	02-Dec-24	01-Feb-24	29-Feb-24	87d
ENG-STR-1210-B	MTO - TOPSIDE - GRILLAGE & FASTENING - IFC	10d	10d	20-Nov-24	30-Nov-24	26-Oct-23	07-Nov-23	56d
ENG-STR-1230-B	MTO - TP - GRILLAGE & FASTENING - IFC	10d	10d	03-Jan-25	15-Jan-25	26-Oct-23	07-Nov-23	21d
Issue For Construction		412d	433d	19-Oct-23 A	25-Mar-25	31-Oct-23	19-Jul-24	19d
ENG-STR-1180-B	MATERIAL SPECIFICATION - IFC	34d	220d	19-Oct-23 A	12-Jul-24 A	14-Nov-23	23-Dec-23	
ENG-STR-1170-B	STRUCTURAL DESIGN PREMISES - IFC	28d	105d	30-Oct-23 A	06-Mar-24 A	13-Nov-23	15-Dec-23	
ENG-STR-1260-B	STANDARD DRAWINGS - GENERAL NOTES - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	20-Nov-23	15-Dec-23	
ENG-STR-1280-B	STANDARD DRAWINGS - TUBULAR JOINTS, STANDARD WELDING DETAILS - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1290-B	STANDARD DRAWINGS - STANDARD BUTT WELD DETAILS - ACCESS FROM ONE SIDE - IFC	22d	252d	30-Oct-23 A	30-Aug-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1310-B	TOPSIDE - STANDARD DRAWINGS - BEAM CONNECTION TYPICAL DETAILS - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1320-B	TOPSIDE - STANDARD DRAWINGS - BOX GIRDER & PLATE GIRDER TYPICAL DETAILS - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1330-B	TOPSIDE - STANDARD DRAWINGS - TYPICAL SUPPORT FOR SKIDDED EQUIPMENT - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1340-B	TOPSIDE - STANDARD DRAWINGS - TYPICAL SUPPORT FOR HORIZONTAL LARGE / HEAVY VESSELS - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1350-B	TOPSIDE - STANDARD DRAWINGS - TYPICAL SUPPORT FOR VERTICAL LARGE / HEAVY VESSELS - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1360-B	TOPSIDE - STANDARD DRAWINGS - TYPICAL DRAIN BOX AND DRAIN FUNNEL - IFC	22d	252d	30-Oct-23 A	30-Aug-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1370-B	STANDARD DRAWINGS - TYPICAL HANDRAIL DETAILS - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1380-B	STANDARD DRAWINGS - TYPICAL STAIRWAY DETAILS - IFC	22d	80d	30-Oct-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1390-B	STANDARD DRAWINGS - TYPICAL SIDE ENTRY LADDER DETAILS - IFC	22d	211d	30-Oct-23 A	12-Jul-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1400-B	STANDARD DRAWINGS - TYPICAL PLATING/GRATING AND PENETRATION DETAILS - IFC	22d	252d	30-Oct-23 A	30-Aug-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1410-B	TOPSIDE PRIMARY STEEL - ELEVATION ROW A - IFC	16d	80d	30-Oct-23 A	06-Feb-24 A	27-Nov-23	15-Dec-23	
ENG-STR-1270-B	STANDARD DRAWINGS - DETAILS OF TUBULAR JOINT CONNECTIONS - IFC	22d	78d	02-Nov-23 A	06-Feb-24 A	09-Dec-23	08-Jan-24	
ENG-STR-1420-B	TOPSIDE - PRIMARY STEEL - ELEVATION ROW B - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1430-B	TOPSIDE - PRIMARY STEEL - ELEVATION ROW C - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1440-B	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 1 - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1450-B	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 2 - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1460-B	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 3 - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1470-B	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 4 - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1480-B	TOPSIDE - PRIMARY STEEL - ELEVATION ROW 5 - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1490-B	TOPSIDE - PRIMARY STEEL - PLAN EL +23310 - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1500-B	TOPSIDE - PRIMARY STEEL - PLAN EL +30310 - IFC	16d	42d	02-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1560-B	TOPSIDE - LIFTING POINTS - DETAILS - IFC	22d	12d	02-Nov-23 A	15-Nov-23 A	27-Nov-23	22-Dec-23	
ENG-STR-1300-B	STANDARD DRAWINGS - STANDARD BUTT WELD DETAILS - ACCESS FROM BOTH SIDES - IFC	22d	77d	03-Nov-23 A	06-Feb-24 A	13-Nov-23	07-Dec-23	
ENG-STR-1510-B	TOPSIDE - PRIMARY JOINTS - PLAN AT EL +23310 TOS - IFC	16d	41d	03-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1520-B	TOPSIDE - PRIMARY JOINTS - PLAN AT EL +30310 TOS - IFC	16d	41d	03-Nov-23 A	21-Dec-23 A	27-Nov-23	15-Dec-23	
ENG-STR-1550-B	TOPSIDE - LIFTING POINTS - GENERAL ARRANGEMENT - IFC	22d	92d	03-Nov-23 A	23-Feb-24 A	27-Nov-23	22-Dec-23	
ENG-STR-1780-B	TP - PRIMARY STEEL - ELEVATION ROW A - IFC	17d	30d	16-Nov-23 A	21-Dec-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1810-B	TP - PRIMARY STEEL - ELEVATION ROW 2 - IFC	17d	30d	16-Nov-23 A	21-Dec-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1830-B	TP - PRIMARY STEEL - PLAN AT EL +17050 TOS (FLANGE CONNECTION) - IFC	17d	30d	16-Nov-23 A	21-Dec-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1850-B	TP - PRIMARY STEEL - PLAN AT EL +21710 TOS - IFC	17d	30d	16-Nov-23 A	21-Dec-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1860-B	TP - TOPSIDE SUPPORT POINTS - IFC	17d	30d	16-Nov-23 A	21-Dec-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1790-B	TP - PRIMARY STEEL - ELEVATION ROW B - IFC - deleted	17d	5d	20-Nov-23 A	24-Nov-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1800-B	TP - PRIMARY STEEL - ELEVATION ROW C - IFC - deleted	17d	5d	20-Nov-23 A	24-Nov-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1820-B	TP - PRIMARY STEEL - ELEVATION ROW 4 - IFC - deleted	17d	5d	20-Nov-23 A	24-Nov-23 A	27-Nov-23	16-Dec-23	

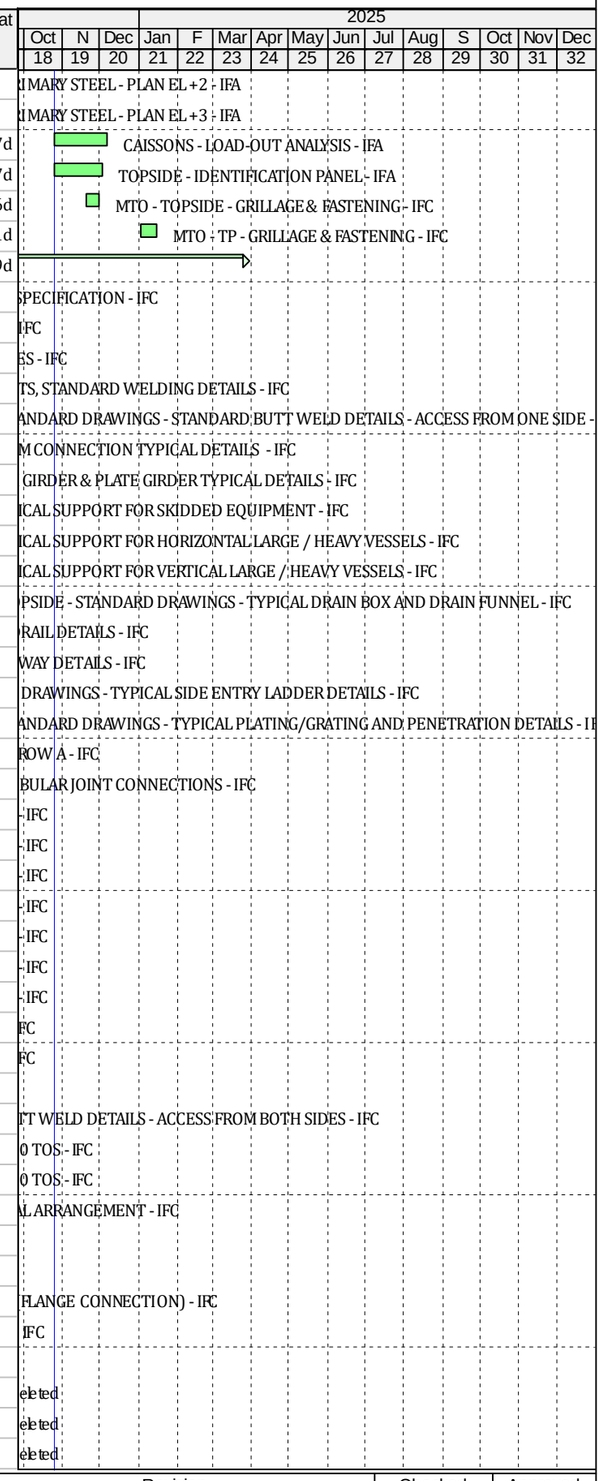


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-STR-1840-B	TP - PRIMARY STEEL - PLAN AT EL +17300 TO +19242 TOS - IFC - deleted	17d	5d	20-Nov-23 A	24-Nov-23 A	27-Nov-23	16-Dec-23	
ENG-STR-1530-B	TOPSIDE - PRIMARY JOINTS - PLAN AT EL +30310 TOS - CRANE PEDESTAL - IFC - deleted	17d	17d	02-Dec-23 A	22-Dec-23 A	02-Dec-23	22-Dec-23	
ENG-STR-1570-B	TOPSIDE - SECONDARY STEEL - PLAN AT EL 23310 TOS 30310 - IFC	17d	139d	05-Dec-23 A	24-May-24 A	04-Jan-24	24-Jan-24	
ENG-STR-1580-B	TOPSIDE - SECONDARY STEEL - PLAN +30310 TOP - IFC	17d	139d	05-Dec-23 A	24-May-24 A	04-Jan-24	24-Jan-24	
ENG-STR-1590-B	TOPSIDE - FLOORING - PLAN AT EL +23310 ??? - IFC	17d	175d	13-Dec-23 A	12-Jul-24 A	04-Jan-24	24-Jan-24	
ENG-STR-1600-B	TOPSIDE - FLOORING - PLAN AT EL +30310 ??? - IFC	17d	175d	13-Dec-23 A	12-Jul-24 A	04-Jan-24	24-Jan-24	
ENG-STR-1000-B	BLPH PLATFORM - IN-SERVICE ANALYSIS - IFC	31d	270d	18-Dec-23 A	07-Nov-24	20-Dec-23	29-Jan-24	39d
ENG-STR-1540-B	TOPSIDE - TOPSIDE TO JACKET WELD CONNECTION DETAILS - IFC	22d	118d	08-Jan-24 A	28-May-24 A	16-Nov-23	12-Dec-23	
ENG-STR-1040-B	BLPH PLATFORM - LIFTING ANALYSIS - IFC	37d	273d	19-Jan-24 A	09-Dec-24	18-Dec-23	02-Feb-24	106d
ENG-STR-1920-B	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFC	19d	61d	24-Jan-24 A	05-Apr-24 A	01-Mar-24	22-Mar-24	
ENG-STR-1020-B	BLPH PLATFORM - TRANSPORTATION ANALYSIS - IFC	15d	241d	25-Jan-24 A	07-Nov-24	30-Jan-24	09-Mar-24	39d
ENG-STR-1670-B	TOPSIDE - TECHNICAL ROOM EL +23310 - IFC - deleted	17d	17d	25-Jan-24 A	13-Feb-24 A	25-Jan-24	13-Feb-24	
ENG-STR-1680-B	TOPSIDE - TECHNICAL ROOM EL +30310 - IFC - deleted	17d	17d	25-Jan-24 A	13-Feb-24 A	25-Jan-24	13-Feb-24	
ENG-STR-1630-B	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFC	17d	46d	05-Feb-24 A	28-Mar-24 A	25-Jan-24	13-Feb-24	
ENG-STR-1640-B	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFC	17d	46d	05-Feb-24 A	28-Mar-24 A	13-May-24	31-May-24	
ENG-STR-1650-B	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFC	17d	46d	05-Feb-24 A	28-Mar-24 A	13-May-24	31-May-24	
ENG-STR-1660-B	TOPSIDE - WALKWAYS & STAIRS - ASSEMBLY & DETAILS - IFC	17d	46d	05-Feb-24 A	28-Mar-24 A	13-May-24	31-May-24	
ENG-STR-1010-B	BLPH PLATFORM - LOAD-OUT ANALYSIS - IFC	32d	228d	09-Feb-24 A	07-Nov-24	16-Mar-24	24-Apr-24	39d
ENG-STR-1900-B	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFC	31d	29d	01-Mar-24 A	05-Apr-24 A	01-Mar-24	22-Mar-24	
ENG-STR-1930-B	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFC	31d	29d	01-Mar-24 A	05-Apr-24 A	01-Mar-24	22-Mar-24	
ENG-STR-1890-B	TP - TOPSIDE BOLTED CONNECTION DETAILS - IFC - deleted	20d	23d	04-Mar-24 A	29-Mar-24 A	04-Mar-24	29-Mar-24	
ENG-STR-1090-B	TP - TRANSPORTATION ANALYSIS - IFC	39d	230d	12-Mar-24 A	11-Dec-24	04-Mar-24	19-Apr-24	69d
ENG-STR-1910-B	TP - WALKWAYS & STAIRS - ACCESS PLATFORM - IFC	31d	1d	08-Apr-24 A	09-Apr-24 A	01-Mar-24	22-Mar-24	
ENG-STR-1750-B	TOPSIDE - DRAIN SYSTEM - IFC - DELETED	15d	15d	15-Apr-24 A	03-May-24 A	15-Apr-24	03-May-24	
ENG-STR-1250-B	DRAWINGS LIST - IFC	22d	177d	26-Apr-24 A	21-Nov-24	20-Nov-23	15-Dec-23	121d
ENG-STR-1070-B	BLPH PLATFORM - FE ANALYSES - IFC	28d	186d	29-Apr-24 A	04-Dec-24	06-May-24	13-Jun-24	110d
ENG-STR-1610-B	TOPSIDE - MONORAILS - PLANS - IFC - deleted	16d	16d	29-Apr-24 A	17-May-24 A	29-Apr-24	17-May-24	
ENG-STR-1620-B	TOPSIDE - MONORAILS - DETAILS - IFC - deleted	16d	16d	29-Apr-24 A	17-May-24 A	29-Apr-24	17-May-24	
ENG-STR-1770-B	TOPSIDE - TERTIARY STRUCTURES - IFC - deleted	16d	16d	29-Apr-24 A	17-May-24 A	29-Apr-24	17-May-24	
ENG-STR-1080-B	TP - LOAD-OUT ANALYSIS - IFC	37d	179d	13-May-24 A	09-Dec-24	25-Mar-24	10-May-24	69d
ENG-STR-1190-B	FABRICATION SPECIFICATION - IFC	10d	53d	13-May-24 A	12-Jul-24 A	31-Oct-23	11-Nov-23	
ENG-STR-1060-B	BLPH PLATFORM - SECONDARY STRUCTURES DESIGN & CRANE PEDESTAL DESIGN REPORT - IFC	37d	178d	14-May-24 A	09-Dec-24	25-Mar-24	10-May-24	47d
ENG-STR-1730-B	TOPSIDE - PIPING & E&I PIPE RACKS EL+23310 -IFC - deleted	16d	1d	17-May-24 A	17-May-24 A	29-Apr-24	17-May-24	
ENG-STR-1740-B	TOPSIDE - PIPING & E&I PIPE RACKS EL+30310 -IFC - deleted	16d	1d	17-May-24 A	17-May-24 A	29-Apr-24	17-May-24	
ENG-STR-1050-B	BLPH PLATFORM - JOINT CHECK DESIGN REPORT - IFC	33d	168d	21-May-24 A	04-Dec-24	22-Apr-24	31-May-24	110d
ENG-STR-1240-B	3D GENERAL ARRANGEMENT - IFC	22d	38d	21-May-24 A	03-Jul-24 A	20-Nov-23	15-Dec-23	
ENG-STR-1110-B	TP - LIFTING ANALYSIS - IFC	35d	165d	27-May-24 A	06-Dec-24	19-Feb-24	29-Mar-24	69d
ENG-STR-1130-B	TP-MP FLANGE CONNECTION VERIFICATION - IFC	21d	149d	29-May-24 A	20-Nov-24	18-Mar-24	26-Apr-24	69d
ENG-STR-1160-B	CAISSONS - LIFTING ANALYSIS - IFC - DELETED	22d	41d	03-Jun-24 A	19-Jul-24 A	03-Jun-24	19-Jul-24	
ENG-STR-1710-B	STORAGE VESSEL - PRIMARY STEEL - PLAN EL +2 - IFC	15d	75d	03-Jun-24 A	30-Aug-24 A	15-Apr-24	03-May-24	
ENG-STR-1720-B	STORAGE VESSEL - PRIMARY STEEL - PLAN EL +3 - IFC	15d	75d	03-Jun-24 A	30-Aug-24 A	15-Apr-24	03-May-24	
ENG-STR-1870-B	TP - LIFTING POINTS - GENERAL ARRANGEMENT - IFC	15d	44d	10-Jul-24 A	30-Aug-24 A	11-Dec-23	12-Jan-24	
ENG-STR-1880-B	TP - LIFTING POINTS - DETAILS - IFC	14d	44d	10-Jul-24 A	30-Aug-24 A	11-Dec-23	12-Jan-24	
ENG-STR-1120-B	TP - JOINT CHECK DESIGN REPORT - IFC	39d	114d	30-Jul-24 A	11-Dec-24	04-Mar-24	19-Apr-24	104d
ENG-STR-1150-B	CAISSONS - TRANSPORTATION ANALYSIS - IFC	33d	103d	05-Aug-24 A	04-Dec-24	22-Apr-24	31-May-24	110d
ENG-STR-1940-B	CAISSONS ELEVATION - IFC	19d	56d	13-Sep-24 A	18-Nov-24	07-Mar-24	28-Mar-24	124d

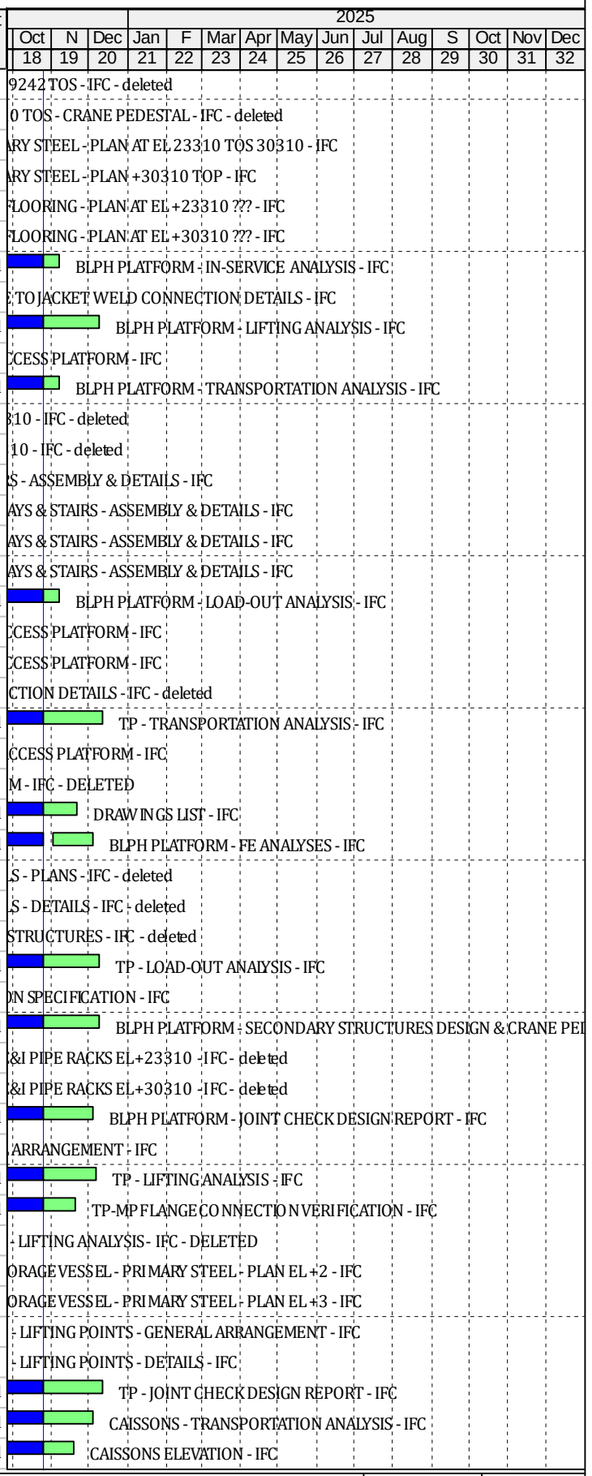


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-STR-1950-B	CAISSONS DETAILS - IFC	19d	56d	13-Sep-24 A	18-Nov-24	07-Mar-24	28-Mar-24	124d
ENG-STR-1030-B	BLPH PLATFORM - TRANSPORTATION FATIGUE ANALYSIS - IFC	10d	10d	09-Nov-24	20-Nov-24	04-May-24	15-May-24	38d
ENG-STR-1690-B	TOPSIDE - EQUIPMENT SUPPORTS GENERAL ARRANGEMENT EL +23310 - IFC	17d	17d	22-Nov-24	11-Dec-24	25-Jan-24	13-Feb-24	104d
ENG-STR-1700-B	TOPSIDE - EQUIPMENT SUPPORTS GENERAL ARRANGEMENT EL +30310 - IFC	17d	17d	22-Nov-24	11-Dec-24	25-Jan-24	13-Feb-24	104d
ENG-STR-1760-B	TOPSIDE - IDENTIFICATION PANEL - IFC	15d	15d	14-Dec-24	03-Jan-25	15-Apr-24	03-May-24	87d
ENG-STR-1960-B	CAISSON DETAILS - IFC	19d	19d	30-Dec-24	22-Jan-25	07-Mar-24	28-Mar-24	72d
ENG-STR-1140-B	CAISSONS - LOAD-OUT ANALYSIS - IFC	33d	33d	14-Jan-25	20-Feb-25	22-Apr-24	31-May-24	47d
ENG-STR-1100-B	TP - TRANSPORTATION FATIGUE ANALYSIS - IFC	39d	39d	08-Feb-25	25-Mar-25	04-Mar-24	19-Apr-24	19d
Piping Engineering		424d	432d	06-Sep-23 A	08-Feb-25	15-Sep-23	05-Aug-24	69d
Issue For Approval		409d	417d	06-Sep-23 A	22-Jan-25	15-Sep-23	18-Jul-24	21d
ENG-PIP-1000-A	Pipe Material Classes - IFA	15d	1d	06-Sep-23 A	06-Sep-23 A	15-Sep-23	02-Oct-23	
ENG-PIP-1340-A	Technical Specification for Piping materials narrative - IFA	10d	1d	06-Sep-23 A	06-Sep-23 A	21-Sep-23	02-Oct-23	
ENG-PIP-1350-A	Technical Specification for Manual Valves & Strainers - IFA	10d	1d	06-Sep-23 A	06-Sep-23 A	20-Oct-23	31-Oct-23	
ENG-PIP-1080-A	TDS - Manual Valves - IFA	10d	1d	15-Sep-23 A	15-Sep-23 A	20-Oct-23	31-Oct-23	
ENG-PIP-1010-A	Plot Plans - IFA	10d	11d	20-Oct-23 A	02-Nov-23 A	20-Oct-23	31-Oct-23	
ENG-PIP-1070-A	Valves List - IFA	10d	16d	23-Oct-23 A	10-Nov-23 A	20-Oct-23	31-Oct-23	
ENG-PIP-1270-A	MR - Gate, Globe & Check Valves - Issue for RfQ	10d	15d	06-Nov-23 A	22-Nov-23 A	25-Oct-23	06-Nov-23	
ENG-PIP-1280-A	MR - Ball Valves - Issue for RfQ	10d	15d	06-Nov-23 A	22-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-PIP-1290-A	MR - Double Block and Bleed Valves - Issue for RfQ	10d	15d	06-Nov-23 A	22-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-PIP-1300-A	MR - DBB & SBB Valves (Instrument connections) - Issue for RfQ	10d	15d	06-Nov-23 A	22-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-PIP-1090-A	TDS - Y Type Strainers - IFA	10d	9d	13-Nov-23 A	22-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-PIP-1630-A	Typical Piping Assembly - IFA	20d	44d	13-Nov-23 A	08-Jan-24 A	14-Nov-23	06-Dec-23	
ENG-PIP-1640-A	Piping Special Item list - IFA	10d	11d	13-Nov-23 A	24-Nov-23 A	14-Nov-23	24-Nov-23	
ENG-PIP-1660-A	Pipe Support Standard - IFA	15d	24d	13-Nov-23 A	11-Dec-23 A	15-Nov-23	01-Dec-23	
ENG-PIP-1110-A	TDS - Bird screen - IFA - DELETED	10d	5d	20-Nov-23 A	24-Nov-23 A	25-Nov-23	06-Dec-23	
ENG-PIP-1330-A	Technical Specification for Piping Special Parts - IFA - DELETED	10d	10d	25-Nov-23 A	06-Dec-23 A	25-Nov-23	06-Dec-23	
ENG-PIP-1320-A	MR - Bird screen - Issue for RfQ - DELETED	10d	10d	07-Dec-23 A	19-Dec-23 A	07-Dec-23	19-Dec-23	
ENG-PIP-1130-A	30% 3D Model Review & Report - IFA	10d	4d	11-Dec-23 A	14-Dec-23 A	03-Nov-23	14-Nov-23	
ENG-PIP-1100-A	TDS - Flame Arresters - IFA - DELETED	10d	10d	20-Dec-23 A	03-Jan-24 A	20-Dec-23	03-Jan-24	
ENG-PIP-1310-A	MR - Flame Arresters - Issue for RfQ - DELETED	10d	10d	04-Jan-24 A	16-Jan-24 A	04-Jan-24	16-Jan-24	
ENG-PIP-1160-A	MR - Y Type Strainers - Issue for RfQ - DELETED	10d	1d	08-Jan-24 A	08-Jan-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1170-A	MR - Studs and Bolts - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	10-Jan-24	20-Jan-24	
ENG-PIP-1180-A	MR - Gaskets - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	14-Feb-24	24-Feb-24	
ENG-PIP-1190-A	MR - Super Duplex and SS Materials - Flanges - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1200-A	MR - Carbon Steel Materials - Flanges - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1210-A	MR - Duplex and SS Materials - Pipes - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1220-A	MR - Carbon Steel Materials - Pipes - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1230-A	MR - Super Duplex and SS Materials - Forged Fittings - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1240-A	MR - Carbon Steel Materials - Forged Fittings - Issue for RfQ - DELETED	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1250-A	MR - Super Duplex and SS Materials - Bw Fittings - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1260-A	MR - Carbon Steel and LTCS Materials - Bw Fittings - Issue for RfQ	10d	18d	19-Jan-24 A	08-Feb-24 A	22-Dec-23	05-Jan-24	
ENG-PIP-1690-A	MTO - Piping Bulk - IFA	15d	11d	26-Jan-24 A	07-Feb-24 A	04-Dec-23	21-Dec-23	
ENG-PIP-1020-A	Stress & Vibration Analysis Report - IFA	13d	26d	15-Feb-24 A	15-Mar-24 A	26-Oct-23	13-Nov-23	
ENG-PIP-1140-A	60% 3D Model Review & Report - IFA	4d	8d	04-Mar-24 A	12-Mar-24 A	17-Feb-24	28-Feb-24	
ENG-PIP-1590-A	Piping floor penetration Lower deck EL. +23.310m- Typical & detail - IFA	13d	26d	08-Apr-24 A	09-May-24 A	17-Feb-24	11-Mar-24	
ENG-PIP-1600-A	Piping floor penetration Upper deck EL. +30.310m- Typical & detail - IFA	13d	26d	08-Apr-24 A	09-May-24 A	17-Feb-24	11-Mar-24	

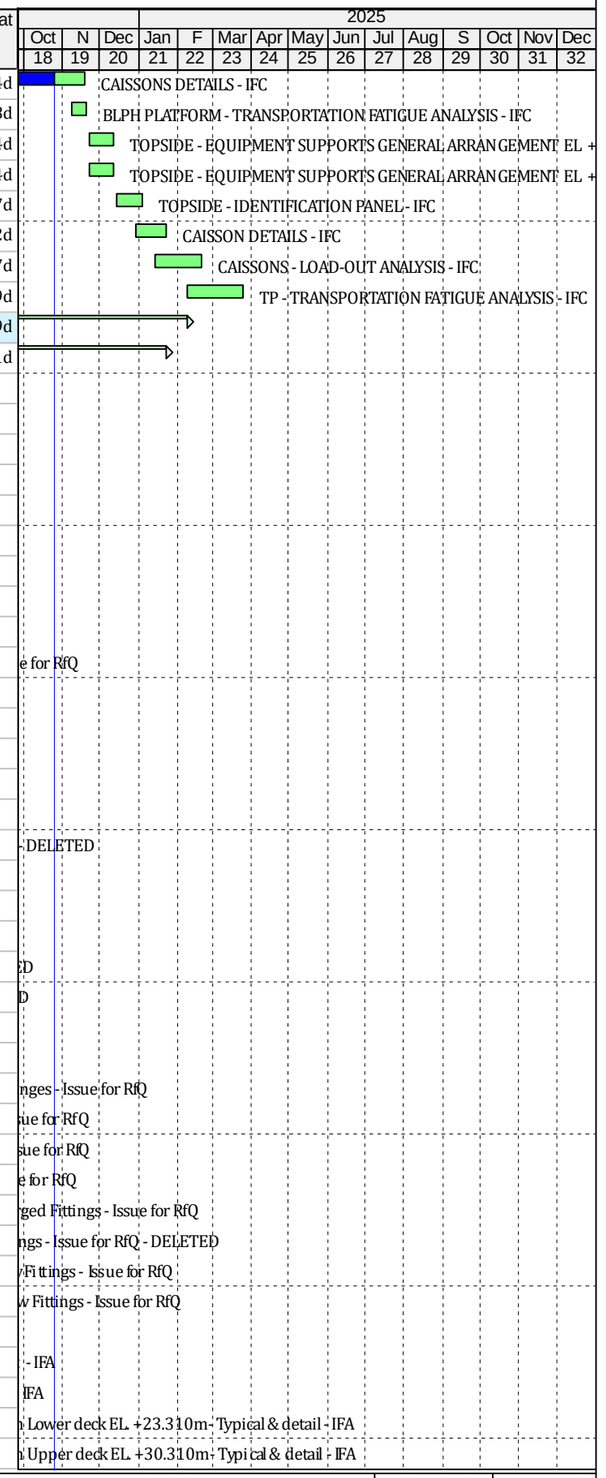


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-PIP-1610-A	Piping floor penetration from EL. +31.410m to EL.+36.210m - IFA - DELETED	13d	1d	08-Apr-24 A	08-Apr-24 A	17-Feb-24	11-Mar-24	
ENG-PIP-1620-A	Piping floor penetration from EL. +36.210m to Above - IFA - DELETED	13d	1d	08-Apr-24 A	08-Apr-24 A	17-Feb-24	11-Mar-24	
ENG-PIP-1060-A	Isometrics drawing & List - IFA	20d	30d	10-May-24 A	13-Jun-24 A	14-Mar-24	08-Apr-24	
ENG-PIP-1650-A	Piping Hook-up list - IFA	11d	74d	14-May-24 A	07-Aug-24 A	14-May-24	24-May-24	
ENG-PIP-1560-A	Piping and support general arrangement - Above Upper Deck - IFA	30d	138d	18-May-24 A	26-Oct-24	29-Feb-24	05-Apr-24	69d
ENG-PIP-1530-A	Piping and support general arrangement - Below Lower Deck - IFA	30d	133d	24-May-24 A	26-Oct-24	29-Feb-24	05-Apr-24	69d
ENG-PIP-1540-A	Piping and support general arrangement - Above Lower Deck - IFA	30d	133d	24-May-24 A	26-Oct-24	29-Feb-24	05-Apr-24	69d
ENG-PIP-1550-A	Piping and support general arrangement - Below Upper Deck - IFA	30d	133d	24-May-24 A	26-Oct-24	29-Feb-24	05-Apr-24	69d
ENG-PIP-1570-A	Piping and support general arrangement from EL.+31.410m to EL. +36.210m - IFA	30d	133d	24-May-24 A	26-Oct-24	29-Feb-24	05-Apr-24	69d
ENG-PIP-1580-A	Piping and support general arrangement from EL.+36.210m to Above - IFA	30d	133d	24-May-24 A	26-Oct-24	29-Feb-24	05-Apr-24	69d
ENG-PIP-1670-A	Piping Support Book - IFA	10d	65d	28-Jun-24 A	12-Sep-24 A	09-Apr-24	19-Apr-24	
ENG-PIP-1680-A	MTO - Piping Support - IFA	10d	65d	28-Jun-24 A	12-Sep-24 A	17-Feb-24	28-Feb-24	
ENG-PIP-1150-A	90% 3D Model Review & Report - IFA	10d	10d	15-Jul-24 A	25-Jul-24 A	08-Jun-24	19-Jun-24	
ENG-PIP-1030-A	Piping Fabrication & Installation Specification - IFA	15d	15d	26-Oct-24	13-Nov-24	15-Nov-23	01-Dec-23	49d
ENG-PIP-1040-A	Pressure testing of Pipework Specification - IFA	15d	15d	26-Oct-24	13-Nov-24	07-Dec-23	27-Dec-23	62d
ENG-PIP-1050-A	Chemical Cleaning of Pipework Specification - IFA	5d	5d	17-Jan-25	22-Jan-25	13-Jul-24	18-Jul-24	16d
Issue For Construction		399d	409d	03-Oct-23 A	08-Feb-25	14-Oct-23	05-Aug-24	69d
ENG-PIP-1000-B	Pipe Material Classes - IFC	15d	41d	03-Oct-23 A	20-Nov-23 A	26-Oct-23	13-Nov-23	
ENG-PIP-1080-B	TDS - Manual Valves - IFC	10d	41d	03-Oct-23 A	20-Nov-23 A	14-Nov-23	24-Nov-23	
ENG-PIP-1340-B	Technical Specification for Piping materials narrative - IFC	10d	82d	03-Oct-23 A	12-Jan-24 A	14-Oct-23	25-Oct-23	
ENG-PIP-1350-B	Technical Specification for Manual Valves & Strainers - IFC	10d	59d	03-Oct-23 A	12-Dec-23 A	02-Nov-23	13-Nov-23	
ENG-PIP-1270-B	MR - Gate, Globe & Check Valves - Issue for PO Placement	10d	15d	06-Nov-23 A	22-Nov-23 A	18-Nov-23	29-Nov-23	
ENG-PIP-1290-B	MR - Double Block and Bleed Valves - Issue for PO Placement	10d	15d	06-Nov-23 A	22-Nov-23 A	25-Nov-23	06-Dec-23	
ENG-PIP-1300-B	MR - DBB & SBB Valves (Instrument connections) - Issue for PO Placement	10d	15d	06-Nov-23 A	22-Nov-23 A	25-Nov-23	06-Dec-23	
ENG-PIP-1010-B	Plot Plans - IFC	10d	154d	23-Nov-23 A	30-May-24 A	14-Mar-24	25-Mar-24	
ENG-PIP-1070-B	Valves List - IFC	5d	98d	24-Nov-23 A	22-Mar-24 A	14-Mar-24	19-Mar-24	
ENG-PIP-1640-B	Piping Special Item list - IFC	10d	54d	12-Dec-23 A	16-Feb-24 A	07-Dec-23	19-Dec-23	
ENG-PIP-1090-B	TDS - Y Type Strainers - IFC - DELETED	10d	3d	13-Dec-23 A	15-Dec-23 A	25-Nov-23	06-Dec-23	
ENG-PIP-1110-B	TDS - Bird screen - IFC - DELETED	10d	12d	18-Dec-23 A	03-Jan-24 A	20-Dec-23	03-Jan-24	
ENG-PIP-1280-B	MR - Ball Valves - Issue for PO Placement	10d	15d	18-Dec-23 A	08-Jan-24 A	25-Nov-23	06-Dec-23	
ENG-PIP-1330-B	Technical Specification for Piping Special Parts - IFC - DELETED	10d	10d	20-Dec-23 A	03-Jan-24 A	20-Dec-23	03-Jan-24	
ENG-PIP-1660-B	Pipe Support Standard - IFC	10d	24d	03-Jan-24 A	31-Jan-24 A	20-Dec-23	03-Jan-24	
ENG-PIP-1320-B	MR - Bird screen - Issue for PO Placement - DELETED	10d	10d	04-Jan-24 A	16-Jan-24 A	04-Jan-24	16-Jan-24	
ENG-PIP-1100-B	TDS - Flame Arresters - IFC - DELETED	10d	10d	17-Jan-24 A	27-Jan-24 A	17-Jan-24	27-Jan-24	
ENG-PIP-1130-B	30% 3D Model Review Report - IFC	10d	43d	19-Jan-24 A	08-Mar-24 A	27-Nov-23	07-Dec-23	
ENG-PIP-1160-B	MR - Y Type Strainers - Issue for PO Placement - DELETED	10d	10d	19-Jan-24 A	30-Jan-24 A	19-Jan-24	30-Jan-24	
ENG-PIP-1240-B	MR - Carbon Steel Materials - Forged Fittings - Issue for PO Placement - deleted	10d	10d	19-Jan-24 A	30-Jan-24 A	19-Jan-24	30-Jan-24	
ENG-PIP-1630-B	Typical Piping Assembly - IFC	16d	23d	22-Jan-24 A	16-Feb-24 A	04-Jan-24	22-Jan-24	
ENG-PIP-1310-B	MR - Flame Arresters - Issue for PO Placement - DELETED	10d	10d	29-Jan-24 A	08-Feb-24 A	29-Jan-24	08-Feb-24	
ENG-PIP-1690-B	MTO - Piping Bulk - IFC	13d	29d	12-Feb-24 A	15-Mar-24 A	13-Jan-24	30-Jan-24	
ENG-PIP-1170-B	MR - Studs and Bolts - Issue for PO Placement	10d	40d	08-Mar-24 A	26-Apr-24 A	02-Feb-24	13-Feb-24	
ENG-PIP-1200-B	MR - Carbon Steel Materials - Flanges - Issue for PO Placement	10d	40d	08-Mar-24 A	26-Apr-24 A	19-Jan-24	30-Jan-24	
ENG-PIP-1210-B	MR - Duplex and SS Materials - Pipes - Issue for PO Placement	10d	37d	08-Mar-24 A	22-Apr-24 A	19-Jan-24	30-Jan-24	
ENG-PIP-1220-B	MR - Carbon Steel Materials - Pipes - Issue for PO Placement	10d	37d	08-Mar-24 A	22-Apr-24 A	31-Jan-24	10-Feb-24	
ENG-PIP-1250-B	MR - Super Duplex and SS Materials - Bw Fittings - Issue for PO Placement	10d	40d	08-Mar-24 A	26-Apr-24 A	19-Jan-24	30-Jan-24	
ENG-PIP-1260-B	MR - Carbon Steel and LTCS Materials - Bw Fittings - Issue for PO Placement	10d	40d	08-Mar-24 A	26-Apr-24 A	19-Jan-24	30-Jan-24	

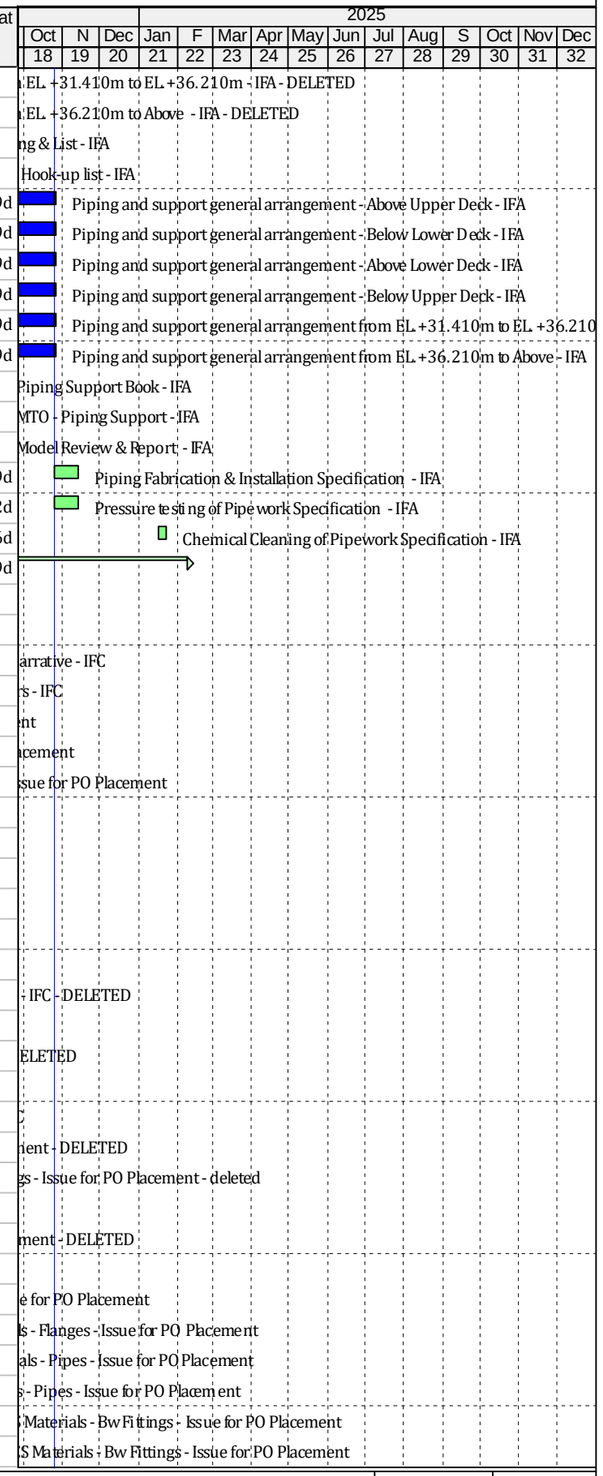

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-PIP-1180-B	MR - Gaskets - Issue for PO Placement	10d	38d	11-Mar-24 A	26-Apr-24 A	08-Mar-24	19-Mar-24	
ENG-PIP-1190-B	MR - Super Duplex and SS Materials - Flanges - Issue for PO Placement	10d	38d	11-Mar-24 A	26-Apr-24 A	19-Jan-24	30-Jan-24	
ENG-PIP-1230-B	MR - Super Duplex and SS Materials - Forged Fittings - Issue for PO Placement	10d	38d	11-Mar-24 A	26-Apr-24 A	19-Jan-24	30-Jan-24	
ENG-PIP-1610-B	Piping floor penetration from EL. +31.410m to EL. +36.210m - IFC - DELETED	15d	15d	12-Apr-24 A	30-Apr-24 A	12-Apr-24	30-Apr-24	
ENG-PIP-1620-B	Piping floor penetration from EL. +36.210m to Above - IFC -DELETED	15d	15d	12-Apr-24 A	30-Apr-24 A	12-Apr-24	30-Apr-24	
ENG-PIP-1020-B	Stress & Vibration Analysis Report - IFC	10d	73d	17-Apr-24 A	12-Jul-24 A	25-Nov-23	06-Dec-23	
ENG-PIP-1140-B	60% 3D Model Review Report - IFC	10d	75d	17-Apr-24 A	15-Jul-24 A	20-Mar-24	02-Apr-24	
ENG-PIP-1590-B	Piping floor penetration Lower deck EL. +23.310m- Typical & detail - IFC	15d	35d	27-May-24 A	05-Jul-24 A	12-Apr-24	30-Apr-24	
ENG-PIP-1600-B	Piping floor penetration Upper deck EL. +30.310m- Typical & detail - IFC	15d	34d	28-May-24 A	05-Jul-24 A	12-Apr-24	30-Apr-24	
ENG-PIP-1060-B	Isometrics drawing & List - IFC	10d	4d	23-Jul-24 A	26-Jul-24 A	16-May-24	27-May-24	
ENG-PIP-1650-B	Piping Hook-up list - IFC	10d	39d	27-Aug-24 A	10-Oct-24 A	06-Jun-24	17-Jun-24	
ENG-PIP-1680-B	MTO - Piping Support - IFC	10d	48d	12-Sep-24 A	07-Nov-24	08-Jun-24	19-Jun-24	63d
ENG-PIP-1670-B	Piping Support Book - IFC	10d	10d	26-Oct-24	07-Nov-24	28-May-24	07-Jun-24	63d
ENG-PIP-1530-B	Piping and support general arrangement - Below Lower Deck - IFC	19d	19d	09-Nov-24	30-Nov-24	18-Apr-24	13-May-24	125d
ENG-PIP-1540-B	Piping and support general arrangement - Above Lower Deck - IFC	19d	19d	09-Nov-24	30-Nov-24	18-Apr-24	13-May-24	125d
ENG-PIP-1550-B	Piping and support general arrangement - Below Upper Deck - IFC	19d	19d	09-Nov-24	30-Nov-24	18-Apr-24	13-May-24	125d
ENG-PIP-1560-B	Piping and support general arrangement - Above Upper Deck - IFC	19d	19d	09-Nov-24	30-Nov-24	18-Apr-24	13-May-24	125d
ENG-PIP-1570-B	Piping and support general arrangement from EL. +31.410m to EL. +36.210m - IFC	19d	19d	09-Nov-24	30-Nov-24	18-Apr-24	13-May-24	125d
ENG-PIP-1580-B	Piping and support general arrangement from EL. +36.210m to Above - IFC	19d	19d	09-Nov-24	30-Nov-24	18-Apr-24	13-May-24	125d
ENG-PIP-1030-B	Piping Fabrication & Installation Specification - IFC	15d	15d	23-Nov-24	10-Dec-24	29-Dec-23	17-Jan-24	49d
ENG-PIP-1040-B	Pressure testing of Pipework Specification - IFC	10d	10d	11-Dec-24	21-Dec-24	11-Jan-24	22-Jan-24	49d
ENG-PIP-1150-B	90% 3D Model Review Report - IFC	10d	10d	04-Jan-25	16-Jan-25	02-Jul-24	12-Jul-24	13d
ENG-PIP-1050-B	Chemical Cleaning of Pipework Specification - IFC	5d	5d	04-Feb-25	08-Feb-25	31-Jul-24	05-Aug-24	16d
Issue For Information		103d	106d	18-Dec-23 A	26-Apr-24 A	28-Nov-23	26-Mar-24	
ENG-PIP-1470-A	TBE - Gate, Globe & Check Valves - IFI	15d	92d	18-Dec-23 A	09-Apr-24 A	28-Nov-23	15-Dec-23	
ENG-PIP-1480-A	TBE - Ball Valves - IFI	15d	92d	18-Dec-23 A	09-Apr-24 A	28-Nov-23	15-Dec-23	
ENG-PIP-1490-A	TBE - Double Block and Bleed Valves - IFI	15d	92d	18-Dec-23 A	09-Apr-24 A	28-Nov-23	15-Dec-23	
ENG-PIP-1500-A	TBE - DBB & SBB Valves (Monoflange) - IFI	15d	92d	18-Dec-23 A	09-Apr-24 A	28-Nov-23	15-Dec-23	
ENG-PIP-1360-A	TBE - Y Type Strainers - IFI - DELETED	15d	15d	20-Jan-24 A	06-Feb-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1440-A	TBE - Carbon Steel Materials - Forged Fittings - IFI - to be deleted	15d	15d	20-Jan-24 A	06-Feb-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1510-A	TBE - Flame Arresters - IFI - DELETED	15d	15d	31-Jan-24 A	16-Feb-24 A	31-Jan-24	16-Feb-24	
ENG-PIP-1520-A	TBE - Bird screen - IFI - DELETED	15d	15d	31-Jan-24 A	16-Feb-24 A	31-Jan-24	16-Feb-24	
ENG-PIP-1370-A	TBE - Studs and Bolts - IFI	15d	21d	02-Apr-24 A	26-Apr-24 A	03-Feb-24	20-Feb-24	
ENG-PIP-1380-A	TBE - Gaskets - IFI	15d	21d	02-Apr-24 A	26-Apr-24 A	09-Mar-24	26-Mar-24	
ENG-PIP-1390-A	TBE - Super Duplex and SS Materials - Flanges - IFI	15d	21d	02-Apr-24 A	26-Apr-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1400-A	TBE - Carbon Steel Materials - Flanges - IFI	15d	18d	02-Apr-24 A	22-Apr-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1410-A	TBE - Duplex and SS Materials - Pipes - IFI	15d	21d	02-Apr-24 A	26-Apr-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1420-A	TBE - Carbon Steel Materials - Pipes - IFI	15d	18d	02-Apr-24 A	22-Apr-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1430-A	TBE - Super Duplex and SS Materials - Forged Fittings - IFI	15d	21d	02-Apr-24 A	26-Apr-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1450-A	TBE - Super Duplex and SS Materials - Bw Fittings - IFI	15d	21d	02-Apr-24 A	26-Apr-24 A	20-Jan-24	06-Feb-24	
ENG-PIP-1460-A	TBE - Carbon Steel and LTCS Materials - Bw Fittings - IFI	15d	21d	02-Apr-24 A	26-Apr-24 A	20-Jan-24	06-Feb-24	
Mechanical Engineering		388d	388d	29-Aug-23 A	06-Dec-24	29-Aug-23	27-Feb-24	44d
Issue For Approval		368d	368d	29-Aug-23 A	13-Nov-24	29-Aug-23	12-Jan-24	52d
ENG-MECH-1250-A	MR - H2 Service Storage Vessel - Issue for RfQ	5d	18d	29-Aug-23 A	18-Sep-23 A	28-Sep-23	03-Oct-23	
ENG-MECH-1260-A	Technical Specification for CS Horizontal Pressure Vessels in H2 Service - IFA	10d	19d	29-Aug-23 A	19-Sep-23 A	29-Aug-23	08-Sep-23	
ENG-MECH-1270-A	TDS - H2 Storage Vessel - V-25001 - IFA	5d	18d	29-Aug-23 A	18-Sep-23 A	22-Sep-23	27-Sep-23	

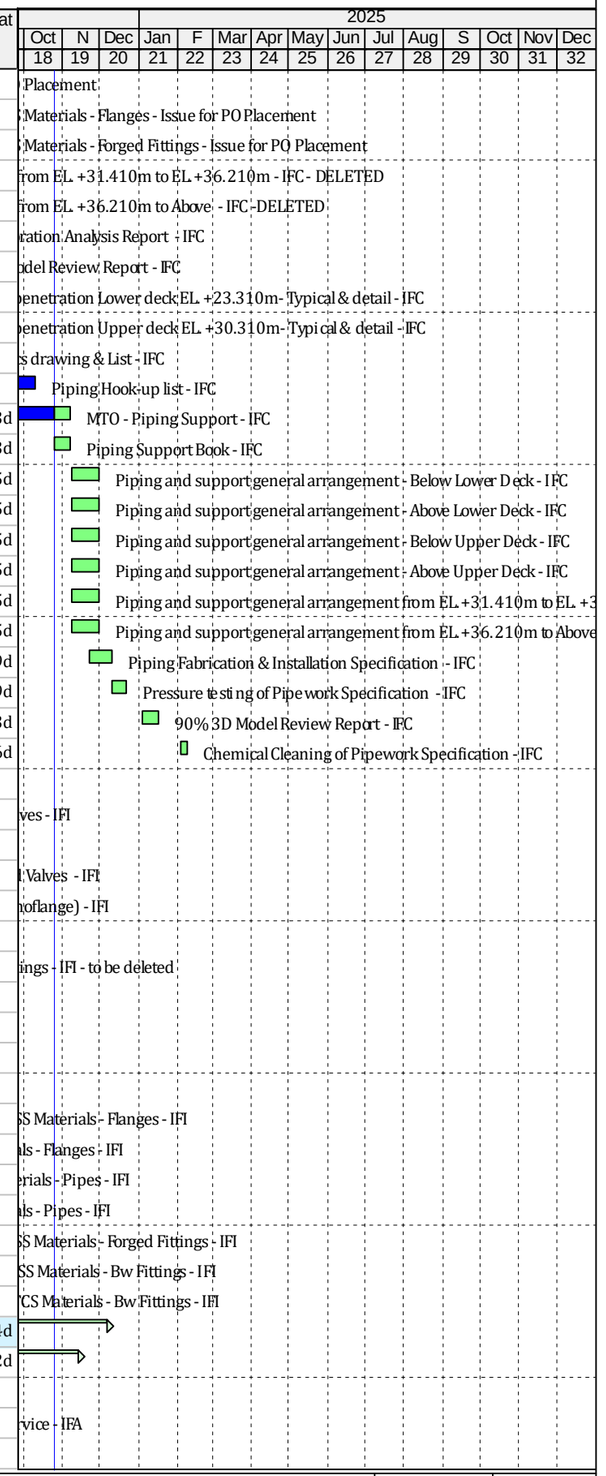

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-MECH-1060-A	MR - Tank CS - Issue for RfQ	16d	22d	09-Oct-23 A	03-Nov-23 A	02-Oct-23	19-Oct-23	
ENG-MECH-1070-A	Technical Specification for Tank CS - IFA	10d	22d	09-Oct-23 A	03-Nov-23 A	09-Oct-23	19-Oct-23	
ENG-MECH-1080-A	TDS - Tank T-5501 - Waste Water Tank - IFA	10d	22d	09-Oct-23 A	03-Nov-23 A	09-Oct-23	19-Oct-23	
ENG-MECH-1100-A	TDS - Tank T-63001 - Instrument Air Receiver - IFA - deleted	10d	10d	09-Oct-23 A	19-Oct-23 A	09-Oct-23	19-Oct-23	
ENG-MECH-1300-A	MR - Instrument Air Package - A-63000 - Issue for RfQ	10d	17d	09-Oct-23 A	27-Oct-23 A	02-Oct-23	12-Oct-23	
ENG-MECH-1310-A	Technical Specification for Instrument Air Package - A-63000 - IFA	10d	17d	09-Oct-23 A	27-Oct-23 A	02-Oct-23	12-Oct-23	
ENG-MECH-1090-A	TDS - Tank T-5XXX - N2 Receiver - IFA - deleted	10d	10d	18-Oct-23 A	28-Oct-23 A	18-Oct-23	28-Oct-23	
ENG-MECH-1400-A	TDS - Nitrogen Bottles rack -U-64000 - IFA - deleted	10d	10d	18-Oct-23 A	28-Oct-23 A	18-Oct-23	28-Oct-23	
ENG-MECH-1380-A	MR - Nitrogen Bottles rack -U-64000 - Issue for RfQ	10d	23d	20-Oct-23 A	16-Nov-23 A	18-Oct-23	28-Oct-23	
ENG-MECH-1390-A	Technical Specification for Nitrogen Bottles rack -U-64000 - IFA	10d	23d	20-Oct-23 A	16-Nov-23 A	18-Oct-23	28-Oct-23	
ENG-MECH-1420-A	MR - Hydrogen Vent - U-43004 - Issue for RfQ	10d	101d	20-Oct-23 A	21-Feb-24 A	06-Oct-23	17-Oct-23	
ENG-MECH-1010-A	MR - Tank GRP - Issue for RfQ	10d	5d	23-Oct-23 A	27-Oct-23 A	08-Nov-23	18-Nov-23	
ENG-MECH-1020-A	Technical Specification for Tank GRP - IFA	10d	5d	23-Oct-23 A	27-Oct-23 A	08-Nov-23	18-Nov-23	
ENG-MECH-1030-A	TDS - Tank T-5600 - Filtered Seawater Tank - IFA	10d	5d	23-Oct-23 A	27-Oct-23 A	08-Nov-23	18-Nov-23	
ENG-MECH-1040-A	TDS - Tank T-5800 - Fresh Water Tank - IFA	10d	5d	23-Oct-23 A	27-Oct-23 A	08-Nov-23	18-Nov-23	
ENG-MECH-1120-A	MR - Progressive Cavity Pump -50001 A/B - Issue for RfQ	10d	113d	23-Oct-23 A	08-Mar-24 A	24-Oct-23	04-Nov-23	
ENG-MECH-1130-A	Technical Specification for Progressive Cavity Pump -50001 A/B - IFA	10d	111d	23-Oct-23 A	06-Mar-24 A	12-Oct-23	23-Oct-23	
ENG-MECH-1140-A	TDS - Progressive Cavity Pump -50001 A/B - IFA	10d	111d	23-Oct-23 A	06-Mar-24 A	12-Oct-23	23-Oct-23	
ENG-MECH-1230-A	TDS - Electro-Chlorination Unit - A-50002 - IFA	10d	12d	23-Oct-23 A	06-Nov-23 A	20-Oct-23	31-Oct-23	
ENG-MECH-1170-A	Technical Specification for Water Treatmement Package - IFA	10d	10d	06-Nov-23 A	16-Nov-23 A	08-Nov-23	18-Nov-23	
ENG-MECH-1210-A	TDS - Ultra Filtrartion Unit - - IFA	10d	10d	06-Nov-23 A	16-Nov-23 A	08-Nov-23	18-Nov-23	
ENG-MECH-1220-A	TDS - Desalination Unit (SWRO) - A-50008 - IFA	10d	10d	06-Nov-23 A	16-Nov-23 A	08-Nov-23	18-Nov-23	
ENG-MECH-1160-A	MR - Water Tretment Package - Issue for RfQ	10d	4d	13-Nov-23 A	16-Nov-23 A	20-Nov-23	30-Nov-23	
ENG-MECH-1180-A	TDS - Fresh Water Pump - P-50009 A/B - IFA	10d	4d	13-Nov-23 A	16-Nov-23 A	29-Nov-23	11-Dec-23	
ENG-MECH-1190-A	TDS - Sea Water Coarse Filter Package - A-50003 - IFA	10d	4d	13-Nov-23 A	16-Nov-23 A	29-Nov-23	11-Dec-23	
ENG-MECH-1200-A	TDS - UV Water Filter - S-50010 - IFA	10d	4d	13-Nov-23 A	16-Nov-23 A	20-Nov-23	30-Nov-23	
ENG-MECH-1440-A	TDS - Hydrogen Vent - U-43004 - IFA	10d	66d	01-Dec-23 A	21-Feb-24 A	25-Sep-23	05-Oct-23	
ENG-MECH-1280-A	TDS - Hydrogen Vent KO Drum - V-43001 - IFA	10d	14d	04-Dec-23 A	20-Dec-23 A	30-Dec-23	12-Jan-24	
ENG-MECH-1360-A	TDS - DAVIT CRANE - IFA - to be deleted	10d	10d	13-Dec-23 A	23-Dec-23 A	13-Dec-23	23-Dec-23	
ENG-MECH-1430-A	Technical Specification for Hydrogen Vent - U-43004 - IFA	10d	23d	26-Jan-24 A	21-Feb-24 A	25-Sep-23	05-Oct-23	
ENG-MECH-1000-A	Master Equipment List - IFA	30d	149d	31-Jan-24 A	26-Jul-24 A	20-Oct-23	31-Oct-23	
ENG-MECH-1330-A	MR - DAVIT CRANE - Issue for RfQ	13d	9d	18-Mar-24 A	27-Mar-24 A	27-Dec-23	12-Jan-24	
ENG-MECH-1340-A	Technical Specification for DAVIT CRANE - IFA	10d	9d	18-Mar-24 A	27-Mar-24 A	13-Dec-23	23-Dec-23	
ENG-MECH-1350-A	TDS - Davit Crane - IFA	10d	9d	18-Mar-24 A	27-Mar-24 A	13-Dec-23	23-Dec-23	
ENG-MECH-1460-A	First Fill / Lubricants List - IFA	15d	15d	26-Oct-24	13-Nov-24	02-Nov-23	18-Nov-23	44d
Issue For Construction		352d	388d	29-Aug-23 A	06-Dec-24	10-Oct-23	27-Feb-24	44d
ENG-MECH-1250-B	MR - H2 Service Storage Vessel - Issue for PO Placement	10d	20d	29-Aug-23 A	20-Sep-23 A	21-Oct-23	02-Nov-23	
ENG-MECH-1260-B	Technical Specification for CS Horizontal Pressure Vessels in H2 Service - IFC	10d	47d	28-Sep-23 A	22-Nov-23 A	10-Oct-23	20-Oct-23	
ENG-MECH-1270-B	TDS - H2 Storage Vessel - V-25001 - IFC	10d	47d	28-Sep-23 A	22-Nov-23 A	10-Oct-23	20-Oct-23	
ENG-MECH-1060-B	MR - Tank CS - Issue for PO Placement	10d	26d	09-Oct-23 A	08-Nov-23 A	24-Nov-23	05-Dec-23	
ENG-MECH-1300-B	MR - Instrument Air Package - A-63000 - Issue for PO Placement	10d	17d	09-Oct-23 A	27-Oct-23 A	17-Nov-23	28-Nov-23	
ENG-MECH-1010-B	MR - Tank GRP - Issue for PO Placement	10d	7d	20-Oct-23 A	27-Oct-23 A	29-Dec-23	11-Jan-24	
ENG-MECH-1380-B	MR - Nitrogen Bottles rack -U-64000 - Issue for PO Placement	10d	23d	20-Oct-23 A	16-Nov-23 A	12-Dec-23	22-Dec-23	
ENG-MECH-1160-B	MR - Water Tretment Package - Issue for PO Placement	10d	6d	10-Nov-23 A	16-Nov-23 A	11-Jan-24	22-Jan-24	
ENG-MECH-1030-B	TDS - Tank T-5600 - Filtered Seawater Tank - IFC - DELETED	10d	37d	13-Nov-23 A	28-Dec-23 A	15-Dec-23	28-Dec-23	
ENG-MECH-1040-B	TDS - Tank T-5800 - Fresh Water Tank - IFC - DELETED	10d	37d	13-Nov-23 A	28-Dec-23 A	15-Dec-23	28-Dec-23	

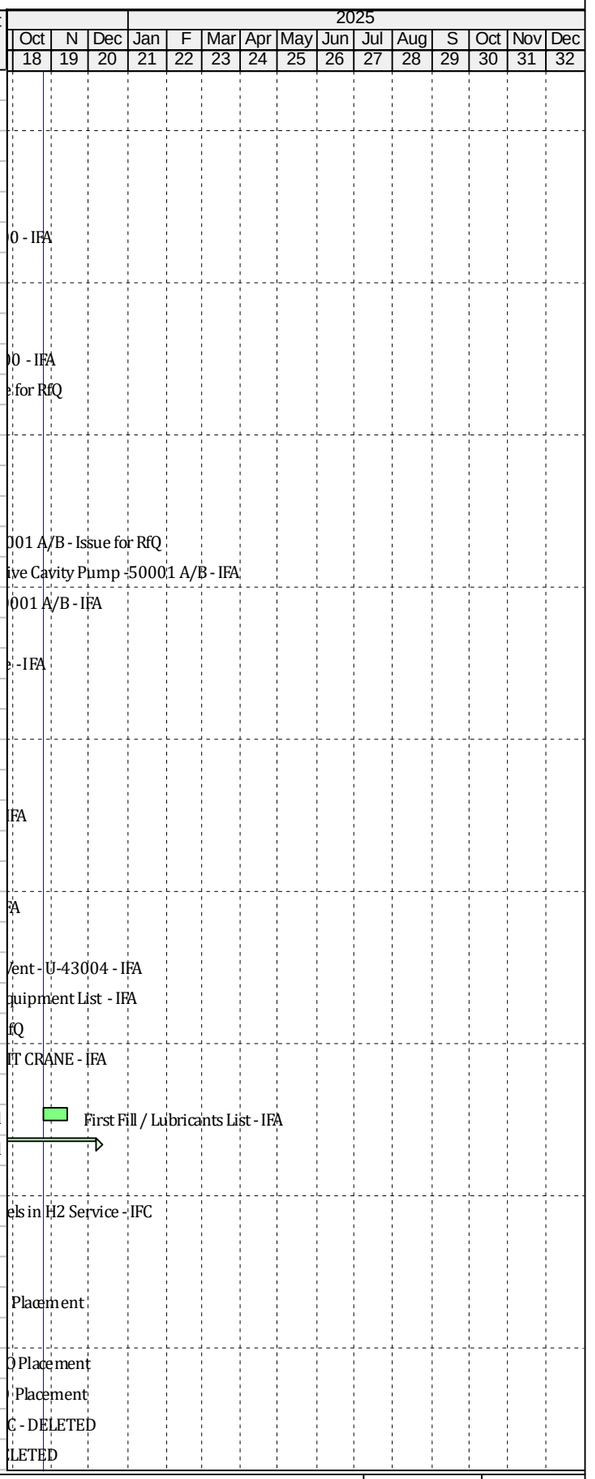

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-MECH-1070-B	Technical Specification for Tank CS - IFC	10d	10d	13-Nov-23 A	23-Nov-23 A	13-Nov-23	23-Nov-23	
ENG-MECH-1100-B	TDS - Tank T-63001 - Instrument Air Receiver - IFC - deleted	10d	10d	13-Nov-23 A	23-Nov-23 A	13-Nov-23	23-Nov-23	
ENG-MECH-1310-B	Technical Specification for Instrument Air Package - A-63000 - IFC	10d	276d	16-Nov-23 A	14-Oct-24 A	06-Nov-23	16-Nov-23	
ENG-MECH-1080-B	TDS - Tank T-5501 - Waste Water Tank - IFC - DELETED	10d	7d	23-Nov-23 A	30-Nov-23 A	20-Nov-23	30-Nov-23	
ENG-MECH-1020-B	Technical Specification for Tank GRP - IFC	10d	285d	29-Nov-23 A	07-Nov-24	15-Dec-23	28-Dec-23	45d
ENG-MECH-1090-B	TDS - Tank T-5XXX - N2 Receiver - IFC - deleted	10d	10d	29-Nov-23 A	11-Dec-23 A	29-Nov-23	11-Dec-23	
ENG-MECH-1400-B	TDS - Nitrogen Bottles rack -U-64000 - IFC - deleted	10d	10d	29-Nov-23 A	11-Dec-23 A	29-Nov-23	11-Dec-23	
ENG-MECH-1390-B	Technical Specification for Nitrogen Bottles rack -U-64000 - IFC	10d	101d	08-Dec-23 A	11-Apr-24 A	22-Nov-23	02-Dec-23	
ENG-MECH-1180-B	TDS - Fresh Water Pump - P-50009 A/B - IFC	10d	148d	13-Dec-23 A	12-Jun-24 A	16-Feb-24	27-Feb-24	
ENG-MECH-1190-B	TDS - Sea Water Coarse Filter Package - A-50003 - IFC	10d	148d	13-Dec-23 A	12-Jun-24 A	15-Jan-24	25-Jan-24	
ENG-MECH-1200-B	TDS - UV Water Filter - S-50010 - IFC	10d	148d	13-Dec-23 A	12-Jun-24 A	05-Jan-24	17-Jan-24	
ENG-MECH-1220-B	TDS - Desalination Unit (SWRO) - A-50008 - IFC	10d	157d	13-Dec-23 A	21-Jun-24 A	11-Jan-24	22-Jan-24	
ENG-MECH-1170-B	Technical Specification for Water Treatmement Package - IFC	10d	141d	18-Dec-23 A	07-Jun-24 A	08-Jan-24	18-Jan-24	
ENG-MECH-1210-B	TDS - Ultra Filtrartion Unit - - IFC	10d	147d	18-Dec-23 A	14-Jun-24 A	07-Dec-23	19-Dec-23	
ENG-MECH-1230-B	TDS - Electro-Chlorination Unit - A-50002 - IFC	10d	153d	18-Dec-23 A	21-Jun-24 A	12-Dec-23	22-Dec-23	
ENG-MECH-1280-B	TDS - Hydrogen Vent KO Drum - V-43001 - IFC	10d	139d	20-Dec-23 A	07-Jun-24 A	25-Jan-24	05-Feb-24	
ENG-MECH-1350-B	TDS - Davit Crane - IFC - DELETED	10d	10d	10-Jan-24 A	20-Jan-24 A	10-Jan-24	20-Jan-24	
ENG-MECH-1360-B	TDS - DAVIT CRANE - IFC - DELETED	10d	10d	10-Jan-24 A	20-Jan-24 A	10-Jan-24	20-Jan-24	
ENG-MECH-1420-B	MR - Hydrogen Vent - U-43004 - Issue for PO Placement	10d	41d	11-Mar-24 A	30-Apr-24 A	10-Nov-23	21-Nov-23	
ENG-MECH-1430-B	Technical Specification for Hydrogen Vent - U-43004 - IFC	10d	65d	11-Mar-24 A	29-May-24 A	28-Oct-23	09-Nov-23	
ENG-MECH-1440-B	TDS - Hydrogen Vent - U-43004 - IFC	10d	65d	11-Mar-24 A	29-May-24 A	28-Oct-23	09-Nov-23	
ENG-MECH-1120-B	MR - Progressive Cavity Pump -50001 A/B - Issue for PO Placement	10d	34d	26-Mar-24 A	08-May-24 A	09-Dec-23	20-Dec-23	
ENG-MECH-1130-B	Technical Specification for Progressive Cavity Pump -50001 A/B - IFC	10d	64d	26-Mar-24 A	12-Jun-24 A	27-Nov-23	07-Dec-23	
ENG-MECH-1140-B	TDS - Progressive Cavity Pump -50001 A/B - IFC	10d	54d	26-Mar-24 A	31-May-24 A	27-Nov-23	07-Dec-23	
ENG-MECH-1330-B	MR - DAVIT CRANE - Issue for PO Placement	10d	58d	17-Apr-24 A	26-Jun-24 A	25-Jan-24	05-Feb-24	
ENG-MECH-1340-B	Technical Specification for DAVIT CRANE - IFC	10d	60d	17-Apr-24 A	27-Jun-24 A	10-Jan-24	20-Jan-24	
ENG-MECH-1000-B	Master Equipment List - IFC	10d	74d	12-Aug-24 A	07-Nov-24	14-Nov-23	24-Nov-23	59d
ENG-MECH-1460-B	First Fill / Lubricants List - IFC	10d	10d	26-Nov-24	06-Dec-24	01-Dec-23	13-Dec-23	44d
Issue For Information		243d	204d	12-Sep-23 A	17-May-24 A	12-Sep-23	13-Feb-24	
ENG-MECH-1290-A	TBE - H2 Service Storage Vessel - IFI	10d	33d	12-Sep-23 A	19-Oct-23 A	12-Sep-23	22-Sep-23	
ENG-MECH-1110-A	TBE - Tank CS - IFI - DELETED	15d	15d	04-Nov-23 A	21-Nov-23 A	04-Nov-23	21-Nov-23	
ENG-MECH-1320-A	TBE - Instrument Air Package A-63000 - IFI	15d	55d	01-Dec-23 A	08-Feb-24 A	27-Oct-23	14-Nov-23	
ENG-MECH-1050-A	TBE - Tank GRP - IFI	15d	15d	04-Dec-23 A	21-Dec-23 A	02-Dec-23	20-Dec-23	
ENG-MECH-1150-A	TBE - Progressive Cavity Pump -50001 A/B - IFI	15d	127d	04-Dec-23 A	09-May-24 A	18-Nov-23	05-Dec-23	
ENG-MECH-1240-A	TBE - Progressive Water Treatmement Package - IFI	15d	72d	04-Dec-23 A	01-Mar-24 A	28-Nov-23	15-Dec-23	
ENG-MECH-1410-A	TBE - Nitrogen Bottles rack -U-64000 - IFI	15d	53d	04-Dec-23 A	08-Feb-24 A	14-Nov-23	30-Nov-23	
ENG-MECH-1450-A	TBE - Hydrogen Vent - U-43004 - IFI	15d	38d	04-Mar-24 A	18-Apr-24 A	02-Nov-23	18-Nov-23	
ENG-MECH-1370-A	TBE - DAVIT CRANE - IFI	15d	27d	15-Apr-24 A	17-May-24 A	27-Jan-24	13-Feb-24	
Electrical Engineering		461d	461d	10-Jul-23 A	16-Jan-25	10-Jul-23	07-Aug-24	239d
ENGEIT1030	ELECTRICAL CALCUAITIONS & STUDY ANALYSIS	180d	368d	10-Aug-23 A	26-Oct-24	26-Sep-23	03-May-24	305d
ENGEIT1050	ELECTRICAL TECHNICAL BID EVALUATION	185d	177d	17-Aug-23 A	16-Mar-24 A	16-Aug-23	25-Mar-24	
ENGEIT1040	ELECTRICAL MR / SPECIFICATION / DATA SHEETS	162d	340d	13-Sep-23 A	26-Oct-24	23-Aug-23	05-Mar-24	305d
ENGEIT1020	ELECTRICAL PHILOSPOHIES (IFR, IFA, IFC)	133d	323d	03-Oct-23 A	26-Oct-24	14-Sep-23	22-Feb-24	305d
ENGEIT1060	OVERALL KEY SINGLE LINE DIAGRAM (SLD)	132d	312d	16-Oct-23 A	26-Oct-24	16-Oct-23	08-Apr-24	305d
ENGEIT1080	ELECTRICAL LAYOUTS & CABLE ROUTING LAYOUTS (IFR, IFA, IFC)	174d	318d	20-Oct-23 A	07-Nov-24	09-Oct-23	09-May-24	54d
ENGEIT1110	ELECTRICAL SCHEDULES (IFR, IFA, IFC)	114d	226d	31-Oct-23 A	31-Jul-24 A	07-Oct-23	03-Apr-24	

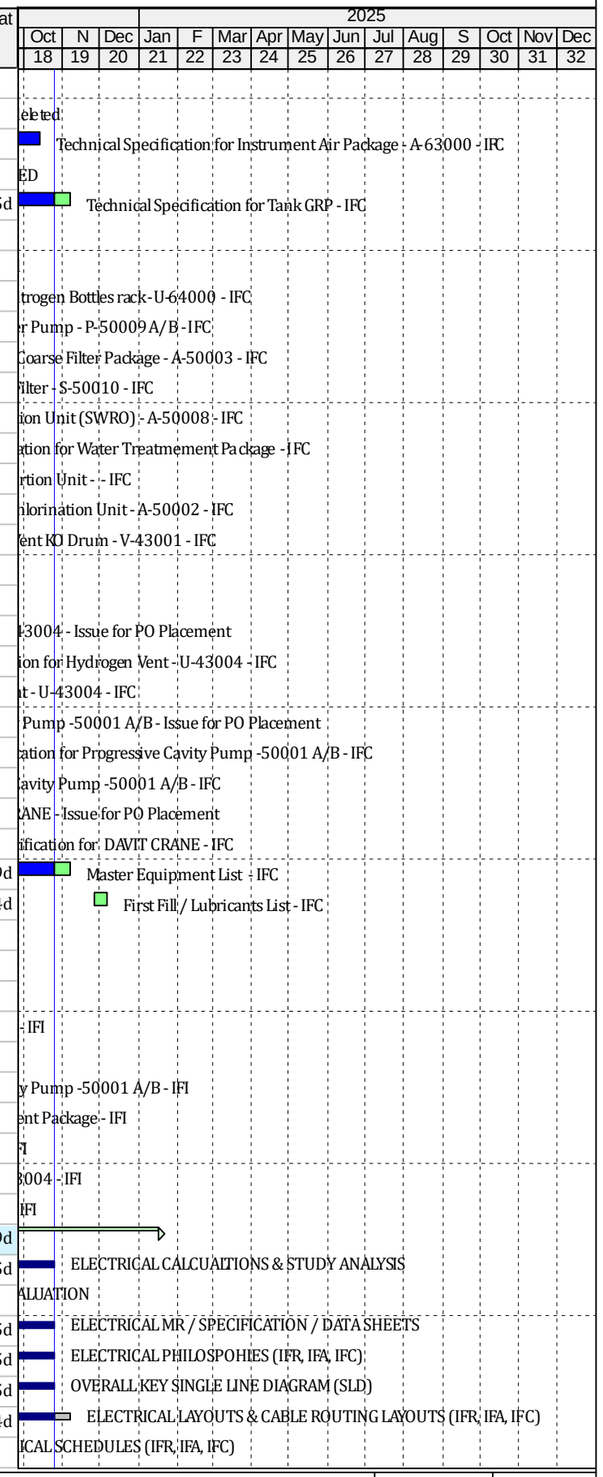

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

CROSSWIND


HOLLANDSE KUST NOORD WIND PARK Project

BASE LOAD POWER HUB

Contract No. CW-I-WP4-2023-05

ROSETTI MARINO

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENGEIT1070	ELECTRICAL DIAGRAMS (IFR, IFA, IFC)	192d	295d	06-Nov-23 A	26-Oct-24	26-Sep-23	01-Jun-24	305d
ENGEIT1090	ELECTRICAL I/O INTERFACE (IFR, IFA, IFC)	71d	118d	15-Nov-23 A	08-Apr-24 A	15-Nov-23	08-Apr-24	
ENGEIT1100	ELECTRICAL BULK MTOs	97d	52d	23-Jan-24 A	22-Mar-24 A	28-Dec-23	15-Apr-24	
ENG-ELE-1000	CPI Load List - Input Frozen	0d	0d	26-Oct-24*		06-Oct-23		14d
ENG-ELE-1010	CPI SOLAR FARM - Input Frozen	0d	0d	26-Oct-24*		15-Nov-23		14d
Issue For Approval		416d	416d	10-Jul-23 A	20-Nov-24	10-Jul-23	02-Aug-24	208d
ENG-ELE-2730-A	Utility data (electrical) schedule - IFA - to be deleted	10d	10d	10-Jul-23 A	20-Jul-23 A	10-Jul-23	20-Jul-23	
ENG-ELE-1430-A	Electrical Load List & Balance (CCS MODE 'CHARGING') - IFA	20d	11d	10-Aug-23 A	23-Aug-23 A	10-Oct-23	02-Nov-23	
ENG-ELE-1880-A	MR - for Power Transformers - Issue for RfQ	10d	11d	10-Aug-23 A	23-Aug-23 A	19-Sep-23	29-Sep-23	
ENG-ELE-1890-A	Technical Specification, IDS and DDS for Power Transformers - IFA	10d	11d	10-Aug-23 A	23-Aug-23 A	01-Sep-23	12-Sep-23	
ENG-ELE-1900-A	TDS - 66/6.9 kV Power Transformers - IFA	20d	11d	10-Aug-23 A	23-Aug-23 A	01-Sep-23	23-Sep-23	
ENG-ELE-1910-A	TDS - 6.6/0.42 kV Power Transformers - IFA	20d	12d	10-Aug-23 A	24-Aug-23 A	01-Sep-23	23-Sep-23	
ENG-ELE-1920-A	TDS - 6.6/0.8 kV Power Transformers - IFA	20d	11d	10-Aug-23 A	23-Aug-23 A	01-Sep-23	23-Sep-23	
ENG-ELE-1940-A	MR - for Neutral Earthing Resistor (NER) - Issue for RfQ	10d	15d	10-Aug-23 A	28-Aug-23 A	27-Sep-23	07-Oct-23	
ENG-ELE-1950-A	Technical Specification, IDS and DDS for Neutral Earthing Resistor (NER) - IFA	20d	15d	10-Aug-23 A	28-Aug-23 A	09-Sep-23	02-Oct-23	
ENG-ELE-1960-A	TDS - Neutral Earthing Resistor (NER) - IFA	20d	15d	10-Aug-23 A	28-Aug-23 A	09-Sep-23	02-Oct-23	
ENG-ELE-1980-A	MR - for 66kV Switchgears (GIS) - Issue for RfQ	10d	11d	10-Aug-23 A	23-Aug-23 A	21-Jul-23	01-Aug-23	
ENG-ELE-1990-A	Technical Specification, IDS and DDS for 66kV Switchgear (GIS) - IFA	10d	12d	10-Aug-23 A	24-Aug-23 A	10-Jul-23	20-Jul-23	
ENG-ELE-2000-A	TDS - 66kV Switchgear (GIS) - IFA	10d	12d	10-Aug-23 A	24-Aug-23 A	10-Jul-23	20-Jul-23	
ENG-ELE-2030-A	Technical Specification, IDS and DDS for 6.6kV Switchgear - IFA - ABB INPUT	29d	43d	14-Sep-23 A	03-Nov-23 A	14-Sep-23	17-Oct-23	
ENG-ELE-2070-A	Technical Specification, IDS and DDS for LV Switchgear - IFA - ABB INPUT	29d	43d	14-Sep-23 A	03-Nov-23 A	14-Sep-23	17-Oct-23	
ENG-ELE-1740-A	Electrical System Study Report - Short Circuit - IFA - ABB INPUT	12d	28d	26-Sep-23 A	27-Oct-23 A	26-Sep-23	09-Oct-23	
ENG-ELE-1750-A	Electrical System Study Report - Arc Flash Energy Calculation - IFA - ABB INPUT	13d	34d	02-Oct-23 A	10-Nov-23 A	02-Oct-23	16-Oct-23	
ENG-ELE-2040-A	TDS - 6.6kV Switchgear - IFA - ABB INPUT	29d	27d	03-Oct-23 A	03-Nov-23 A	14-Sep-23	17-Oct-23	
ENG-ELE-2080-A	TDS - LV Switchgear - IFA - ABB INPUT	25d	26d	03-Oct-23 A	02-Nov-23 A	14-Sep-23	12-Oct-23	
ENG-ELE-2230-A	Technical Specification, IDS and DDS for Electrical Monitoring and Control System (EMCS) - IFA	10d	41d	03-Oct-23 A	20-Nov-23 A	17-Oct-23	27-Oct-23	
ENG-ELE-2150-A	Technical Specification, IDS and DDS for AC UPS Systems - IFA	10d	15d	06-Oct-23 A	23-Oct-23 A	06-Oct-23	17-Oct-23	
ENG-ELE-2160-A	TDS - AC UPS Systems - IFA	10d	15d	06-Oct-23 A	23-Oct-23 A	06-Oct-23	17-Oct-23	
ENG-ELE-2180-A	MR - for DC UPS System - Issue for RfQ	10d	15d	06-Oct-23 A	23-Oct-23 A	06-Oct-23	17-Oct-23	
ENG-ELE-2190-A	Technical Specification, IDS and DDS for DC UPS System - IFA	10d	15d	06-Oct-23 A	23-Oct-23 A	06-Oct-23	17-Oct-23	
ENG-ELE-2200-A	TDS - DC UPS System - IFA	10d	15d	06-Oct-23 A	23-Oct-23 A	06-Oct-23	17-Oct-23	
ENG-ELE-1440-A	Electrical Load List & Balance (CCS MODE 'HOT STANDBY') - IFA	20d	82d	09-Oct-23 A	18-Jan-24 A	10-Oct-23	02-Nov-23	
ENG-ELE-1450-A	Electrical Load List & Balance (CCS MODE 'DISCHARGING') - IFA	20d	82d	09-Oct-23 A	18-Jan-24 A	10-Oct-23	02-Nov-23	
ENG-ELE-1460-A	Electrical Load List & Balance (CCS MODE 'COLD STANDBY') - IFA	20d	82d	09-Oct-23 A	18-Jan-24 A	10-Oct-23	02-Nov-23	
ENG-ELE-1470-A	Electrical Load List & Balance (CCS MODE 'EMERGENCY MODE (Island)' - IFA	20d	82d	09-Oct-23 A	18-Jan-24 A	10-Oct-23	02-Nov-23	
ENG-ELE-1480-A	Electrical Load List & Balance (CCS MODE 'POWER OUT (Blackout)' - IFA	20d	82d	09-Oct-23 A	18-Jan-24 A	10-Oct-23	02-Nov-23	
ENG-ELE-1730-A	Electrical System Study Report - Load Flow - IFA - ABB INPUT	12d	14d	09-Oct-23 A	24-Oct-23 A	26-Sep-23	09-Oct-23	
ENG-ELE-2240-A	TDS - Electrical Monitoring and Control System (EMCS) - IFA	10d	28d	09-Oct-23 A	10-Nov-23 A	10-Oct-23	20-Oct-23	
ENG-ELE-1510-A	Cable Sizing Calculation Criteria - IFA - ABB INPUT - deleted	15d	15d	16-Oct-23 A	02-Nov-23 A	16-Oct-23	02-Nov-23	
ENG-ELE-1590-A	Overall/Key Single Line Diagram - IFA - ABB INPUT	15d	16d	16-Oct-23 A	03-Nov-23 A	16-Oct-23	02-Nov-23	
ENG-ELE-2020-A	MR - for 6.6kV Switchgears - Issue for RfQ - deleted	10d	10d	18-Oct-23 A	28-Oct-23 A	18-Oct-23	28-Oct-23	
ENG-ELE-1040-A	Electrical Equipment Layout - HV & MV Switchroom - IFA - ABB INPUT	20d	22d	20-Oct-23 A	15-Nov-23 A	09-Oct-23	31-Oct-23	
ENG-ELE-1520-A	Cable Sizing Calculation Report (including end of line minimum fault current clearance verification) - IFA - ABB	15d	4d	20-Oct-23 A	24-Oct-23 A	16-Oct-23	02-Nov-23	
ENG-ELE-1760-A	Electrical System Study Report - Harmonics - IFA - ABB INPUT - DELETED	13d	1d	20-Oct-23 A	20-Oct-23 A	02-Oct-23	16-Oct-23	
ENG-ELE-2140-A	MR - for AC UPS Systems - Issue for RfQ	10d	3d	20-Oct-23 A	23-Oct-23 A	21-Oct-23	02-Nov-23	
ENG-ELE-2220-A	MR - for Electrical Monitoring and Control System (EMCS) - Issue for RfQ - to be deleted	10d	10d	21-Oct-23 A	02-Nov-23 A	21-Oct-23	02-Nov-23	

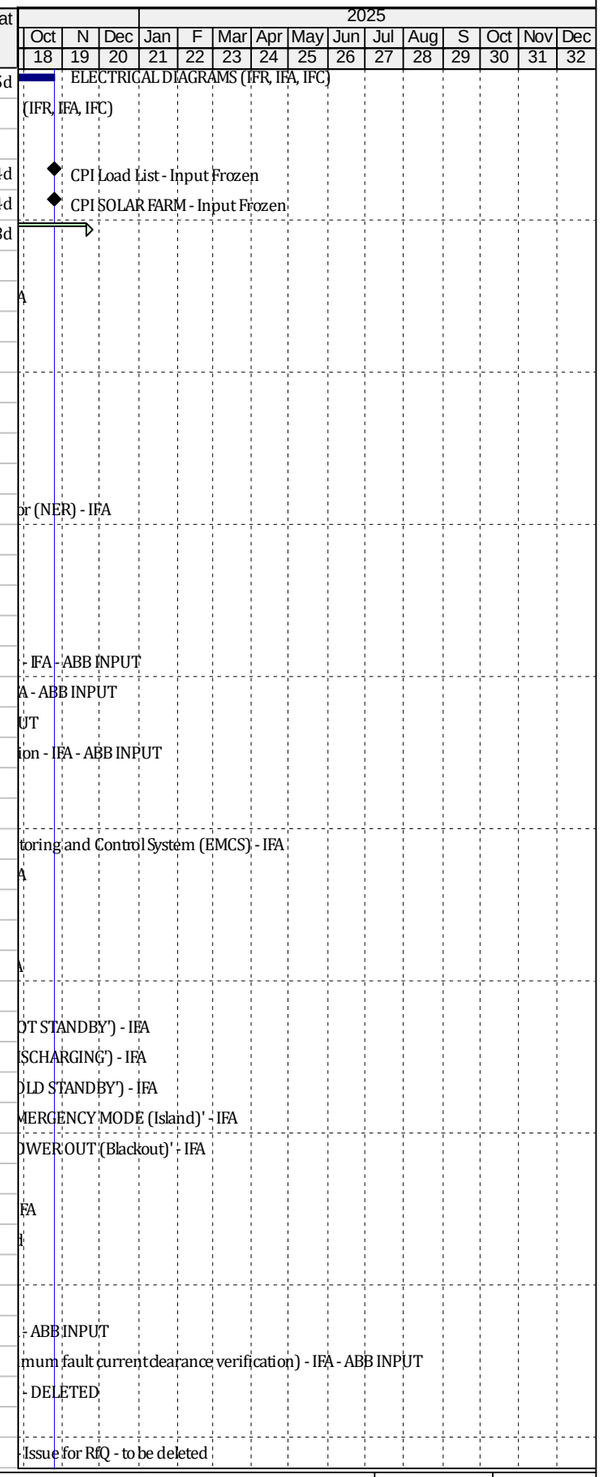

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Data Date: 25-Oct-24

CROSSWIND BLPH EPCI

Level 4 Project Baseline Schedule


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ELE-1050-A	Electrical Equipment Layout - LV Switchroom - IFA - ABB INPUT	15d	16d	23-Oct-23 A	10-Nov-23 A	14-Oct-23	31-Oct-23	
ENG-ELE-1410-A	Electrical System Description & Design Philosophy (Electrical Design Basis) - IFA	78d	187d	23-Oct-23 A	07-Jun-24 A	14-Sep-23	15-Dec-23	
ENG-ELE-2680-A	Electrical Typical Installation Details - Earthing System - IFA	15d	25d	23-Oct-23 A	21-Nov-23 A	07-Oct-23	24-Oct-23	
ENG-ELE-2690-A	Electrical Typical Installation Details - Lighting System - IFA	15d	25d	23-Oct-23 A	21-Nov-23 A	07-Oct-23	24-Oct-23	
ENG-ELE-2700-A	Electrical Typical Installation Details - Power System - IFA	15d	25d	23-Oct-23 A	21-Nov-23 A	07-Oct-23	24-Oct-23	
ENG-ELE-2710-A	Electrical Typical Installation Details - Cable Routes System - IFA	15d	25d	23-Oct-23 A	21-Nov-23 A	07-Oct-23	24-Oct-23	
ENG-ELE-1000-A	Electrical Equipment Layout - Top Deck - IFA	20d	174d	31-Oct-23 A	31-May-24 A	02-Nov-23	24-Nov-23	
ENG-ELE-1010-A	Electrical Equipment Layout - Lower Deck - IFA	20d	106d	31-Oct-23 A	08-Mar-24 A	02-Nov-23	24-Nov-23	
ENG-ELE-1020-A	Electrical Equipment Layout - Stair Towers - IFA	15d	174d	31-Oct-23 A	31-May-24 A	02-Nov-23	18-Nov-23	
ENG-ELE-1030-A	Electrical Equipment Layout - Relief Valve Platform - IFA - DELETED	15d	16d	31-Oct-23 A	18-Nov-23 A	02-Nov-23	18-Nov-23	
ENG-ELE-1060-A	Electrical Equipment Layout - UPSs & Batteries Switchroom - IFA	15d	138d	31-Oct-23 A	17-Apr-24 A	02-Nov-23	18-Nov-23	
ENG-ELE-1670-A	Electrical Schedules (Switchgears) - IFA - ABB INPUT	12d	73d	31-Oct-23 A	30-Jan-24 A	07-Oct-23	20-Oct-23	
ENG-ELE-1820-A	Technical Specification for LV Motors - IFA	10d	18d	31-Oct-23 A	21-Nov-23 A	02-Oct-23	12-Oct-23	
ENG-ELE-1830-A	Technical Specification, IDS and DDS for Electrical Requirement in Packaged Units - IFA	10d	41d	31-Oct-23 A	19-Dec-23 A	02-Oct-23	12-Oct-23	
ENG-ELE-1000 - ABB	Documents not yet foreseen in MDR for ABB scope of work	228d	305d	31-Oct-23 A	02-Nov-24	31-Oct-23	02-Aug-24	42d
ENG-ELE-2110-A	Technical Specification, IDS and DDS for LV Distribution Boards - IFA - DELETED	10d	10d	04-Nov-23 A	15-Nov-23 A	04-Nov-23	15-Nov-23	
ENG-ELE-1610-A	Electrical Single Line Diagrams LV System - IFA - ABB INPUT	10d	69d	06-Nov-23 A	30-Jan-24 A	10-Oct-23	20-Oct-23	
ENG-ELE-1650-A	Electrical Control, Protection and Metering Diagrams - IFA - ABB INPUT	20d	54d	06-Nov-23 A	12-Jan-24 A	10-Oct-23	02-Nov-23	
ENG-ELE-1660-A	Electrical Typical Schematic Diagrams (Distribution Boards, AC UPS, DC UPS, etc) - IFA	15d	182d	06-Nov-23 A	14-Jun-24 A	07-Oct-23	24-Oct-23	
ENG-ELE-2250-A	Block Diagram (ECMS) - IFA	12d	9d	06-Nov-23 A	15-Nov-23 A	26-Sep-23	09-Oct-23	
ENG-ELE-1490-A	Electrical Power & Control Cable Schedule (as per Rosetti Marino template) - IFA	17d	108d	11-Nov-23 A	21-Mar-24 A	03-Nov-23	20-Nov-23	
ENG-ELE-1600-A	Electrical Single Line Diagram HV & MV Systems - IFA - ABB INPUT	10d	19d	13-Nov-23 A	04-Dec-23 A	10-Oct-23	20-Oct-23	
ENG-ELE-1690-A	Electrical Protection Philosophy - IFA - ABB INPUT	17d	48d	13-Nov-23 A	12-Jan-24 A	07-Oct-23	26-Oct-23	
ENG-ELE-1420-A	Electrical Equipment List - IFA - ABB INPUT	27d	57d	14-Nov-23 A	24-Jan-24 A	14-Nov-23	15-Dec-23	
ENG-ELE-1580-A	Electrical I/O Signal List - IFA - ABB INPUT - deleted	10d	10d	15-Nov-23 A	25-Nov-23 A	15-Nov-23	25-Nov-23	
ENG-ELE-1210-A	Lighting & Socket Layout - Relief Valve Platform - IFA - DELETED	20d	20d	20-Nov-23 A	13-Dec-23 A	20-Nov-23	13-Dec-23	
ENG-ELE-1540-A	Lighting Calculation Study Report - IFA	15d	52d	20-Nov-23 A	24-Jan-24 A	02-Nov-23	18-Nov-23	
ENG-ELE-1840-A	MR - for Navigation Aid System - Issue for RfQ	10d	66d	20-Nov-23 A	09-Feb-24 A	22-Nov-23	02-Dec-23	
ENG-ELE-1850-A	Technical Specification, IDS and DDS for Navigation Aid System - IFA	10d	52d	20-Nov-23 A	24-Jan-24 A	04-Nov-23	15-Nov-23	
ENG-ELE-1860-A	TDS - Navigation Aid System - IFA	15d	52d	20-Nov-23 A	24-Jan-24 A	04-Nov-23	21-Nov-23	
ENG-ELE-2100-A	MR - for LV Distribution Boards - Issue for RfQ - DELETED	10d	10d	22-Nov-23 A	02-Dec-23 A	22-Nov-23	02-Dec-23	
ENG-ELE-2340-A	MR - for Solar Farm - In-Feed Power Isolator Panel - Issue for RfQ - DELETED	10d	10d	27-Nov-23 A	07-Dec-23 A	27-Nov-23	07-Dec-23	
ENG-ELE-1770-A	Electrical System Study Report - Vital Supply Recovery - IFA - ABB INPUT	27d	148d	30-Nov-23 A	30-May-24 A	23-Oct-23	23-Nov-23	
ENG-ELE-1790-A	Electrical System Study Report - Transient In-Rush - IFA - ABB INPUT	27d	87d	30-Nov-23 A	15-Mar-24 A	23-Oct-23	23-Nov-23	
ENG-ELE-1800-A	Electromagnetic Compatibility Study - IFA - ABB INPUT	15d	87d	30-Nov-23 A	15-Mar-24 A	28-Nov-23	15-Dec-23	
ENG-ELE-1350-A	Earthing & Lightining Layout - Relief Valve Platform - IFA - DELETED	20d	20d	01-Dec-23 A	27-Dec-23 A	01-Dec-23	27-Dec-23	
ENG-ELE-1180-A	Lighting & Socket Layout - Top Deck - IFA	20d	146d	04-Dec-23 A	31-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1190-A	Lighting & Socket Layout - Lower Deck - IFA	20d	146d	04-Dec-23 A	31-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1200-A	Lighting & Socket Layout - Stair Towers - IFA	20d	164d	04-Dec-23 A	21-Jun-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1220-A	Lighting & Socket Layout - HV & MV Switchroom - IFA	20d	128d	04-Dec-23 A	10-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1230-A	Lighting & Socket Layout - LV Switchroom - IFA	20d	128d	04-Dec-23 A	10-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1240-A	Lighting & Socket Layout - UPSs & Batteries Switchroom - IFA	20d	128d	04-Dec-23 A	10-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1530-A	Electrical Equipment Sizing Calculation Report - IFA - ABB INPUT	13d	127d	04-Dec-23 A	09-May-24 A	02-Oct-23	16-Oct-23	
ENG-ELE-1550-A	Lightning Protection System Calculation Report - IFA	15d	54d	04-Dec-23 A	09-Feb-24 A	02-Nov-23	18-Nov-23	
ENG-ELE-1100-A	Electrical Cables Routing Layout - Relief Valve Platform - IFA - DELETED	10d	10d	16-Dec-23 A	29-Dec-23 A	16-Dec-23	29-Dec-23	
ENG-ELE-1700-A	Electrical Protection Relay Settings Criteria - IFA - ABB INPUT - DELETED	20d	20d	16-Dec-23 A	12-Jan-24 A	16-Dec-23	12-Jan-24	

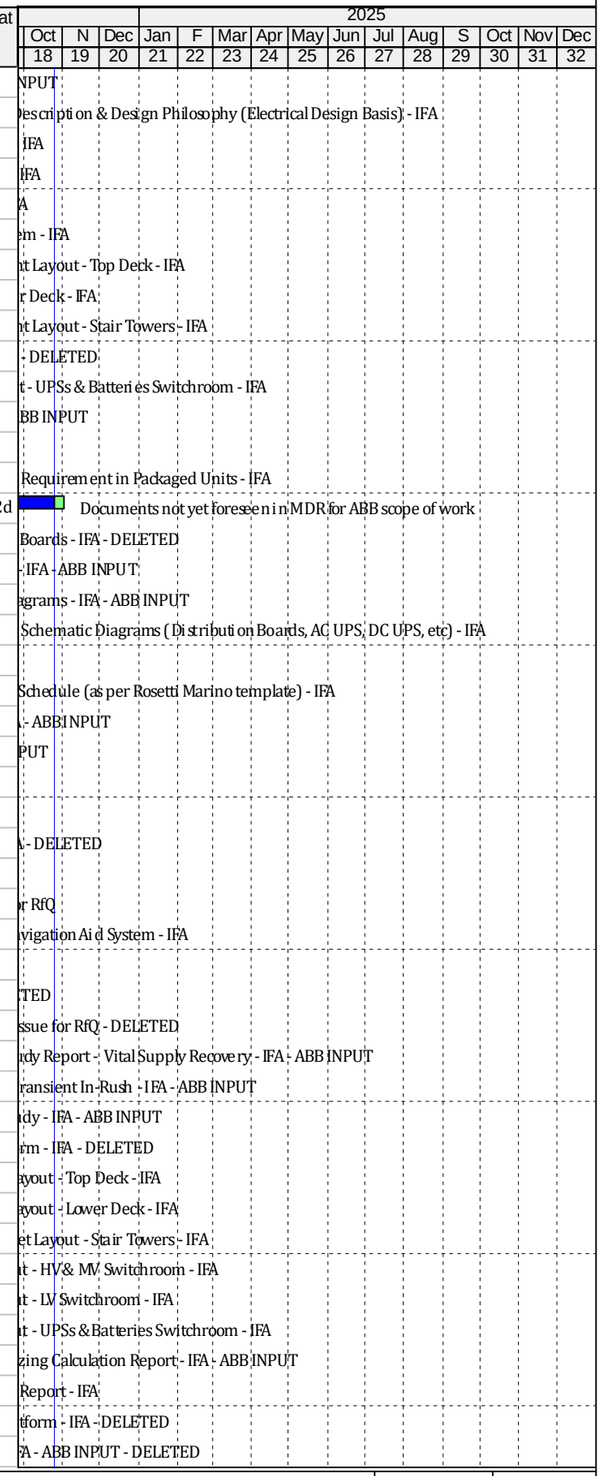


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ELE-1720-A	Electrical Protection Relay Setting Schedule - IFA- ABB INPUT - DELETED	17d	17d	16-Dec-23 A	09-Jan-24 A	16-Dec-23	09-Jan-24	
ENG-ELE-2120-A	TDS - LV Distribution Boards - IFA	15d	43d	18-Dec-23 A	09-Feb-24 A	04-Nov-23	21-Nov-23	
ENG-ELE-2350-A	TDS - Solar Farm - In-Feed Power Isolator Panel - IFA	10d	43d	18-Dec-23 A	09-Feb-24 A	15-Nov-23	25-Nov-23	
ENG-ELE-1170-A	Electrical MCT Composition Layout - ReliefValve Platform - IFA - DELETED	15d	15d	30-Dec-23 A	18-Jan-24 A	30-Dec-23	18-Jan-24	
ENG-ELE-1070-A	Electrical Cables Routing Layout - Top Deck - IFA	15d	139d	08-Jan-24 A	21-Jun-24 A	16-Dec-23	05-Jan-24	
ENG-ELE-1080-A	Electrical Cables Routing Layout - Lower Deck - IFA	20d	145d	08-Jan-24 A	28-Jun-24 A	16-Dec-23	12-Jan-24	
ENG-ELE-1090-A	Electrical Cables Routing Layout - Stair Towers - IFA	15d	157d	08-Jan-24 A	12-Jul-24 A	16-Dec-23	05-Jan-24	
ENG-ELE-1110-A	Electrical Cable Routing Layout - HV & MV Switchroom - IFA	15d	97d	08-Jan-24 A	03-May-24 A	16-Dec-23	05-Jan-24	
ENG-ELE-1120-A	Electrical Cable Routing Layout - LV Switchroom - IFA	15d	127d	08-Jan-24 A	07-Jun-24 A	16-Dec-23	05-Jan-24	
ENG-ELE-1130-A	Electrical Cable Routing Layout - UPSs & Batteries Switchroom - IFA	15d	115d	08-Jan-24 A	24-May-24 A	16-Dec-23	05-Jan-24	
ENG-ELE-1400-A	Electrical Heat Tracing (EHT) Layouts - IFA	20d	145d	08-Jan-24 A	28-Jun-24 A	02-Nov-23	24-Nov-23	
ENG-ELE-2420-A	TDS - Electrical Power and Control Cables - IFA	10d	64d	08-Jan-24 A	21-Mar-24 A	13-Jan-24	24-Jan-24	
ENG-ELE-2510-A	TDS - Control Stations, Junction Boxes and Sockets - IFA	10d	139d	08-Jan-24 A	21-Jun-24 A	14-Dec-23	27-Dec-23	
ENG-ELE-1810-A	SAFOP Close Out Report - IFA	13d	213d	13-Jan-24 A	23-Sep-24 A	13-Jan-24	24-Jan-24	
ENG-ELE-1560-A	UPS & Battery Sizing Calculations - IFA	10d	65d	19-Jan-24 A	05-Apr-24 A	22-Dec-23	05-Jan-24	
ENG-ELE-2060-A	MR - for LV Switchgears - Issue for RfQ	10d	1d	19-Jan-24 A	19-Jan-24 A	18-Oct-23	28-Oct-23	
ENG-ELE-2310-A	MR - for IAC Cable Extension - Interface JB + Solar PV Power cable JB - Issue for RfQ	10d	25d	19-Jan-24 A	16-Feb-24 A	27-Nov-23	07-Dec-23	
ENG-ELE-2320-A	TDS - IAC Cable Extension - Interface JB + Solar PV Power cable JB - IFA	10d	43d	19-Jan-24 A	08-Mar-24 A	15-Nov-23	25-Nov-23	
ENG-ELE-2410-A	Technical Specification, IDS and DDS for Electrical Cables - IFA	10d	55d	19-Jan-24 A	22-Mar-24 A	13-Jan-24	24-Jan-24	
ENG-ELE-1390-A	Navigation Aid System General Layouts - IFA	15d	17d	26-Jan-24 A	14-Feb-24 A	13-Jan-24	30-Jan-24	
ENG-ELE-1570-A	Electrical Control Alarm and Monitoring Table - IFA - ABB INPUT	21d	43d	26-Jan-24 A	15-Mar-24 A	21-Nov-23	15-Dec-23	
ENG-ELE-1640-A	Electrical Single Line Diagrams (Distribution Boards, AC UPS, DC UPS, etc.) - IFA	10d	37d	26-Jan-24 A	08-Mar-24 A	21-Oct-23	02-Nov-23	
ENG-ELE-1680-A	Electrical Schedules (Distribution Boards, AC UPS, DC UPS, etc.) - IFA	20d	48d	26-Jan-24 A	21-Mar-24 A	27-Oct-23	20-Nov-23	
ENG-ELE-2400-A	MR - for Electrical Power and Control Cables - Issue for RfQ	10d	31d	26-Jan-24 A	01-Mar-24 A	19-Jan-24	30-Jan-24	
ENG-ELE-1620-A	Electrical Single Line Diagrams AC UPS Systems - IFA	22d	19d	31-Jan-24 A	21-Feb-24 A	03-Nov-23	20-Nov-23	
ENG-ELE-1630-A	Electrical Single Line Diagrams DC UPS System - IFA	22d	13d	31-Jan-24 A	14-Feb-24 A	03-Nov-23	20-Nov-23	
ENG-ELE-2380-A	TDS - T-Connectors & HV/MV Terminations - IFA	10d	39d	31-Jan-24 A	15-Mar-24 A	31-Jan-24	10-Feb-24	
ENG-ELE-2470-A	MR - for Lighting Fixtures & Accessories - Issue for RfQ	10d	45d	31-Jan-24 A	22-Mar-24 A	14-Dec-23	27-Dec-23	
ENG-ELE-2480-A	TDS - Lighting Fixtures & Accessories - IFA	10d	75d	31-Jan-24 A	30-Apr-24 A	14-Dec-23	27-Dec-23	
ENG-ELE-2560-A	MR - for Conduits, Fittings & Accessories - Issue for RfQ	10d	33d	31-Jan-24 A	08-Mar-24 A	03-Feb-24	14-Feb-24	
ENG-ELE-2660-A	MTO - Electrical Power and Control Cables - IFA	10d	45d	31-Jan-24 A	22-Mar-24 A	25-Jan-24	05-Feb-24	
ENG-ELE-2280-A	Technical Specification, IDS and DDS for Electrical Heat Tracing (EHT) System - IFA	13d	59d	09-Feb-24 A	19-Apr-24 A	28-Dec-23	10-Jan-24	
ENG-ELE-2290-A	TDS - Electrical Heat Tracing (EHT) System - IFA	13d	59d	09-Feb-24 A	19-Apr-24 A	28-Dec-23	10-Jan-24	
ENG-ELE-1140-A	Electrical MCT Composition Layout - Top Deck - IFA	30d	62d	15-Feb-24 A	30-Apr-24 A	22-Dec-23	05-Jan-24	
ENG-ELE-1150-A	Electrical MCT Composition Layout - Lower Deck - IFA	15d	52d	15-Feb-24 A	17-Apr-24 A	13-Jan-24	30-Jan-24	
ENG-ELE-1160-A	Electrical MCT Composition Layout - Stair Towers - IFA	13d	52d	15-Feb-24 A	17-Apr-24 A	08-Jan-24	18-Jan-24	
ENG-ELE-1320-A	Earthing & Lightining Layout - Top Deck - IFA	13d	87d	15-Feb-24 A	30-May-24 A	01-Dec-23	19-Dec-23	
ENG-ELE-1330-A	Earthing & Lightining Layout - Lower Deck - IFA	14d	87d	15-Feb-24 A	30-May-24 A	25-Nov-23	13-Dec-23	
ENG-ELE-1340-A	Earthing & Lightining Layout - Stair Towers - IFA	12d	88d	15-Feb-24 A	31-May-24 A	01-Dec-23	27-Dec-23	
ENG-ELE-1360-A	Earthing & Lightining Layout - HV & MV Switchroom - IFA	49d	82d	15-Feb-24 A	24-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1370-A	Earthing & Lightining Layout - LV Switchroom - IFA	49d	82d	15-Feb-24 A	24-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-1380-A	Earthing & Lightining Layout - UPSs & Batteries Switchroom - IFA	19d	82d	15-Feb-24 A	24-May-24 A	20-Nov-23	13-Dec-23	
ENG-ELE-2370-A	MR - for T-Connectors & HV/MV Terminations - Issue for RfQ	10d	6d	15-Feb-24 A	21-Feb-24 A	12-Feb-24	22-Feb-24	
ENG-ELE-2450-A	TDS - Electrical Cables Trays & Accessories - IFA	10d	61d	15-Feb-24 A	29-Apr-24 A	23-Jan-24	02-Feb-24	
ENG-ELE-2500-A	MR - for Control Stations, Junction Boxes and Sockets - Issue for RfQ	10d	10d	20-Feb-24 A	01-Mar-24 A	14-Dec-23	27-Dec-23	
ENG-ELE-2530-A	MR - for Cables Glands, Fittings & Accessories - Issue for RfQ	10d	11d	26-Feb-24 A	08-Mar-24 A	25-Jan-24	05-Feb-24	

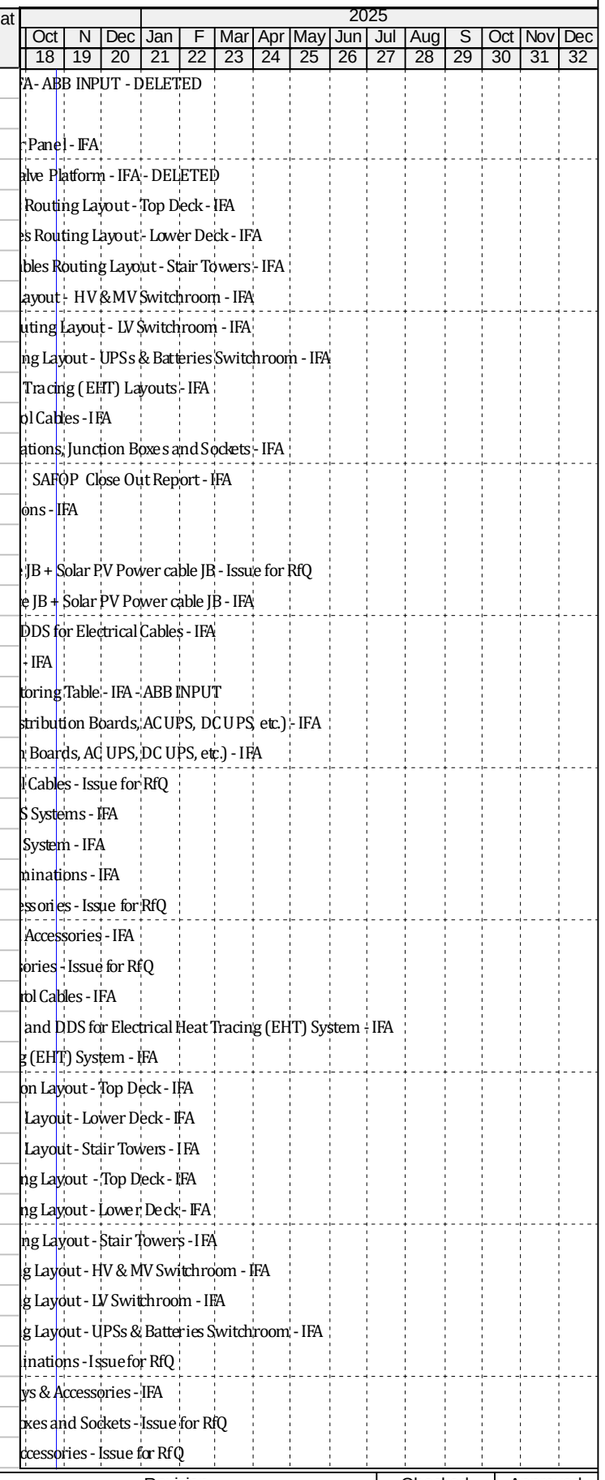

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ELE-2620-A	MR - for Electrical MCTs - Issue for RfQ	10d	11d	26-Feb-24 A	08-Mar-24 A	12-Feb-24	22-Feb-24	
ENG-ELE-2270-A	MR - for Electrical Heat Tracing (EHT) System - Issue for RfQ	10d	5d	11-Mar-24 A	15-Mar-24 A	11-Jan-24	22-Jan-24	
ENG-ELE-2440-A	MR - for Electrical Cables Trays & Accessories - Issue for RfQ	10d	5d	11-Mar-24 A	15-Mar-24 A	03-Feb-24	14-Feb-24	
ENG-ELE-2590-A	MR - for Earthing and Lightning Materials - Issue for RfQ	10d	5d	11-Mar-24 A	15-Mar-24 A	28-Dec-23	10-Jan-24	
ENG-ELE-2600-A	TDS - Earthing and Lightning Materials - IFA	10d	92d	02-Apr-24 A	19-Jul-24 A	28-Dec-23	10-Jan-24	
ENG-ELE-2630-A	TDS - Electrical MCTs - IFA	10d	23d	02-Apr-24 A	29-Apr-24 A	31-Jan-24	10-Feb-24	
ENG-ELE-1250-A	Lighting & Socket Circuit Diagram - Top Deck - IFA	15d	45d	15-Apr-24 A	07-Jun-24 A	15-Apr-24	03-May-24	
ENG-ELE-1260-A	Lighting & Socket Circuit Diagram - Lower Deck - IFA - deleted	15d	15d	15-Apr-24 A	03-May-24 A	15-Apr-24	03-May-24	
ENG-ELE-1270-A	Lighting & Socket Circuit Diagram - Stair Towers - IFA - deleted	15d	15d	15-Apr-24 A	03-May-24 A	15-Apr-24	03-May-24	
ENG-ELE-1280-A	Lighting & Socket Circuit Diagram - Relief Valve Platform - IFA - deleted	15d	15d	15-Apr-24 A	03-May-24 A	15-Apr-24	03-May-24	
ENG-ELE-1290-A	Lighting & Socket Circuit Diagram - HV & MV Switchroom - IFA - DELETED	15d	15d	15-Apr-24 A	03-May-24 A	15-Apr-24	03-May-24	
ENG-ELE-1300-A	Lighting & Socket Circuit Diagram - LV Switchroom - IFA DELETED	15d	15d	15-Apr-24 A	03-May-24 A	15-Apr-24	03-May-24	
ENG-ELE-1310-A	Lighting & Socket Circuit Diagram - UPSs & Batteries Switchroom - IFA DELETED	15d	15d	15-Apr-24 A	03-May-24 A	15-Apr-24	03-May-24	
ENG-ELE-1780-A	Electrical System Study Report - Power Factor Compensation - IFA - ABB INPUT	27d	6d	03-May-24 A	09-May-24 A	23-Oct-23	23-Nov-23	
ENG-ELE-2650-A	MTO - Electrical Bulk, Power, Lighting, Earthing Materials - IFA - ISSUED AS IFI	10d	102d	10-May-24 A	06-Sep-24 A	28-Dec-23	10-Jan-24	
ENG-ELE-1710-A	Electrical Protection Relay Selectivity Study Report - IFA - ABB INPUT	19d	22d	01-Jun-24 A	26-Jun-24 A	15-Nov-23	09-Dec-23	
ENG-ELE-1500-A	Electrical Interconnecting Wiring Diagram - IFA	20d	29d	10-Jun-24 A	12-Jul-24 A	08-Apr-24	02-May-24	
ENG-ELE-2540-A	TDS - Cables Glands, Fittings & Accessories - IFA	20d	138d	10-Jun-24 A	19-Nov-24	25-Jan-24	05-Feb-24	69d
ENG-ELE-2570-A	TDS - Conduits, Fittings & Accessories - IFA	29d	5d	08-Jul-24 A	12-Jul-24 A	23-Jan-24	02-Feb-24	
ENG-ELE-2720-A	Ex equipment register (in suitable format for import into the computerised maintenance management system	20d	20d	28-Oct-24	20-Nov-24	24-May-24	15-Jun-24	13d
Issue For Construction		424d	451d	21-Jul-23 A	16-Jan-25	02-Aug-23	07-Aug-24	163d
ENG-ELE-1980-B	MR - for 66kV Switchgears (GIS) - Issue for PO Placement	10d	28d	21-Jul-23 A	23-Aug-23 A	13-Sep-23	23-Sep-23	
ENG-ELE-2730-B	Utility data (electrical) schedule - IFC - to be deleted	10d	10d	02-Aug-23 A	12-Aug-23 A	02-Aug-23	12-Aug-23	
ENG-ELE-1880-B	MR - for Power Transformers - Issue for PO Placement	10d	11d	10-Aug-23 A	23-Aug-23 A	12-Oct-23	23-Oct-23	
ENG-ELE-1940-B	MR - for Neutral Earthing Resistor (NER) - Issue for PO Placement	10d	15d	10-Aug-23 A	28-Aug-23 A	26-Oct-23	07-Nov-23	
ENG-ELE-1430-B	Electrical Load List & Balance (CCS MODE 'CHARGING') - IFC	15d	239d	13-Sep-23 A	28-Jun-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1890-B	Technical Specification, IDS and DDS for Power Transformers - IFC	10d	191d	13-Sep-23 A	03-May-24 A	25-Sep-23	05-Oct-23	
ENG-ELE-1900-B	TDS - 66/6.9 kV Power Transformers - IFC	10d	189d	13-Sep-23 A	30-Apr-24 A	06-Oct-23	17-Oct-23	
ENG-ELE-1910-B	TDS - 6.6/0.42 kV Power Transformers - IFC	10d	189d	13-Sep-23 A	30-Apr-24 A	06-Oct-23	17-Oct-23	
ENG-ELE-1920-B	TDS - 6.6/0.8 kV Power Transformers - IFC	10d	189d	13-Sep-23 A	30-Apr-24 A	18-Oct-23	28-Oct-23	
ENG-ELE-1950-B	Technical Specification, IDS and DDS for Neutral Earthing Resistor (NER) - IFC	10d	203d	13-Sep-23 A	17-May-24 A	14-Oct-23	25-Oct-23	
ENG-ELE-1960-B	TDS - Neutral Earthing Resistor (NER) - IFC	10d	174d	13-Sep-23 A	11-Apr-24 A	14-Oct-23	25-Oct-23	
ENG-ELE-1990-B	Technical Specification, IDS and DDS for 66kV Switchgear (GIS) - IFC	10d	221d	13-Sep-23 A	07-Jun-24 A	23-Aug-23	02-Sep-23	
ENG-ELE-2000-B	TDS - 66kV Switchgear (GIS) - IFC	10d	221d	13-Sep-23 A	07-Jun-24 A	23-Aug-23	02-Sep-23	
ENG-ELE-2180-B	MR - for DC UPS System - Issue for PO Placement	10d	15d	06-Oct-23 A	23-Oct-23 A	30-Oct-23	10-Nov-23	
ENG-ELE-2140-B	MR - for AC UPS Systems - Issue for PO Placement	10d	3d	20-Oct-23 A	23-Oct-23 A	21-Mar-24	03-Apr-24	
ENG-ELE-2150-B	Technical Specification, IDS and DDS for AC UPS Systems - IFC - DELETED	10d	10d	30-Oct-23 A	10-Nov-23 A	30-Oct-23	10-Nov-23	
ENG-ELE-2240-B	TDS - Electrical Monitoring and Control System (EMCS) - IFC - DELETED	10d	10d	03-Nov-23 A	14-Nov-23 A	03-Nov-23	14-Nov-23	
ENG-ELE-1760-B	Electrical System Study Report - Harmonics - IFC - ABB INPUT - DELETED	15d	15d	04-Nov-23 A	21-Nov-23 A	04-Nov-23	21-Nov-23	
ENG-ELE-2230-B	Technical Specification, IDS and DDS for Electrical Monitoring and Control System (EMCS) - IFC - DELETED	10d	10d	10-Nov-23 A	21-Nov-23 A	10-Nov-23	21-Nov-23	
ENG-ELE-2250-B	Block Diagram (ECMS) - IFC - DELETED	15d	15d	16-Nov-23 A	02-Dec-23 A	16-Nov-23	02-Dec-23	
ENG-ELE-2020-B	MR - for 6.6kV Switchgears - Issue for PO Placement	24d	10d	17-Nov-23 A	28-Nov-23 A	17-Nov-23	28-Nov-23	
ENG-ELE-2060-B	MR - for LV Switchgears - Issue for PO Placement	10d	10d	18-Nov-23 A	29-Nov-23 A	18-Nov-23	29-Nov-23	
ENG-ELE-1520-B	Cable Sizing Calculation Report (including end of line minimum fault current clearance verification) - IFC - ABB	15d	117d	27-Nov-23 A	18-Apr-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-2160-B	TDS - AC UPS Systems - IFC	10d	22d	27-Nov-23 A	22-Dec-23 A	30-Oct-23	10-Nov-23	
ENG-ELE-2190-B	Technical Specification, IDS and DDS for DC UPS System - IFC	10d	22d	27-Nov-23 A	22-Dec-23 A	30-Oct-23	10-Nov-23	

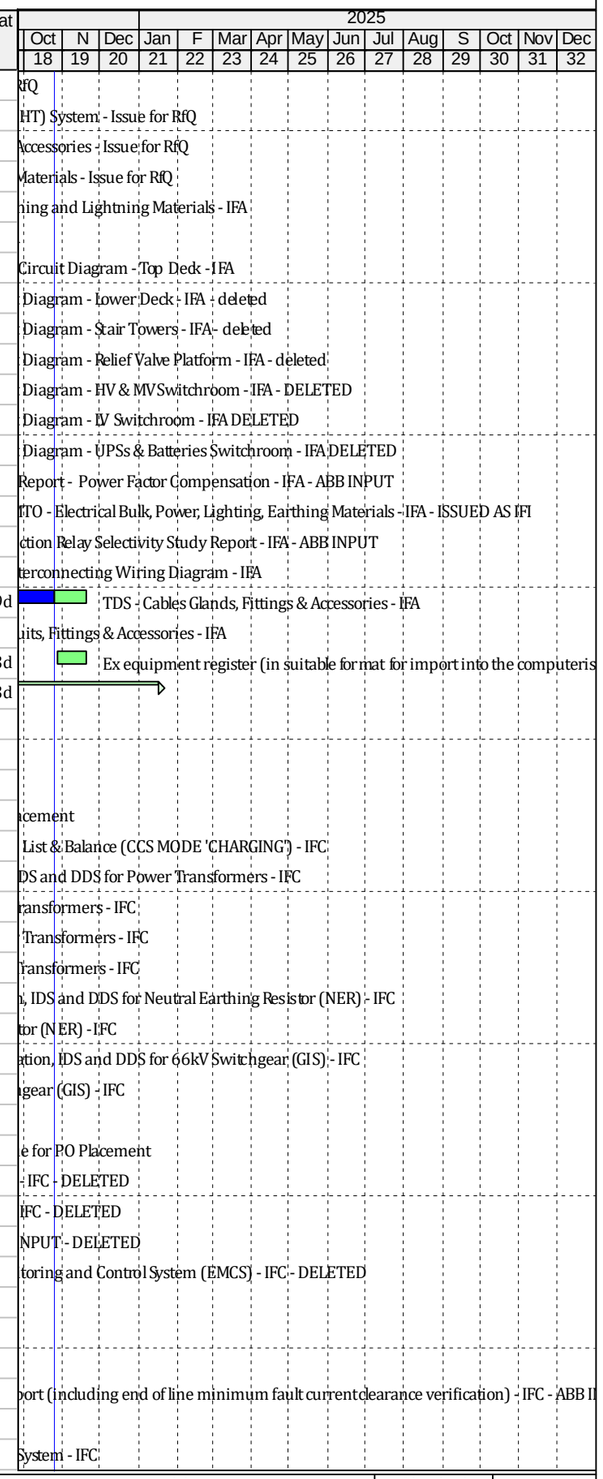

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ELE-2200-B	TDS - DC UPS System - IFC	10d	22d	27-Nov-23 A	22-Dec-23 A	30-Oct-23	10-Nov-23	
ENG-ELE-1590-B	Overall/Key Single Line Diagram - IFC - ABB INPUT	10d	216d	28-Nov-23 A	16-Aug-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-2110-B	Technical Specification, IDS and DDS for LV Distribution Boards - IFC - DELETED	10d	10d	30-Nov-23 A	12-Dec-23 A	30-Nov-23	12-Dec-23	
ENG-ELE-2220-B	MR - for Electrical Monitoring and Control System (EMCS) - Issue for PO Placement - to be deleted	10d	10d	04-Dec-23 A	15-Dec-23 A	04-Dec-23	15-Dec-23	
ENG-ELE-1730-B	Electrical System Study Report - Load Flow - IFC - ABB INPUT	15d	118d	08-Dec-23 A	03-May-24 A	27-Oct-23	14-Nov-23	
ENG-ELE-2080-B	TDS - LV Switchgear - IFC - ABB INPUT	15d	127d	08-Dec-23 A	14-May-24 A	31-Oct-23	17-Nov-23	
ENG-ELE-1040-B	Electrical Equipment Layout - HV & MV Switchroom - IFC - ABB INPUT	15d	139d	13-Dec-23 A	31-May-24 A	08-Mar-24	25-Mar-24	
ENG-ELE-1050-B	Electrical Equipment Layout - LV Switchroom - IFC - ABB INPUT	10d	139d	13-Dec-23 A	31-May-24 A	14-Mar-24	25-Mar-24	
ENG-ELE-1740-B	Electrical System Study Report - Short Circuit - IFC - ABB INPUT	15d	120d	13-Dec-23 A	09-May-24 A	27-Oct-23	14-Nov-23	
ENG-ELE-1750-B	Electrical System Study Report - Arc Flash Energy Calculation - IFC - ABB INPUT	15d	163d	13-Dec-23 A	28-Jun-24 A	04-Nov-23	21-Nov-23	
ENG-ELE-2040-B	TDS - 6.6kV Switchgear - IFC - ABB INPUT	15d	120d	13-Dec-23 A	09-May-24 A	30-Oct-23	16-Nov-23	
ENG-ELE-2100-B	MR - for LV Distribution Boards - Issue for PO Placement - DELETED	10d	10d	16-Dec-23 A	29-Dec-23 A	16-Dec-23	29-Dec-23	
ENG-ELE-2070-B	Technical Specification, IDS and DDS for LV Switchgear - IFC - ABB INPUT	10d	146d	19-Dec-23 A	14-Jun-24 A	30-Oct-23	10-Nov-23	
ENG-ELE-2340-B	MR - for Solar Farm - In-Feed Power Isolator Panel - Issue for PO Placement	10d	10d	21-Dec-23 A	04-Jan-24 A	21-Dec-23	04-Jan-24	
ENG-ELE-1600-B	Electrical Single Line Diagram HV & MV Systems - IFC - ABB INPUT	15d	88d	03-Jan-24 A	17-Apr-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1820-B	Technical Specification for LV Motors - IFC	20d	24d	03-Jan-24 A	31-Jan-24 A	25-Oct-23	17-Nov-23	
ENG-ELE-2680-B	Electrical Typical Installation Details - Earthing System - IFC	15d	133d	03-Jan-24 A	11-Jun-24 A	23-Feb-24	11-Mar-24	
ENG-ELE-2690-B	Electrical Typical Installation Details - Lighting System - IFC	15d	159d	03-Jan-24 A	11-Jul-24 A	23-Feb-24	11-Mar-24	
ENG-ELE-2700-B	Electrical Typical Installation Details - Power System - IFC	15d	159d	03-Jan-24 A	11-Jul-24 A	23-Feb-24	11-Mar-24	
ENG-ELE-2710-B	Electrical Typical Installation Details - Cable Routes System - IFC	15d	100d	03-Jan-24 A	03-May-24 A	23-Feb-24	11-Mar-24	
ENG-ELE-1830-B	Technical Specification, IDS and DDS for Electrical Requirement in Packaged Units - IFC	20d	17d	19-Jan-24 A	07-Feb-24 A	07-Nov-23	29-Nov-23	
ENG-ELE-2320-B	TDS - IAC Cable Extension - Interface JB + Solar PV Power cable JB - IFC	4d	163d	19-Jan-24 A	31-Jul-24 A	09-Dec-23	20-Dec-23	
ENG-ELE-2650-B	MTO - Electrical Bulk, Power, Lighting, Earthing Materials - IFC - ISSUED AS IFI	10d	10d	23-Jan-24 A	02-Feb-24 A	23-Jan-24	02-Feb-24	
ENG-ELE-1540-B	Lighting Calculation Study Report - IFC	10d	141d	26-Jan-24 A	12-Jul-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1720-B	Electrical Protection Relay Setting Schedule - IFC - ABB INPUT - DELETED	15d	15d	27-Jan-24 A	13-Feb-24 A	27-Jan-24	13-Feb-24	
ENG-ELE-1700-B	Electrical Protection Relay Settings Criteria - IFC - ABB INPUT - DELETED	15d	15d	31-Jan-24 A	16-Feb-24 A	31-Jan-24	16-Feb-24	
ENG-ELE-2030-B	Technical Specification, IDS and DDS for 6.6kV Switchgear - IFC - ABB INPUT	31d	82d	31-Jan-24 A	09-May-24 A	30-Oct-23	16-Nov-23	
ENG-ELE-1390-B	Navigation Aid System General Layouts - IFC	10d	94d	14-Feb-24 A	07-Jun-24 A	12-Feb-24	22-Feb-24	
ENG-ELE-1510-B	Cable Sizing Calculation Criteria - IFC - ABB INPUT - deleted	15d	15d	04-Mar-24 A	20-Mar-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1440-B	Electrical Load List & Balance (CCS MODE 'HOT STANDBY') - IFC	15d	93d	08-Mar-24 A	28-Jun-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1460-B	Electrical Load List & Balance (CCS MODE 'COLD STANDBY') - IFC	15d	93d	08-Mar-24 A	28-Jun-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1480-B	Electrical Load List & Balance (CCS MODE 'POWER OUT (Blackout)' - IFC	15d	93d	08-Mar-24 A	28-Jun-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1630-B	Electrical Single Line Diagrams DC UPS System - IFC	10d	33d	08-Mar-24 A	17-Apr-24 A	21-Mar-24	03-Apr-24	
ENG-ELE-1860-B	TDS - Navigation Aid System - IFC	25d	23d	08-Mar-24 A	05-Apr-24 A	04-Dec-23	21-Dec-23	
ENG-ELE-1420-B	Electrical Equipment List - IFC - ABB INPUT	15d	132d	11-Mar-24 A	16-Aug-24 A	08-Jan-24	24-Jan-24	
ENG-ELE-1450-B	Electrical Load List & Balance (CCS MODE 'DISCHARGING') - IFC	15d	91d	11-Mar-24 A	28-Jun-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1470-B	Electrical Load List & Balance (CCS MODE 'EMERGENCY MODE (Island)' - IFC	15d	91d	11-Mar-24 A	28-Jun-24 A	04-Mar-24	20-Mar-24	
ENG-ELE-1550-B	Lightning Protection System Calculation Report - IFC	10d	132d	11-Mar-24 A	16-Aug-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1610-B	Electrical Single Line Diagrams LV System - IFC - ABB INPUT	10d	32d	11-Mar-24 A	18-Apr-24 A	04-Mar-24	14-Mar-24	
ENG-ELE-1650-B	Electrical Control, Protection and Metering Diagrams - IFC - ABB INPUT	37d	61d	11-Mar-24 A	24-May-24 A	27-Nov-23	07-Dec-23	
ENG-ELE-1670-B	Electrical Schedules (Switchgears) - IFC - ABB INPUT	15d	61d	11-Mar-24 A	24-May-24 A	15-Nov-23	01-Dec-23	
ENG-ELE-2120-B	TDS - LV Distribution Boards - IFC	15d	41d	11-Mar-24 A	30-Apr-24 A	04-Dec-23	21-Dec-23	
ENG-ELE-1840-B	MR - for Navigation Aid System - Issue for PO Placement	10d	24d	13-Mar-24 A	11-Apr-24 A	22-Dec-23	05-Jan-24	
ENG-ELE-2370-B	MR - for T-Connectors & HV/MV Terminations - Issue for PO Placement	10d	122d	13-Mar-24 A	06-Aug-24 A	06-Mar-24	16-Mar-24	
ENG-ELE-2400-B	MR - for Electrical Power and Control Cables - Issue for PO Placement	10d	255d	13-Mar-24 A	15-Jan-25	17-Feb-24	28-Feb-24	122d
ENG-ELE-1210-B	Lighting & Socket Layout - Relief Valve Platform - IFC - DELETED	20d	20d	14-Mar-24 A	08-Apr-24 A	14-Mar-24	08-Apr-24	

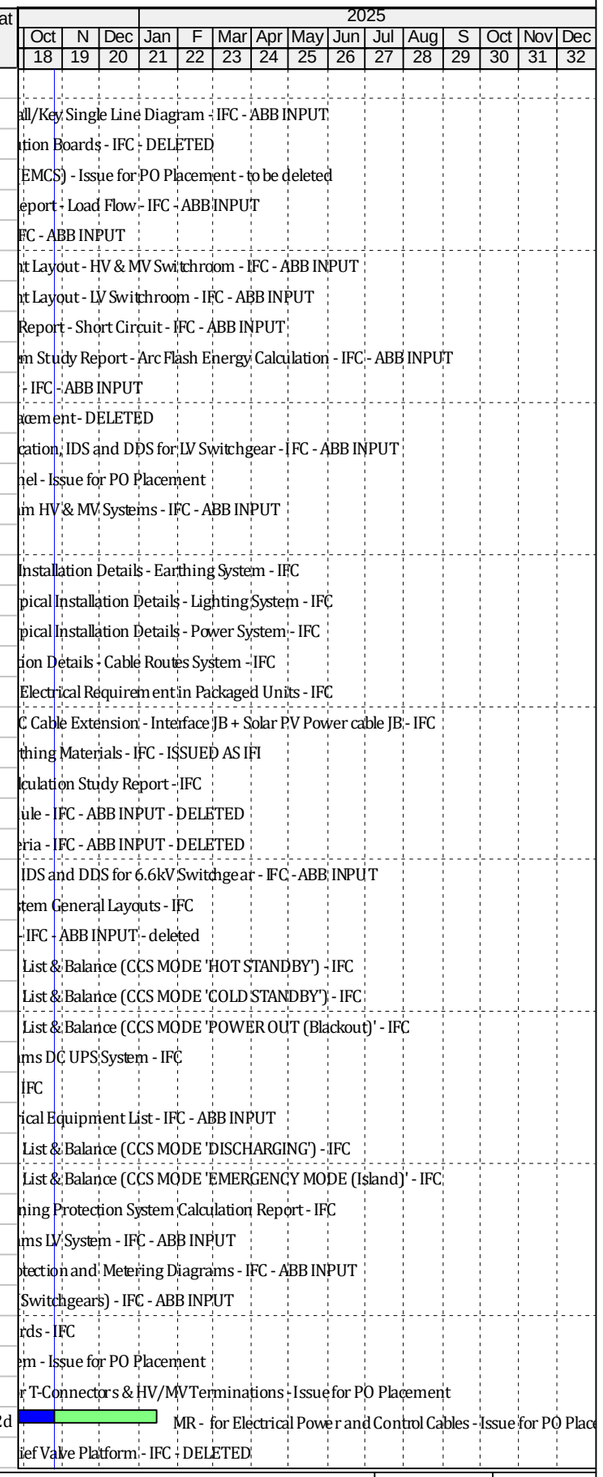

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ELE-1580-B	Electrical I/O Signal List - IFC - ABB INPUT - deleted	20d	20d	14-Mar-24 A	08-Apr-24 A	14-Mar-24	08-Apr-24	
ENG-ELE-1620-B	Electrical Single Line Diagrams AC UPS Systems - IFC	10d	27d	15-Mar-24 A	17-Apr-24 A	21-Mar-24	03-Apr-24	
ENG-ELE-1690-B	Electrical Protection Philosophy - IFC - ABB INPUT	41d	57d	15-Mar-24 A	24-May-24 A	21-Nov-23	11-Dec-23	
ENG-ELE-1850-B	Technical Specification, IDS and DDS for Navigation Aid System - IFC	21d	17d	15-Mar-24 A	05-Apr-24 A	28-Nov-23	09-Dec-23	
ENG-ELE-2310-B	MR - for IAC Cable Extension - Interface JB + Solar PV Power cable JB - Issue for PO Placement	10d	103d	18-Mar-24 A	19-Jul-24 A	21-Dec-23	04-Jan-24	
ENG-ELE-2350-B	TDS - Solar Farm - In-Feed Power Isolator Panel - IFC	10d	46d	18-Mar-24 A	14-May-24 A	09-Dec-23	20-Dec-23	
ENG-ELE-1490-B	Electrical Power & Control Cable Schedule (as per Rosetti Marino template) - IFC	10d	164d	22-Mar-24 A	04-Oct-24 A	21-Mar-24	03-Apr-24	
ENG-ELE-2420-B	TDS - Electrical Power and Control Cables - IFC	28d	111d	22-Mar-24 A	02-Aug-24 A	06-Feb-24	16-Feb-24	
ENG-ELE-2660-B	MTO - Electrical Power and Control Cables - IFC - ISSUED AS IFI	10d	1d	22-Mar-24 A	22-Mar-24 A	04-Apr-24	15-Apr-24	
ENG-ELE-1010-B	Electrical Equipment Layout - Lower Deck - IFC	15d	35d	26-Mar-24 A	09-May-24 A	26-Mar-24	13-Apr-24	
ENG-ELE-1030-B	Electrical Equipment Layout - Relief Valve Platform - IFC - DELETED	10d	10d	26-Mar-24 A	08-Apr-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1640-B	Electrical Single Line Diagrams (Distribution Boards, ACUPS, DCUPS, etc.) - IFC	15d	20d	26-Mar-24 A	19-Apr-24 A	21-Mar-24	09-Apr-24	
ENG-ELE-2530-B	MR - for Cables Glands, Fittings & Accessories - Issue for PO Placement	10d	96d	26-Mar-24 A	19-Jul-24 A	29-Feb-24	11-Mar-24	
ENG-ELE-2560-B	MR - for Conduits, Fittings & Accessories - Issue for PO Placement	10d	97d	26-Mar-24 A	20-Jul-24 A	27-Feb-24	08-Mar-24	
ENG-ELE-2620-B	MR - for Electrical MCTs - Issue for PO Placement	10d	50d	26-Mar-24 A	27-May-24 A	06-Mar-24	16-Mar-24	
ENG-ELE-1100-B	Electrical Cables Routing Layout - Relief Valve Platform - IFC - DELETED	10d	10d	09-Apr-24 A	19-Apr-24 A	09-Apr-24	19-Apr-24	
ENG-ELE-1350-B	Earthing & Lightining Layout - Relief Valve Platform - IFC -DELETED	10d	10d	09-Apr-24 A	19-Apr-24 A	09-Apr-24	19-Apr-24	
ENG-ELE-2380-B	TDS - T-Connectors & HV/MV Terminations - IFC	10d	51d	11-Apr-24 A	12-Jun-24 A	23-Feb-24	05-Mar-24	
ENG-ELE-1790-B	Electrical System Study Report - Transient In-Rush - IFC - ABB INPUT	15d	59d	12-Apr-24 A	21-Jun-24 A	13-Dec-23	02-Jan-24	
ENG-ELE-2440-B	MR - for Electrical Cables Trays & Accessories - Issue for PO Placement	10d	45d	12-Apr-24 A	05-Jun-24 A	20-Apr-24	03-May-24	
ENG-ELE-1800-B	Electromagnetic Compatibility Study - IFC - ABB INPUT	15d	39d	15-Apr-24 A	31-May-24 A	08-Jan-24	24-Jan-24	
ENG-ELE-2270-B	MR - for Electrical Heat Tracing (EHT) System - Issue for PO Placement	10d	174d	15-Apr-24 A	07-Nov-24	15-Feb-24	26-Feb-24	77d
ENG-ELE-2590-B	MR - for Earthing and Lightning Materials - Issue for PO Placement	10d	104d	15-Apr-24 A	16-Aug-24 A	03-Feb-24	14-Feb-24	
ENG-ELE-1680-B	Electrical Schedules (Distribution Boards, AC UPS, DC UPS, etc.) - IFC	15d	89d	17-Apr-24 A	31-Jul-24 A	02-Dec-23	20-Dec-23	
ENG-ELE-2410-B	Technical Specification, IDS and DDS for Electrical Cables - IFC	16d	73d	17-Apr-24 A	12-Jul-24 A	06-Feb-24	16-Feb-24	
ENG-ELE-2470-B	MR - for Lighting Fixtures & Accessories - Issue for PO Placement	10d	172d	17-Apr-24 A	07-Nov-24	23-Jan-24	02-Feb-24	70d
ENG-ELE-1150-B	Electrical MCT Composition Layout - Lower Deck - IFC	10d	88d	18-Apr-24 A	31-Jul-24 A	12-Feb-24	22-Feb-24	
ENG-ELE-1160-B	Electrical MCT Composition Layout - Stair Towers - IFC	15d	90d	18-Apr-24 A	02-Aug-24 A	20-Apr-24	09-May-24	
ENG-ELE-1170-B	Electrical MCT Composition Layout - ReliefValve Platform - IFC - DELETED	15d	15d	20-Apr-24 A	09-May-24 A	20-Apr-24	09-May-24	
ENG-ELE-2290-B	TDS - Electrical Heat Tracing (EHT) System - IFC	10d	55d	22-Apr-24 A	26-Jun-24 A	15-Feb-24	26-Feb-24	
ENG-ELE-2450-B	TDS - Electrical Cables Trays & Accessories - IFC	16d	131d	30-Apr-24 A	01-Oct-24 A	15-Feb-24	26-Feb-24	
ENG-ELE-2630-B	TDS - Electrical MCTs - IFC	10d	81d	30-Apr-24 A	02-Aug-24 A	23-Feb-24	05-Mar-24	
ENG-ELE-1140-B	Electrical MCT Composition Layout - Top Deck - IFC	15d	80d	02-May-24 A	02-Aug-24 A	09-Apr-24	26-Apr-24	
ENG-ELE-2480-B	TDS - Lighting Fixtures & Accessories - IFC	11d	91d	02-May-24 A	16-Aug-24 A	11-Jan-24	22-Jan-24	
ENG-ELE-1060-B	Electrical Equipment Layout - UPSs & Batteries Switchroom - IFC	10d	156d	08-May-24 A	07-Nov-24	26-Mar-24	08-Apr-24	42d
ENG-ELE-1570-B	Electrical Control Alarm and Monitoring Table - IFC - ABB INPUT	15d	86d	08-May-24 A	16-Aug-24 A	13-Jan-24	30-Jan-24	
ENG-ELE-1220-B	Lighting & Socket Layout - HV & MV Switchroom - IFC	38d	71d	10-May-24 A	31-Jul-24 A	14-Mar-24	08-Apr-24	
ENG-ELE-1230-B	Lighting & Socket Layout - LV Switchroom - IFC	38d	71d	10-May-24 A	31-Jul-24 A	14-Mar-24	08-Apr-24	
ENG-ELE-1240-B	Lighting & Socket Layout - UPSs & Batteries Switchroom - IFC	38d	71d	10-May-24 A	31-Jul-24 A	14-Mar-24	08-Apr-24	
ENG-ELE-1560-B	UPS & Battery Sizing Calculations - IFC	10d	71d	13-May-24 A	02-Aug-24 A	20-Apr-24	03-May-24	
ENG-ELE-2280-B	Technical Specification, IDS and DDS for Electrical Heat Tracing (EHT) System - IFC	10d	37d	15-May-24 A	26-Jun-24 A	15-Feb-24	26-Feb-24	
ENG-ELE-1280-B	Lighting & Socket Circuit Diagram - Relief Valve Platform - IFC -DELETED	10d	12d	20-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	
ENG-ELE-1260-B	Lighting & Socket Circuit Diagram - Lower Deck - IFC - deleted	10d	10d	22-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	
ENG-ELE-1270-B	Lighting & Socket Circuit Diagram - Stair Towers - IFC - delted	10d	10d	22-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	
ENG-ELE-1290-B	Lighting & Socket Circuit Diagram - HV & MV Switchroom - IFC - DELETED	10d	10d	22-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	
ENG-ELE-1300-B	Lighting & Socket Circuit Diagram - LV Switchroom - IFC	10d	9d	22-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	

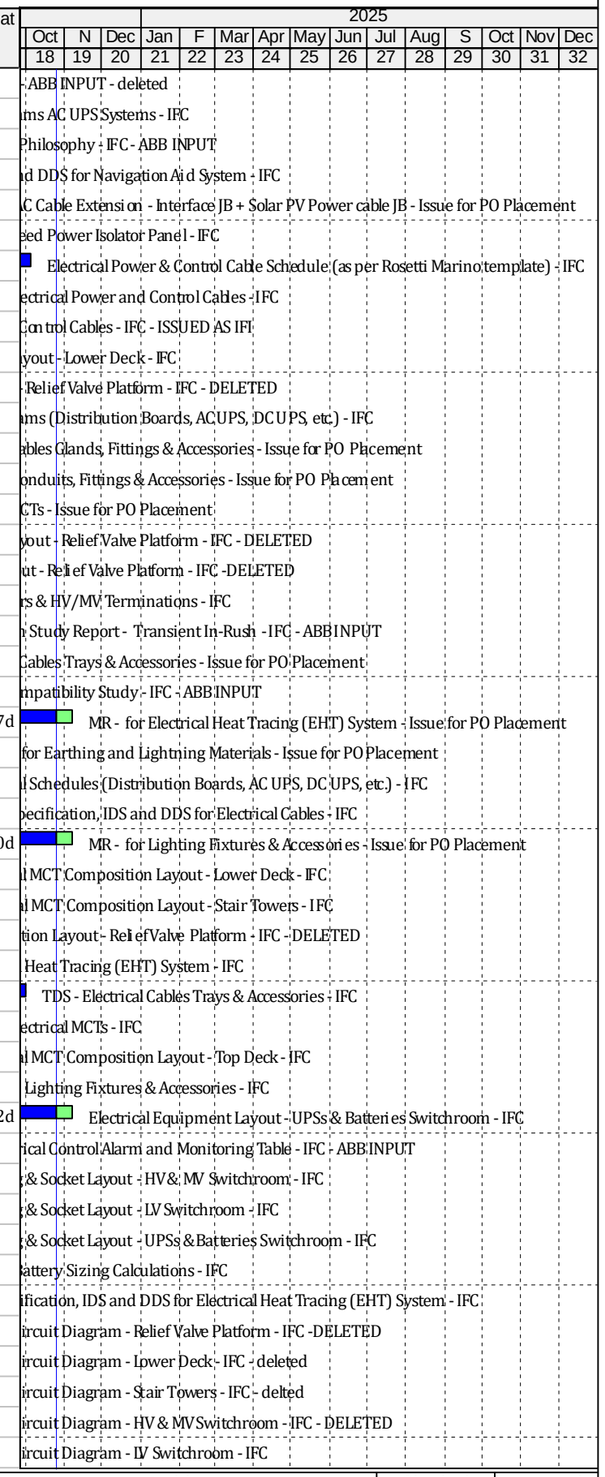

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ELE-1310-B	Lighting & Socket Circuit Diagram - UPSs & Batteries Switchroom - IFC	10d	9d	22-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	
ENG-ELE-1110-B	Electrical Cable Routing Layout - HV & MV Switchroom - IFC	10d	73d	23-May-24 A	16-Aug-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1360-B	Earthing & Lightining Layout - HV & MV Switchroom - IFC	10d	59d	27-May-24 A	02-Aug-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1370-B	Earthing & Lightining Layout - LV Switchroom - IFC	10d	59d	27-May-24 A	02-Aug-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1380-B	Earthing & Lightining Layout - UPSs & Batteries Switchroom - IFC	10d	57d	27-May-24 A	31-Jul-24 A	09-Apr-24	19-Apr-24	
ENG-ELE-1320-B	Earthing & Lightining Layout - Top Deck - IFC	10d	55d	31-May-24 A	02-Aug-24 A	15-Apr-24	26-Apr-24	
ENG-ELE-1330-B	Earthing & Lightining Layout - Lower Deck - IFC	10d	55d	31-May-24 A	02-Aug-24 A	15-Apr-24	26-Apr-24	
ENG-ELE-1180-B	Lighting & Socket Layout - Top Deck - IFC	38d	64d	03-Jun-24 A	16-Aug-24 A	14-Mar-24	08-Apr-24	
ENG-ELE-1190-B	Lighting & Socket Layout - Lower Deck - IFC	38d	64d	03-Jun-24 A	16-Aug-24 A	14-Mar-24	08-Apr-24	
ENG-ELE-1340-B	Earthing & Lightining Layout - Stair Towers - IFC	10d	53d	03-Jun-24 A	02-Aug-24 A	09-Apr-24	19-Apr-24	
ENG-ELE-1530-B	Electrical Equipment Sizing Calculation Report - IFC - ABB INPUT	20d	45d	05-Jun-24 A	26-Jul-24 A	09-Apr-24	03-May-24	
ENG-ELE-1780-B	Electrical System Study Report - Power Factor Compensation - IFC - ABB INPUT	15d	43d	05-Jun-24 A	24-Jul-24 A	13-Dec-23	02-Jan-24	
ENG-ELE-1250-B	Lighting & Socket Circuit Diagram - Top Deck - IFC	10d	58d	10-Jun-24 A	16-Aug-24 A	22-May-24	01-Jun-24	
ENG-ELE-1130-B	Electrical Cable Routing Layout - UPSs & Batteries Switchroom - IFC	10d	55d	13-Jun-24 A	16-Aug-24 A	09-Apr-24	19-Apr-24	
ENG-ELE-1200-B	Lighting & Socket Layout - Stair Towers - IFC	38d	48d	21-Jun-24 A	16-Aug-24 A	14-Mar-24	08-Apr-24	
ENG-ELE-2510-B	TDS - Control Stations, Junction Boxes and Sockets - IFC	11d	47d	21-Jun-24 A	16-Aug-24 A	11-Jan-24	22-Jan-24	
ENG-ELE-1000-B	Electrical Equipment Layout - Top Deck - IFC	15d	30d	27-Jun-24 A	31-Jul-24 A	26-Mar-24	13-Apr-24	
ENG-ELE-1020-B	Electrical Equipment Layout - Stair Towers - IFC	10d	30d	27-Jun-24 A	31-Jul-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-2540-B	TDS - Cables Glands, Fittings & Accessories - IFC	10d	66d	27-Jun-24 A	12-Sep-24 A	17-Feb-24	28-Feb-24	
ENG-ELE-1400-B	Electrical Heat Tracing (EHT) Layouts - IFC	10d	93d	01-Jul-24 A	17-Oct-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1770-B	Electrical System Study Report - Vital Supply Recovery - IFC - ABB INPUT	15d	42d	11-Jul-24 A	29-Aug-24 A	13-Dec-23	02-Jan-24	
ENG-ELE-2570-B	TDS - Conduits, Fittings & Accessories - IFC	33d	28d	15-Jul-24 A	16-Aug-24 A	15-Feb-24	26-Feb-24	
ENG-ELE-1070-B	Electrical Cables Routing Layout - Top Deck - IFC	10d	16d	16-Jul-24 A	02-Aug-24 A	15-Apr-24	26-Apr-24	
ENG-ELE-1120-B	Electrical Cable Routing Layout - LV Switchroom - IFC	10d	25d	18-Jul-24 A	16-Aug-24 A	26-Mar-24	08-Apr-24	
ENG-ELE-1660-B	Electrical Typical Schematic Diagrams (Distribution Boards, AC UPS, DC UPS, etc) - IFC	15d	12d	18-Jul-24 A	31-Jul-24 A	23-Feb-24	11-Mar-24	
ENG-ELE-1080-B	Electrical Cables Routing Layout - Lower Deck - IFC	15d	24d	19-Jul-24 A	16-Aug-24 A	15-Apr-24	03-May-24	
ENG-ELE-2500-B	MR - for Control Stations, Junction Boxes and Sockets - Issue for PO Placement	10d	1d	19-Jul-24 A	19-Jul-24 A	23-Jan-24	02-Feb-24	
ENG-ELE-1410-B	Electrical System Description & Design Philosophy (Electrical Design Basis) - IFC	25d	62d	23-Jul-24 A	03-Oct-24 A	25-Jan-24	22-Feb-24	
ENG-ELE-1710-B	Electrical Protection Relay Selectivity Study Report - IFC - ABB INPUT	20d	28d	25-Jul-24 A	27-Aug-24 A	08-Jan-24	30-Jan-24	
ENG-ELE-1090-B	Electrical Cables Routing Layout - Stair Towers - IFC	10d	85d	30-Jul-24 A	07-Nov-24	09-Apr-24	19-Apr-24	54d
ENG-ELE-1500-B	Electrical Interconnecting Wiring Diagram - IFC	15d	68d	30-Jul-24 A	17-Oct-24 A	15-May-24	31-May-24	
ENG-ELE-2600-B	TDS - Earthing and Lightning Materials - IFC	10d	3d	10-Sep-24 A	12-Sep-24 A	23-Jan-24	02-Feb-24	
ENG-ELE-1810-B	SAFOP Close Out Report - IFC	10d	10d	26-Oct-24	07-Nov-24	06-Feb-24	16-Feb-24	54d
ENG-ELE-2720-B	Ex equipment register (in suitable format for import into the computerised maintenance management system	15d	15d	28-Dec-24	16-Jan-25	22-Jul-24	07-Aug-24	13d
Issue For Information		336d	297d	17-Aug-23 A	08-Aug-24 A	16-Aug-23	25-Mar-24	
ENG-ELE-2010-A	TBE - 66kV Switchgear (GIS) - IFI	15d	37d	17-Aug-23 A	28-Sep-23 A	17-Aug-23	02-Sep-23	
ENG-ELE-1930-A	TBE - Power Transformers - IFI	15d	34d	02-Sep-23 A	11-Oct-23 A	02-Sep-23	19-Sep-23	
ENG-ELE-1970-A	TBE - Neutral Earthing Resistor (NER) - IFI	15d	26d	12-Sep-23 A	11-Oct-23 A	12-Sep-23	28-Sep-23	
ENG-ELE-2260-A	TBE - Electrical Monitoring and Control System (EMCS) - IFI - to be deleted	15d	3d	31-Oct-23 A	03-Nov-23 A	16-Aug-23	01-Sep-23	
ENG-ELE-2050-A	TBE - 6.6kV Switchgear - IFI	15d	4d	18-Dec-23 A	21-Dec-23 A	16-Aug-23	01-Sep-23	
ENG-ELE-2090-A	TBE- LV Switchgear - IFI	15d	29d	18-Dec-23 A	24-Jan-24 A	16-Aug-23	01-Sep-23	
ENG-ELE-2170-A	TBE - AC UPS Systems - IFI	15d	42d	18-Dec-23 A	08-Feb-24 A	17-Nov-23	04-Dec-23	
ENG-ELE-2210-A	TBE - DC UPS System - IFI	15d	42d	18-Dec-23 A	08-Feb-24 A	02-Nov-23	18-Nov-23	
ENG-ELE-2130-A	TBE - LV Distribution Boards - IFI	15d	1d	21-Dec-23 A	21-Dec-23 A	19-Dec-23	09-Jan-24	
ENG-ELE-2330-A	TBE - IAC Cable Extension - Interface JB + Solar PV Power cable JB - IFI - DELETED	15d	17d	21-Dec-23 A	13-Jan-24 A	23-Dec-23	13-Jan-24	
ENG-ELE-2360-A	TBE - Solar Farm - In-Feed Power Isolator Panel - IFI - deleted	15d	1d	21-Dec-23 A	21-Dec-23 A	23-Dec-23	13-Jan-24	

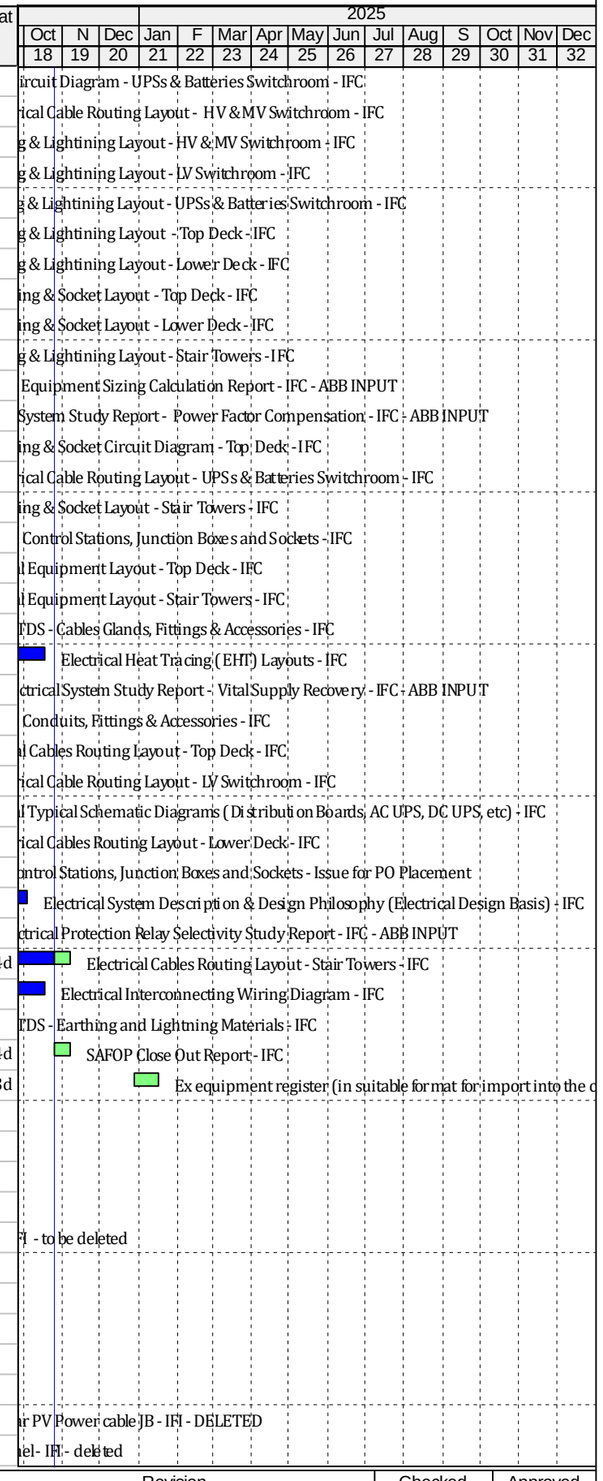

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ELE-2610-A	TBE - Earthing and Lightning Materials - IFI - DELETED	15d	15d	25-Jan-24 A	10-Feb-24 A	25-Jan-24	10-Feb-24	
ENG-ELE-2460-A	TBE - Electrical Cables Trays & Accessories - IFI DELETED	15d	14d	29-Feb-24 A	16-Mar-24 A	29-Feb-24	16-Mar-24	
ENG-ELE-2550-A	TBE - Cables Glands, Fittings & Accessories - IFI - DELETED	5d	15d	29-Feb-24 A	16-Mar-24 A	29-Feb-24	16-Mar-24	
ENG-ELE-2580-A	TBE - Conduits, Fittings & Accessories - IFI - DELETED	5d	15d	29-Feb-24 A	16-Mar-24 A	29-Feb-24	16-Mar-24	
ENG-ELE-2670-A	TBE - Electrical Bulk Materials - IFI DELETED	10d	10d	29-Feb-24 A	11-Mar-24 A	29-Feb-24	11-Mar-24	
ENG-ELE-1870-A	TBE - Navigation Aid System - IFI	15d	27d	04-Mar-24 A	05-Apr-24 A	19-Dec-23	09-Jan-24	
ENG-ELE-2390-A	TBE - T-Connectors & HV/MV Terminations - IFI - DELETED	15d	15d	08-Mar-24 A	25-Mar-24 A	08-Mar-24	25-Mar-24	
ENG-ELE-2430-A	TBE - Electrical Power and Control Cables - IFI	15d	39d	22-Apr-24 A	07-Jun-24 A	20-Feb-24	07-Mar-24	
ENG-ELE-2490-A	TBE - Lighting Fixtures & Accessories - IFI	15d	37d	10-May-24 A	21-Jun-24 A	12-Jan-24	29-Jan-24	
ENG-ELE-2640-A	TBE - Electrical MCTs - IFI	15d	3d	25-May-24 A	28-May-24 A	08-Mar-24	25-Mar-24	
ENG-ELE-2520-A	TBE - Control Stations, Junction Boxes and Sockets - IFI	15d	29d	10-Jun-24 A	12-Jul-24 A	12-Jan-24	29-Jan-24	
ENG-ELE-2300-A	TBE - Electrical Heat Tracing (EHT) System - IFI	15d	4d	05-Aug-24 A	08-Aug-24 A	06-Feb-24	22-Feb-24	
Instrumentation Engineering		412d	409d	14-Sep-23 A	21-Jan-25	14-Sep-23	23-Aug-24	235d
ENG-INS-1000	ABB Engineering Kick Off Meeting	0d	0d	14-Sep-23 A		14-Sep-23		
ENGEIT1120	I&C GENERAL SPECIFICATION & PROCEDURE (IFR, IFA, IFC)	285d	409d	14-Sep-23 A	21-Jan-25	14-Sep-23	23-Aug-24	52d
ENGEIT1140	I&C MR / SPECIFICATION / DATA SHEETS	195d	346d	18-Sep-23 A	07-Nov-24	07-Oct-23	01-Jun-24	14d
ENGEIT1160	INSTRUMENTATION SCHEDULE (IFR, IFA, IFC)	167d	368d	20-Oct-23 A	09-Jan-25	20-Oct-23	21-May-24	52d
ENGEIT1170	INSTRUMENT INDEX (IFR, IFA, IFC)	122d	140d	20-Oct-23 A	09-Apr-24 A	20-Oct-23	25-Mar-24	
ENGEIT1180	I/O LIST & SUMMARY (IFR, IFA, IFC)	124d	375d	20-Oct-23 A	17-Jan-25	14-Oct-23	13-Mar-24	69d
ENGEIT1210	INSTRUMENTATION LAYOUTS & CABLE ROUTING LAYOUTS (IFR, IFA, IFC)	147d	299d	31-Oct-23 A	26-Oct-24	14-Oct-23	09-May-24	305d
ENGEIT1150	I&C TECHNICAL BID EVALUATION	92d	294d	07-Nov-23 A	26-Oct-24	07-Nov-23	22-Mar-24	305d
ENGEIT1130	I&C REPORTS & CALCULATION SHEET (IFR, IFA, IFC)	88d	348d	25-Nov-23 A	21-Jan-25	25-Nov-23	22-Feb-24	52d
ENGEIT1200	INSTRUMENTATION DIAGRAMS (IFR, IFA, IFC)	105d	265d	26-Jan-24 A	06-Dec-24	14-Nov-23	13-Apr-24	57d
ENGEIT1190	INSTRUMENTATION BULK MTOs	88d	26d	01-Apr-24 A	03-May-24 A	29-Jan-24	01-Jun-24	
ENG-INS-1250-A10	Alarm Management Workshop	2d	2d	26-Oct-24	28-Oct-24	25-Nov-23	27-Nov-23	79d
Issue For Approval		356d	403d	18-Sep-23 A	17-Jan-25	27-Sep-23	24-Jul-24	192d
ENG-INS-1180-A	Data Network Design Specification - IFA - ABB INPUT	17d	39d	18-Sep-23 A	02-Nov-23 A	02-Oct-23	20-Oct-23	
ENG-INS-2000-A	System Specification for Main Automation Contractor - IFA - ABB INPUT	23d	54d	18-Sep-23 A	20-Nov-23 A	07-Oct-23	03-Nov-23	
ENG-INS-1190-A	Data Network Architecture Drawings - IFA - ABB INPUT	15d	38d	27-Sep-23 A	10-Nov-23 A	11-Oct-23	27-Oct-23	
ENG-INS-1970-A	Instrumentation for Package Unit Specification - IFA	11d	27d	02-Oct-23 A	02-Nov-23 A	02-Oct-23	13-Oct-23	
ENG-INS-1230-A	Cyber Security Design Philosophy - IFA - ABB INPUT	15d	26d	03-Oct-23 A	02-Nov-23 A	27-Sep-23	13-Oct-23	
ENG-INS-1960-A	Control System Philosophy - IFA - ABB INPUT	11d	26d	03-Oct-23 A	02-Nov-23 A	02-Oct-23	13-Oct-23	
ENG-INS-1040-A	Functional Safety Management Plan - IFA - ABB INPUT - DELETED	18d	18d	13-Oct-23 A	03-Nov-23 A	13-Oct-23	03-Nov-23	
ENG-INS-1010-A	Fire & Gas Cause & Effect Diagrams - IFA - deleted	20d	20d	20-Oct-23 A	13-Nov-23 A	20-Oct-23	13-Nov-23	
ENG-INS-1020-A	Fire & Gas Cause & Effect Matrix - IFA	20d	118d	20-Oct-23 A	12-Mar-24 A	20-Oct-23	13-Nov-23	
ENG-INS-1910-A	Instrument List - IFA	15d	18d	20-Oct-23 A	10-Nov-23 A	20-Oct-23	07-Nov-23	
ENG-INS-1920-A	Instrument I/O List - IFA	15d	18d	20-Oct-23 A	10-Nov-23 A	14-Oct-23	31-Oct-23	
ENG-INS-1300-A	TDS - SDV/BDV and Tigh Shut-Off XV Valves - IFA	10d	16d	23-Oct-23 A	10-Nov-23 A	20-Oct-23	31-Oct-23	
ENG-INS-1990-A	Control System Architecture Detailed Drawings - IFA - ABB INPUT	17d	25d	23-Oct-23 A	21-Nov-23 A	14-Oct-23	03-Nov-23	
ENG-INS-2020-A	Control System (CCS) Specification - IFA - ABB INPUT	12d	76d	23-Oct-23 A	25-Jan-24 A	14-Oct-23	27-Oct-23	
ENG-INS-2040-A	Safety System (ESD, Fire and Gas) Specification - IFA - ABB INPUT	25d	28d	23-Oct-23 A	24-Nov-23 A	05-Oct-23	03-Nov-23	
ENG-INS-1120-A	Layout Drawings (Onshore CCR, Offshore ITER) - IFA	20d	9d	31-Oct-23 A	10-Nov-23 A	14-Oct-23	07-Nov-23	
ENG-INS-1310-A	MR - SDV/BDV and Tigh Shut-Off XV Valves - Issue for RfQ	10d	13d	31-Oct-23 A	15-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-INS-1360-A	TDS - Control Valves - IFA	10d	13d	31-Oct-23 A	15-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-INS-1930-A	Instrument I/O Serial Mapping List - IFA - ABB INPUT	25d	366d	31-Oct-23 A	17-Jan-25	02-Nov-23	30-Nov-23	69d
ENG-INS-1280-A	Lyfe Cycle Management Plan (Obsolescence issues and timing requirements) - IFA - ABB INPUT - deleted	55d	25d	04-Nov-23 A	02-Dec-23 A	04-Nov-23	02-Dec-23	

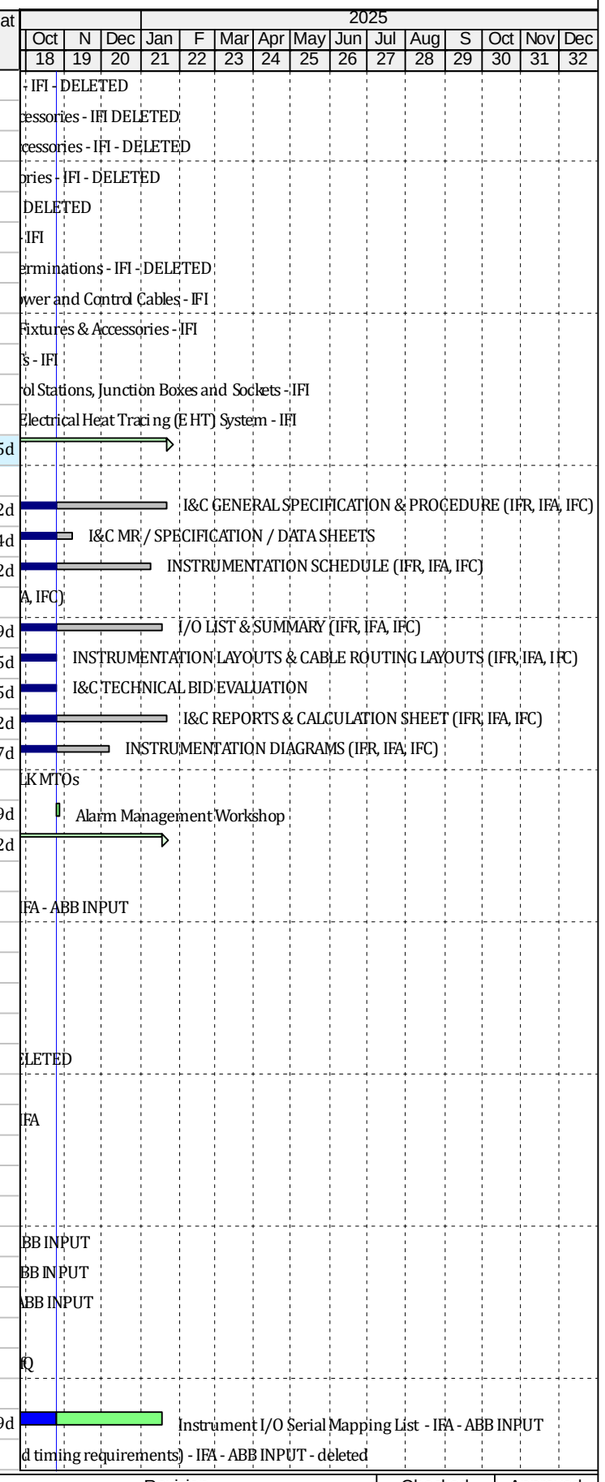

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-INS-1000-A	Process Safety Cause & Effect Matrix - IFA	20d	17d	06-Nov-23 A	24-Nov-23 A	08-Nov-23	30-Nov-23	
ENG-INS-1060-A	SIS Safety Requirement Specification (SRS) - IFA - ABB INPUT - DELETED	10d	10d	07-Nov-23 A	17-Nov-23 A	07-Nov-23	17-Nov-23	
ENG-INS-1290-A	Automation Detailed Design and Construction Package - IFA - ABB INPUT	18d	27d	13-Nov-23 A	14-Dec-23 A	13-Oct-23	03-Nov-23	
ENG-INS-1330-A	TDS - Pressure Safety Valves - IFA	10d	27d	13-Nov-23 A	14-Dec-23 A	15-Nov-23	25-Nov-23	
ENG-INS-1340-A	MR - Pressure Safety Valves - Issue for RfQ	10d	27d	13-Nov-23 A	14-Dec-23 A	15-Nov-23	25-Nov-23	
ENG-INS-1370-A	MR - Control Valves - Issue for RfQ	10d	8d	13-Nov-23 A	21-Nov-23 A	14-Nov-23	24-Nov-23	
ENG-INS-1840-A	Instrument Layout - Upper Deck- TOS EL. 30.310m - IFA	20d	34d	13-Nov-23 A	22-Dec-23 A	08-Nov-23	30-Nov-23	
ENG-INS-1080-A	SIF Logic Description - IFA - ABB INPUT - DELETED	15d	15d	18-Nov-23 A	05-Dec-23 A	18-Nov-23	05-Dec-23	
ENG-INS-1130-A	Earthing layouts drawings (Onshore CCR, Offshore ITER) - IFA - ABB INPUT	15d	53d	20-Nov-23 A	25-Jan-24 A	16-Nov-23	02-Dec-23	
ENG-INS-1600-A	TDS - F&G Field Equipments - IFA	10d	64d	20-Nov-23 A	07-Feb-24 A	21-Nov-23	01-Dec-23	
ENG-INS-1830-A	Instrument Layout - Lower Deck - TOS EL. 23.310m - IFA	20d	28d	20-Nov-23 A	22-Dec-23 A	25-Nov-23	19-Dec-23	
ENG-INS-1090-A	Safety related equipment register - IFA - ABB INPUT - DELETED	15d	15d	25-Nov-23 A	13-Dec-23 A	25-Nov-23	13-Dec-23	
ENG-INS-1050-A	Functional Safety Assessment Reports 1, 2,3 and 5 - IFA - ABB INPUT - DELETED	25d	25d	28-Nov-23 A	29-Dec-23 A	28-Nov-23	29-Dec-23	
ENG-INS-1240-A	Alarm System Requirements Specification - IFA - ABB INPUT	15d	155d	30-Nov-23 A	07-Jun-24 A	02-Nov-23	18-Nov-23	
ENG-INS-1270-A	Master Alarm Database - IFA - ABB INPUT	15d	209d	30-Nov-23 A	09-Aug-24 A	16-Dec-23	05-Jan-24	
ENG-INS-1630-A	TDS - Instrument Junction Boxes - IFA	10d	17d	01-Dec-23 A	21-Dec-23 A	14-Nov-23	24-Nov-23	
ENG-INS-1390-A	TDS - Pressure, Temperature and Diff. Pressure Level Transmitters - IFA	10d	35d	04-Dec-23 A	18-Jan-24 A	07-Dec-23	19-Dec-23	
ENG-INS-1420-A	TDS - Radar Level Transmitters - IFA	10d	70d	04-Dec-23 A	28-Feb-24 A	07-Dec-23	19-Dec-23	
ENG-INS-1450-A	TDS - Variable Area Flow Transmitters - IFA	10d	68d	04-Dec-23 A	26-Feb-24 A	07-Dec-23	19-Dec-23	
ENG-INS-1480-A	TDS - Ultrasonic Flow Transmitters and Flow gauges - IFA	10d	84d	04-Dec-23 A	15-Mar-24 A	07-Dec-23	19-Dec-23	
ENG-INS-1540-A	TDS - Dew Point Analyser - IFA - deleted	10d	13d	04-Dec-23 A	19-Dec-23 A	07-Dec-23	19-Dec-23	
ENG-INS-1570-A	TDS - Restriction Orifices RO - IFA	10d	188d	04-Dec-23 A	19-Jul-24 A	25-Nov-23	06-Dec-23	
ENG-INS-1850-A	Instrument Main Cables Routing - Lower Deck - TOS EL. 23.310m - IFA	12d	28d	04-Dec-23 A	10-Jan-24 A	20-Dec-23	10-Jan-24	
ENG-INS-1860-A	Instrument Main Cables Routing - Upper Deck- TOS EL. 30.310m - IFA	15d	28d	04-Dec-23 A	10-Jan-24 A	01-Dec-23	19-Dec-23	
ENG-INS-1070-A	SIF Final Reports - IFA - ABB INPUT - deleted	10d	10d	06-Dec-23 A	18-Dec-23 A	06-Dec-23	18-Dec-23	
ENG-INS-1030-A	SIF UZ Grouping Register - IFA - ABB INPUT - DELETED	10d	10d	13-Dec-23 A	23-Dec-23 A	13-Dec-23	23-Dec-23	
ENG-INS-1110-A	SIF Test Procedures - IFA - ABB INPUT	15d	15d	16-Dec-23 A	05-Jan-24 A	16-Dec-23	05-Jan-24	
ENG-INS-1400-A	MR - Pressure, Temperature and Diff. Pressure Level Transmitters - Issue for RfQ	10d	10d	08-Jan-24 A	18-Jan-24 A	20-Dec-23	03-Jan-24	
ENG-INS-1430-A	MR - Radar Level Transmitters - Issue for RfQ	10d	45d	08-Jan-24 A	28-Feb-24 A	20-Dec-23	03-Jan-24	
ENG-INS-1460-A	MR - Variable Area Flow Transmitters and Flow gauges - Issue for RfQ	10d	45d	08-Jan-24 A	28-Feb-24 A	20-Dec-23	03-Jan-24	
ENG-INS-1490-A	MR - Ultrasonic Flow Transmitters - Issue for RfQ	10d	65d	08-Jan-24 A	22-Mar-24 A	20-Dec-23	03-Jan-24	
ENG-INS-1550-A	MR - Dew Point Analyser - Issue for RfQ - deleted	10d	44d	08-Jan-24 A	27-Feb-24 A	20-Dec-23	03-Jan-24	
ENG-INS-1940-A	Instrument Cable List - IFA	10d	47d	08-Jan-24 A	01-Mar-24 A	11-Jan-24	22-Jan-24	
ENG-INS-1610-A	MR - F&G Field Equipments - Issue for RfQ	10d	17d	19-Jan-24 A	07-Feb-24 A	02-Dec-23	14-Dec-23	
ENG-INS-1100-A	Override Procedures for Process Safeguarding Systems - IFA - ABB INPUT	20d	28d	26-Jan-24 A	27-Feb-24 A	10-Nov-23	02-Dec-23	
ENG-INS-1150-A	Instrument - CCS Wiring Diagrams - IFA	30d	27d	26-Jan-24 A	26-Feb-24 A	14-Nov-23	19-Dec-23	
ENG-INS-1160-A	Instrument - Safety System Wiring Diagrams - IFA	20d	27d	26-Jan-24 A	26-Feb-24 A	20-Dec-23	16-Jan-24	
ENG-INS-1250-A	Alarm Management Workshop Terms of Reference - IFI - ABB INPUT	15d	102d	26-Jan-24 A	28-May-24 A	08-Nov-23	24-Nov-23	
ENG-INS-1670-A	TDS - Instrument Cables - IFA	10d	49d	26-Jan-24 A	22-Mar-24 A	23-Jan-24	02-Feb-24	
ENG-INS-1700-A	Instrument Cables Specification - IFA	15d	49d	26-Jan-24 A	22-Mar-24 A	23-Jan-24	08-Feb-24	
ENG-INS-1980-A	Process Control Logics Description - IFA - ABB INPUT	25d	141d	26-Jan-24 A	12-Jul-24 A	14-Nov-23	13-Dec-23	
ENG-INS-1950-A	Instrument Tubing List - IFA	10d	10d	29-Jan-24 A	08-Feb-24 A	29-Jan-24	08-Feb-24	
ENG-INS-1710-A	TDS - Instrument and Telecom Cable Trays - IFA	10d	55d	31-Jan-24 A	05-Apr-24 A	24-Jan-24	03-Feb-24	
ENG-INS-2500-A	MR - Automation systems CCS-SIS & EMS - Issue for RfQ	10d	25d	31-Jan-24 A	28-Feb-24 A	18-Oct-23	28-Oct-23	
ENG-INS-1810-A	Instrument Pneumatic Hook-up - IFA	20d	12d	01-Feb-24 A	14-Feb-24 A	15-Apr-24	09-May-24	
ENG-INS-1800-A	Instrument Process Hook-up - IFA	20d	5d	02-Feb-24 A	07-Feb-24 A	15-Apr-24	09-May-24	

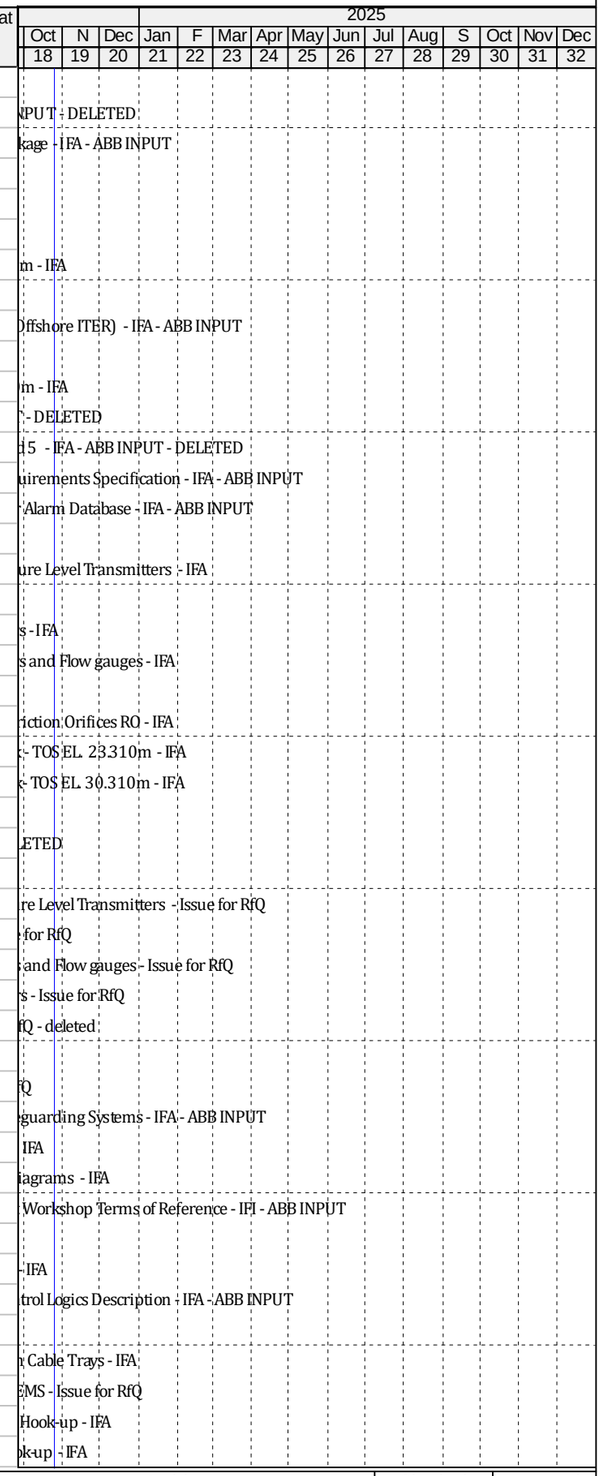

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-INS-1870-A	Instrument Tubing Layout - Lower Deck - TOS EL. 23.310m - IFA	15d	6d	20-Feb-24 A	26-Feb-24 A	11-Jan-24	27-Jan-24	
ENG-INS-1880-A	Instrument Tubing Layout - Upper Deck- TOS EL. 30.310m - IFA	15d	6d	20-Feb-24 A	26-Feb-24 A	20-Dec-23	10-Jan-24	
ENG-INS-1580-A	MR - Restriction Orifices RO - Issue for RfQ	10d	115d	04-Mar-24 A	19-Jul-24 A	07-Dec-23	19-Dec-23	
ENG-INS-1680-A	MR - Instrument Cables - Issue for RfQ	10d	5d	11-Mar-24 A	15-Mar-24 A	09-Feb-24	20-Feb-24	
ENG-INS-1650-A	TDS - Instrument Cable Glands and Accessory - IFA	10d	9d	18-Mar-24 A	27-Mar-24 A	03-Feb-24	14-Feb-24	
ENG-INS-1730-A	TDS - Tubing and Fittings - IFA	28d	9d	18-Mar-24 A	27-Mar-24 A	29-Jan-24	08-Feb-24	
ENG-INS-1780-A	MTO - Pneumetic Bulk Material - IFA	10d	26d	01-Apr-24 A	03-May-24 A	29-Jan-24	08-Feb-24	
ENG-INS-1820-A	Instrument Electrical Hook-up - IFA	15d	4d	01-Apr-24 A	05-Apr-24 A	15-Apr-24	03-May-24	
ENG-INS-1770-A	Instrument and Telecom MCT Composition - IFA	15d	56d	02-Apr-24 A	07-Jun-24 A	11-Jan-24	27-Jan-24	
ENG-INS-1790-A	MTO - Electrical Bulk Material - IFA	10d	10d	02-Apr-24 A	12-Apr-24 A	15-Feb-24	26-Feb-24	
ENG-INS-1890-A	Instrument and Telecom MCT Layout - Lower Deck - TOS EL. 23.310m - IFA	15d	21d	08-Apr-24 A	03-May-24 A	11-Jan-24	27-Jan-24	
ENG-INS-1900-A	Instrument and Telecom MCT Layout - Upper Deck- TOS EL. 30.310m - IFA	15d	43d	08-Apr-24 A	29-May-24 A	20-Dec-23	10-Jan-24	
ENG-INS-2500-B	MR - Automation systems CCS-SIS & EMS - Issue for PO Placement	10d	1d	11-Apr-24 A	11-Apr-24 A	18-Nov-23	29-Nov-23	
ENG-INS-1750-A	TDS - Instrument and Telecom MCTs - IFA	10d	39d	22-Apr-24 A	07-Jun-24 A	29-Jan-24	08-Feb-24	
ENG-INS-1170-A	Instrument Installation Details - IFA	20d	55d	10-May-24 A	12-Jul-24 A	14-Mar-24	08-Apr-24	
ENG-INS-1140-A	Instrument Loop Diagrams - IFA	20d	90d	28-Jun-24 A	11-Oct-24 A	29-Jan-24	20-Feb-24	
ENG-SAF-1410-A	SIL Verification excluding Packages (including of CPI available information) - IFA	15d	15d	08-Jul-24 A	24-Jul-24 A	08-Jul-24	24-Jul-24	
ENG-INS-1200-A	DATA Network Equipment Register - IFA - ABB INPUT	25d	25d	26-Oct-24	25-Nov-24	04-Nov-23	02-Dec-23	52d
ENG-INS-1260-A	Alarm Management Workshop Report - IFA - ABB INPUT	23d	23d	26-Oct-24	22-Nov-24	25-Nov-23	06-Dec-23	79d
ENG-INS-1220-A	DATA Network Plant Integration and Configuration Details - IFA - ABB INPUT	8d	8d	02-Nov-24	11-Nov-24	16-Nov-23	15-Dec-23	59d
ENG-INS-1210-A	DATA Network Cable Schedule - IFA - ABB INPUT	15d	15d	12-Nov-24	28-Nov-24	16-Dec-23	05-Jan-24	59d
Issue For Construction		341d	369d	31-Oct-23 A	21-Jan-25	08-Nov-23	23-Aug-24	189d
ENG-INS-1310-B	MR - SDV/BDV and Tigh Shut-Off XV Valves - Issue for PO Placement	10d	13d	31-Oct-23 A	15-Nov-23 A	25-Nov-23	06-Dec-23	
ENG-INS-1370-B	MR - Control Valves - Issue for PO Placement	10d	8d	13-Nov-23 A	21-Nov-23 A	07-Dec-23	19-Dec-23	
ENG-INS-1230-B	Cyber Security Design Philosophy - IFC - ABB INPUT	10d	299d	24-Nov-23 A	19-Nov-24	20-Nov-23	30-Nov-23	61d
ENG-INS-1300-B	TDS - SDV/BDV and Tigh Shut-Off XV Valves - IFC	10d	229d	27-Nov-23 A	30-Aug-24 A	14-Nov-23	24-Nov-23	
ENG-INS-1910-B	Instrument List - IFC	10d	109d	27-Nov-23 A	09-Apr-24 A	14-Mar-24	25-Mar-24	
ENG-INS-1040-B	Functional Safety Management Plan - IFC - ABB INPUT - DELETED	20d	20d	28-Nov-23 A	21-Dec-23 A	28-Nov-23	21-Dec-23	
ENG-INS-1190-B	Data Network Architecture Drawings - IFC - ABB INPUT	20d	281d	29-Nov-23 A	02-Nov-24	16-Nov-23	09-Dec-23	69d
ENG-INS-1060-B	SIS Safety Requirement Specification (SRS) - IFC - ABB INPUT - DELETED	10d	10d	30-Nov-23 A	12-Dec-23 A	30-Nov-23	12-Dec-23	
ENG-INS-1360-B	TDS - Control Valves - IFC	10d	219d	08-Dec-23 A	30-Aug-24 A	25-Nov-23	06-Dec-23	
ENG-INS-1920-B	Instrument I/O List - IFC	10d	80d	08-Dec-23 A	15-Mar-24 A	02-Mar-24	13-Mar-24	
ENG-INS-1970-B	Instrumentation for Package Unit Specification - IFC	20d	287d	08-Dec-23 A	19-Nov-24	08-Nov-23	30-Nov-23	69d
ENG-INS-1960-B	Control System Philosophy - IFC - ABB INPUT	20d	285d	12-Dec-23 A	19-Nov-24	08-Nov-23	30-Nov-23	61d
ENG-INS-2040-B	Safety System (ESD, Fire and Gas) Specification - IFC - ABB INPUT DELETED	20d	262d	15-Dec-23 A	25-Oct-24 A	03-Feb-24	26-Feb-24	
ENG-INS-1120-B	Layout Drawings (Onshore CCR, Offshore ITER) - IFC	20d	132d	18-Dec-23 A	28-May-24 A	01-Dec-23	27-Dec-23	
ENG-INS-1080-B	SIF Logic Description - IFC - ABB INPUT - DELETED	10d	10d	19-Dec-23 A	02-Jan-24 A	19-Dec-23	02-Jan-24	
ENG-INS-1990-B	Control System Architecture Detailed Drawings - IFC - ABB INPUT DELETED	20d	258d	20-Dec-23 A	25-Oct-24 A	22-Nov-23	15-Dec-23	
ENG-INS-1280-B	Lyfe Cycle Management Plan (Obsolescence issues and timing requirements) - IFC - ABB INPUT - deleted	15d	15d	22-Dec-23 A	12-Jan-24 A	22-Dec-23	12-Jan-24	
ENG-INS-1250-B	Alarm Management Workshop Terms of Reference - IFC - ABB INPUT - to be deleted	10d	10d	28-Dec-23 A	10-Jan-24 A	28-Dec-23	10-Jan-24	
ENG-INS-1180-B	Data Network Design Specification - IFC - ABB INPUT	15d	255d	03-Jan-24 A	02-Nov-24	09-Nov-23	25-Nov-23	69d
ENG-INS-2000-B	System Specification for Main Automation Contractor - IFC - ABB INPUT DELETED	25d	249d	03-Jan-24 A	25-Oct-24 A	22-Nov-23	21-Dec-23	
ENG-INS-1540-B	TDS - Dew Point Analyser - IFC - deleted	10d	10d	04-Jan-24 A	16-Jan-24 A	04-Jan-24	16-Jan-24	
ENG-INS-1400-B	MR - Pressure, Temperature and Diff. Pressure Level Transmitters - Issue for PO Placement	10d	10d	08-Jan-24 A	18-Jan-24 A	17-Jan-24	27-Jan-24	
ENG-INS-1090-B	Safety related equipment register - IFC - ABB INPUT - DELETED	15d	15d	17-Jan-24 A	02-Feb-24 A	17-Jan-24	02-Feb-24	
ENG-INS-1550-B	MR - Dew Point Analyser - Issue for PO Placement - deleted	10d	10d	17-Jan-24 A	27-Jan-24 A	17-Jan-24	27-Jan-24	

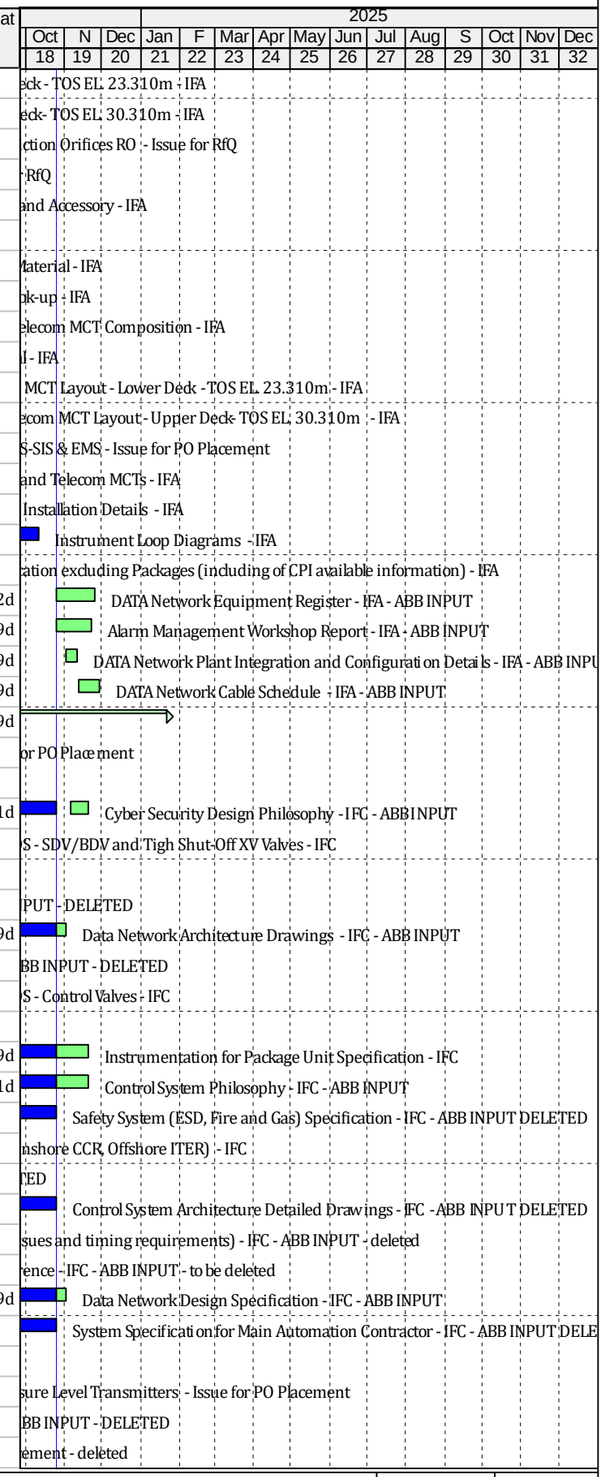

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-INS-1110-B	SIF Test Procedures - IFC - ABB INPUT - DELETED	10d	10d	19-Jan-24 A	30-Jan-24 A	19-Jan-24	30-Jan-24	
ENG-INS-1330-B	TDS - Pressure Safety Valves - IFC	10d	188d	19-Jan-24 A	30-Aug-24 A	09-Dec-23	20-Dec-23	
ENG-INS-1340-B	MR - Pressure Safety Valves - Issue for PO Placement	10d	246d	19-Jan-24 A	07-Nov-24	21-Dec-23	04-Jan-24	14d
ENG-INS-1000-B	Process Safety Cause & Effect Matrix - IFC	15d	44d	22-Jan-24 A	12-Mar-24 A	13-Jan-24	30-Jan-24	
ENG-INS-1630-B	TDS - Instrument Junction Boxes - IFC	10d	144d	22-Jan-24 A	11-Jul-24 A	29-Jan-24	08-Feb-24	
ENG-INS-1830-B	Instrument Layout - Lower Deck - TOS EL. 23.310m - IFC	15d	185d	23-Jan-24 A	30-Aug-24 A	26-Mar-24	13-Apr-24	
ENG-INS-1840-B	Instrument Layout - Upper Deck- TOS EL. 30.310m - IFC	15d	185d	23-Jan-24 A	30-Aug-24 A	26-Mar-24	13-Apr-24	
ENG-INS-1050-B	Functional Safety Assessment Reports 1, 2,3 and 5 - IFC - ABB INPUT - DELETED	20d	20d	25-Jan-24 A	16-Feb-24 A	25-Jan-24	16-Feb-24	
ENG-INS-1130-B	Earthing layouts drawings (Onshore CCR, Offshore ITER) - IFC - ABB INPUT	10d	96d	26-Jan-24 A	21-May-24 A	30-Dec-23	12-Jan-24	
ENG-INS-1290-B	Automation Detailed Design and Construction Package - IFC - ABB INPUT	20d	250d	26-Jan-24 A	19-Nov-24	28-Nov-23	21-Dec-23	69d
ENG-INS-1030-B	SIF UZ Grouping Register - IFC - ABB INPUT - DELETED	10d	10d	31-Jan-24 A	10-Feb-24 A	31-Jan-24	10-Feb-24	
ENG-INS-1070-B	SIF Final Reports - IFC - ABB INPUT - deleted	10d	10d	12-Feb-24 A	22-Feb-24 A	12-Feb-24	22-Feb-24	
ENG-INS-1850-B	Instrument Main Cables Routing - Lower Deck - TOS EL. 23.310m - IFC	10d	145d	12-Feb-24 A	02-Aug-24 A	15-Apr-24	26-Apr-24	
ENG-INS-1860-B	Instrument Main Cables Routing - Upper Deck- TOS EL. 30.310m - IFC	10d	145d	12-Feb-24 A	02-Aug-24 A	15-Apr-24	26-Apr-24	
ENG-INS-1390-B	TDS - Pressure, Temperature and Diff. Pressure Level Transmitters - IFC	10d	162d	19-Feb-24 A	30-Aug-24 A	04-Jan-24	16-Jan-24	
ENG-INS-1600-B	TDS - F&G Field Equipments - IFC	10d	144d	11-Mar-24 A	30-Aug-24 A	15-Dec-23	28-Dec-23	
ENG-INS-1610-B	MR - F&G Field Equipments - Issue for PO Placement	10d	32d	11-Mar-24 A	18-Apr-24 A	29-Dec-23	11-Jan-24	
ENG-INS-1800-B	Instrument Process Hook-up - IFC	15d	102d	11-Mar-24 A	11-Jul-24 A	28-May-24	13-Jun-24	
ENG-INS-1810-B	Instrument Pneumatic Hook-up - IFC	15d	102d	11-Mar-24 A	11-Jul-24 A	28-May-24	13-Jun-24	
ENG-INS-1870-B	Instrument Tubing Layout - Lower Deck - TOS EL. 23.310m - IFC	10d	141d	11-Mar-24 A	27-Aug-24 A	27-Apr-24	09-May-24	
ENG-INS-1880-B	Instrument Tubing Layout - Upper Deck- TOS EL. 30.310m - IFC	10d	141d	11-Mar-24 A	27-Aug-24 A	27-Apr-24	09-May-24	
ENG-INS-1420-B	TDS - Radar Level Transmitters - IFC	10d	143d	12-Mar-24 A	30-Aug-24 A	04-Jan-24	16-Jan-24	
ENG-INS-1430-B	MR - Radar Level Transmitters - Issue for PO Placement	10d	53d	12-Mar-24 A	16-May-24 A	17-Jan-24	27-Jan-24	
ENG-INS-1450-B	TDS - Variable Area Flow Transmitters - IFC	10d	143d	12-Mar-24 A	30-Aug-24 A	04-Jan-24	16-Jan-24	
ENG-INS-2020-B	Control System (CCS) Specification - IFC - ABB INPUT DELETED	10d	191d	12-Mar-24 A	25-Oct-24 A	10-Nov-23	21-Nov-23	
ENG-INS-1460-B	MR - Variable Area Flow Transmitters and Flow gauges - Issue for PO Placement	10d	27d	13-Mar-24 A	15-Apr-24 A	17-Jan-24	27-Jan-24	
ENG-INS-1940-B	Instrument Cable List - IFC	10d	177d	13-Mar-24 A	10-Oct-24 A	27-Apr-24	09-May-24	
ENG-INS-1010-B	Fire & Gas Cause & Effect Diagrams - IFC - deleted	20d	20d	14-Mar-24 A	08-Apr-24 A	14-Mar-24	08-Apr-24	
ENG-INS-1150-B	Instrument - CCS Wiring Diagrams - IFC	20d	167d	26-Mar-24 A	11-Oct-24 A	04-Jan-24	27-Jan-24	
ENG-INS-1160-B	Instrument - Safety System Wiring Diagrams - IFC	15d	167d	26-Mar-24 A	11-Oct-24 A	29-Jan-24	14-Feb-24	
ENG-INS-1480-B	TDS - Ultrasonic Flow Transmitters and Flow gauges - IFC	10d	140d	26-Mar-24 A	10-Sep-24 A	04-Jan-24	16-Jan-24	
ENG-INS-1680-B	MR - Instrument Cables - Issue for PO Placement	10d	189d	26-Mar-24 A	07-Nov-24	22-May-24	01-Jun-24	122d
ENG-INS-1670-B	TDS - Instrument Cables - IFC	10d	139d	27-Mar-24 A	10-Sep-24 A	15-Feb-24	26-Feb-24	
ENG-INS-1650-B	TDS - Instrument Cable Glands and Accessory - IFC	10d	163d	28-Mar-24 A	09-Oct-24 A	27-Feb-24	08-Mar-24	
ENG-INS-1730-B	TDS - Tubing and Fittings - IFC	10d	138d	28-Mar-24 A	10-Sep-24 A	21-Feb-24	02-Mar-24	
ENG-INS-1710-B	TDS - Instrument and Telecom Cable Trays - IFC	10d	131d	08-Apr-24 A	10-Sep-24 A	16-Feb-24	27-Feb-24	
ENG-INS-1100-B	Override Procedures for Process Safeguarding Systems - IFC - ABB INPUT	15d	88d	11-Apr-24 A	24-Jul-24 A	22-Dec-23	12-Jan-24	
ENG-INS-1490-B	MR - Ultrasonic Flow Transmitters - Issue for PO Placement	10d	63d	15-Apr-24 A	28-Jun-24 A	17-Jan-24	27-Jan-24	
ENG-INS-1020-B	Fire & Gas Cause & Effect Matrix - IFC	20d	42d	24-Apr-24 A	13-Jun-24 A	14-Mar-24	08-Apr-24	
ENG-INS-1700-B	Instrument Cables Specification - IFC	10d	137d	25-Apr-24 A	04-Oct-24 A	10-May-24	21-May-24	
ENG-INS-1780-B	MTO - Pneumetic Bulk Material - IFC - ISSUED AS IFI	10d	1d	03-May-24 A	03-May-24 A	10-May-24	21-May-24	
ENG-INS-1790-B	MTO - Electrical Bulk Material - IFC - ISSUED AS IFI	10d	1d	03-May-24 A	03-May-24 A	22-May-24	01-Jun-24	
ENG-INS-1820-B	Instrument Electrical Hook-up - IFC	10d	107d	08-May-24 A	10-Sep-24 A	16-May-24	27-May-24	
ENG-INS-1950-B	Instrument Tubing List - IFC- deleted	10d	10d	10-May-24 A	21-May-24 A	10-May-24	21-May-24	
ENG-INS-1890-B	Instrument and Telecom MCT Layout - Lower Deck - TOS EL. 23.310m - IFC	10d	33d	03-Jun-24 A	10-Jul-24 A	27-Apr-24	09-May-24	
ENG-INS-1750-B	TDS - Instrument and Telecom MCTs - IFC	10d	97d	19-Jun-24 A	10-Oct-24 A	27-Apr-24	09-May-24	

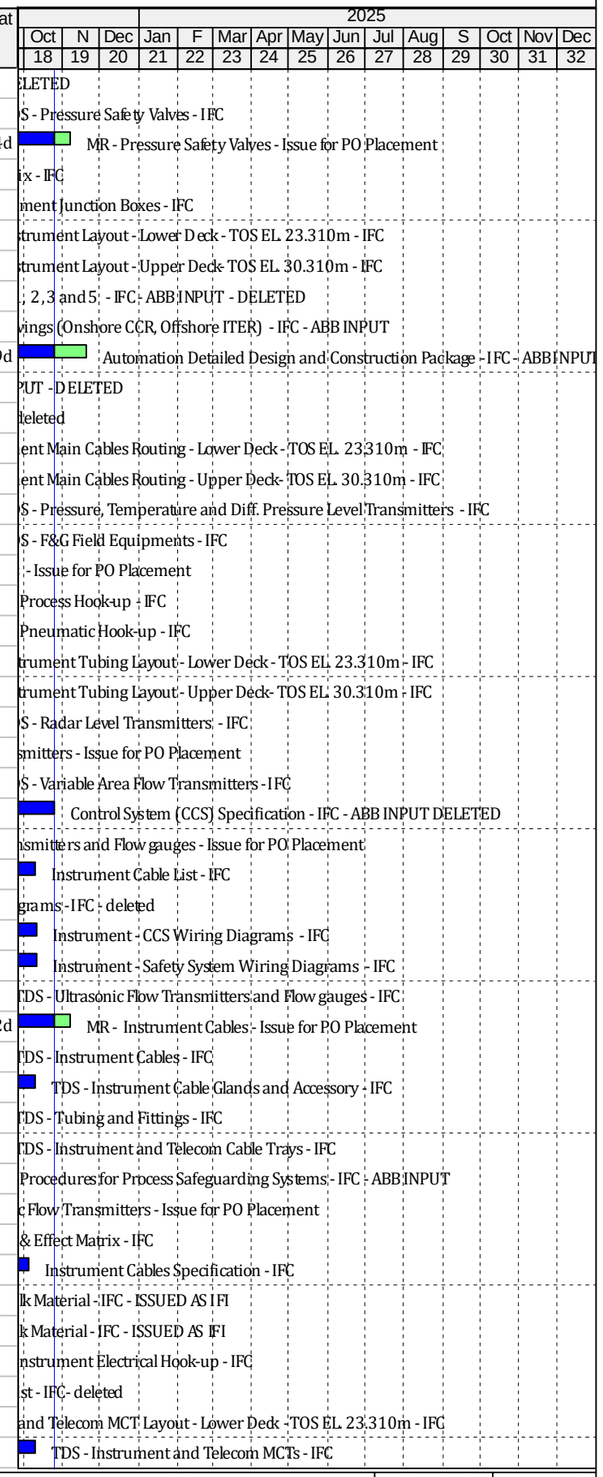

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-INS-1900-B	Instrument and Telecom MCT Layout - Upper Deck- TOS EL. 30.310m - IFC	10d	19d	19-Jun-24 A	10-Jul-24 A	27-Apr-24	09-May-24	
ENG-INS-1770-B	Instrument and Telecom MCT Composition - IFC	10d	68d	23-Jul-24 A	10-Oct-24 A	27-Apr-24	09-May-24	
ENG-INS-1570-B	TDS - Restriction Orifices RO - IFC	10d	44d	06-Aug-24 A	26-Sep-24 A	04-Jan-24	16-Jan-24	
ENG-INS-1580-B	MR - Restriction Orifices RO - Issue for PO Placement	10d	44d	06-Aug-24 A	27-Sep-24 A	17-Jan-24	27-Jan-24	
ENG-SAF-1410-B	SIL Verification excluding Packages (including of CPI available information) - IFC	15d	15d	06-Aug-24 A	23-Aug-24 A	06-Aug-24	23-Aug-24	
ENG-INS-1170-B	Instrument Installation Details - IFC	15d	22d	16-Aug-24 A	10-Sep-24 A	20-Apr-24	09-May-24	
ENG-INS-1980-B	Process Control Logics Description - IFC - ABB INPUT	20d	81d	16-Aug-24 A	19-Nov-24	11-Jan-24	02-Feb-24	57d
ENG-INS-1240-B	Alarm System Requirements Specification - IFC - ABB INPUT	10d	69d	19-Aug-24 A	07-Nov-24	14-Dec-23	27-Dec-23	69d
ENG-INS-1270-B	Master Alarm Database - IFC - ABB INPUT	15d	16d	13-Sep-24 A	01-Oct-24 A	31-Jan-24	16-Feb-24	
ENG-INS-1930-B	Instrument I/O Serial Mapping List - IFC - ABB INPUT DELETED	15d	1d	24-Sep-24 A	24-Sep-24 A	26-Feb-24	13-Mar-24	
ENG-INS-1140-B	Instrument Loop Diagrams - IFC	15d	15d	20-Nov-24	06-Dec-24	26-Mar-24	13-Apr-24	57d
ENG-INS-1200-B	DATA Network Equipment Register - IFC - ABB INPUT	10d	10d	07-Dec-24	18-Dec-24	16-Dec-23	29-Dec-23	52d
ENG-INS-1220-B	DATA Network Plant Integration and Configuration Details - IFC - ABB INPUT	20d	20d	07-Dec-24	02-Jan-25	13-Jan-24	05-Feb-24	57d
ENG-INS-1210-B	DATA Network Cable Schedule - IFC - ABB INPUT	15d	15d	19-Dec-24	09-Jan-25	19-Jan-24	05-Feb-24	52d
ENG-INS-1260-B	Alarm Management Workshop Report - IFC - ABB INPUT	10d	10d	10-Jan-25	21-Jan-25	11-Jan-24	22-Jan-24	52d
Issue For Information		218d	294d	07-Nov-23 A	25-Oct-24 A	07-Nov-23	22-Mar-24	
ENG-INS-2050-A	TBE - Safety System (ESD, Fire and Gas) - IFI - deleted	15d	15d	07-Nov-23 A	23-Nov-23 A	07-Nov-23	23-Nov-23	
ENG-INS-1320-A	TBE - SDV/BDV and Tigh Shut-Off XV Valves - IFI	15d	49d	01-Dec-23 A	01-Feb-24 A	28-Nov-23	15-Dec-23	
ENG-INS-1380-A	TBE - Control Valves - IFI	15d	98d	06-Dec-23 A	05-Apr-24 A	12-Dec-23	30-Dec-23	
ENG-INS-2030-A	TBE - Control System (CCS) - IFI	15d	83d	18-Dec-23 A	27-Mar-24 A	07-Nov-23	23-Nov-23	
ENG-INS-1350-A	TBE - Pressure Safety Valves - IFI	15d	85d	22-Dec-23 A	05-Apr-24 A	12-Dec-23	30-Dec-23	
ENG-INS-1590-A	TBE - Restriction Orifices RO - IFI - DELETED	15d	15d	08-Jan-24 A	24-Jan-24 A	08-Jan-24	24-Jan-24	
ENG-INS-1560-A	TBE - Dew Point Analyser - IFI - DELETED	15d	15d	18-Jan-24 A	03-Feb-24 A	18-Jan-24	03-Feb-24	
ENG-INS-1410-A	TBE - Pressure, Temperature and Diff. Pressure Level Transmitters - IFI	15d	55d	26-Feb-24 A	03-May-24 A	18-Jan-24	03-Feb-24	
ENG-INS-1620-A	TBE - F&G Field Equipments - IFI	15d	33d	26-Feb-24 A	05-Apr-24 A	03-Jan-24	20-Jan-24	
ENG-INS-1440-A	TBE - Radar Level Transmitters - IFI - DELETED	15d	1d	04-Mar-24 A	04-Mar-24 A	18-Jan-24	03-Feb-24	
ENG-INS-1470-A	TBE - Variable Area Flow Transmitters and Flowgauges - IFI	15d	30d	04-Mar-24 A	09-Apr-24 A	18-Jan-24	03-Feb-24	
ENG-INS-1690-A	TBE - Instrument Cables - IFI	12d	56d	02-Apr-24 A	07-Jun-24 A	06-Mar-24	22-Mar-24	
ENG-INS-1720-A	TBE - Instrument and Telecom Cable Trays - IFI DELETED	11d	0d	14-Apr-24 A	14-Apr-24 A	17-Feb-24	05-Mar-24	
ENG-INS-1500-A	TBE - Ultrasonic Flow Transmitters - IFI	15d	43d	10-May-24 A	28-Jun-24 A	18-Jan-24	03-Feb-24	
ENG-INS-1740-A	TBE - Tubing and Fittings - IFI	12d	42d	10-May-24 A	27-Jun-24 A	23-Feb-24	11-Mar-24	
ENG-INS-1760-A	TBE - Instrument and Telecom MCTs - IFI	12d	18d	25-May-24 A	14-Jun-24 A	23-Feb-24	11-Mar-24	
ENG-INS-1640-A	TBE - Instrument Junction Boxes - IFI	15d	16d	10-Jun-24 A	27-Jun-24 A	12-Dec-23	30-Dec-23	
ENG-INS-1660-A	TBE - Instrument Cable Glands and Accessory - IFI - DELETED	13d	118d	10-Jun-24 A	25-Oct-24 A	29-Feb-24	16-Mar-24	
Telecomm Engineering		255d	235d	14-Sep-23 A	25-Jun-24 A	14-Oct-23	25-Jun-24	
ENGEIT1220	TELECOM GENERAL SPECIFICATION & PROCEDURE (IFR, IFA, IFC)	65d	65d	14-Sep-23 A	29-Nov-23 A	14-Oct-23	03-Jan-24	
ENGEIT1250	TELECOM MR / SPECIFICATION / DATA SHEETS	174d	219d	02-Oct-23 A	25-Jun-24 A	25-Nov-23	25-Jun-24	
ENGEIT1280	TELECOM BULK MTOs	174d	219d	02-Oct-23 A	25-Jun-24 A	25-Nov-23	25-Jun-24	
ENGEIT1300	TELECOM LAYOUTS (IFR, IFA, IFC)	192d	174d	02-Nov-23 A	01-Jun-24 A	02-Nov-23	01-Jun-24	
ENGEIT1230	TELECOM REPORTS (IFR, IFA, IFC)	35d	40d	25-Nov-23 A	16-Jan-24 A	25-Nov-23	16-Jan-24	
ENGEIT1260	TELECOM TECHNICAL BID EVALUATION	87d	69d	18-Dec-23 A	11-Mar-24 A	22-Dec-23	11-Mar-24	
ENGEIT1240	TELECOM SCHEDULE (IFR, IFA, IFC)	53d	124d	17-Jan-24 A	13-Jun-24 A	17-Jan-24	13-Jun-24	
ENGEIT1290	TELECOM DIAGRAMS (IFR, IFA, IFC)	58d	69d	04-Mar-24 A	27-May-24 A	04-Mar-24	27-May-24	
ENGEIT1270	CYBER SECURITY	53d	49d	27-Apr-24 A	25-Jun-24 A	27-Apr-24	25-Jun-24	
Issue For Approval		255d	235d	14-Sep-23 A	25-Jun-24 A	14-Oct-23	25-Jun-24	
ENG-TEL-1070-A	Telecom System Philosophy & Specifications - IFA	35d	22d	14-Sep-23 A	09-Oct-23 A	14-Oct-23	24-Nov-23	

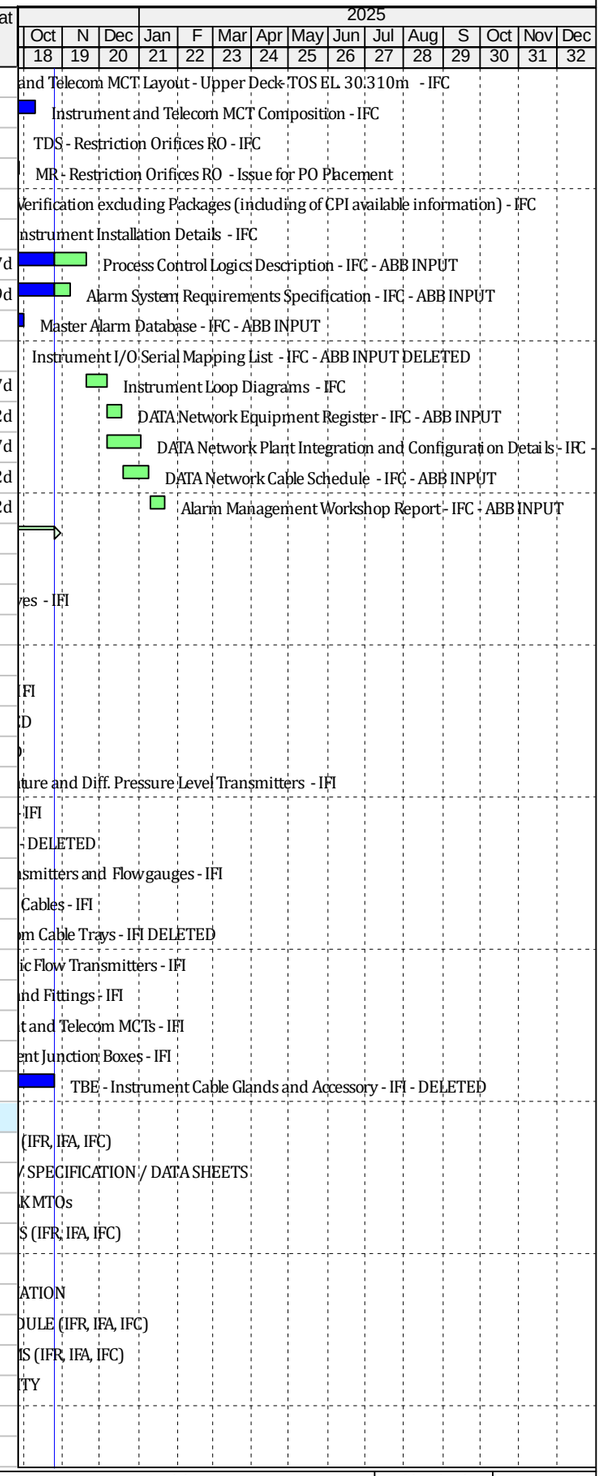

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-TEL-1000-A	MR - Telecom System - Issue for RfQ	10d	13d	02-Oct-23 A	16-Oct-23 A	25-Nov-23	06-Dec-23	
ENG-TEL-1030-A	Telecom Equipment Locations - IFA - deleted	20d	20d	02-Nov-23 A	24-Nov-23 A	02-Nov-23	24-Nov-23	
ENG-TEL-1000-B	MR - Telecom System - Issue for PO Placement	10d	22d	06-Nov-23 A	30-Nov-23 A	07-Dec-23	19-Dec-23	
ENG-TEL-1080-A	Telecom System Shutdown Philosophy - IFA - deleted	15d	15d	25-Nov-23 A	13-Dec-23 A	25-Nov-23	13-Dec-23	
ENG-TEL-1050-A	Telecom System Cable Routing - IFA - deleted	20d	20d	20-Dec-23 A	16-Jan-24 A	20-Dec-23	16-Jan-24	
ENG-TEL-1020-A	Telecom Systems Cable Schedules - IFA - deleted	10d	10d	17-Jan-24 A	27-Jan-24 A	17-Jan-24	27-Jan-24	
ENG-TEL-1090-A	Telecom Cables Specifications & Data Sheets - IFA - deleted	10d	10d	29-Jan-24 A	08-Feb-24 A	29-Jan-24	08-Feb-24	
ENG-TEL-1100-A	MR - Telecom Cables - Issue for RfQ - deleted	10d	10d	29-Jan-24 A	08-Feb-24 A	29-Jan-24	08-Feb-24	
ENG-TEL-1040-A	Telecom System Earthing Diagrams - IFA - deleted	15d	15d	04-Mar-24 A	20-Mar-24 A	04-Mar-24	20-Mar-24	
ENG-TEL-1060-A	Telecom Equipment Hook-ups - IFA - deleted	10d	10d	15-Apr-24 A	26-Apr-24 A	15-Apr-24	26-Apr-24	
ENG-TEL-1100-B	MR - Telecom Cables - Issue for PO Placement - deleted	10d	10d	14-Jun-24 A	25-Jun-24 A	14-Jun-24	25-Jun-24	
Issue For Construction		209d	191d	06-Nov-23 A	25-Jun-24 A	07-Dec-23	25-Jun-24	
ENG-TEL-1070-B	Telecom System Philosophy & Specifications - IFC	20d	21d	06-Nov-23 A	29-Nov-23 A	07-Dec-23	03-Jan-24	
ENG-TEL-1080-B	Telecom System Shutdown Philosophy - IFC - deleted	10d	10d	04-Jan-24 A	16-Jan-24 A	04-Jan-24	16-Jan-24	
ENG-TEL-1030-B	Telecom Equipment Locations - IFC - deleted	15d	15d	27-Apr-24 A	15-May-24 A	27-Apr-24	15-May-24	
ENG-TEL-1040-B	Telecom System Earthing Diagrams - IFC - deleted	10d	10d	16-May-24 A	27-May-24 A	16-May-24	27-May-24	
ENG-TEL-1050-B	Telecom System Cable Routing - IFC - deleted	15d	15d	16-May-24 A	01-Jun-24 A	16-May-24	01-Jun-24	
ENG-TEL-1060-B	Telecom Equipment Hook-ups - IFC - deleted	10d	10d	16-May-24 A	27-May-24 A	16-May-24	27-May-24	
ENG-TEL-1020-B	Telecom Systems Cable Schedules - IFC - deleted	10d	10d	03-Jun-24 A	13-Jun-24 A	03-Jun-24	13-Jun-24	
ENG-TEL-1090-B	Telecom Cables Specifications & Data Sheets - IFC - deleted	10d	10d	14-Jun-24 A	25-Jun-24 A	14-Jun-24	25-Jun-24	
Issue For Information		187d	69d	18-Dec-23 A	11-Mar-24 A	22-Dec-23	11-Mar-24	
ENG-TEL-1010-A	TBE - Telecom System - IFI	23d	58d	18-Dec-23 A	27-Feb-24 A	22-Dec-23	12-Jan-24	
ENG-TEL-1110-A	TBE - Telecom Cables - IFI - deleted	15d	15d	23-Feb-24 A	11-Mar-24 A	23-Feb-24	11-Mar-24	
Architectural Engineering		340d	364d	11-Sep-23 A	21-Nov-24	20-Oct-23	29-Oct-24	80d
Issue For Approval		312d	352d	11-Sep-23 A	07-Nov-24	20-Oct-23	05-Oct-24	82d
ENG-ARCH-1070-A	Supply Specification for LV (400V) Switchroom - IFA	10d	33d	11-Sep-23 A	18-Oct-23 A	20-Oct-23	31-Oct-23	
ENG-ARCH-1080-A	LV (400V) Switchroom - General Layout (plan, view, section) - IFA	5d	33d	11-Sep-23 A	18-Oct-23 A	26-Oct-23	31-Oct-23	
ENG-ARCH-1090-A	LV (400V) Switchroom - Doors Map/Schedule - IFA	5d	33d	11-Sep-23 A	18-Oct-23 A	26-Oct-23	31-Oct-23	
ENG-ARCH-1100-A	LV (400V) Switchroom - Flooring & Lining layout - IFA	5d	33d	11-Sep-23 A	18-Oct-23 A	26-Oct-23	31-Oct-23	
ENG-ARCH-1110-A	LV (400V) Switchroom - Fire rated requirement layout (plan, section, typical detail) - IFA	5d	33d	11-Sep-23 A	18-Oct-23 A	26-Oct-23	31-Oct-23	
ENG-ARCH-1120-A	MR - LV (400V) Switchroom - Issue for RfQ	10d	33d	11-Sep-23 A	18-Oct-23 A	20-Oct-23	31-Oct-23	
ENG-ARCH-1010-A	HV-MV (66kV / 6.6kV) Switchroom - General Layout (plan, view, section) - IFA	5d	25d	29-Sep-23 A	27-Oct-23 A	02-Nov-23	07-Nov-23	
ENG-ARCH-1020-A	HV-MV (66kV / 6.6kV) Switchroom - Doors Map/Schedule - IFA	5d	25d	29-Sep-23 A	27-Oct-23 A	02-Nov-23	07-Nov-23	
ENG-ARCH-1030-A	HV-MV (66kV / 6.6kV) Switchroom - Flooring & Lining layout - IFA	5d	25d	29-Sep-23 A	27-Oct-23 A	02-Nov-23	07-Nov-23	
ENG-ARCH-1040-A	HV-MV (66kV / 6.6kV) Switchroom - Fire rated requirement layout (plan, section, typical detail) - IFA	5d	25d	29-Sep-23 A	27-Oct-23 A	02-Nov-23	07-Nov-23	
ENG-ARCH-1210-A	Supply Specification for I&T Equipment Room - IFA	10d	18d	10-Oct-23 A	30-Oct-23 A	02-Nov-23	13-Nov-23	
ENG-ARCH-1260-A	MR - I&T Equipment Room - Issue for RfQ	10d	18d	10-Oct-23 A	30-Oct-23 A	02-Nov-23	13-Nov-23	
ENG-ARCH-1280-A	Supply Specification for AC UPS fitted with UPS system Equipment Room - IFA	10d	18d	10-Oct-23 A	30-Oct-23 A	02-Nov-23	13-Nov-23	
ENG-ARCH-1290-A	AC UPS fitted with UPS system Equipment Room - General Layout (plan, view, section) - IFA	5d	18d	10-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1300-A	AC UPS fitted with UPS system Equipment Room - Doors Map/Schedule - IFA	5d	18d	10-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1310-A	AC UPS fitted with UPS system Equipment Room - Flooring & Lining layout - IFA	5d	18d	10-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1320-A	AC UPS fitted with UPS system Equipment Room - Fire rated requirement layout (plan, section, typical detail) - I	5d	18d	10-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1330-A	MR - AC UPS fitted with UPS system Equipment Room - Issue for RfQ	10d	18d	10-Oct-23 A	30-Oct-23 A	02-Nov-23	13-Nov-23	
ENG-ARCH-1000-A	Supply Specification for HVforMV (66kV / 6.6kV) Switchroom - IFA	10d	11d	16-Oct-23 A	27-Oct-23 A	26-Oct-23	07-Nov-23	
ENG-ARCH-1050-A	MR - HV-MV (66kV / 6.6kV) Switchroom - Issue for RfQ	10d	11d	16-Oct-23 A	27-Oct-23 A	26-Oct-23	07-Nov-23	
ENG-ARCH-1220-A	I&T Equipment Room - General Layout (plan, view, section) - IFA	5d	13d	16-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	

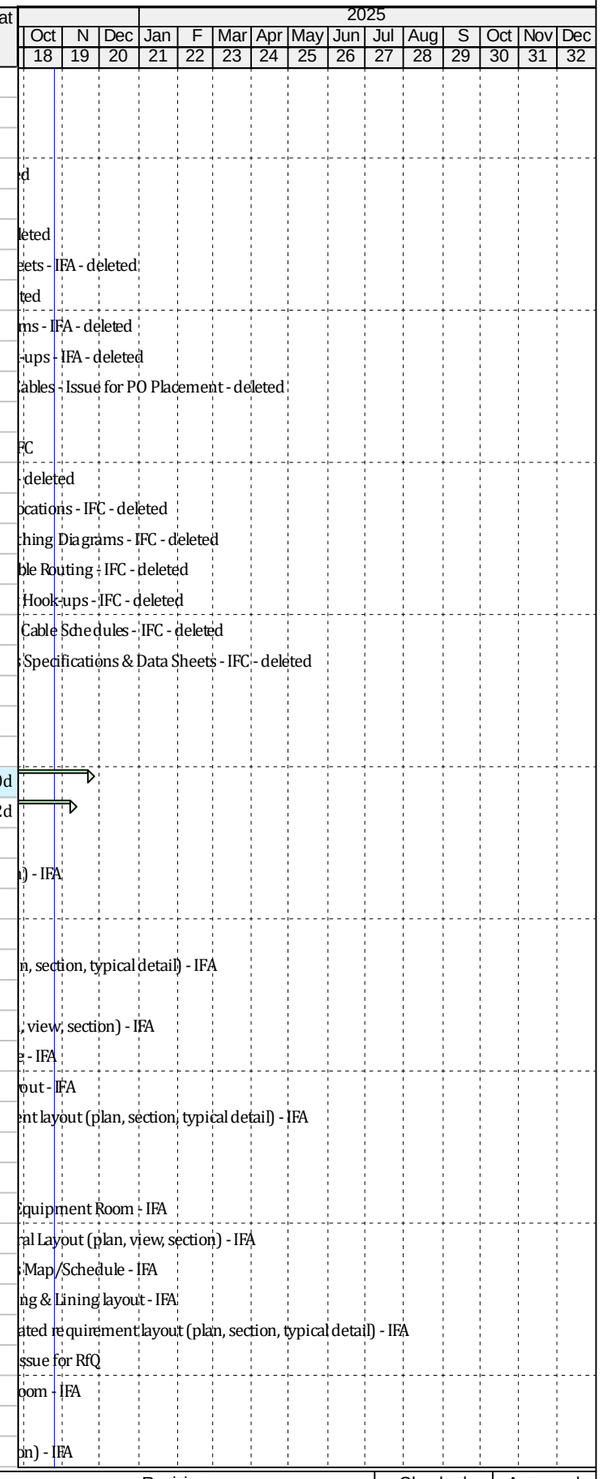

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ARCH-1230-A	I&T Equipment Room - Doors Map/Schedule - IFA	5d	13d	16-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1240-A	I&T Equipment Room - Flooring & Lining layout - IFA	5d	13d	16-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1250-A	I&T Equipment Room - Fire rated requirement layout (plan, section, typical detail) - IFA	5d	13d	16-Oct-23 A	30-Oct-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1140-A	Supply Specification - Container 40' ISO for Water treatment system - IFA - deleted	10d	10d	02-Nov-23 A	13-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-ARCH-1190-A	MR - Container 40' ISO for Water treatment system - Issue for RfQ - deleted	10d	10d	02-Nov-23 A	13-Nov-23 A	02-Nov-23	13-Nov-23	
ENG-ARCH-1150-A	Container 40' ISO for Water treatment system - General Layout (plan, view, section) - IFA	5d	5d	08-Nov-23 A	13-Nov-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1160-A	Container 40' ISO for Water treatment system - Doors Map/Schedule - IFA - deleted	5d	5d	08-Nov-23 A	13-Nov-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1170-A	Container 40' ISO for Water treatment system - Flooring & Lining layout - IFA - deleted	5d	5d	08-Nov-23 A	13-Nov-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1180-A	Container 40' ISO for Water treatment system - Fire rated requirement layout (plan, section, typical detail) - IFA	5d	5d	08-Nov-23 A	13-Nov-23 A	08-Nov-23	13-Nov-23	
ENG-ARCH-1390-A	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFA	10d	9d	18-Mar-24 A	27-Mar-24 A	27-Apr-24	09-May-24	
ENG-ARCH-1410-A	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFA	10d	7d	02-Apr-24 A	09-Apr-24 A	27-Apr-24	09-May-24	
ENG-ARCH-1420-A	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFA - DELETED	10d	10d	27-Apr-24 A	09-May-24 A	27-Apr-24	09-May-24	
ENG-ARCH-1430-A	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFA - DELETED	10d	10d	27-Apr-24 A	09-May-24 A	27-Apr-24	09-May-24	
ENG-ARCH-1350-A	Safety Equipment Support - Tag: " " - Assembly & Details - IFA (only if needed)	10d	16d	19-Oct-24 A	07-Nov-24	25-Sep-24	05-Oct-24	82d
ENG-ARCH-1360-A	Safety Equipment Support - Tag: " " - Assembly & Details - IFA (only if needed)	10d	16d	19-Oct-24 A	07-Nov-24	25-Sep-24	05-Oct-24	80d
ENG-ARCH-1370-A	Safety Equipment Support - Tag: " " - Assembly & Details - IFA (only if needed)	10d	16d	19-Oct-24 A	07-Nov-24	25-Sep-24	05-Oct-24	80d
ENG-ARCH-1380-A	Safety Equipment Support - Tag: " " - Assembly & Details - IFA (only if needed)	10d	16d	19-Oct-24 A	07-Nov-24	25-Sep-24	05-Oct-24	80d
Issue For Construction		305d	364d	11-Sep-23 A	21-Nov-24	14-Nov-23	29-Oct-24	80d
ENG-ARCH-1120-B	MR - LV (400V) Switchroom - Issue for PO Placement	10d	33d	11-Sep-23 A	18-Oct-23 A	14-Nov-23	24-Nov-23	
ENG-ARCH-1260-B	MR - I&T Equipment Room - Issue for PO Placement	10d	18d	10-Oct-23 A	30-Oct-23 A	25-Nov-23	06-Dec-23	
ENG-ARCH-1330-B	MR - AC UPS fitted with UPS system Equipment Room - Issue for PO Placement	10d	18d	10-Oct-23 A	30-Oct-23 A	09-Jan-24	19-Jan-24	
ENG-ARCH-1050-B	MR - HV-MV (66kV / 6.6kV) Switchroom - Issue for PO Placement	10d	11d	16-Oct-23 A	27-Oct-23 A	20-Nov-23	30-Nov-23	
ENG-ARCH-1080-B	LV (400V) Switchroom - General Layout (plan, view, section) - IFC	15d	102d	13-Nov-23 A	15-Mar-24 A	31-Jan-24	16-Feb-24	
ENG-ARCH-1100-B	LV (400V) Switchroom - Flooring & Lining layout - IFC	15d	102d	13-Nov-23 A	15-Mar-24 A	17-Feb-24	05-Mar-24	
ENG-ARCH-1110-B	LV (400V) Switchroom - Fire rated requirement layout (plan, section, typical detail) - IFC	15d	102d	13-Nov-23 A	15-Mar-24 A	17-Feb-24	05-Mar-24	
ENG-ARCH-1070-B	Supply Specification for LV (400V) Switchroom - IFC	10d	133d	14-Nov-23 A	24-Apr-24 A	14-Nov-23	24-Nov-23	
ENG-ARCH-1090-B	LV (400V) Switchroom - Doors Map/Schedule - IFC	15d	92d	24-Nov-23 A	15-Mar-24 A	17-Feb-24	05-Mar-24	
ENG-ARCH-1140-B	Supply Specification - Container 40' ISO for Water treatment system - IFC	10d	10d	25-Nov-23 A	06-Dec-23 A	25-Nov-23	06-Dec-23	
ENG-ARCH-1190-B	MR - Container 40' ISO for Water treatment system - Issue for PO Placement - deleted	10d	10d	25-Nov-23 A	06-Dec-23 A	25-Nov-23	06-Dec-23	
ENG-ARCH-1000-B	Supply Specification for HVforMV (66kV / 6.6kV) Switchroom - IFC	10d	122d	27-Nov-23 A	24-Apr-24 A	20-Nov-23	30-Nov-23	
ENG-ARCH-1010-B	HV-MV (66kV / 6.6kV) Switchroom - General Layout (plan, view, section) - IFC	15d	82d	27-Nov-23 A	06-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1020-B	HV-MV (66kV / 6.6kV) Switchroom - Doors Map/Schedule - IFC	15d	82d	27-Nov-23 A	06-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1030-B	HV-MV (66kV / 6.6kV) Switchroom - Flooring & Lining layout - IFC	15d	82d	27-Nov-23 A	06-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1040-B	HV-MV (66kV / 6.6kV) Switchroom - Fire rated requirement layout (plan, section, typical detail) - IFC	15d	82d	27-Nov-23 A	06-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1210-B	Supply Specification for I&T Equipment Room - IFC	10d	122d	27-Nov-23 A	24-Apr-24 A	25-Nov-23	06-Dec-23	
ENG-ARCH-1220-B	I&T Equipment Room - General Layout (plan, view, section) - IFC	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1230-B	I&T Equipment Room - Doors Map/Schedule - IFC	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1240-B	I&T Equipment Room - Flooring & Lining layout - IFC	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1250-B	I&T Equipment Room - Fire rated requirement layout (plan, section, typical detail) - IFC	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1280-B	Supply Specification for AC UPS fitted with UPS system Equipment Room - IFC	10d	122d	27-Nov-23 A	24-Apr-24 A	25-Nov-23	06-Dec-23	
ENG-ARCH-1290-B	AC UPS fitted with UPS system Equipment Room - General Layout (plan, view, section) - IFC	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1300-B	AC UPS fitted with UPS system Equipment Room - Doors Map/Schedule - IFC	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1310-B	AC UPS fitted with UPS system Equipment Room - Flooring & Lining layout - IFC	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1320-B	AC UPS fitted with UPS system Equipment Room - Fire rated requirement layout (plan, section, typical detail) - I	15d	83d	27-Nov-23 A	07-Mar-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1150-B	Container 40' ISO for Water treatment system - General Layout (plan, view, section) - IFC	15d	15d	09-Apr-24 A	26-Apr-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1160-B	Container 40' ISO for Water treatment system - Doors Map/Schedule - IFC - deleted	15d	15d	09-Apr-24 A	26-Apr-24 A	09-Apr-24	26-Apr-24	

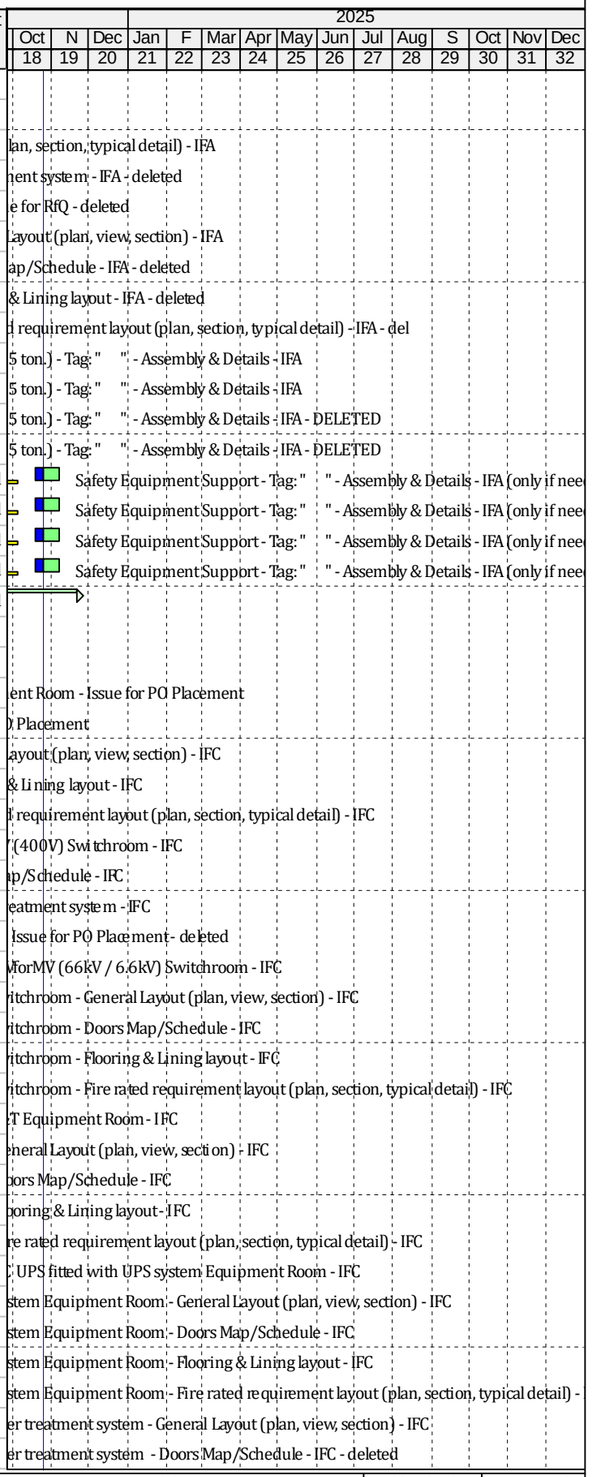

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-ARCH-1170-B	Container 40' ISO for Water treatment system - Flooring & Lining layout - IFC - deleted	15d	15d	09-Apr-24 A	26-Apr-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1180-B	Container 40' ISO for Water treatment system - Fire rated requirement layout (plan, section, typical detail) - IFC	15d	15d	09-Apr-24 A	26-Apr-24 A	09-Apr-24	26-Apr-24	
ENG-ARCH-1390-B	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFC	10d	13d	23-Apr-24 A	09-May-24 A	22-May-24	01-Jun-24	
ENG-ARCH-1410-B	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFC	10d	15d	08-May-24 A	24-May-24 A	22-May-24	01-Jun-24	
ENG-ARCH-1420-B	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFC - DELETED	10d	10d	22-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	
ENG-ARCH-1430-B	Equipment Support (< 5 ton.) - Tag: " " - Assembly & Details - IFC - DELETED	10d	10d	22-May-24 A	01-Jun-24 A	22-May-24	01-Jun-24	
ENG-ARCH-1350-B	Safety Equipment Support - Tag: " " - Assembly & Details - IFC - Only if needed	10d	27d	18-Oct-24 A	20-Nov-24	18-Oct-24	29-Oct-24	82d
ENG-ARCH-1360-B	Safety Equipment Support - Tag: " " - Assembly & Details - IFC - Only if needed	10d	29d	18-Oct-24 A	21-Nov-24	18-Oct-24	29-Oct-24	80d
ENG-ARCH-1370-B	Safety Equipment Support - Tag: " " - Assembly & Details - IFC - Only if needed	10d	29d	18-Oct-24 A	21-Nov-24	18-Oct-24	29-Oct-24	80d
ENG-ARCH-1380-B	Safety Equipment Support - Tag: " " - Assembly & Details - IFC - Only if needed	10d	29d	18-Oct-24 A	21-Nov-24	18-Oct-24	29-Oct-24	80d
Issue For Information		51d	89d	11-Sep-23 A	27-Dec-23 A	28-Nov-23	27-Dec-23	
ENG-ARCH-1060-A	TBE - HV-MV (66kV / 6.6kV) Switchroom - IFI	15d	87d	11-Sep-23 A	22-Dec-23 A	28-Nov-23	15-Dec-23	
ENG-ARCH-1200-A	TBE Container 40' ISO for Water treatment system - IFI - deleted	15d	22d	29-Nov-23 A	27-Dec-23 A	07-Dec-23	27-Dec-23	
ENG-ARCH-1130-A	TBE - LV (400V) Switchroom - IFI	15d	5d	18-Dec-23 A	22-Dec-23 A	28-Nov-23	15-Dec-23	
ENG-ARCH-1270-A	TBE - I&T Equipment Room - IFI	15d	5d	18-Dec-23 A	22-Dec-23 A	07-Dec-23	27-Dec-23	
ENG-ARCH-1340-A	TBE - AC UPS fitted with UPS system Equipment Room - IFI	15d	5d	18-Dec-23 A	22-Dec-23 A	28-Nov-23	15-Dec-23	
Safety Engineering		440d	468d	04-Sep-23 A	20-Mar-25	04-Sep-23	18-Jan-25	185d
ENGSAF1020	PROJECT TECHNICAL SAFETY PHILOSOPHIES (IFR, IFA, IFC)	66d	311d	04-Sep-23 A	12-Sep-24 A	04-Sep-23	20-Nov-23	
ENGSAF1030	F&G PHILOSOPHY (IFR, IFA, IFC)	223d	304d	12-Sep-23 A	12-Sep-24 A	10-Oct-23	06-Jul-24	
ENG-SAF-2500-A	HAZID WORKSHOP	2d	1d	05-Oct-23 A	05-Oct-23 A	04-Oct-23	05-Oct-23	
ENGSAF1060	LAYOUT SAFETY REVIEW REPORT	213d	325d	06-Nov-23 A	30-Nov-24	02-Dec-23	07-Aug-24	123d
ENGSAF1100	SAFETY LAYOUTS (IFR, IFA, IFC)	192d	308d	06-Nov-23 A	11-Nov-24	02-Nov-23	25-Jun-24	50d
ENGSAF1090	HAZARDOUS AREA CLASSIFICATION (REPORT & DRAWINGS) (IFR, IFA, IFC)	137d	296d	20-Nov-23 A	11-Nov-24	25-Nov-23	03-May-24	140d
ENGSAF1010	HAZOP WORKSHOP	5d	4d	04-Dec-23 A	08-Dec-23 A	27-Nov-23	01-Dec-23	
ENGSAF1050	HAZOP REPORT	45d	281d	04-Dec-23 A	07-Nov-24	02-Dec-23	29-Jan-24	143d
ENGSAF1110	TECHNICAL SAFETY MR / SPECIFICATION / DATA SHEETS	192d	262d	08-Jan-24 A	14-Nov-24	14-Nov-23	18-Jul-24	32d
ENGSAF1070	TECHNICAL SAFETY STUDIES	201d	204d	26-Feb-24 A	26-Oct-24	24-Feb-24	07-Aug-24	305d
ENG-SAF-1110-A10	ALARP WORKSHOP	1d	25d	10-May-24 A	07-Jun-24 A	18-May-24	18-May-24	
ENGSAF1120	TECHNICAL SAFETY TECHNICAL BID EVALUATION	39d	89d	15-Aug-24 A	28-Nov-24	28-Jun-24	15-Jul-24	8d
ENG-SAF-1450-A10	Safety Critical Task Analyses Terms of Reference - IFI - new doc	15d	15d	26-Oct-24	13-Nov-24	02-Apr-24	18-Apr-24	59d
ENG-SAF-1420-A10	SIMOP/MOPO WORKSHOP	1d	1d	26-Oct-24	26-Oct-24	13-Jun-24	13-Jun-24	88d
ENG-SAF-1450-A20	Safety Critical Task Analyses WORKSHOP	1d	1d	02-Dec-24	02-Dec-24	09-May-24	09-May-24	59d
Issue For Approval		371d	371d	04-Sep-23 A	22-Nov-24	04-Sep-23	09-Jul-24	130d
ENG-SAF-1020-A	Design HSSE plan - IFA	11d	4d	04-Sep-23 A	07-Sep-23 A	04-Sep-23	15-Sep-23	
ENG-SAF-1500-A	HSE Design Philosophy - IFA	11d	9d	04-Sep-23 A	13-Sep-23 A	04-Sep-23	15-Sep-23	
ENG-SAF-1010-A	Fire Protection Philosophy	15d	13d	12-Sep-23 A	26-Sep-23 A	10-Oct-23	26-Oct-23	
ENG-SAF-1080-A	HAZID Terms of Reference - IFI	15d	5d	16-Sep-23 A	21-Sep-23 A	16-Sep-23	03-Oct-23	
ENG-SAF-1090-A	HAZID Report - IFA	7d	9d	06-Oct-23 A	16-Oct-23 A	06-Oct-23	13-Oct-23	
ENG-SAF-1050-A	HAZOP Terms of Reference - IFI	15d	20d	23-Oct-23 A	15-Nov-23 A	19-Oct-23	06-Nov-23	
ENG-SAF-1390-A	LOPA ToR - IFI	15d	20d	23-Oct-23 A	15-Nov-23 A	19-Oct-23	06-Nov-23	
ENG-SAF-1040-A	HSSE Action Tracking Register and Close out report - IFA	15d	7d	06-Nov-23 A	13-Nov-23 A	15-Dec-23	04-Jan-24	
ENG-SAF-1290-A	Escape Routes, Fire Fighting, Life Saving Equipment and Safety Equipment Layouts Drawings - lower deck - IFA	10d	71d	06-Nov-23 A	01-Feb-24 A	02-Nov-23	13-Nov-23	
ENG-SAF-1300-A	Escape Routes, Fire Fighting, Life Saving Equipment and Safety Equipment Layouts Drawings - upper deck - IFA	10d	71d	06-Nov-23 A	01-Feb-24 A	02-Nov-23	13-Nov-23	
ENG-SAF-1100-A	HAZID Close Out Report - IFA	12d	283d	13-Nov-23 A	18-Oct-24 A	14-Oct-23	27-Oct-23	
ENG-SAF-1130-A	Hazardous Area Classification Schedule - IFA	10d	27d	20-Nov-23 A	21-Dec-23 A	25-Nov-23	06-Dec-23	
ENG-SAF-1230-A	Hazardous Area Classification Layout - lower deck - IFA	10d	66d	20-Nov-23 A	09-Feb-24 A	25-Nov-23	06-Dec-23	

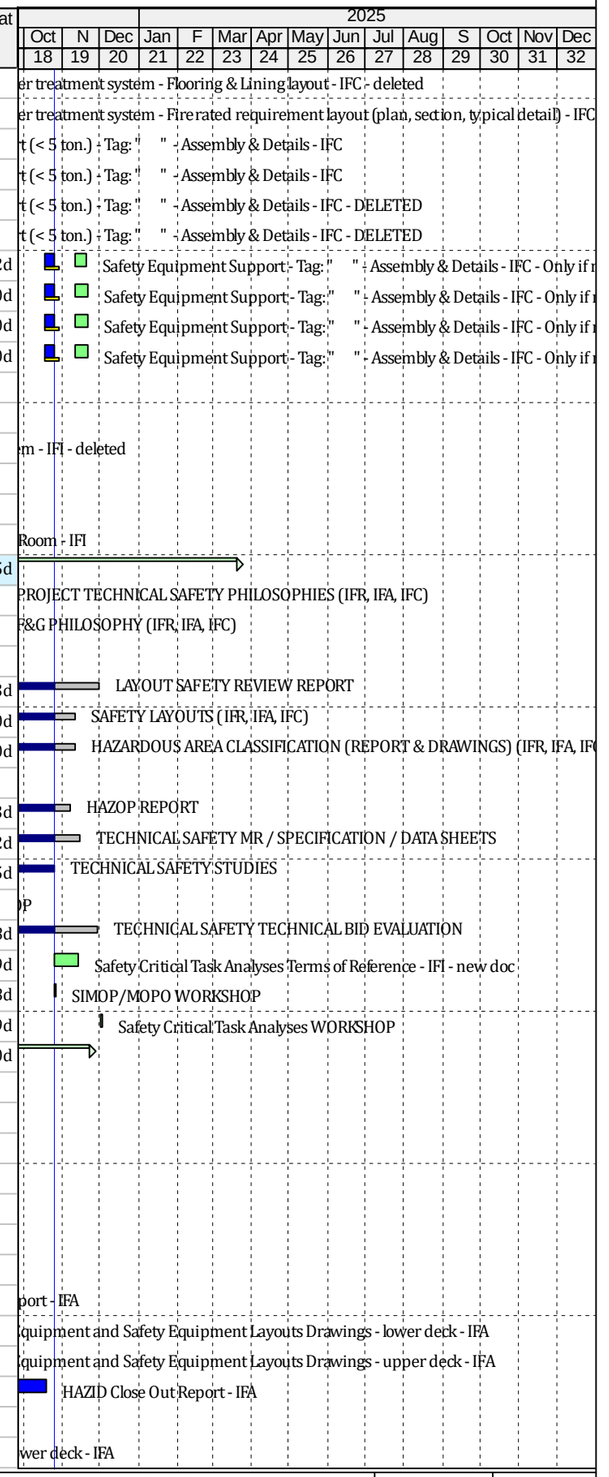


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-SAF-1250-A	Hazardous Area Classification Layout - section - IFA	10d	66d	20-Nov-23 A	09-Feb-24 A	25-Nov-23	06-Dec-23	
ENG-SAF-1310-A	F&G detectors Layout - lower deck - IFA	10d	71d	20-Nov-23 A	15-Feb-24 A	14-Nov-23	24-Nov-23	
ENG-SAF-1320-A	F&G detectors Layout - upper deck - IFA	10d	71d	20-Nov-23 A	15-Feb-24 A	14-Nov-23	24-Nov-23	
ENG-SAF-1240-A	Hazardous Area Classification Layout - upper deck - IFA - deleted	10d	10d	25-Nov-23 A	06-Dec-23 A	25-Nov-23	06-Dec-23	
ENG-SAF-1060-A	HAZOP Report - IFA	10d	13d	04-Dec-23 A	19-Dec-23 A	02-Dec-23	14-Dec-23	
ENG-SAF-1150-A	Assumption Register - IFA	17d	10d	04-Dec-23 A	15-Dec-23 A	27-Nov-23	16-Dec-23	
ENG-SAF-1060-A10	HAZOP WORKSHOP	5d	4d	04-Dec-23 A	08-Dec-23 A	27-Nov-23	01-Dec-23	
ENG-SAF-1400-A	LOPA Allocation report - IFA	15d	36d	18-Dec-23 A	01-Feb-24 A	02-Dec-23	20-Dec-23	
ENG-SAF-1360-A	FF and Safety Equipment Specifications - IFA	10d	121d	08-Jan-24 A	31-May-24 A	14-Nov-23	24-Nov-23	
ENG-SAF-1070-A	HAZOP Close Out Report - IFA	15d	195d	31-Jan-24 A	19-Sep-24 A	15-Dec-23	04-Jan-24	
ENG-SAF-1210-A	Fire and Explosion Risk Analys (FERA) report - IFA	20d	13d	31-Jan-24 A	14-Feb-24 A	01-Feb-24	23-Feb-24	
ENG-SAF-1030-A	Safety Critical ELEMENTS (SCE) and Performance Standard - IFA	15d	7d	20-Feb-24 A	27-Feb-24 A	02-Apr-24	18-Apr-24	
ENG-SAF-1220-A	Vent Gas Dispersion / and Potential Radiation Study - IFA	24d	11d	26-Feb-24 A	08-Mar-24 A	26-Feb-24	14-Mar-24	
ENG-SAF-1200-A	Quantified Risk Assessment (QRA) Report - IFA	10d	9d	18-Mar-24 A	27-Mar-24 A	07-Mar-24	18-Mar-24	
ENG-SAF-1160-A	Evacuation, Escape and Rescue Assessment (EERA) Report - IFA	15d	10d	08-Apr-24 A	18-Apr-24 A	07-Mar-24	23-Mar-24	
ENG-SAF-1370-A	TDS - FF and Safety Equipment - IFA	10d	26d	01-May-24 A	31-May-24 A	14-Nov-23	24-Nov-23	
ENG-SAF-1110-A	ALARP Terms of Reference - I FI	15d	25d	10-May-24 A	07-Jun-24 A	19-Apr-24	08-May-24	
ENG-SAF-1190-A	Dropped Object and Swinging Loads Study - IFA	10d	19d	10-May-24 A	31-May-24 A	24-Feb-24	06-Mar-24	
ENG-SAF-1450-A	Safety Critical Task Analyses Report - I FA	15d	114d	10-May-24 A	20-Sep-24 A	10-May-24	27-May-24	
ENG-SAF-1420-A	SIMOP/MOPO ToR - I FI	10d	38d	21-May-24 A	03-Jul-24 A	21-May-24	31-May-24	
ENG-SAF-1350-A	MR - FF and Safety Equipment MR - Issue for RfQ	10d	28d	01-Jun-24 A	03-Jul-24 A	14-Nov-23	24-Nov-23	
ENG-SAF-1180-A	Emergency Systems Survivability Assessment Report (ESSA) - IFA	15d	11d	10-Jun-24 A	21-Jun-24 A	19-Apr-24	08-May-24	
ENG-SAF-1430-A	SIMOP/MOPO report - IFA	10d	90d	14-Jun-24 A	27-Sep-24 A	14-Jun-24	25-Jun-24	
ENG-SAF-1470-A	MR - Safety Sign - Issue for RfQ	12d	98d	28-Jun-24 A	21-Oct-24 A	03-Jun-24	13-Jun-24	
ENG-SAF-1480-A	Safety Sign Specifications and Datasheets - IFA	10d	71d	28-Jun-24 A	19-Sep-24 A	03-Jun-24	13-Jun-24	
ENG-SAF-1330-A	safety sign Layout - lower deck - IFA	10d	68d	15-Jul-24 A	02-Oct-24 A	22-May-24	01-Jun-24	
ENG-SAF-1340-A	safety sign Layout - upper deck - IFA	10d	68d	15-Jul-24 A	02-Oct-24 A	22-May-24	01-Jun-24	
ENG-SAF-1460-A	Noise Assessment Study Report - IFA	20d	80d	15-Jul-24 A	16-Oct-24 A	17-Jun-24	09-Jul-24	
ENG-SAF-1440-A	SIMOP close out reports - IFA	10d	3d	24-Sep-24 A	27-Sep-24 A	26-Jun-24	06-Jul-24	
ENG-SAF-1000-A	Hazardous Material Register and Inventory - IFA	24d	6d	28-Sep-24 A	04-Oct-24 A	05-Mar-24	21-Mar-24	
ENG-SAF-1120-A	Design ALARP Demonstration Report - IFA	10d	10d	26-Oct-24	07-Nov-24	20-May-24	30-May-24	33d
ENG-SAF-1170-A	Emergency Response Plan - IFA	15d	15d	06-Nov-24	22-Nov-24	20-Jun-24	06-Jul-24	100d
Issue For Construction		419d	463d	09-Sep-23 A	20-Mar-25	28-Sep-23	18-Jan-25	33d
ENG-SAF-1080-B	HAZID Terms of Reference - IFC - to be deleted	0d	21d	09-Sep-23 A	03-Oct-23 A	04-Oct-23	04-Oct-23	
ENG-SAF-1020-B	Design HSSE plan - IFC	15d	65d	26-Sep-23 A	12-Dec-23 A	28-Sep-23	14-Oct-23	
ENG-SAF-1500-B	HSE Design Philosophy - IFC	15d	46d	28-Sep-23 A	21-Nov-23 A	16-Oct-23	02-Nov-23	
ENG-SAF-1050-B	HAZOP Terms of Reference - IFC - to be deleted	0d	20d	23-Oct-23 A	15-Nov-23 A	02-Dec-23	02-Dec-23	
ENG-SAF-1390-B	LOPA ToR - IFC - to be deleted	0d	20d	23-Oct-23 A	15-Nov-23 A	02-Dec-23	02-Dec-23	
ENG-SAF-1010-B	Fire Protection Philosophy - IFC	10d	261d	02-Nov-23 A	12-Sep-24 A	09-Nov-23	20-Nov-23	
ENG-SAF-1090-B	HAZID Report - IFC	10d	19d	02-Nov-23 A	23-Nov-23 A	26-Oct-23	07-Nov-23	
ENG-SAF-1040-B	HSSE Action Tracking Register and Close out report - IFC	305d	394d	30-Nov-23 A	20-Mar-25	18-Jan-24	18-Jan-25	33d
ENG-SAF-1150-B	Assumption Register - IFC	10d	119d	09-Jan-24 A	30-May-24 A	02-Jan-24	13-Jan-24	
ENG-SAF-1130-B	Hazardous Area Classification Schedule - IFC	10d	100d	22-Jan-24 A	21-May-24 A	20-Apr-24	03-May-24	
ENG-SAF-1060-B	HAZOP Report - IFC	10d	142d	25-Jan-24 A	12-Jul-24 A	29-Dec-23	11-Jan-24	
ENG-SAF-1290-B	Escape Routes, Fire Fighting, Life Saving Equipment and Safety Equipment Layouts Drawings - lower deck - IFC	10d	109d	04-Mar-24 A	12-Jul-24 A	26-Mar-24	08-Apr-24	
ENG-SAF-1300-B	Escape Routes, Fire Fighting, Life Saving Equipment and Safety Equipment Layouts Drawings - upper deck - IFC	10d	109d	04-Mar-24 A	12-Jul-24 A	26-Mar-24	08-Apr-24	

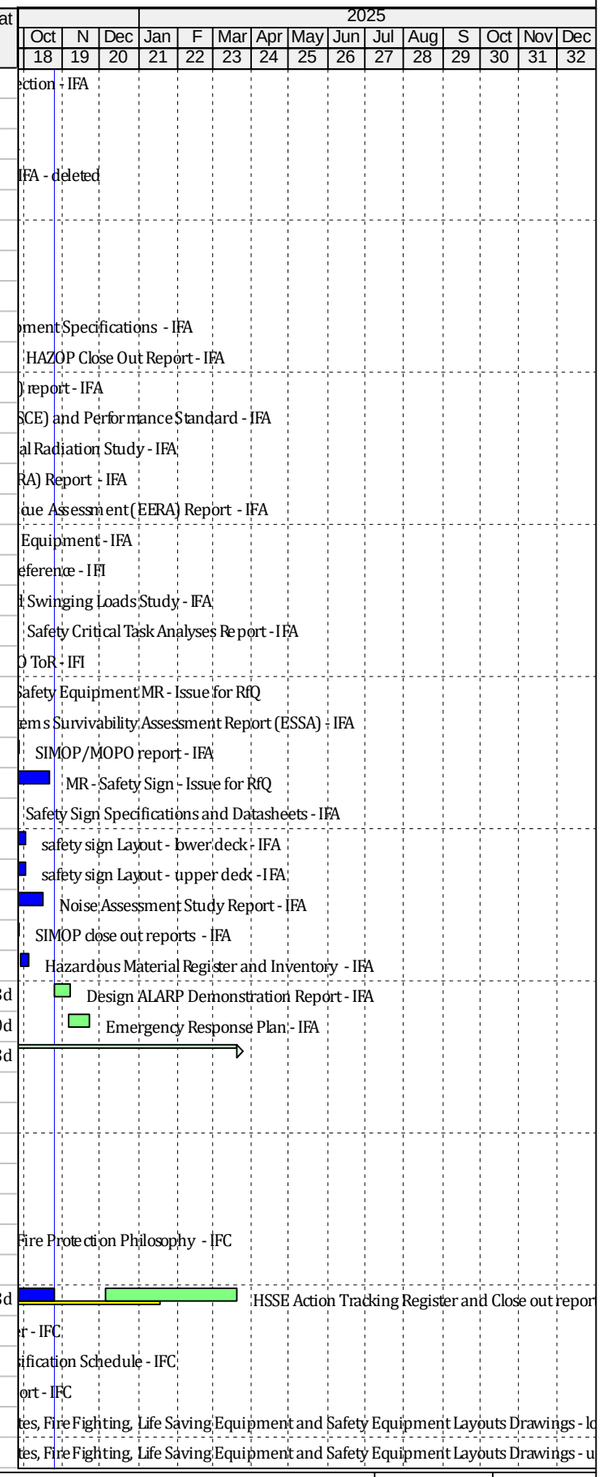

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-SAF-1310-B	F&G detectors Layout - lower deck - IFC	10d	105d	08-Mar-24 A	12-Jul-24 A	09-Apr-24	19-Apr-24	
ENG-SAF-1320-B	F&G detectors Layout - upper deck - IFC	10d	105d	08-Mar-24 A	12-Jul-24 A	09-Apr-24	19-Apr-24	
ENG-SAF-1230-B	Hazardous Area Classification Layout - lower deck - IFC	10d	193d	11-Mar-24 A	26-Oct-24	20-Apr-24	03-May-24	6d
ENG-SAF-1250-B	Hazardous Area Classification Layout - section - IFC	10d	205d	11-Mar-24 A	11-Nov-24	20-Apr-24	03-May-24	50d
ENG-SAF-1400-B	LOPA Allocation report - IFC	10d	23d	12-Mar-24 A	09-Apr-24 A	05-Jan-24	17-Jan-24	
ENG-SAF-1210-B	Fire and Explosion Risk Analys (FERA) report - IFC	15d	61d	18-Mar-24 A	31-May-24 A	20-Jun-24	06-Jul-24	
ENG-SAF-1030-B	Safety Critical ELEMENTS (SCE) and Performance Standard - IFC	10d	34d	27-Mar-24 A	09-May-24 A	15-May-24	25-May-24	
ENG-SAF-1220-B	Vent Gas Dispersion / and Potential Radiation Study - IFC	15d	27d	27-Mar-24 A	30-Apr-24 A	27-Mar-24	15-Apr-24	
ENG-SAF-1240-B	Hazardous Area Classification Layout - upper deck - IFC - deleted	10d	10d	20-Apr-24 A	03-May-24 A	20-Apr-24	03-May-24	
ENG-SAF-1160-B	Evacuation, Escape and Rescue Assessment (EERA) Report - IFC	10d	28d	07-May-24 A	07-Jun-24 A	09-May-24	20-May-24	
ENG-SAF-1200-B	Quantified Risk Assessment (QRA) Report - IFC	10d	27d	08-May-24 A	07-Jun-24 A	26-Apr-24	08-May-24	
ENG-SAF-1110-B	ALARP Terms of Reference - IFC - DELETED	10d	10d	21-May-24 A	31-May-24 A	21-May-24	31-May-24	
ENG-SAF-1420-B	SIMOP/MOPO ToR - IFC - to be deleted	0d	0d	13-Jun-24 A	13-Jun-24 A	13-Jun-24	13-Jun-24	
ENG-SAF-1190-B	Dropped Object and Swinging Loads Study - IFC	10d	28d	18-Jun-24 A	19-Jul-24 A	13-Apr-24	24-Apr-24	
ENG-SAF-1360-B	FF and Safety Equipment Specifications - IFC	10d	74d	18-Jun-24 A	12-Sep-24 A	20-Dec-23	03-Jan-24	
ENG-SAF-1370-B	TDS - FF and Safety Equipment - IFC	10d	22d	18-Jun-24 A	12-Jul-24 A	09-Apr-24	19-Apr-24	
ENG-SAF-1180-B	Emergency Systems Survivability Assessment Report (ESSA) - IFC	10d	91d	23-Jul-24 A	07-Nov-24	21-May-24	31-May-24	143d
ENG-SAF-1350-B	MR - FF and Safety Equipment MR - Issue for PO Placement	10d	50d	30-Jul-24 A	27-Sep-24 A	20-Apr-24	03-May-24	
ENG-SAF-1440-B	SIMOP close out reports - IFC DELETED	10d	3d	24-Sep-24 A	27-Sep-24 A	19-Jul-24	30-Jul-24	
ENG-SAF-1480-B	Safety Sign Specifications and Datasheets - IFC	10d	16d	08-Oct-24 A	25-Oct-24 A	26-Jun-24	06-Jul-24	
ENG-SAF-1070-B	HAZOP Close Out Report - IFC	10d	20d	15-Oct-24 A	07-Nov-24	18-Jan-24	29-Jan-24	143d
ENG-SAF-1340-B	safety sign Layout - upper deck - IFC	10d	15d	21-Oct-24 A	07-Nov-24	14-Jun-24	25-Jun-24	38d
ENG-SAF-1000-B	Hazardous Material Register and Inventory - IFC	10d	11d	25-Oct-24 A	07-Nov-24	05-Apr-24	16-Apr-24	143d
ENG-SAF-1100-B	HAZID Close Out Report - IFC	10d	15d	25-Oct-24 A	12-Nov-24	10-Nov-23	21-Nov-23	139d
ENG-SAF-1330-B	safety sign Layout - lower deck - IFC	10d	11d	25-Oct-24 A	07-Nov-24	14-Jun-24	25-Jun-24	38d
ENG-SAF-1430-B	SIMOP/MOPO report - IFC	10d	11d	25-Oct-24 A	07-Nov-24	08-Jul-24	18-Jul-24	53d
ENG-SAF-1450-B	Safety Critical Task Analyses Report - IFC	10d	11d	25-Oct-24 A	07-Nov-24	08-Jun-24	19-Jun-24	53d
ENG-SAF-1460-B	Noise Assessment Study Report - IFC	15d	15d	30-Oct-24	16-Nov-24	22-Jul-24	07-Aug-24	45d
ENG-SAF-1470-B	MR - Safety Sign - Issue for PO Placement	10d	10d	02-Nov-24	14-Nov-24	08-Jul-24	18-Jul-24	32d
ENG-SAF-1120-B	Design ALARP Demonstration Report - IFC	10d	10d	20-Nov-24	30-Nov-24	12-Jun-24	22-Jun-24	33d
ENG-SAF-1170-B	Emergency Response Plan - IFC	10d	10d	17-Dec-24	30-Dec-24	31-Jul-24	10-Aug-24	100d
Issue For Information		70d	89d	15-Aug-24 A	28-Nov-24	28-Jun-24	15-Jul-24	44d
ENG-SAF-1380-A	TBE - FF and Safety Equipment - IFI	15d	12d	15-Aug-24 A	29-Aug-24 A	28-Jun-24	15-Jul-24	
ENG-SAF-1490-A	TBE - Safety Signs - IFI	15d	15d	12-Nov-24	28-Nov-24	28-Jun-24	15-Jul-24	8d
Engineering Follow-Up		400d	395d	02-Oct-23 A	25-Apr-25	25-Sep-23	25-Apr-25	38d
PRO-EQ-MR06-1120	MR06 - SDL - HV Switchgear 66kV	400d	395d	02-Oct-23 A	25-Apr-25	25-Sep-23	25-Apr-25	38d
PRO-EQ-MR05-1050	MR05 - SDL - Transformer Main 66/6.6kV	300d	297d	16-Oct-23 A	17-Dec-24	11-Oct-23	17-Dec-24	38d
PRO-EQ-MR05-1120	MR05 - SDL - Transformer Aux. 6.6/0.4kV	300d	295d	16-Oct-23 A	13-Dec-24	09-Oct-23	13-Dec-24	38d
PRO-EQ-MR05-1190	MR05 - SDL - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	300d	295d	16-Oct-23 A	13-Dec-24	09-Oct-23	13-Dec-24	38d
PRO-EQ-MR06-1050	MR05 - SDL - Neutral earthing resistor 400A	300d	301d	16-Oct-23 A	23-Dec-24	17-Oct-23	23-Dec-24	38d
PRO-EQ-MR01-1050	MR01 - SDL - H2 Storage Vessel	360d	353d	24-Oct-23 A	19-Mar-25	13-Oct-23	19-Mar-25	38d
PRO-EQ-MR11-1050	MR11 - SDL - Waste Water Tank	58d	235d	12-Dec-23 A	14-Nov-24	12-Dec-23	14-Nov-24	75d
PRO-EQ-MR09-1050	MR09 - SDL - Essential process load distribution panel	143d	217d	21-Dec-23 A	29-Oct-24	26-Jan-24	06-Aug-24	52d
PRO-EQ-MR09-1120	MR09 - SDL - Process load distribution panel	107d	220d	21-Dec-23 A	04-Nov-24	24-Jan-24	02-Aug-24	52d
PRO-EQ-MR09-1190	MR09 - SDL - Distribution board for top deck lights (820m2)	143d	217d	21-Dec-23 A	29-Oct-24	26-Jan-24	06-Aug-24	52d
PRO-EQ-MR09-1260	MR09 - SDL - Distribution board for lower deck lights (850m 2)	143d	217d	21-Dec-23 A	29-Oct-24	26-Jan-24	06-Aug-24	52d

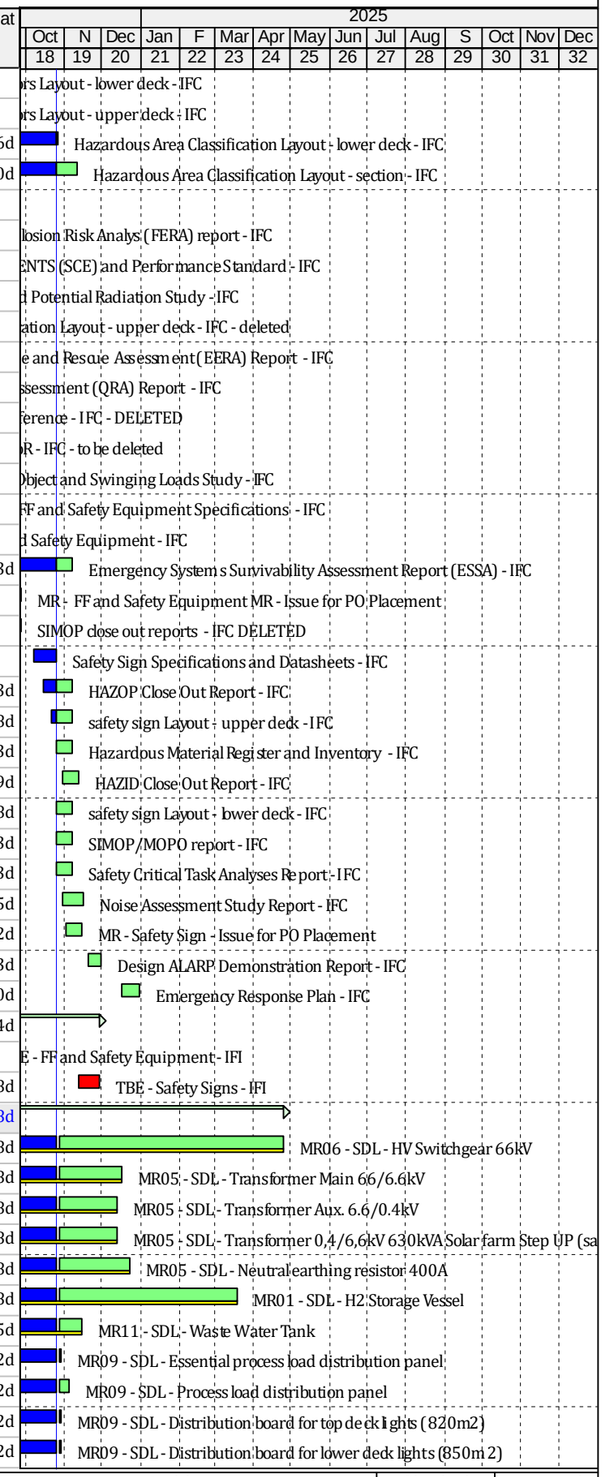

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR09-1330	MR09 - SDL - Distribution board for stair tower lights (25m2)	143d	217d	21-Dec-23 A	29-Oct-24	26-Jan-24	06-Aug-24	52d
PRO-EQ-MR09-1400	MR09 - SDL - Distribution board for Relief valve platform lights (32m2)	143d	217d	21-Dec-23 A	29-Oct-24	26-Jan-24	06-Aug-24	52d
PRO-EQ-MR09-1470	MR09 - SDL - Distribution board for Emergency light	143d	217d	21-Dec-23 A	29-Oct-24	26-Jan-24	06-Aug-24	52d
PRO-EQ-MR06-1190	MR06 - SDL - MV Switchgear 6.6kV	220d	221d	22-Dec-23 A	06-Nov-24	05-Oct-23	06-Nov-24	38d
PRO-EQ-MR06-1260	MR06 - SDL - Low Voltage Switchgear	217d	218d	22-Dec-23 A	31-Oct-24	09-Oct-23	31-Oct-24	38d
PRO-EQ-MR07-1050	MR07 - SDL - Shelter for plant instrument room	181d	206d	11-Jan-24 A	30-Oct-24	12-Jan-24	23-Oct-24	34d
PRO-EQ-MR07-1120	MR07 - SDL - Shelter for LV switchgear room	193d	207d	11-Jan-24 A	31-Oct-24	08-Jan-24	17-Oct-24	34d
PRO-EQ-MR07-1190	MR07 - SDL - Shelter for HV switchgear room	195d	207d	11-Jan-24 A	31-Oct-24	08-Jan-24	17-Oct-24	34d
PRO-EQ-MR07-1260	MR07 - SDL - Shelter for AC UPS fitted with UPS system (exc. Nav.Aids. UPS & DC system)	196d	207d	11-Jan-24 A	31-Oct-24	08-Jan-24	17-Oct-24	34d
PRO-EQ-MR08-1050	MR08 - SDL - DC UPS panel board Feeder A 10kW & Feeder B10kW with common battery back up (225Ah)	145d	205d	12-Jan-24 A	30-Oct-24	04-Dec-23	18-Sep-24	38d
PRO-EQ-MR01-1120	MR01 - SDL - Hydrogen Vent KO Drum	171d	206d	26-Jan-24 A	15-Nov-24	12-Feb-24	15-Nov-24	38d
PRO-EQ-MR19-1050	MR19 - SDL - SDV & BDV	225d	222d	01-Feb-24 A	13-Dec-24	08-Jan-24	13-Dec-24	11d
PRO-EQ-MR08-1120	MR08 - SDL - AC UPS for CCS, SIS field instruments) Rectifier 15 kW & 15kW Bypass	156d	178d	21-Feb-24 A	31-Oct-24	20-Dec-23	03-Oct-24	38d
PRO-EQ-MR08-1190	MR08 - SDL - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	167d	178d	22-Feb-24 A	04-Nov-24	09-Jan-24	18-Oct-24	100d
PRO-EQ-MR02-1050	MR02 - SDL - Electro-Chlorination Unit	164d	189d	23-Feb-24 A	20-Nov-24	25-Jan-24	20-Nov-24	38d
PRO-EQ-MR02-1120	MR02 - SDL - Ultra Filtration Unit	169d	189d	23-Feb-24 A	20-Nov-24	18-Jan-24	20-Nov-24	38d
PRO-EQ-MR02-1190	MR02 - SDL - UV Water Filter	169d	189d	23-Feb-24 A	20-Nov-24	18-Jan-24	20-Nov-24	38d
PRO-EQ-MR02-1260	MR02 - SDL - Sea Water Coarse Filter Package	83d	174d	23-Feb-24 A	29-Oct-24	26-Jan-24	06-Aug-24	38d
PRO-EQ-MR02-1330	MR02 - SDL - Fresh Water Pump (Gear pumps)	30d	202d	23-Feb-24 A	09-Dec-24	28-Feb-24	10-Apr-24	38d
PRO-EQ-MR03-1050	MR03 - SDL - Filtered Seawater Tank	160d	190d	23-Feb-24 A	21-Nov-24	12-Jan-24	21-Nov-24	38d
PRO-EQ-MR03-1120	MR03 - SDL - Fresh Water Tank	174d	185d	23-Feb-24 A	14-Nov-24	12-Jan-24	14-Nov-24	38d
PRO-EQ-MR13-1050	MR13 - SDL - Instrument Air Package	167d	177d	23-Feb-24 A	04-Nov-24	29-Nov-23	18-Oct-24	38d
PRO-EQ-MR17-1050	MR17 - SDL - Container 40' ISO for Water treatment system	120d	175d	23-Feb-24 A	30-Oct-24	12-Jan-24	23-Oct-24	34d
PRO-EQ-MR02-1510	MR02 - SDL - Desalination Unit (SWRO)	164d	188d	23-Feb-24 A	19-Nov-24	24-Jan-24	19-Nov-24	11d
PRO-EQ-MR11-1120	MR11 - SDL - Instrument Air Receiver	164d	176d	26-Feb-24 A	04-Nov-24	06-Dec-23	25-Oct-24	38d
PRO-EQ-MR10-1050	MR10 - SDL - Telecom System	166d	184d	27-Feb-24 A	15-Nov-24	29-Jan-24	15-Nov-24	34d
PRO-EQ-MR19-1230	MR19 - SDL - Pressure Safety Valves	190d	202d	08-Mar-24 A	23-Dec-24	16-Jan-24	23-Dec-24	11d
PRO-EQ-MR06-1330	MR06 - SDL - Solar farm in-feed power isolator panel 600x400x400	96d	159d	18-Mar-24 A	30-Oct-24	29-Jan-24	07-Aug-24	38d
PRO-EQ-MR06-1400	MR06 - SDL - Automation systems CCS-SIS & EMS	167d	165d	18-Mar-24 A	08-Nov-24	09-Oct-23	08-Nov-24	38d
PRO-EQ-MR19-1150	MR19 - SDL - Actuated Control Valves	196d	182d	08-Apr-24 A	23-Dec-24	16-Jan-24	23-Dec-24	11d
PRO-EQ-MR20-1050	MR20 - SDL - Nav. Aids & anti collision system (incl. AC UPS)	72d	143d	12-Apr-24 A	04-Nov-24	24-Jan-24	02-Aug-24	38d
PRO-EQ-MR16-1050	MR16 - SDL - Hydrogen Vent	109d	112d	27-May-24 A	30-Oct-24	04-Dec-23	09-Oct-24	38d
PRO-EQ-MR14-1050	MR14 - SDL - Seawater Intake Pump - Seawater Intake Pump - Vertical suspended motor type	203d	203d	17-Jun-24 A	03-Apr-25	21-Dec-23	11-Apr-25	11d
PRO-EQ-MR12-1050	MR12 - SDL - Davit Crane	85d	85d	01-Jul-24 A	28-Oct-24	28-Feb-24	30-Sep-24	38d
PRO-EQ-MR18-1050	MR18 - SDL - JB with disconnector for Temporary Generator	86d	127d	30-Aug-24 A	03-Mar-25	26-Feb-24	14-Aug-24	75d
PRO-EQ-MR15-1050	MR15 - SDL - Liferaft	40d	40d	28-Oct-24	23-Dec-24	30-May-24	24-Jul-24	60d
Engineering Support during Fabrication / Construction Engineering		430d	459d	23-Oct-23 A	02-May-25	28-Oct-23	02-Apr-25	33d
ENG-CONSTENG-1000	Construction Engineering - Management & Administration	430d	435d	23-Oct-23 A	31-Mar-25	28-Oct-23	31-Mar-25	27d
ENG-CONSTENG-1010	Construction Engineering - Structural & Civil	305d	409d	17-Nov-23 A	25-Mar-25	28-Oct-23	30-Oct-24	19d
ENG-CONSTENG-1050	Construction Engineering - Methods	218d	301d	06-May-24 A	02-May-25	03-Apr-24	02-Apr-25	3d
ENG-CONSTENG-1020	Construction Engineering - Piping & Pressure Vessels	154d	82d	10-Jun-24 A	13-Sep-24 A	14-Mar-24	26-Nov-24	
ENG-CONSTENG-1030	Construction Engineering - Mechanical	156d	179d	24-Jun-24 A	24-Jan-25	07-May-24	04-Dec-24	82d
ENG-CONSTENG-1040	Construction Engineering - E&I, Telecomm, F&G & Automation	41d	120d	15-Jul-24 A	03-Dec-24	15-Jul-24	03-Dec-24	154d
Engineering Load-Out, Transport & Installation		351d	424d	04-Dec-23 A	02-May-25	22-Jan-24	14-Feb-25	76d
Transportation & Installation		351d	424d	04-Dec-23 A	02-May-25	22-Jan-24	14-Feb-25	76d
Issue For Approval		332d	405d	04-Dec-23 A	05-Apr-25	22-Jan-24	29-Nov-24	95d

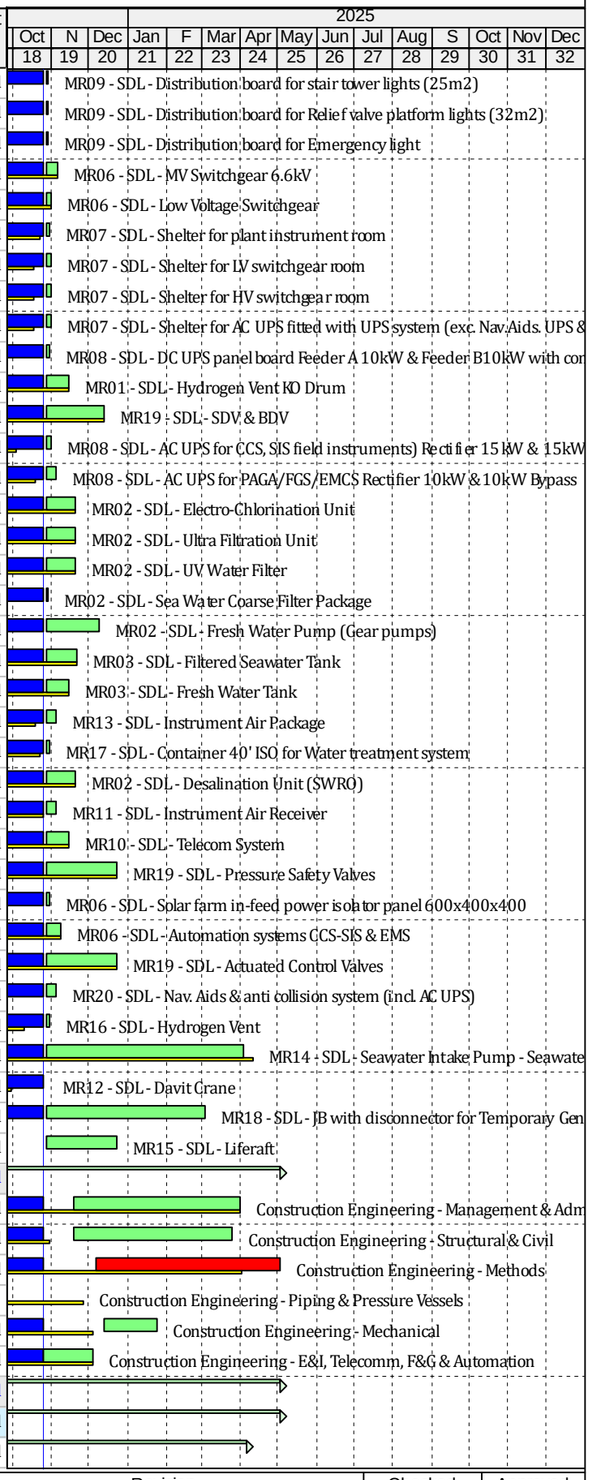

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-T&I-1140-A	SPECIFICATION FOR TP, TOPSIDE & CAISSONS TRANSPORTATION AND INSTALLATION - IFA	52d	6d	04-Dec-23 A	11-Dec-23 A	02-Sep-24	31-Oct-24	
ENG-T&I-1150-A	BARGE LAYOUT - IFA	23d	5d	08-Jan-24 A	12-Jan-24 A	22-Jan-24	16-Feb-24	
ENG-T&I-1160-A	TOPSIDE - BLPH UPPER GRILLAGE - IFA - Deleted	20d	20d	22-Jan-24 A	13-Feb-24 A	22-Jan-24	13-Feb-24	
ENG-T&I-1170-A	TOPSIDE - BLPH UPPER GRILLAGE - IFA - Deleted	20d	20d	22-Jan-24 A	13-Feb-24 A	22-Jan-24	13-Feb-24	
ENG-T&I-1180-A	TOPSIDE - BLPH UPPER GRILLAGE - IFA - Deleted	20d	20d	22-Jan-24 A	13-Feb-24 A	22-Jan-24	13-Feb-24	
ENG-T&I-1190-A	TOPSIDE - BLPH UPPER GRILLAGE - IFA - Deleted	20d	20d	22-Jan-24 A	13-Feb-24 A	22-Jan-24	13-Feb-24	
ENG-T&I-1200-A	TOPSIDE - BLPH UPPER GRILLAGE - IFA - Deleted	20d	20d	22-Jan-24 A	13-Feb-24 A	22-Jan-24	13-Feb-24	
ENG-T&I-1290-A	TOPSIDE - INSTALLATION AIDS - IFA - deleted	27d	27d	14-Feb-24 A	15-Mar-24 A	14-Feb-24	15-Mar-24	
ENG-T&I-1300-A	TOPSIDE - INSTALLATION AIDS - IFA - deleted	27d	27d	14-Feb-24 A	15-Mar-24 A	14-Feb-24	15-Mar-24	
ENG-T&I-1310-A	TOPSIDE - INSTALLATION AIDS (STABBING GUIDES) - IFA - deleted	27d	27d	14-Feb-24 A	15-Mar-24 A	14-Feb-24	15-Mar-24	
ENG-T&I-1320-A	TOPSIDE - RIGGING PLATFORM - IFA - deleted	27d	27d	14-Feb-24 A	15-Mar-24 A	14-Feb-24	15-Mar-24	
ENG-T&I-1330-A	TOPSIDE – PIN CATCHERS - IFA - deleted	17d	17d	26-Feb-24 A	15-Mar-24 A	26-Feb-24	15-Mar-24	
ENG-T&I-1430-A	TP - INSTALLATION AIDS - IFA	20d	175d	02-Mar-24 A	27-Sep-24 A	02-Mar-24	29-Mar-24	
ENG-T&I-1030-A	TP - INSTALLATION AIDS DESIGN REPORT - IFA - to be deleted	110d	150d	18-Mar-24 A	13-Sep-24 A	18-Mar-24	13-Sep-24	
ENG-T&I-1360-A	TP - UPPER GRILLAGE - PLAN VIEW - IFA	24d	7d	22-Apr-24 A	30-Apr-24 A	02-Mar-24	29-Mar-24	
ENG-T&I-1370-A	TP - UPPER GRILLAGE - SECTIONS - IFA	24d	7d	22-Apr-24 A	30-Apr-24 A	02-Mar-24	29-Mar-24	
ENG-T&I-1380-A	TP - UPPER GRILLAGE - SECTIONS AND DETAILS - IFA	24d	7d	22-Apr-24 A	30-Apr-24 A	02-Mar-24	29-Mar-24	
ENG-T&I-1420-A	TP - INSTALLATION AIDS - STABBING GUIDES - ASSEMBLY AND DETAILS - IFA	24d	7d	05-Jul-24 A	12-Jul-24 A	02-Mar-24	29-Mar-24	
ENG-T&I-1000-A	TOPSIDE - INSTALLATION AIDS DESIGN REPORT - IFA	70d	119d	30-Aug-24 A	21-Jan-25	18-Mar-24	31-Jul-24	5d
ENG-T&I-1280-A	TOPSIDE - INSTALLATION AIDS - IFA	27d	76d	30-Aug-24 A	27-Nov-24	14-Feb-24	15-Mar-24	85d
ENG-T&I-1010-A	TOPSIDE - GRILLAGE AND SEAFASTENING DESIGN REPORT - IFA	81d	81d	26-Oct-24	03-Feb-25	19-Mar-24	13-Jul-24	3d
ENG-T&I-1040-A	TP - GRILLAGE AND SEAFASTENING DESIGN REPORT - IFA	106d	106d	26-Oct-24	04-Mar-25	18-Mar-24	13-Sep-24	2d
ENG-T&I-1060-A	CAISSONS - INSTALLATION AIDS DESIGN REPORT - IFA	108d	108d	26-Oct-24	06-Mar-25	18-Mar-24	30-Sep-24	2d
ENG-T&I-1070-A	CAISSONS - GRILLAGE AND SEAFASTENING DESIGN REPORT - IFA	110d	110d	26-Oct-24	08-Mar-25	18-Mar-24	30-Sep-24	4d
ENG-T&I-1090-A	TRANSPORT BARGE STABILITY AND BOLLARD PULL ANALYSIS - IFA	34d	34d	26-Oct-24*	05-Dec-24	02-Sep-24	18-Oct-24	72d
ENG-T&I-1100-A	BARGE INTEGRITY CHECK - IFA	114d	114d	26-Oct-24	13-Mar-25	18-Mar-24	29-Nov-24	5d
ENG-T&I-1210-A	TOPSIDE - BLPH LOWER GRILLAGE - IFA	15d	15d	26-Oct-24*	13-Nov-24	22-Jan-24	13-Feb-24	21d
ENG-T&I-1220-A	TOPSIDE - BLPH LOWER GRILLAGE - IFA	18d	18d	26-Oct-24	16-Nov-24	22-Jan-24	13-Feb-24	43d
ENG-T&I-1230-A	TOPSIDE - BLPH LOWER GRILLAGE - IFA	18d	18d	26-Oct-24	16-Nov-24	22-Jan-24	13-Feb-24	43d
ENG-T&I-1240-A	TOPSIDE - SEA FASTENING DRAWINGS - IFA	15d	15d	26-Oct-24	13-Nov-24	22-Jan-24	13-Feb-24	21d
ENG-T&I-1250-A	TOPSIDE - SEA FASTENING DRAWINGS - IFA	15d	15d	26-Oct-24	13-Nov-24	22-Jan-24	13-Feb-24	21d
ENG-T&I-1260-A	TOPSIDE - SEA FASTENING DRAWINGS - IFA	15d	15d	26-Oct-24	13-Nov-24	22-Jan-24	13-Feb-24	21d
ENG-T&I-1270-A	TOPSIDE - SEA FASTENING DRAWINGS - IFA	15d	15d	26-Oct-24	13-Nov-24	22-Jan-24	13-Feb-24	21d
ENG-T&I-1390-A	TP - SEA FASTENING DRAWINGS - IFA	20d	20d	26-Oct-24*	19-Nov-24	02-Mar-24	29-Mar-24	51d
ENG-T&I-1400-A	TP - SEA FASTENING DRAWINGS - IFA	20d	20d	26-Oct-24	19-Nov-24	02-Mar-24	29-Mar-24	51d
ENG-T&I-1410-A	TP - SEA FASTENING DRAWINGS - IFA	20d	20d	26-Oct-24	19-Nov-24	02-Mar-24	29-Mar-24	61d
ENG-T&I-1440-A	TP - INSTALLATION AIDS - IFA	20d	20d	26-Oct-24	19-Nov-24	02-Mar-24	29-Mar-24	91d
ENG-T&I-1470-A	CAISSONS - GRILLAGE - IFA	14d	14d	26-Oct-24*	12-Nov-24	02-Apr-24	19-Apr-24	95d
ENG-T&I-1480-A	CAISSONS - SEA FASTENING DRAWINGS - IFA	14d	14d	26-Oct-24	12-Nov-24	02-Apr-24	19-Apr-24	95d
ENG-T&I-1490-A	CAISSONS - INSTALLATION AIDS - IFA	13d	13d	26-Oct-24	11-Nov-24	02-Apr-24	19-Apr-24	103d
ENG-T&I-1460-A	TP - INSTALLATION AIDS - IFA	20d	20d	26-Oct-24	19-Nov-24	02-Mar-24	29-Mar-24	96d
ENG-T&I-1450-A	TP - INSTALLATION AIDS - IFA	20d	20d	26-Oct-24	19-Nov-24	02-Mar-24	29-Mar-24	96d
ENG-T&I-1500-A	CAISSONS - INSTALLATION AIDS - IFA	13d	13d	26-Oct-24	11-Nov-24	02-Apr-24	19-Apr-24	103d
ENG-T&I-1510-A	CAISSONS - INSTALLATION AIDS - IFA	13d	13d	26-Oct-24	11-Nov-24	02-Apr-24	19-Apr-24	103d
ENG-T&I-1050-A	TP - LOAD OUT MANUAL INCLUDING BALLAST SEQUENCE - IFA	106d	106d	30-Oct-24*	07-Mar-25	01-Jul-24	29-Nov-24	19d
ENG-T&I-1080-A	CAISSONS - LOAD OUT MANUAL INCLUDING BALLAST SEQUENCE - IFA	97d	97d	15-Nov-24*	12-Mar-25	01-Jul-24	15-Nov-24	20d

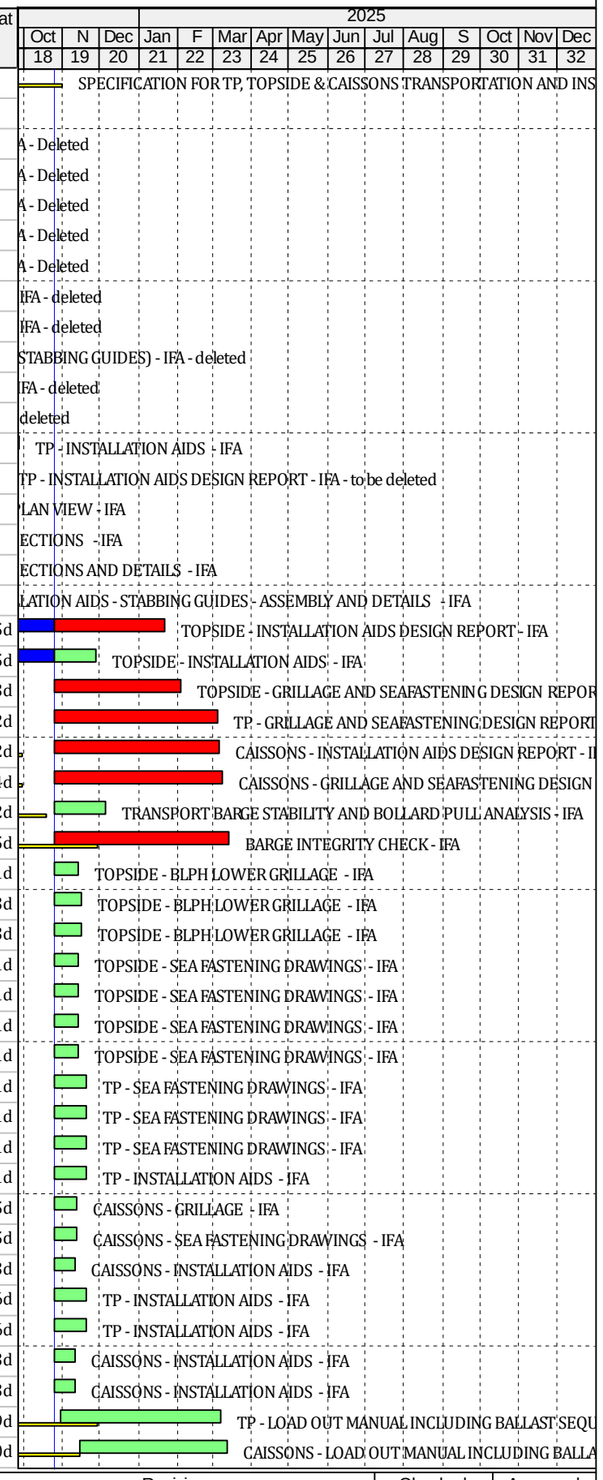


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-T&I-1020-A	TOPSIDE - LOAD OUT MANUAL INCLUDING BALLAST SEQUENCE - IFA	98d	98d	25-Nov-24*	22-Mar-25	01-Jul-24	15-Nov-24	11d
ENG-T&I-1110-A	TRANSPORT MANUAL - IFA	21d	21d	31-Dec-24*	25-Jan-25	02-Sep-24	30-Sep-24	19d
ENG-T&I-1120-A	TOPSIDE YARD CHECKLIST - IFA	45d	45d	31-Dec-24	22-Feb-25	02-Sep-24	15-Nov-24	19d
ENG-T&I-1130-A	TP & CAISSONS YARD CHECKLIST - IFA	45d	45d	31-Dec-24	22-Feb-25	02-Sep-24	15-Nov-24	19d
ENG-T&I-1340-A	PBY YARD – BARGE MOORING PLAN 1 - IFA	20d	20d	14-Mar-25	05-Apr-25	16-Sep-24	11-Oct-24	3d
ENG-T&I-1350-A	PBY YARD – BARGE MOORING PLAN 2 - IFA	20d	20d	14-Mar-25	05-Apr-25	16-Sep-24	11-Oct-24	95d
Issue For Construction		326d	385d	24-Jan-24 A	02-May-25	16-Mar-24	14-Feb-25	3d
ENG-T&I-1150-B	BARGE LAYOUT - IFC	27d	217d	24-Jan-24 A	08-Oct-24 A	18-Mar-24	19-Apr-24	
ENG-T&I-1140-B	SPECIFICATION FOR TP, TOPSIDE & CAISSONS TRANSPORTATION AND INSTALLATION - IFC	49d	174d	04-Mar-24 A	27-Sep-24 A	02-Dec-24	31-Jan-25	
ENG-T&I-1160-B	TOPSIDE - BLPH UPPER GRILLAGE - IFC - DELETED	28d	28d	16-Mar-24 A	19-Apr-24 A	16-Mar-24	19-Apr-24	
ENG-T&I-1170-B	TOPSIDE - BLPH UPPER GRILLAGE - IFC - DELETED	28d	28d	16-Mar-24 A	19-Apr-24 A	16-Mar-24	19-Apr-24	
ENG-T&I-1180-B	TOPSIDE - BLPH UPPER GRILLAGE - IFC - DELETED	28d	28d	16-Mar-24 A	19-Apr-24 A	16-Mar-24	19-Apr-24	
ENG-T&I-1190-B	TOPSIDE - BLPH UPPER GRILLAGE - IFC - DELETED	28d	28d	16-Mar-24 A	19-Apr-24 A	16-Mar-24	19-Apr-24	
ENG-T&I-1200-B	TOPSIDE - BLPH UPPER GRILLAGE - IFC - DELETED	28d	28d	16-Mar-24 A	19-Apr-24 A	16-Mar-24	19-Apr-24	
ENG-T&I-1290-B	TOPSIDE - INSTALLATION AIDS - IFC - deleted	24d	24d	11-Apr-24 A	10-May-24 A	11-Apr-24	10-May-24	
ENG-T&I-1300-B	TOPSIDE - INSTALLATION AIDS - IFC - deleted	24d	24d	11-Apr-24 A	10-May-24 A	11-Apr-24	10-May-24	
ENG-T&I-1310-B	TOPSIDE - INSTALLATION AIDS (STABBING GUIDES) - IFC - deleted	24d	24d	11-Apr-24 A	10-May-24 A	11-Apr-24	10-May-24	
ENG-T&I-1320-B	TOPSIDE - RIGGING PLATFORM - IFC - deleted	24d	24d	11-Apr-24 A	10-May-24 A	11-Apr-24	10-May-24	
ENG-T&I-1330-B	TOPSIDE – PIN CATCHERS - IFC - deleted	19d	19d	17-Apr-24 A	10-May-24 A	17-Apr-24	10-May-24	
ENG-T&I-1360-B	TP - UPPER GRILLAGE - PLAN VIEW - IFC	25d	167d	13-May-24 A	25-Nov-24	03-May-24	31-May-24	81d
ENG-T&I-1370-B	TP - UPPER GRILLAGE - SECTIONS - IFC	37d	160d	21-May-24 A	25-Nov-24	03-May-24	31-May-24	81d
ENG-T&I-1380-B	TP - UPPER GRILLAGE - SECTIONS AND DETAILS - IFC	25d	160d	21-May-24 A	25-Nov-24	03-May-24	31-May-24	81d
ENG-T&I-1420-B	TP - INSTALLATION AIDS - STABBING GUIDES - ASSEMBLY AND DETAILS - IFC	25d	32d	24-Jul-24 A	30-Aug-24 A	03-May-24	31-May-24	
ENG-T&I-1030-B	TP - INSTALLATION AIDS DESIGN REPORT - IFC	28d	39d	14-Oct-24 A	28-Nov-24	14-Oct-24	15-Nov-24	108d
ENG-T&I-1430-B	TP - INSTALLATION AIDS - IFC	25d	25d	26-Oct-24	25-Nov-24	03-May-24	31-May-24	111d
ENG-T&I-1470-B	CAISSONS - GRILLAGE - IFC	27d	27d	13-Nov-24	13-Dec-24	22-May-24	21-Jun-24	95d
ENG-T&I-1480-B	CAISSONS - SEA FASTENING DRAWINGS - IFC	27d	27d	13-Nov-24	13-Dec-24	22-May-24	21-Jun-24	95d
ENG-T&I-1490-B	CAISSONS - INSTALLATION AIDS - IFC	20d	20d	13-Nov-24	05-Dec-24	22-May-24	21-Jun-24	102d
ENG-T&I-1500-B	CAISSONS - INSTALLATION AIDS - IFC	20d	20d	13-Nov-24	05-Dec-24	22-May-24	21-Jun-24	102d
ENG-T&I-1210-B	TOPSIDE - BLPH LOWER GRILLAGE - IFC	25d	25d	14-Nov-24	12-Dec-24	16-Mar-24	19-Apr-24	46d
ENG-T&I-1240-B	TOPSIDE - SEA FASTENING DRAWINGS - IFC	25d	25d	14-Nov-24	12-Dec-24	16-Mar-24	19-Apr-24	21d
ENG-T&I-1250-B	TOPSIDE - SEA FASTENING DRAWINGS - IFC	25d	25d	14-Nov-24	12-Dec-24	16-Mar-24	19-Apr-24	21d
ENG-T&I-1260-B	TOPSIDE - SEA FASTENING DRAWINGS - IFC	20d	20d	14-Nov-24	06-Dec-24	16-Mar-24	19-Apr-24	21d
ENG-T&I-1270-B	TOPSIDE - SEA FASTENING DRAWINGS - IFC	20d	20d	14-Nov-24	06-Dec-24	16-Mar-24	19-Apr-24	21d
ENG-T&I-1220-B	TOPSIDE - BLPH LOWER GRILLAGE - IFC	25d	25d	18-Nov-24	16-Dec-24	16-Mar-24	19-Apr-24	43d
ENG-T&I-1230-B	TOPSIDE - BLPH LOWER GRILLAGE - IFC	25d	25d	18-Nov-24	16-Dec-24	16-Mar-24	19-Apr-24	43d
ENG-T&I-1390-B	TP - SEA FASTENING DRAWINGS - IFC	25d	25d	20-Nov-24	18-Dec-24	03-May-24	31-May-24	61d
ENG-T&I-1440-B	TP - INSTALLATION AIDS - IFC	25d	25d	20-Nov-24	18-Dec-24	03-May-24	31-May-24	91d
ENG-T&I-1450-B	TP - INSTALLATION AIDS - IFC	20d	20d	20-Nov-24	12-Dec-24	03-May-24	31-May-24	96d
ENG-T&I-1460-B	TP - INSTALLATION AIDS - IFC	20d	20d	20-Nov-24	12-Dec-24	03-May-24	31-May-24	96d
ENG-T&I-1510-B	CAISSONS - INSTALLATION AIDS - IFC	20d	20d	20-Nov-24	12-Dec-24	22-May-24	21-Jun-24	96d
ENG-T&I-1280-B	TOPSIDE - INSTALLATION AIDS - IFC	24d	24d	28-Nov-24	27-Dec-24	11-Apr-24	10-May-24	85d
ENG-T&I-1400-B	TP - SEA FASTENING DRAWINGS - IFC	25d	25d	02-Dec-24	02-Jan-25	03-May-24	31-May-24	51d
ENG-T&I-1410-B	TP - SEA FASTENING DRAWINGS - IFC	25d	25d	02-Dec-24	02-Jan-25	03-May-24	31-May-24	51d
ENG-T&I-1090-B	TRANSPORT BARGE STABILITY AND BOLLARD PULL ANALYSIS - IFC	15d	15d	06-Dec-24	23-Dec-24	13-Nov-24	29-Nov-24	87d
ENG-T&I-1000-B	TOPSIDE - INSTALLATION AIDS DESIGN REPORT - IFC	26d	26d	22-Jan-25	20-Feb-25	29-Aug-24	27-Sep-24	40d

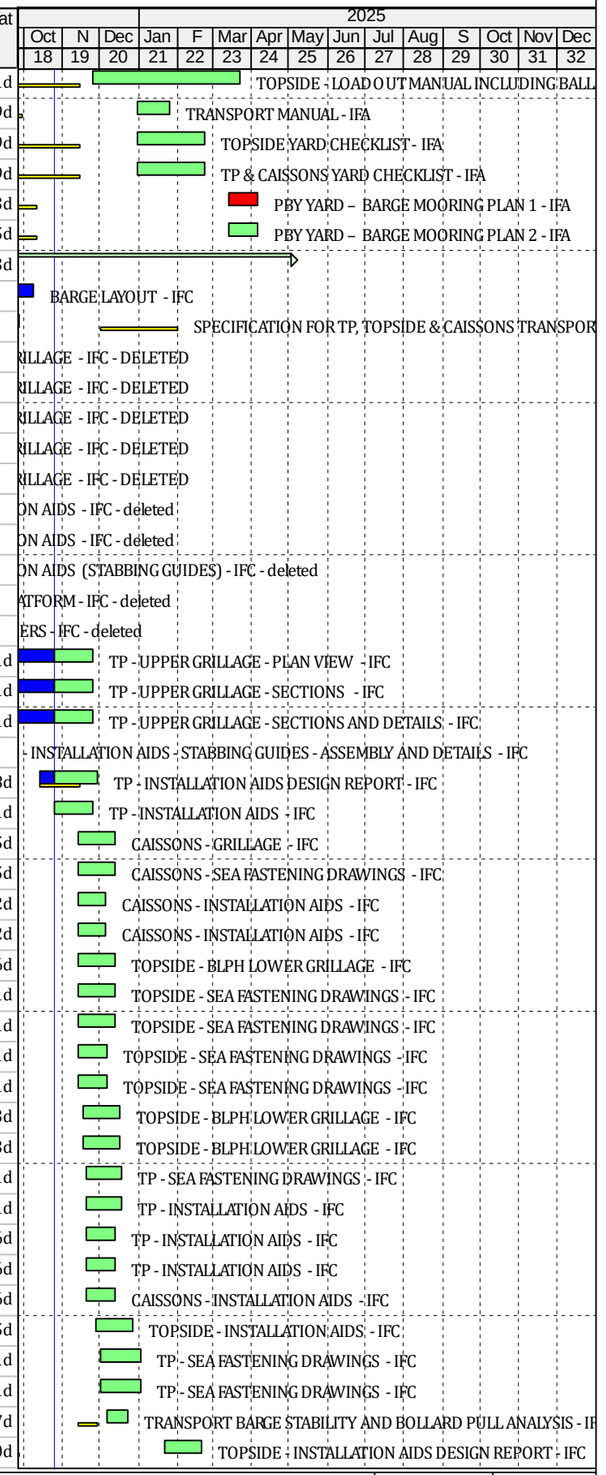


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
ENG-T&I-1110-B	TRANSPORT MANUAL - IFC	15d	15d	27-Jan-25	12-Feb-25	30-Oct-24	16-Nov-24	47d
ENG-T&I-1010-B	TOPSIDE - GRILLAGE AND SEAFASTENING DESIGN REPORT - IFC	20d	20d	04-Feb-25	26-Feb-25	26-Jul-24	28-Aug-24	3d
ENG-T&I-1120-B	TOPSIDE YARD CHECKLIST - IFC	30d	30d	24-Feb-25	29-Mar-25	16-Dec-24	31-Jan-25	28d
ENG-T&I-1130-B	TP & CAISSONS YARD CHECKLIST - IFC	30d	30d	24-Feb-25	29-Mar-25	16-Dec-24	31-Jan-25	28d
ENG-T&I-1040-B	TP - GRILLAGE AND SEAFASTENING DESIGN REPORT - IFC	28d	28d	05-Mar-25	05-Apr-25	14-Oct-24	15-Nov-24	2d
ENG-T&I-1060-B	CAISSONS - INSTALLATION AIDS DESIGN REPORT - IFC	26d	26d	07-Mar-25	05-Apr-25	30-Oct-24	29-Nov-24	2d
ENG-T&I-1050-B	TP - LOAD OUT MANUAL INCLUDING BALLAST SEQUENCE - IFC	28d	28d	08-Mar-25	09-Apr-25	09-Jan-25	14-Feb-25	19d
ENG-T&I-1070-B	CAISSONS - GRILLAGE AND SEAFASTENING DESIGN REPORT - IFC	22d	22d	10-Mar-25	03-Apr-25	30-Oct-24	29-Nov-24	4d
ENG-T&I-1080-B	CAISSONS - LOAD OUT MANUAL INCLUDING BALLAST SEQUENCE - IFC	23d	23d	13-Mar-25	08-Apr-25	30-Dec-24	31-Jan-25	20d
ENG-T&I-1100-B	BARGE INTEGRITY CHECK - IFC	27d	27d	14-Mar-25	14-Apr-25	09-Jan-25	14-Feb-25	5d
ENG-T&I-1020-B	TOPSIDE - LOAD OUT MANUAL INCLUDING BALLAST SEQUENCE - IFC	23d	23d	24-Mar-25	18-Apr-25	30-Dec-24	31-Jan-25	11d
ENG-T&I-1340-B	PBY YARD – BARGE MOORING PLAN 1 - IFC	19d	19d	07-Apr-25	02-May-25	12-Nov-24	06-Dec-24	3d
ENG-T&I-1350-B	PBY YARD – BARGE MOORING PLAN 2 - IFC	19d	19d	07-Apr-25	02-May-25	12-Nov-24	06-Dec-24	3d
As-Built Documentation		80d	80d	19-Mar-25	25-Jun-25	02-Apr-25	09-Jul-25	31d
ENG-ASBUILT-1000	AS-Built Documentation	80d	80d	19-Mar-25	25-Jun-25	02-Apr-25	09-Jul-25	31d
Procurement		528d	461d	21-Aug-23 A	26-Feb-25	01-Aug-23	12-Feb-25	204d
Company Provided Items		156d	168d	01-Jun-24 A	17-Dec-24	30-Apr-24	15-Aug-24	22d
Electrolysers - CPI		91d	104d	15-Aug-24 A	17-Dec-24	15-Aug-24	15-Aug-24	22d
PRO-CPI1070	COMPANY Delay - Electrolysers & Electrlyser Transformer CPI - Delivery At Yard	5d	104d	15-Aug-24 A	16-Dec-24			22d
PRO-CPI1040	Electrolysers & Electrlyser Transformer CPI - Delivery At Yard	0d	0d	17-Dec-24*		15-Aug-24		30d
Fuell Cells - CPI		95d	109d	01-Jun-24 A	18-Sep-24 A	30-May-24	30-May-24	
PRO-CPI1060	COMPANY Delay - Fuel Cells CPI - Delivery At Yard	95d	109d	01-Jun-24 A	18-Sep-24 A			
PRO-CPI1020	Fuel Cells CPI - Delivery At Yard (Contract 30.05.2024)	0d	0d	18-Sep-24 A		30-May-24		
BESS Battery - CPI		52d	52d	01-Jun-24 A	22-Jul-24 A	30-May-24	30-May-24	
PRO-CPI1050	COMPANY Delay - Bess Battery CPI - Delivery At Yard	30d	52d	01-Jun-24 A	22-Jul-24 A			
PRO-CPI1030	Bess Battery CPI - Delivery At Yard (Contract 30.05.2024)	0d	0d	22-Jul-24 A		30-May-24		
ICCP - CPI		0d	0d	03-Jul-24 A	03-Jul-24 A	30-Apr-24	30-Apr-24	
PRO-CPI1000	ICCP CPI - Delivery At Yard	0d	0d	03-Jul-24 A		30-Apr-24		
Equipment		528d	425d	21-Aug-23 A	15-Jan-25	01-Aug-23	12-Feb-25	38d
H2 Storage Vessel		399d	363d	29-Aug-23 A	07-Nov-24	29-Aug-23	22-Nov-24	64d
PRO-EQ-MR01-1000	MR01 - MR Issued - H2 Storage Vessel	0d	0d	29-Aug-23 A		29-Aug-23		
PRO-EQ-MR01-1160	MR01 - Request for Quotation - H2 Storage Vessel	1d	1d	29-Aug-23 A	29-Aug-23 A	29-Aug-23	29-Aug-23	
PRO-EQ-MR01-1170	MR01 - Vendor Quotation - H2 Storage Vessel	9d	10d	30-Aug-23 A	12-Sep-23 A	30-Aug-23	11-Sep-23	
PRO-EQ-MR01-1030	MR01 - Purchase Order - H2 Storage Vessel	10d	2d	20-Oct-23 A	23-Oct-23 A	29-Sep-23	12-Oct-23	
PRO-EQ-MR01-1040	MR01 - Manufacturing & Ex-Works - H2 Storage Vessel	375d	354d	24-Oct-23 A	07-Nov-24	13-Oct-23	17-Nov-24	55d
PRO-EQ-MR01-1060	MR01 - Transportation & Yard Delivery - H2 Storage Vessel	7d	38d	30-Sep-24 A	07-Nov-24	18-Nov-24	22-Nov-24	74d
Hydrogen Vent KO Drum		217d	259d	30-Nov-23 A	08-Oct-24 A	15-Jan-24	25-Oct-24	
PRO-EQ-MR01-1070	MR01 - Request for Quotation - Hydrogen Vent KO Drum	1d	2d	30-Nov-23 A	01-Dec-23 A	15-Jan-24	15-Jan-24	
PRO-EQ-MR01-1140	MR01 - MR Issued - Hydrogen Vent KO Drum	0d	0d	30-Nov-23 A		15-Jan-24		
PRO-EQ-MR01-1150	MR01 - Vendor Quotation - Hydrogen Vent KO Drum	9d	3d	01-Dec-23 A	05-Dec-23 A	16-Jan-24	26-Jan-24	
PRO-EQ-MR01-1100	MR01 - Purchase Order - Hydrogen Vent KO Drum	10d	34d	05-Dec-23 A	25-Jan-24 A	29-Jan-24	09-Feb-24	
PRO-EQ-MR01-1110	MR01 - Manufacturing & Ex-Works - Hydrogen Vent KO Drum	240d	242d	25-Jan-24 A	07-Oct-24 A	10-Feb-24	20-Oct-24	
PRO-EQ-MR01-1130	MR01 - Transportation & Yard Delivery - Hydrogen Vent KO Drum	5d	3d	06-Oct-24 A	08-Oct-24 A	21-Oct-24	25-Oct-24	
Electro-Chlorination Unit		287d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	25-Aug-24	48d
PRO-EQ-MR02-1000	MR02 - Request for Quotation - Electro-Chlorination Unit	1d	1d	15-Nov-23 A	15-Nov-23 A	01-Dec-23	01-Dec-23	
PRO-EQ-MR02-1350	MR02 - MR Issued - Electro-Chlorination Unit	0d	0d	15-Nov-23 A		01-Dec-23		

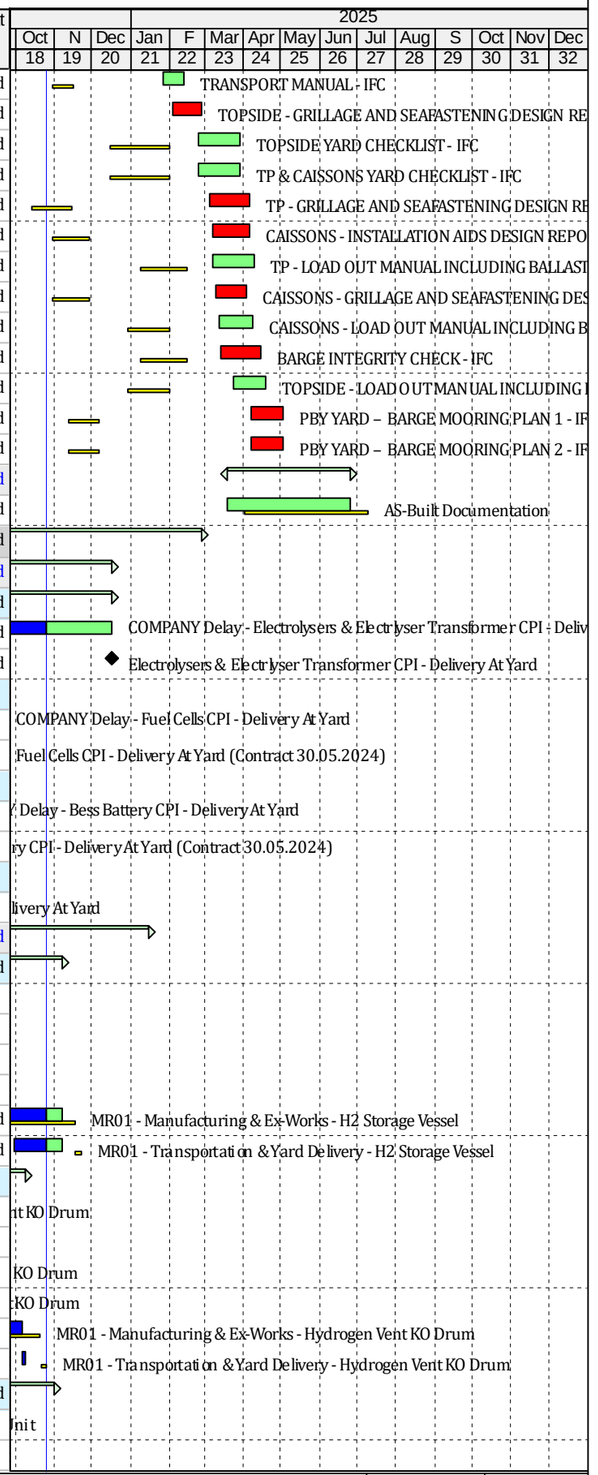


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR02-1360	MR02 - Vendor Quotation - Electro-Chlorination Unit	9d	12d	16-Nov-23 A	01-Dec-23 A	04-Dec-23	15-Dec-23	
PRO-EQ-MR02-1530	MR02 - Vendor Ealuation - Electro-Chlorination Unit	15d	57d	01-Dec-23 A	23-Feb-24 A	18-Dec-23	10-Jan-24	
PRO-EQ-MR02-1030	MR02 - Purchase Order - Electro-Chlorination Unit	10d	1d	23-Feb-24 A	23-Feb-24 A	11-Jan-24	24-Jan-24	
PRO-EQ-MR02-1040	MR02 - Manufacturing & Ex-Works - Electro-Chlorination Unit	231d	238d	23-Feb-24 A	31-Oct-24	25-Jan-24	20-Aug-24	54d
PRO-EQ-MR02-1060	MR02 - Transportation & Yard Delivery - Electro-Chlorination Unit	5d	5d	27-Oct-24	31-Oct-24	21-Aug-24	25-Aug-24	56d
Desalinisation Unit (SWRO)		282d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	24-Aug-24	48d
PRO-EQ-MR02-1450	MR02 - Request for Quotation - Desalination Unit (SWRO)	1d	1d	15-Nov-23 A	15-Nov-23 A	01-Dec-23	01-Dec-23	
PRO-EQ-MR02-1460	MR02 - MR Issued - Desalination Unit (SWRO)	0d	0d	15-Nov-23 A		01-Dec-23		
PRO-EQ-MR02-1470	MR02 - Vendor Quotation - Desalination Unit (SWRO)	9d	13d	15-Nov-23 A	01-Dec-23 A	04-Dec-23	15-Dec-23	
PRO-EQ-MR02-1480	MR02 - Technical Bid Evaluation - Desalination Unit (SWRO)	14d	57d	01-Dec-23 A	23-Feb-24 A	18-Dec-23	09-Jan-24	
PRO-EQ-MR02-1490	MR02 - Purchase Order - Desalination Unit (SWRO)	10d	1d	23-Feb-24 A	23-Feb-24 A	10-Jan-24	23-Jan-24	
PRO-EQ-MR02-1500	MR02 - Manufacturing & Ex-Works - Desalination Unit (SWRO)	197d	235d	26-Feb-24 A	31-Oct-24	24-Jan-24	19-Aug-24	18d
PRO-EQ-MR02-1520	MR02 - Transportation & Yard Delivery - Desalination Unit (SWRO)	5d	5d	27-Oct-24	31-Oct-24	20-Aug-24	24-Aug-24	56d
Ultra Filtration Unit		287d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	04-Aug-24	48d
PRO-EQ-MR02-1070	MR02 - Request for Quotation - Ultra Filtration Unit	1d	1d	15-Nov-23 A	15-Nov-23 A	01-Dec-23	01-Dec-23	
PRO-EQ-MR02-1370	MR02 - MR Issued - Ultra Filtration Unit	0d	0d	15-Nov-23 A		01-Dec-23		
PRO-EQ-MR02-1380	MR02 - Vendor Quotation - Ultra Filtration Unit	9d	12d	16-Nov-23 A	01-Dec-23 A	04-Dec-23	15-Dec-23	
PRO-EQ-MR02-1540	MR02 - Vendor Ealuation - Ultra Filtration Unit	10d	57d	01-Dec-23 A	23-Feb-24 A	18-Dec-23	03-Jan-24	
PRO-EQ-MR02-1100	MR02 - Purchase Order - Ultra Filtration Unit	10d	1d	23-Feb-24 A	23-Feb-24 A	04-Jan-24	17-Jan-24	
PRO-EQ-MR02-1110	MR02 - Manufacturing & Ex-Works - Ultra Filtration Unit	231d	238d	23-Feb-24 A	31-Oct-24	18-Jan-24	30-Jul-24	54d
PRO-EQ-MR02-1130	MR02 - Transportation & Yard Delivery - Ultra Filtration Unit	5d	5d	27-Oct-24	31-Oct-24	31-Jul-24	04-Aug-24	56d
UV Water Filter		282d	292d	15-Nov-23 A	31-Oct-24	01-Dec-23	04-Aug-24	48d
PRO-EQ-MR02-1140	MR02 - Request for Quotation - UV Water Filter	1d	1d	15-Nov-23 A	15-Nov-23 A	01-Dec-23	01-Dec-23	
PRO-EQ-MR02-1390	MR02 - MR Issued - UV Water Filter	0d	0d	15-Nov-23 A		01-Dec-23		
PRO-EQ-MR02-1400	MR02 - Vendor Quotation - UV Water Filter	9d	12d	16-Nov-23 A	01-Dec-23 A	04-Dec-23	15-Dec-23	
PRO-EQ-MR02-1550	MR02 - Vendor Ealuation - UV Water Filter	10d	57d	01-Dec-23 A	23-Feb-24 A	18-Dec-23	03-Jan-24	
PRO-EQ-MR02-1170	MR02 - Purchase Order - UV Water Filter	10d	1d	23-Feb-24 A	23-Feb-24 A	04-Jan-24	17-Jan-24	
PRO-EQ-MR02-1180	MR02 - Manufacturing & Ex-Works - UV Water Filter	203d	238d	23-Feb-24 A	31-Oct-24	18-Jan-24	30-Jul-24	54d
PRO-EQ-MR02-1200	MR02 - Transportation & Yard Delivery - UV Water Filter	5d	5d	27-Oct-24	31-Oct-24	31-Jul-24	04-Aug-24	56d
Sea Water Coarse Filter Package		282d	292d	15-Nov-23 A	31-Oct-24	12-Dec-23	16-Jul-24	48d
PRO-EQ-MR02-1210	MR02 - Request for Quotation - Sea Water Coarse Filter Package	1d	9d	15-Nov-23 A	27-Nov-23 A	12-Dec-23	12-Dec-23	
PRO-EQ-MR02-1410	MR02 - MR Issued - Sea Water Coarse Filter Package	0d	0d	15-Nov-23 A		12-Dec-23		
PRO-EQ-MR02-1420	MR02 - Vendor Quotation - Sea Water Coarse Filter Package	9d	12d	16-Nov-23 A	01-Dec-23 A	13-Dec-23	27-Dec-23	
PRO-EQ-MR02-1560	MR02 - Vendor Ealuation - Sea Water Coarse Filter Package	10d	57d	01-Dec-23 A	23-Feb-24 A	28-Dec-23	11-Jan-24	
PRO-EQ-MR02-1240	MR02 - Purchase Order - Sea Water Coarse Filter Package	10d	1d	23-Feb-24 A	23-Feb-24 A	12-Jan-24	25-Jan-24	
PRO-EQ-MR02-1250	MR02 - Manufacturing & Ex-Works - Sea Water Coarse Filter Package	184d	238d	23-Feb-24 A	31-Oct-24	26-Jan-24	11-Jul-24	54d
PRO-EQ-MR02-1270	MR02 - Transportation & Yard Delivery - Sea Water Coarse Filter Package	5d	5d	27-Oct-24	31-Oct-24	12-Jul-24	16-Jul-24	56d
Fresh Water Pump		281d	291d	15-Nov-23 A	30-Oct-24	12-Dec-23	07-Apr-24	49d
PRO-EQ-MR02-1280	MR02 - Request for Quotation - Fresh Water Pump (Gear pumps)	1d	1d	15-Nov-23 A	15-Nov-23 A	12-Dec-23	12-Dec-23	
PRO-EQ-MR02-1430	MR02 - MR Issued - Fresh Water Pump (Gear pumps)	0d	0d	15-Nov-23 A		12-Dec-23		
PRO-EQ-MR02-1440	MR02 - Vendor Quotation - Fresh Water Pump (Gear pumps)	9d	12d	16-Nov-23 A	01-Dec-23 A	13-Dec-23	27-Dec-23	
PRO-EQ-MR02-1570	MR02 - Vendor Ealuation - Fresh Water Pump (Gear pumps)	15d	57d	01-Dec-23 A	23-Feb-24 A	28-Dec-23	18-Jan-24	
PRO-EQ-MR02-1310	MR02 - Purchase Order - Fresh Water Pump (Gear pumps)	10d	1d	23-Feb-24 A	23-Feb-24 A	19-Jan-24	01-Feb-24	
PRO-EQ-MR02-1320	MR02 - Manufacturing & Ex-Works - Fresh Water Pump (Gear pumps)	196d	237d	23-Feb-24 A	30-Oct-24	28-Feb-24	02-Apr-24	55d
PRO-EQ-MR02-1340	MR02 - Transportation & Yard Delivery - Fresh Water Pump (Gear pumps)	5d	5d	26-Oct-24	30-Oct-24	03-Apr-24	07-Apr-24	57d
Filtered Seawater Tank		296d	307d	27-Oct-23 A	31-Oct-24	20-Nov-23	29-Jul-24	48d

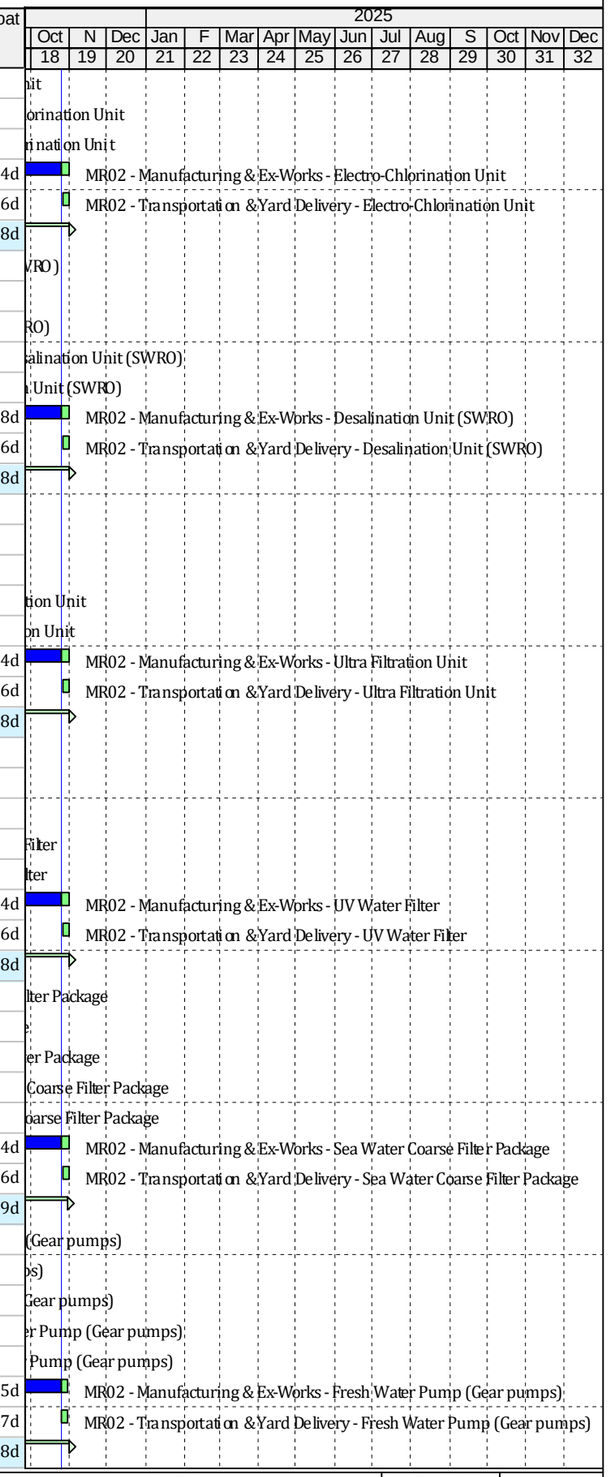

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR03-1000	MR03 - Request for Quotation - Filtered Seawater Tank	1d	1d	27-Oct-23 A	27-Oct-23 A	20-Nov-23	20-Nov-23	
PRO-EQ-MR03-1140	MR03 - MR Issued - Filtered Seawater Tank	0d	0d	27-Oct-23 A		20-Nov-23		
PRO-EQ-MR03-1150	MR03 - Vendor Quotation - Filtered Seawater Tank	9d	5d	30-Oct-23 A	06-Nov-23 A	21-Nov-23	01-Dec-23	
PRO-EQ-MR03-1010	MR03 - Vendor Evaluation - Filtered Seawater Tank	15d	75d	07-Nov-23 A	23-Feb-24 A	04-Dec-23	27-Dec-23	
PRO-EQ-MR03-1030	MR03 - Purchase Order - Filtered Seawater Tank	10d	1d	23-Feb-24 A	23-Feb-24 A	28-Dec-23	11-Jan-24	
PRO-EQ-MR03-1040	MR03 - Manufacturing & Ex-Works - Filtered Seawater Tank	188d	238d	23-Feb-24 A	31-Oct-24	12-Jan-24	24-Jul-24	54d
PRO-EQ-MR03-1060	MR03 - Transportation & Yard Delivery - Filtered Seawater Tank	5d	5d	27-Oct-24	31-Oct-24	25-Jul-24	29-Jul-24	56d
Fresh Water Tank		301d	307d	27-Oct-23 A	31-Oct-24	20-Nov-23	29-Jul-24	48d
PRO-EQ-MR03-1070	MR03 - Request for Quotation - Fresh Water Tank	1d	1d	27-Oct-23 A	27-Oct-23 A	20-Nov-23	20-Nov-23	
PRO-EQ-MR03-1160	MR03 - MR Issued - Fresh Water Tank	0d	0d	27-Oct-23 A		20-Nov-23		
PRO-EQ-MR03-1170	MR03 - Vendor Quotation - Fresh Water Tank	9d	5d	30-Oct-23 A	06-Nov-23 A	21-Nov-23	01-Dec-23	
PRO-EQ-MR03-1080	MR03 - Technical Bid Evaluation - Fresh Water Tank - IFA - to be deleted	0d	65d	20-Nov-23 A	22-Feb-24 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR03-1100	MR03 - Purchase Order - Fresh Water Tank	10d	2d	22-Feb-24 A	23-Feb-24 A	21-Dec-23	08-Jan-24	
PRO-EQ-MR03-1110	MR03 - Manufacturing & Ex-Works - Fresh Water Tank	231d	238d	23-Feb-24 A	31-Oct-24	12-Jan-24	24-Jul-24	54d
PRO-EQ-MR03-1130	MR03 - Transportation & Yard Delivery - Fresh Water Tank	5d	5d	27-Oct-24	31-Oct-24	25-Jul-24	29-Jul-24	56d
Transformer Main 66/6.6kV		344d	291d	21-Aug-23 A	05-Aug-24 A	21-Aug-23	03-Nov-24	
PRO-EQ-MR05-1210	MR05 - MR Issued - Transformer Main 66/6.6kV	0d	0d	21-Aug-23 A		21-Aug-23		
PRO-EQ-MR05-1000	MR05 - Request for Quotation - Transformer Main 66/6.6kV	1d	2d	22-Aug-23 A	23-Aug-23 A	21-Aug-23	21-Aug-23	
PRO-EQ-MR05-1220	MR05 - Vendor Quotation - Transformer Main 66/6.6kV	9d	12d	24-Aug-23 A	08-Sep-23 A	22-Aug-23	01-Sep-23	
PRO-EQ-MR05-1030	MR05 - Purchase Order - Transformer Main 66/6.6kV	10d	3d	11-Oct-23 A	13-Oct-23 A	27-Sep-23	10-Oct-23	
PRO-EQ-MR05-1040	MR05 - Manufacturing & Ex-Works - Transformer Main 66/6.6kV	302d	281d	16-Oct-23 A	05-Aug-24 A	11-Oct-23	03-Sep-24	
PRO-EQ-MR05-1060	MR05 - Transportation & Yard Delivery - Transformer Main 66/6.6kV	19d	1d	05-Aug-24 A	05-Aug-24 A	04-Sep-24	03-Nov-24	
Transformer Aux. 6.6/0.4kV		362d	287d	21-Aug-23 A	31-Jul-24 A	21-Aug-23	29-Oct-24	
PRO-EQ-MR05-1250	MR05 - MR Issued - Transformer Aux. 6.6/0.4kV	0d	0d	21-Aug-23 A		21-Aug-23		
PRO-EQ-MR05-1070	MR05 - Request for Quotation - Transformer Aux. 6.6/0.4kV	1d	2d	22-Aug-23 A	23-Aug-23 A	21-Aug-23	21-Aug-23	
PRO-EQ-MR05-1260	MR05 - Vendor Quotation - Transformer Aux. 6.6/0.4kV	9d	12d	24-Aug-23 A	08-Sep-23 A	22-Aug-23	01-Sep-23	
PRO-EQ-MR05-1270	MR05 - Vendor Evaluation - Transformer Aux. 6.6/0.4kV	10d	20d	11-Sep-23 A	06-Oct-23 A	04-Sep-23	15-Sep-23	
PRO-EQ-MR05-1100	MR05 - Purchase Order - Transformer Aux. 6.6/0.4kV	15d	3d	11-Oct-23 A	13-Oct-23 A	18-Sep-23	06-Oct-23	
PRO-EQ-MR05-1110	MR05 - Manufacturing & Ex-Works - Transformer Aux. 6.6/0.4kV	302d	276d	16-Oct-23 A	30-Jul-24 A	07-Oct-23	30-Aug-24	
PRO-EQ-MR05-1130	MR05 - Transportation & Yard Delivery - Transformer Aux. 6.6/0.4kV	28d	1d	31-Jul-24 A	31-Jul-24 A	31-Aug-24	29-Oct-24	
Transformer 0,4/6,6kV630kVA		362d	286d	21-Aug-23 A	30-Jul-24 A	21-Aug-23	29-Oct-24	
PRO-EQ-MR05-1230	MR05 - MR Issued - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	0d	0d	21-Aug-23 A		21-Aug-23		
PRO-EQ-MR05-1140	MR05 - Request for Quotation - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	1d	2d	22-Aug-23 A	23-Aug-23 A	21-Aug-23	21-Aug-23	
PRO-EQ-MR05-1240	MR05 - Vendor Quotation - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	9d	12d	24-Aug-23 A	08-Sep-23 A	22-Aug-23	01-Sep-23	
PRO-EQ-MR05-1280	MR05 - Vendor Evaluation - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	15d	20d	11-Sep-23 A	06-Oct-23 A	04-Sep-23	22-Sep-23	
PRO-EQ-MR05-1170	MR05 - Purchase Order - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	10d	3d	11-Oct-23 A	13-Oct-23 A	25-Sep-23	06-Oct-23	
PRO-EQ-MR05-1180	MR05 - Manufacturing & Ex-Works - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	302d	276d	16-Oct-23 A	30-Jul-24 A	07-Oct-23	30-Aug-24	
PRO-EQ-MR05-1200	MR05 - Transportation & Yard Delivery - Transformer 0,4/6,6kV 630kVA Solar farm Step UP (safe area)	28d	1d	30-Jul-24 A	30-Jul-24 A	31-Aug-24	29-Oct-24	
Neutral earthing resistor		362d	311d	29-Aug-23 A	06-Sep-24 A	29-Aug-23	29-Oct-24	
PRO-EQ-MR06-1420	MR06 - MR Issued - Neutral earthing resistor 400A	0d	0d	29-Aug-23 A		29-Aug-23		
PRO-EQ-MR06-1000	MR06 - Request for Quotation - Neutral earthing resistor 400A	1d	1d	30-Aug-23 A	30-Aug-23 A	29-Aug-23	29-Aug-23	
PRO-EQ-MR06-1430	MR06 - Vendor Quotation - Neutral earthing resistor 400A	9d	10d	31-Aug-23 A	13-Sep-23 A	30-Aug-23	11-Sep-23	
PRO-EQ-MR06-1030	MR06 - Purchase Order - Neutral earthing resistor 400A	10d	3d	11-Oct-23 A	13-Oct-23 A	03-Oct-23	16-Oct-23	
PRO-EQ-MR06-1040	MR06 - Manufacturing & Ex-Works - Neutral earthing resistor 400A	292d	300d	16-Oct-23 A	06-Sep-24 A	17-Oct-23	30-Aug-24	
PRO-EQ-MR06-1060	MR06 - Transportation & Yard Delivery - Neutral earthing resistor 400A	60d	1d	06-Sep-24 A	06-Sep-24 A	31-Aug-24	29-Oct-24	
HV Switchgear 66kV		443d	425d	21-Aug-23 A	15-Jan-25	02-Aug-23	01-Feb-25	36d

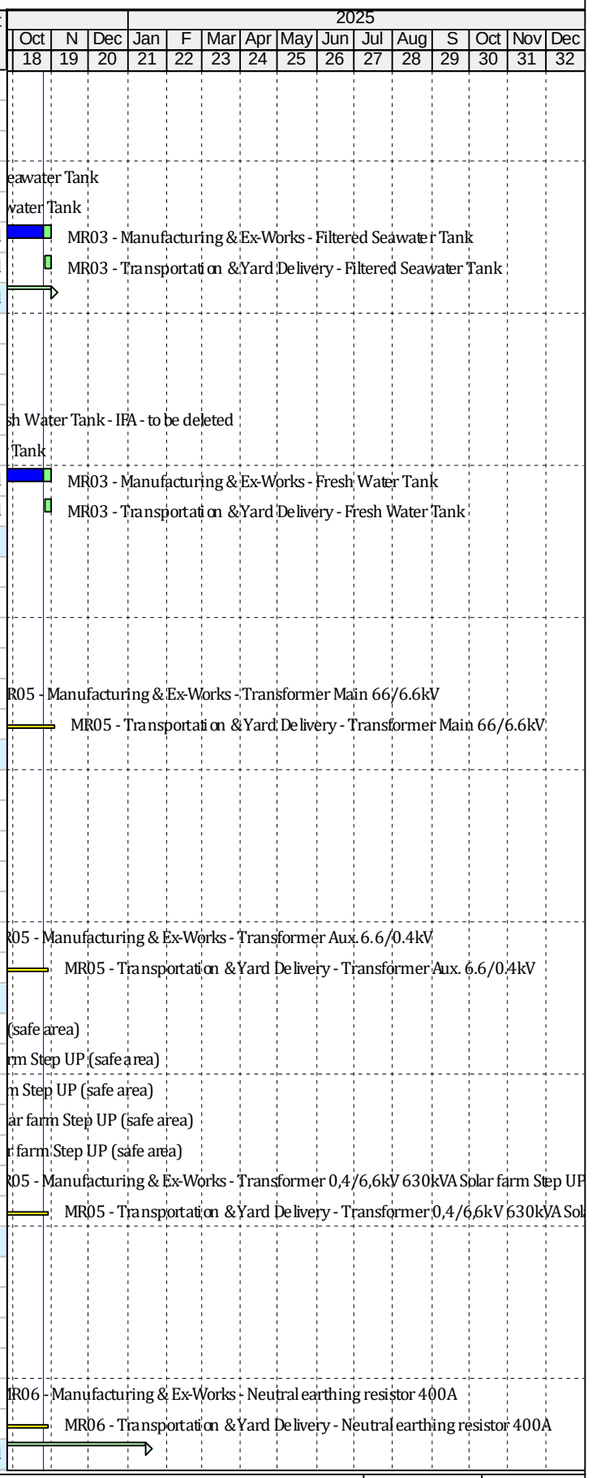

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR06-1070	MR06 - Request for Quotation - HV Switchgear 66kV	1d	2d	21-Aug-23 A	22-Aug-23 A	02-Aug-23	02-Aug-23	
PRO-EQ-MR06-1440	MR06 - MR Issued - HV Switchgear 66kV	0d	0d	21-Aug-23 A		02-Aug-23		
PRO-EQ-MR06-1450	MR06 - Vendor Quotation - HV Switchgear 66kV	9d	8d	23-Aug-23 A	01-Sep-23 A	03-Aug-23	16-Aug-23	
PRO-EQ-MR06-1100	MR06 - Purchase Order - HV Switchgear 66kV	10d	4d	25-Sep-23 A	28-Sep-23 A	04-Sep-23	15-Sep-23	
PRO-EQ-MR06-1110	MR06 - Manufacturing & Ex-Works - HV Switchgear 66kV	393d	423d	02-Oct-23 A	24-Dec-24	23-Sep-23	17-Jan-25	33d
PRO-EQ-MR06-1130	MR06 - Transportation &Yard Delivery - HV Switchgear 66kV	15d	15d	30-Dec-24	15-Jan-25	17-Jan-25	01-Feb-25	42d
MV Switchgear 6.6kV		341d	293d	21-Aug-23 A	07-Aug-24 A	01-Aug-23	31-Aug-24	
PRO-EQ-MR06-1140	MR06 - Request for Quotation - MV Switchgear 6.6kV	1d	1d	21-Aug-23 A	21-Aug-23 A	01-Aug-23	01-Aug-23	
PRO-EQ-MR06-1520	MR06 - MR Issued - MV Switchgear 6.6kV	0d	0d	21-Aug-23 A		01-Aug-23		
PRO-EQ-MR06-1530	MR06 - Vendor Quotation - MV Switchgear 6.6kV	9d	9d	22-Aug-23 A	01-Sep-23 A	02-Aug-23	14-Aug-23	
PRO-EQ-MR06-1170	MR06 - Purchase Order - MV Switchgear 6.6kV	14d	1d	21-Dec-23 A	21-Dec-23 A	04-Sep-23	04-Oct-23	
PRO-EQ-MR06-1180	MR06 - Manufacturing & Ex-Works - MV Switchgear 6.6kV	228d	215d	21-Dec-23 A	07-Aug-24 A	05-Oct-23	26-Aug-24	
PRO-EQ-MR06-1200	MR06 - Transportation &Yard Delivery - MV Switchgear 6.6kV	5d	1d	07-Aug-24 A	07-Aug-24 A	27-Aug-24	31-Aug-24	
Low Voltage Switchgear		355d	293d	21-Aug-23 A	07-Aug-24 A	01-Aug-23	17-Sep-24	
PRO-EQ-MR06-1210	MR06 - Request for Quotation - Low Voltage Switchgear	1d	1d	21-Aug-23 A	21-Aug-23 A	01-Aug-23	01-Aug-23	
PRO-EQ-MR06-1460	MR06 - MR Issued - Low Voltage Switchgear	0d	0d	21-Aug-23 A		01-Aug-23		
PRO-EQ-MR06-1470	MR06 - Vendor Quotation - Low Voltage Switchgear	9d	9d	22-Aug-23 A	01-Sep-23 A	02-Aug-23	14-Aug-23	
PRO-EQ-MR06-1240	MR06 - Purchase Order - Low Voltage Switchgear	14d	1d	21-Dec-23 A	21-Dec-23 A	04-Sep-23	06-Oct-23	
PRO-EQ-MR06-1250	MR06 - Manufacturing & Ex-Works - Low Voltage Switchgear	245d	215d	21-Dec-23 A	07-Aug-24 A	07-Oct-23	12-Sep-24	
PRO-EQ-MR06-1270	MR06 - Transportation &Yard Delivery - Low Voltage Switchgear	5d	1d	07-Aug-24 A	07-Aug-24 A	13-Sep-24	17-Sep-24	
Solar farm in-feed power isolator panel		214d	234d	20-Dec-23 A	27-Sep-24 A	11-Dec-23	14-Jul-24	
PRO-EQ-MR06-1280	MR06 - Request for Quotation - Solar farm in-feed power isolator panel 600x400x400	1d	1d	20-Dec-23 A	20-Dec-23 A	11-Dec-23	11-Dec-23	
PRO-EQ-MR06-1480	MR06 - MR Issued - Solar farm in-feed power isolator panel 600x400x400	0d	0d	20-Dec-23 A		11-Dec-23		
PRO-EQ-MR06-1490	MR06 - Vendor Quotation - Solar farm in-feed power isolator panel 600x400x400	9d	2d	20-Dec-23 A	21-Dec-23 A	12-Dec-23	22-Dec-23	
PRO-EQ-MR06-1310	MR06 - Purchase Order - Solar farm in-feed power isolator panel 600x400x400	10d	1d	21-Dec-23 A	21-Dec-23 A	15-Jan-24	26-Jan-24	
PRO-EQ-MR06-1320	MR06 - Manufacturing & Ex-Works - Solar farm in-feed power isolator panel 600x400x400	165d	236d	21-Jan-24 A	26-Sep-24 A	27-Jan-24	09-Jul-24	
PRO-EQ-MR06-1340	MR06 - Transportation &Yard Delivery - Solar farm in-feed power isolator panel 600x400x400	5d	2d	26-Sep-24 A	27-Sep-24 A	10-Jul-24	14-Jul-24	
Automation systems CCS-SIS & EMS		378d	359d	21-Aug-23 A	25-Oct-24 A	01-Aug-23	02-Sep-24	
PRO-EQ-MR06-1350	MR06 - Request for Quotation - Automation systems CCS-SIS & EMS	1d	1d	21-Aug-23 A	21-Aug-23 A	01-Aug-23	01-Aug-23	
PRO-EQ-MR06-1500	MR06 - MR Issued - Automation systems CCS-SIS & EMS	0d	0d	21-Aug-23 A		01-Aug-23		
PRO-EQ-MR06-1510	MR06 - Vendor Quotation - Automation systems CCS-SIS & EMS	9d	9d	22-Aug-23 A	01-Sep-23 A	02-Aug-23	14-Aug-23	
PRO-EQ-MR06-1380	MR06 - Purchase Order - Automation systems CCS-SIS & EMS	14d	92d	03-Nov-23 A	15-Mar-24 A	04-Sep-23	06-Oct-23	
PRO-EQ-MR06-1390	MR06 - Manufacturing & Ex-Works - Automation systems CCS-SIS & EMS	178d	210d	15-Mar-24 A	25-Oct-24 A	07-Oct-23	28-Aug-24	
PRO-EQ-MR06-1410	MR06 - Transportation &Yard Delivery - Automation systems CCS-SIS & EMS	5d	7d	18-Oct-24 A	25-Oct-24 A	29-Aug-24	02-Sep-24	
Shelter for plant instrument room		208d	226d	03-Nov-23 A	02-Aug-24 A	14-Nov-23	29-Jul-24	
PRO-EQ-MR07-1000	MR07 - Request for Quotation - Shelter for plant instrument room	1d	1d	03-Nov-23 A	03-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-EQ-MR07-1280	MR07 - MR Issued - Shelter for plant instrument room	0d	0d	03-Nov-23 A		14-Nov-23		
PRO-EQ-MR07-1290	MR07 - Vendor Quotation - Shelter for plant instrument room	9d	8d	06-Nov-23 A	15-Nov-23 A	15-Nov-23	27-Nov-23	
PRO-EQ-MR07-1030	MR07 - Purchase Order - Shelter for plant instrument room	10d	12d	22-Dec-23 A	11-Jan-24 A	28-Dec-23	11-Jan-24	
PRO-EQ-MR07-1040	MR07 - Manufacturing & Ex-Works - Shelter for plant instrument room	168d	204d	11-Jan-24 A	01-Aug-24 A	12-Jan-24	24-Jul-24	
PRO-EQ-MR07-1060	MR07 - Transportation &Yard Delivery - Shelter for plant instrument room	5d	1d	02-Aug-24 A	02-Aug-24 A	25-Jul-24	29-Jul-24	
Shelter for LV switchgear room		210d	220d	03-Nov-23 A	26-Jul-24 A	14-Nov-23	24-Jul-24	
PRO-EQ-MR07-1070	MR07 - Request for Quotation - Shelter for LV switchgear room	1d	1d	03-Nov-23 A	03-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-EQ-MR07-1300	MR07 - MR Issued - Shelter for LV switchgear room	0d	0d	03-Nov-23 A		14-Nov-23		
PRO-EQ-MR07-1310	MR07 - Vendor Quotation - Shelter for LV switchgear room	9d	8d	06-Nov-23 A	15-Nov-23 A	15-Nov-23	27-Nov-23	
PRO-EQ-MR07-1100	MR07 - Purchase Order - Shelter for LV switchgear room	10d	12d	22-Dec-23 A	11-Jan-24 A	18-Dec-23	03-Jan-24	

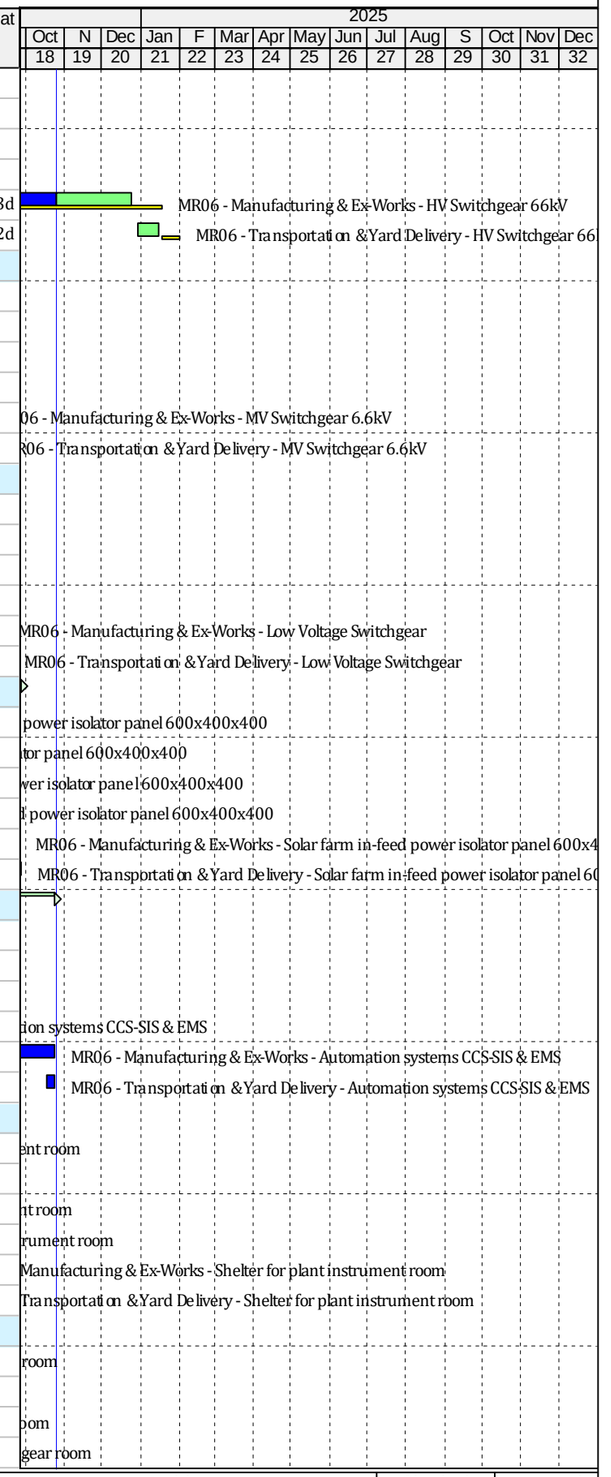

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR07-1110	MR07 - Manufacturing & Ex-Works - Shelter for LV switchgear room	185d	198d	11-Jan-24 A	26-Jul-24 A	07-Jan-24	19-Jul-24	
PRO-EQ-MR07-1130	MR07 - Transportation & Yard Delivery - Shelter for LV switchgear room	5d	1d	26-Jul-24 A	26-Jul-24 A	20-Jul-24	24-Jul-24	
Shelter for HV switchgear room		206d	220d	03-Nov-23 A	26-Jul-24 A	14-Nov-23	24-Jul-24	
PRO-EQ-MR07-1140	MR07 - Request for Quotation - Shelter for HV switchgear room	1d	1d	03-Nov-23 A	03-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-EQ-MR07-1320	MR07 - MR Issued - Shelter for HV switchgear room	0d	0d	03-Nov-23 A		14-Nov-23		
PRO-EQ-MR07-1330	MR07 - Vendor Quotation - Shelter for HV switchgear room	9d	8d	06-Nov-23 A	15-Nov-23 A	15-Nov-23	27-Nov-23	
PRO-EQ-MR07-1170	MR07 - Purchase Order - Shelter for HV switchgear room	10d	1d	11-Jan-24 A	11-Jan-24 A	18-Dec-23	03-Jan-24	
PRO-EQ-MR07-1180	MR07 - Manufacturing & Ex-Works - Shelter for HV switchgear room	189d	198d	11-Jan-24 A	26-Jul-24 A	07-Jan-24	19-Jul-24	
PRO-EQ-MR07-1200	MR07 - Transportation & Yard Delivery - Shelter for HV switchgear room	5d	1d	26-Jul-24 A	26-Jul-24 A	20-Jul-24	24-Jul-24	
Shelter for AC UPS fitted with UPS system		209d	222d	03-Nov-23 A	29-Jul-24 A	14-Nov-23	24-Jul-24	
PRO-EQ-MR07-1210	MR07 - Request for Quotation - Shelter for AC UPS fitted with UPS system (exc. Nav.Aids. UPS & DC system)	1d	1d	03-Nov-23 A	03-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-EQ-MR07-1340	MR07 - MR Issued - Shelter for AC UPS fitted with UPS system (exc. Nav.Aids. UPS & DC system)	0d	0d	03-Nov-23 A		14-Nov-23		
PRO-EQ-MR07-1350	MR07 - Vendor Quotation - Shelter for AC UPS fitted with UPS system (exc. Nav.Aids. UPS & DC system)	9d	8d	06-Nov-23 A	15-Nov-23 A	15-Nov-23	27-Nov-23	
PRO-EQ-MR07-1240	MR07 - Purchase Order - Shelter for AC UPS fitted with UPS system (exc. Nav.Aids. UPS & DC system)	10d	12d	22-Dec-23 A	11-Jan-24 A	18-Dec-23	03-Jan-24	
PRO-EQ-MR07-1250	MR07 - Manufacturing & Ex-Works - Shelter for AC UPS fitted with UPS system (exc. Nav.Aids. UPS & DC system	190d	201d	11-Jan-24 A	29-Jul-24 A	07-Jan-24	19-Jul-24	
PRO-EQ-MR07-1270	MR07 - Transportation & Yard Delivery - Shelter for AC UPS fitted with UPS system (exc. Nav.Aids. UPS & DC sys	5d	1d	29-Jul-24 A	29-Jul-24 A	20-Jul-24	24-Jul-24	
DC UPS panel board		249d	234d	23-Oct-23 A	01-Aug-24 A	18-Oct-23	16-Jul-24	
PRO-EQ-MR08-1000	MR08 - Request for Quotation - DC UPS panel board Feeder A 10kW & Feeder B10kW with common battery bac	1d	2d	23-Oct-23 A	24-Oct-23 A	18-Oct-23	18-Oct-23	
PRO-EQ-MR08-1210	MR08 - MR Issued - DC UPS panel board Feeder A 10kW & Feeder B10kW with common battery back up (225A	0d	0d	23-Oct-23 A		18-Oct-23		
PRO-EQ-MR08-1220	MR08 - Vendor Quotation - DC UPS panel board Feeder A 10kW & Feeder B10kW with common battery back up	9d	9d	24-Oct-23 A	06-Nov-23 A	19-Oct-23	31-Oct-23	
PRO-EQ-MR08-1030	MR08 - Purchase Order - DC UPS panel board Feeder A 10kW & Feeder B10kW with common battery back up (	10d	9d	08-Feb-24 A	20-Feb-24 A	20-Nov-23	01-Dec-23	
PRO-EQ-MR08-1040	MR08 - Manufacturing & Ex-Works - DC UPS panel board Feeder A 10kW & Feeder B10kW with common batte	146d	164d	20-Feb-24 A	01-Aug-24 A	02-Dec-23	11-Jul-24	
PRO-EQ-MR08-1060	MR08 - Transportation & Yard Delivery - DC UPS panel board Feeder A 10kW & Feeder B10kW with common b	5d	1d	01-Aug-24 A	01-Aug-24 A	12-Jul-24	16-Jul-24	
AC UPS for CCS, SIS field instruments		269d	293d	23-Oct-23 A	10-Oct-24 A	03-Nov-23	03-Aug-24	
PRO-EQ-MR08-1070	MR08 - Request for Quotation - AC UPS for CCS, SIS field instruments) Rectifier 15kW & 15kW Bypass	1d	2d	23-Oct-23 A	24-Oct-23 A	03-Nov-23	03-Nov-23	
PRO-EQ-MR08-1230	MR08 - MR Issued - AC UPS for CCS, SIS field instruments) Rectifier 15kW & 15kW Bypass	0d	0d	23-Oct-23 A		03-Nov-23		
PRO-EQ-MR08-1240	MR08 - Vendor Quotation - AC UPS for CCS, SIS field instruments) Rectifier 15kW & 15kW Bypass	9d	9d	24-Oct-23 A	06-Nov-23 A	06-Nov-23	16-Nov-23	
PRO-EQ-MR08-1100	MR08 - Purchase Order - AC UPS for CCS, SIS field instruments) Rectifier 15kW & 15kW Bypass	10d	9d	08-Feb-24 A	20-Feb-24 A	05-Dec-23	19-Dec-23	
PRO-EQ-MR08-1110	MR08 - Manufacturing & Ex-Works - AC UPS for CCS, SIS field instruments) Rectifier 15kW & 15kW Bypass	164d	216d	20-Feb-24 A	07-Oct-24 A	20-Dec-23	29-Jul-24	
PRO-EQ-MR08-1130	MR08 - Transportation & Yard Delivery - AC UPS for CCS, SIS field instruments) Rectifier 15kW & 15kW Bypas	5d	4d	07-Oct-24 A	10-Oct-24 A	30-Jul-24	03-Aug-24	
AC UPS for PAGA/FGS/EMCS Rectifier		263d	291d	23-Oct-23 A	08-Oct-24 A	20-Nov-23	24-Aug-24	
PRO-EQ-MR08-1140	MR08 - Request for Quotation - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	1d	2d	23-Oct-23 A	24-Oct-23 A	20-Nov-23	20-Nov-23	
PRO-EQ-MR08-1250	MR08 - MR Issued - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	0d	0d	23-Oct-23 A		20-Nov-23		
PRO-EQ-MR08-1260	MR08 - Vendor Quotation - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	9d	9d	24-Oct-23 A	06-Nov-23 A	21-Nov-23	01-Dec-23	
PRO-EQ-MR08-1270	MR08 - Vendor Evaluation - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	12d	70d	27-Oct-23 A	08-Feb-24 A	04-Dec-23	20-Dec-23	
PRO-EQ-MR08-1170	MR08 - Purchase Order - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	10d	9d	08-Feb-24 A	20-Feb-24 A	21-Dec-23	08-Jan-24	
PRO-EQ-MR08-1180	MR08 - Manufacturing & Ex-Works - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	164d	218d	20-Feb-24 A	08-Oct-24 A	09-Jan-24	19-Aug-24	
PRO-EQ-MR08-1200	MR08 - Transportation & Yard Delivery - AC UPS for PAGA/FGS/EMCS Rectifier 10kW & 10kW Bypass	5d	3d	06-Oct-24 A	08-Oct-24 A	20-Aug-24	24-Aug-24	
Essential process load distribution panel		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
PRO-EQ-MR09-1000	MR09 - Request for Quotation - Essential process load distribution panel	1d	2d	20-Dec-23 A	21-Dec-23 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR09-1490	MR09 - MR Issued - Essential process load distribution panel	0d	0d	20-Dec-23 A		04-Dec-23		
PRO-EQ-MR09-1030	MR09 - Purchase Order - Essential process load distribution panel	10d	1d	21-Dec-23 A	21-Dec-23 A	12-Jan-24	25-Jan-24	
PRO-EQ-MR09-1500	MR09 - Vendor Quotation - Essential process load distribution panel	9d	1d	21-Dec-23 A	21-Dec-23 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR09-1630	MR09 - Vendor Evaluation - Essential process load distribution panel	15d	1d	21-Dec-23 A	21-Dec-23 A	19-Dec-23	11-Jan-24	
PRO-EQ-MR09-1040	MR09 - Manufacturing & Ex-Works - Essential process load distribution panel	165d	251d	22-Dec-23 A	24-Sep-24 A	26-Jan-24	08-Jul-24	
PRO-EQ-MR09-1060	MR09 - Transportation & Yard Delivery - Essential process load distribution panel	5d	4d	21-Sep-24 A	24-Sep-24 A	09-Jul-24	13-Jul-24	

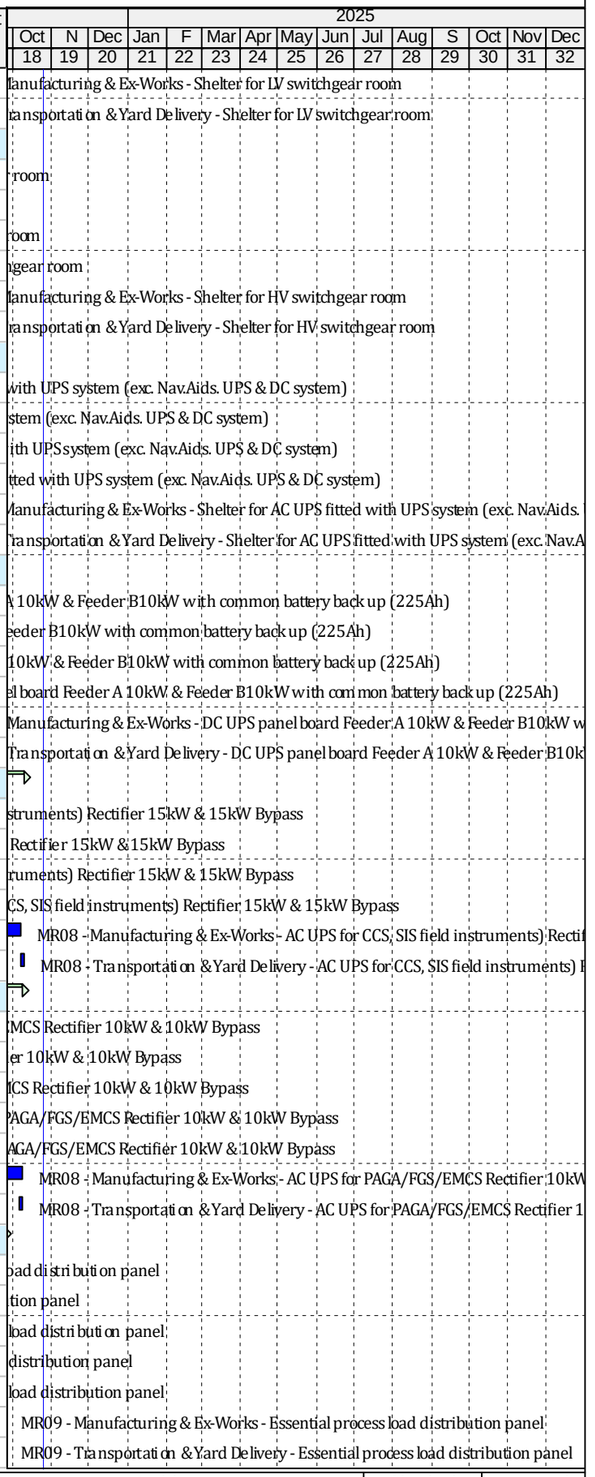

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Process load distribution panel		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	11-Jul-24	
PRO-EQ-MR09-1070	MR09 - Request for Quotation - Process load distribution panel	1d	2d	20-Dec-23 A	21-Dec-23 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR09-1510	MR09 - MR Issued - Process load distribution panel	0d	0d	20-Dec-23 A		04-Dec-23		
PRO-EQ-MR09-1100	MR09 - Purchase Order - Process load distribution panel	10d	1d	21-Dec-23 A	21-Dec-23 A	10-Jan-24	23-Jan-24	
PRO-EQ-MR09-1520	MR09 - Vendor Quotation - Process load distribution panel	9d	1d	21-Dec-23 A	21-Dec-23 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR09-1110	MR09 - Manufacturing & Ex-Works - Process load distribution panel	165d	251d	22-Dec-23 A	24-Sep-24 A	24-Jan-24	06-Jul-24	
PRO-EQ-MR09-1130	MR09 - Transportation & Yard Delivery - Process load distribution panel	5d	4d	21-Sep-24 A	24-Sep-24 A	07-Jul-24	11-Jul-24	
Distribution board for top deck lights		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
PRO-EQ-MR09-1140	MR09 - Request for Quotation - Distribution board for top deck lights (820m2)	1d	2d	20-Dec-23 A	21-Dec-23 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR09-1530	MR09 - MR Issued - Distribution board for top deck lights (820m2)	0d	0d	20-Dec-23 A		04-Dec-23		
PRO-EQ-MR09-1170	MR09 - Purchase Order - Distribution board for top deck lights (820m2)	10d	1d	21-Dec-23 A	21-Dec-23 A	12-Jan-24	25-Jan-24	
PRO-EQ-MR09-1540	MR09 - Vendor Quotation - Distribution board for top deck lights (820m2)	9d	1d	21-Dec-23 A	21-Dec-23 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR09-1640	MR09 - Vendor Evaluation - Distribution board for top deck lights (820m2)	15d	1d	21-Dec-23 A	21-Dec-23 A	19-Dec-23	11-Jan-24	
PRO-EQ-MR09-1180	MR09 - Manufacturing & Ex-Works - Distribution board for top deck lights (820m2)	165d	251d	22-Dec-23 A	24-Sep-24 A	26-Jan-24	08-Jul-24	
PRO-EQ-MR09-1200	MR09 - Transportation & Yard Delivery - Distribution board for top deck lights (820m2)	5d	4d	21-Sep-24 A	24-Sep-24 A	09-Jul-24	13-Jul-24	
Distribution board for lower deck lights		215d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
PRO-EQ-MR09-1210	MR09 - Request for Quotation - Distribution board for lower deck lights (850m2)	1d	2d	20-Dec-23 A	21-Dec-23 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR09-1550	MR09 - MR Issued - Distribution board for lower deck lights (850m2)	0d	0d	20-Dec-23 A		04-Dec-23		
PRO-EQ-MR09-1240	MR09 - Purchase Order - Distribution board for lower deck lights (850m2)	10d	1d	21-Dec-23 A	21-Dec-23 A	12-Jan-24	25-Jan-24	
PRO-EQ-MR09-1560	MR09 - Vendor Quotation - Distribution board for lower deck lights (850m2)	9d	1d	21-Dec-23 A	21-Dec-23 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR09-1650	MR09 - Vendor Evaluation - Distribution board for lower deck lights (850m2)	15d	1d	21-Dec-23 A	21-Dec-23 A	19-Dec-23	11-Jan-24	
PRO-EQ-MR09-1250	MR09 - Manufacturing & Ex-Works - Distribution board for lower deck lights (850m2)	165d	251d	22-Dec-23 A	24-Sep-24 A	26-Jan-24	08-Jul-24	
PRO-EQ-MR09-1270	MR09 - Transportation & Yard Delivery - Distribution board for lower deck lights (850m2)	5d	2d	23-Sep-24 A	24-Sep-24 A	09-Jul-24	13-Jul-24	
Distribution board for stair tower lights		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
PRO-EQ-MR09-1280	MR09 - Request for Quotation - Distribution board for stair tower lights (25m2)	1d	2d	20-Dec-23 A	21-Dec-23 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR09-1570	MR09 - MR Issued - Distribution board for stair tower lights (25m2)	0d	0d	20-Dec-23 A		04-Dec-23		
PRO-EQ-MR09-1310	MR09 - Purchase Order - Distribution board for stair tower lights (25m2)	10d	1d	21-Dec-23 A	21-Dec-23 A	12-Jan-24	25-Jan-24	
PRO-EQ-MR09-1580	MR09 - Vendor Quotation - Distribution board for stair tower lights (25m2)	9d	1d	21-Dec-23 A	21-Dec-23 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR09-1660	MR09 - Vendor Evaluation - Distribution board for stair tower lights (25m2)	15d	1d	21-Dec-23 A	21-Dec-23 A	19-Dec-23	11-Jan-24	
PRO-EQ-MR09-1320	MR09 - Manufacturing & Ex-Works - Distribution board for stair tower lights (25m2)	165d	251d	22-Dec-23 A	24-Sep-24 A	26-Jan-24	08-Jul-24	
PRO-EQ-MR09-1340	MR09 - Transportation & Yard Delivery - Distribution board for stair tower lights (25m2)	5d	4d	21-Sep-24 A	24-Sep-24 A	09-Jul-24	13-Jul-24	
Distribution board for Relief valve platform lights		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
PRO-EQ-MR09-1350	MR09 - Request for Quotation - Distribution board for Relief valve platform lights (32m2)	1d	2d	20-Dec-23 A	21-Dec-23 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR09-1590	MR09 - MR Issued - Distribution board for Relief valve platform lights (32m2)	0d	0d	20-Dec-23 A		04-Dec-23		
PRO-EQ-MR09-1380	MR09 - Purchase Order - Distribution board for Relief valve platform lights (32m2)	10d	1d	21-Dec-23 A	21-Dec-23 A	12-Jan-24	25-Jan-24	
PRO-EQ-MR09-1600	MR09 - Vendor Quotation - Distribution board for Relief valve platform lights (32m2)	9d	1d	21-Dec-23 A	21-Dec-23 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR09-1670	MR09 - Vendor Evaluation - Distribution board for Relief valve platform lights (32m2)	15d	1d	21-Dec-23 A	21-Dec-23 A	19-Dec-23	11-Jan-24	
PRO-EQ-MR09-1390	MR09 - Manufacturing & Ex-Works - Distribution board for Relief valve platform lights (32m2)	165d	251d	22-Dec-23 A	24-Sep-24 A	26-Jan-24	08-Jul-24	
PRO-EQ-MR09-1410	MR09 - Transportation & Yard Delivery - Distribution board for Relief valve platform lights (32m2)	5d	4d	21-Sep-24 A	24-Sep-24 A	09-Jul-24	13-Jul-24	
Distribution board for Emergency light		213d	231d	20-Dec-23 A	24-Sep-24 A	04-Dec-23	13-Jul-24	
PRO-EQ-MR09-1420	MR09 - Request for Quotation - Distribution board for Emergency light	1d	2d	20-Dec-23 A	21-Dec-23 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR09-1610	MR09 - MR Issued - Distribution board for Emergency light	0d	0d	20-Dec-23 A		04-Dec-23		
PRO-EQ-MR09-1450	MR09 - Purchase Order - Distribution board for Emergency light	10d	1d	21-Dec-23 A	21-Dec-23 A	12-Jan-24	25-Jan-24	
PRO-EQ-MR09-1620	MR09 - Vendor Quotation - Distribution board for Emergency light	9d	1d	21-Dec-23 A	21-Dec-23 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR09-1680	MR09 - Vendor Evaluation - Distribution board for Emergency light	15d	1d	21-Dec-23 A	21-Dec-23 A	19-Dec-23	11-Jan-24	
PRO-EQ-MR09-1460	MR09 - Manufacturing & Ex-Works - Distribution board for Emergency light	165d	251d	22-Dec-23 A	24-Sep-24 A	26-Jan-24	08-Jul-24	



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR09-1480	MR09 - Transportation & Yard Delivery - Distribution board for Emergency light	5d	4d	21-Sep-24 A	24-Sep-24 A	09-Jul-24	13-Jul-24	
Telecom System		248d	288d	16-Oct-23 A	27-Sep-24 A	07-Dec-23	11-Oct-24	
PRO-EQ-MR10-1000	MR10 - Request for Quotation - Telecom System	1d	2d	16-Oct-23 A	17-Oct-23 A	07-Dec-23	07-Dec-23	
PRO-EQ-MR10-1070	MR10 - MR Issued - Telecom System	0d	0d	16-Oct-23 A		07-Dec-23		
PRO-EQ-MR10-1080	MR10 - Vendor Quotation - Telecom System	9d	2d	18-Oct-23 A	19-Oct-23 A	11-Dec-23	21-Dec-23	
PRO-EQ-MR10-1030	MR10 - Purchase Order - Telecom System	10d	1d	27-Feb-24 A	27-Feb-24 A	15-Jan-24	26-Jan-24	
PRO-EQ-MR10-1040	MR10 - Manufacturing & Ex-Works - Telecom System	195d	200d	27-Feb-24 A	27-Sep-24 A	27-Jan-24	06-Oct-24	
PRO-EQ-MR10-1060	MR10 - Transportation & Yard Delivery - Telecom System	5d	2d	26-Sep-24 A	27-Sep-24 A	07-Oct-24	11-Oct-24	
Waste Water Tank		322d	274d	02-Nov-23 A	27-Sep-24 A	20-Oct-23	03-Oct-24	
PRO-EQ-MR11-1000	MR11 - Request for Quotation - Waste Water Tank	1d	1d	02-Nov-23 A	02-Nov-23 A	20-Oct-23	20-Oct-23	
PRO-EQ-MR11-1140	MR11 - MR Issued - Waste Water Tank	0d	0d	02-Nov-23 A		20-Oct-23		
PRO-EQ-MR11-1150	MR11 - Vendor Quotation - Waste Water Tank	9d	5d	03-Nov-23 A	09-Nov-23 A	23-Oct-23	03-Nov-23	
PRO-EQ-MR11-1180	MR11 - Vendor Evaluation - Waste Water Tank	15d	120d	03-Nov-23 A	26-Apr-24 A	06-Nov-23	24-Nov-23	
PRO-EQ-MR11-1030	MR11 - Purchase Order - Waste Water Tank	10d	1d	26-Apr-24 A	26-Apr-24 A	27-Nov-23	11-Dec-23	
PRO-EQ-MR11-1040	MR11 - Manufacturing & Ex-Works - Waste Water Tank	195d	141d	26-Apr-24 A	27-Sep-24 A	12-Dec-23	28-Sep-24	
PRO-EQ-MR11-1060	MR11 - Transportation & Yard Delivery - Waste Water Tank	5d	1d	27-Sep-24 A	27-Sep-24 A	29-Sep-24	03-Oct-24	
Instrument Air Receiver		273d	307d	27-Oct-23 A	31-Oct-24	20-Oct-23	17-Sep-24	78d
PRO-EQ-MR11-1070	MR11 - Request for Quotation - Instrument Air Receiver	1d	1d	27-Oct-23 A	27-Oct-23 A	20-Oct-23	20-Oct-23	
PRO-EQ-MR11-1160	MR11 - MR Issued - Instrument Air Receiver	0d	0d	27-Oct-23 A		20-Oct-23		
PRO-EQ-MR11-1170	MR11 - Vendor Quotation - Instrument Air Receiver	9d	9d	30-Oct-23 A	10-Nov-23 A	23-Oct-23	03-Nov-23	
PRO-EQ-MR11-1100	MR11 - Purchase Order - Instrument Air Receiver	10d	12d	08-Feb-24 A	23-Feb-24 A	22-Nov-23	05-Dec-23	
PRO-EQ-MR11-1110	MR11 - Manufacturing & Ex-Works - Instrument Air Receiver	203d	238d	23-Feb-24 A	31-Oct-24	06-Dec-23	12-Sep-24	55d
PRO-EQ-MR11-1130	MR11 - Transportation & Yard Delivery - Instrument Air Receiver	5d	5d	27-Oct-24	31-Oct-24	13-Sep-24	17-Sep-24	91d
Davit Crane		230d	286d	16-Jan-24 A	20-Dec-24	15-Jan-24	13-Sep-24	53d
PRO-EQ-MR12-1000	MR12 - Request for Quotation - Davit Crane	1d	49d	16-Jan-24 A	22-Mar-24 A	15-Jan-24	15-Jan-24	
PRO-EQ-MR12-1070	MR12 - MR Issued - Davit Crane	0d	0d	16-Jan-24 A		15-Jan-24		
PRO-EQ-MR12-1080	MR12 - Vendor Quotation - Davit Crane	9d	12d	22-Mar-24 A	09-Apr-24 A	16-Jan-24	26-Jan-24	
PRO-EQ-MR12-1030	MR12 - Purchase Order - Davit Crane	10d	26d	10-Apr-24 A	17-May-24 A	14-Feb-24	27-Feb-24	
PRO-EQ-MR12-1040	MR12 - Manufacturing & Ex-Works - Davit Crane	100d	199d	17-May-24 A	15-Dec-24	28-Feb-24	08-Sep-24	54d
PRO-EQ-MR12-1060	MR12 - Transportation & Yard Delivery - Davit Crane	5d	5d	16-Dec-24	20-Dec-24	09-Sep-24	13-Sep-24	63d
Instrument Air Package		282d	307d	27-Oct-23 A	31-Oct-24	13-Oct-23	25-Sep-24	71d
PRO-EQ-MR13-1000	MR13 - Request for Quotation - Instrument Air Package	1d	1d	27-Oct-23 A	27-Oct-23 A	13-Oct-23	13-Oct-23	
PRO-EQ-MR13-1070	MR13 - MR Issued - Instrument Air Package	0d	0d	27-Oct-23 A		13-Oct-23		
PRO-EQ-MR13-1080	MR13 - Vendor Quotation - Instrument Air Package	9d	9d	30-Oct-23 A	10-Nov-23 A	16-Oct-23	26-Oct-23	
PRO-EQ-MR13-1030	MR13 - Purchase Order - Instrument Air Package	10d	12d	08-Feb-24 A	23-Feb-24 A	15-Nov-23	28-Nov-23	
PRO-EQ-MR13-1040	MR13 - Manufacturing & Ex-Works - Instrument Air Package	197d	238d	23-Feb-24 A	31-Oct-24	29-Nov-23	20-Sep-24	55d
PRO-EQ-MR13-1060	MR13 - Transportation & Yard Delivery - Instrument Air Package	5d	5d	27-Oct-24	31-Oct-24	21-Sep-24	25-Sep-24	83d
Seawater Intake Pump		346d	247d	01-Mar-24 A	20-Dec-24	06-Nov-23	12-Feb-25	43d
PRO-EQ-MR14-1000	MR14 - Request for Quotation - Seawater Intake Pump - Vertical suspended motor type	1d	2d	01-Mar-24 A	04-Mar-24 A	06-Nov-23	06-Nov-23	
PRO-EQ-MR14-1070	MR14 - MR Issued - Seawater Intake Pump - Verticalsuspended motor type	0d	0d	01-Mar-24 A		06-Nov-23		
PRO-EQ-MR14-1080	MR14 - Vendor Quotation - Seawater Intake Pump - Vertical suspended motor type	9d	10d	04-Mar-24 A	15-Mar-24 A	07-Nov-23	17-Nov-23	
PRO-EQ-MR14-1030	MR14 - Purchase Order - Seawater Intake Pump - Vertical suspended motor type	10d	35d	16-Mar-24 A	08-May-24 A	06-Dec-23	20-Dec-23	
PRO-EQ-MR14-1040	MR14 - Manufacturing & Ex-Works - Seawater Intake Pump - Vertical suspended motor type	280d	208d	08-May-24 A	15-Dec-24	21-Dec-23	07-Feb-25	18d
PRO-EQ-MR14-1060	MR14 - Transportation & Yard Delivery - Seawater Intake Pump - Vertical suspended motor type	5d	5d	16-Dec-24	20-Dec-24	08-Feb-25	12-Feb-25	51d
Liferaft		145d	145d	08-Jul-24 A	27-Dec-24	09-Apr-24	16-Jul-24	51d
PRO-EQ-MR15-1070	MR15 - MR Issued - Liferaft	0d	0d	08-Jul-24 A		09-Apr-24		

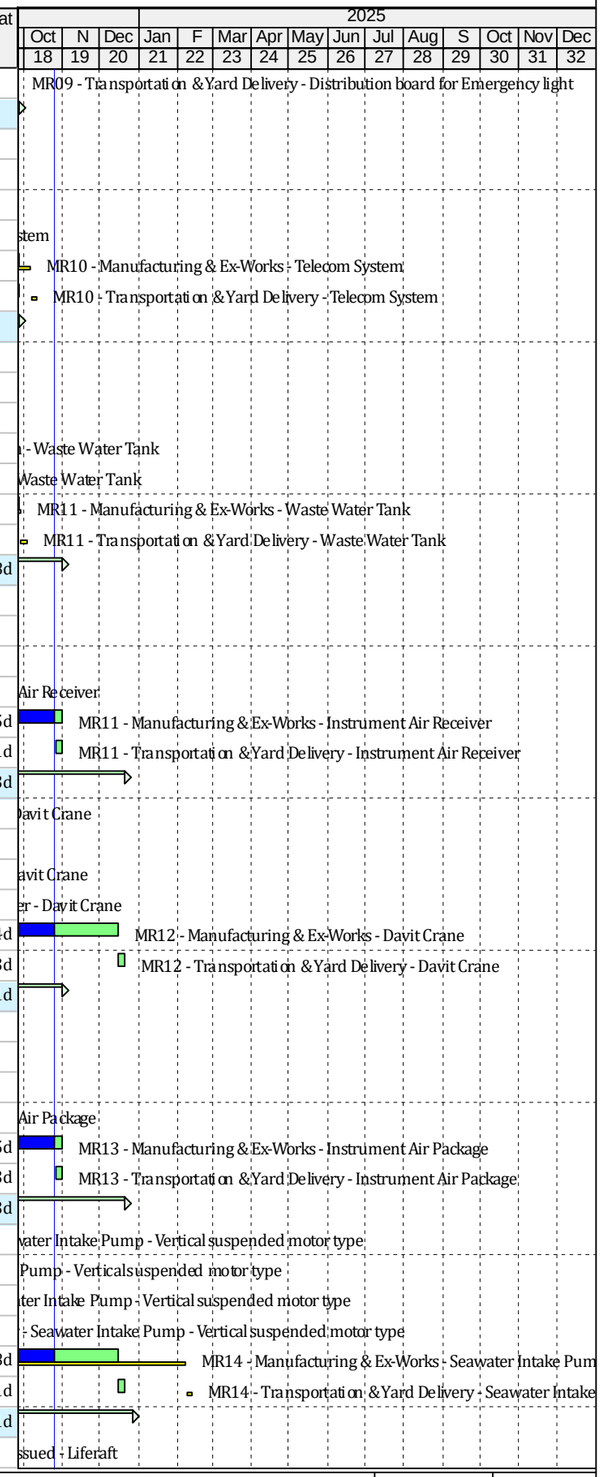


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR15-1000	MR15 - Request for Quotation - Liferaft	1d	1d	11-Jul-24 A	11-Jul-24 A	09-Apr-24	09-Apr-24	
PRO-EQ-MR15-1080	MR15 - Vendor Quotation - Liferaft	9d	6d	11-Jul-24 A	18-Jul-24 A	10-Apr-24	22-Apr-24	
PRO-EQ-MR15-1090	MR15 - Vendor Evaluation - Liferaft	15d	15d	19-Jul-24 A	08-Aug-24 A	23-Apr-24	15-May-24	
PRO-EQ-MR15-1030	MR15 - Purchase Order - Liferaft	10d	1d	09-Aug-24 A	09-Aug-24 A	16-May-24	29-May-24	
PRO-EQ-MR15-1040	MR15 - Manufacturing & Ex-Works - Liferaft	43d	124d	09-Aug-24 A	20-Dec-24	30-May-24	11-Jul-24	51d
PRO-EQ-MR15-1060	MR15 - Transportation &Yard Delivery - Liferaft	5d	5d	21-Dec-24	27-Dec-24	12-Jul-24	16-Jul-24	60d
Hydrogen Vent		238d	247d	09-Feb-24 A	29-Nov-24	18-Oct-23	05-Sep-24	48d
PRO-EQ-MR16-1000	MR16 - Request for Quotation - Hydrogen Vent	1d	1d	09-Feb-24 A	09-Feb-24 A	18-Oct-23	18-Oct-23	
PRO-EQ-MR16-1070	MR16 - MR Issued - Hydrogen Vent	0d	0d	09-Feb-24 A		18-Oct-23		
PRO-EQ-MR16-1080	MR16 - Vendor Quotation - Hydrogen Vent	3d	17d	09-Feb-24 A	04-Mar-24 A	19-Oct-23	31-Oct-23	
PRO-EQ-MR16-1030	MR16 - Purchase Order - Hydrogen Vent	10d	39d	05-Mar-24 A	30-Apr-24 A	20-Nov-23	01-Dec-23	
PRO-EQ-MR16-1040	MR16 - Manufacturing & Ex-Works - Hydrogen Vent	148d	195d	30-Apr-24 A	24-Nov-24	02-Dec-23	31-Aug-24	48d
PRO-EQ-MR16-1060	MR16 - Transportation &Yard Delivery - Hydrogen Vent	5d	5d	25-Nov-24	29-Nov-24	01-Sep-24	05-Sep-24	56d
Container 40' ISO for Water treatment system		278d	292d	15-Nov-23 A	31-Oct-24	14-Nov-23	29-Jul-24	72d
PRO-EQ-MR17-1000	MR17 - Request for Quotation - Container 40' ISO for Water treatment system	1d	1d	15-Nov-23 A	15-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-EQ-MR17-1070	MR17 - MR Issued - Container 40' ISO for Water treatment system	0d	0d	15-Nov-23 A		14-Nov-23		
PRO-EQ-MR17-1080	MR17 - Vendor Quotation - Container 40' ISO for Water treatment system	9d	10d	16-Nov-23 A	29-Nov-23 A	15-Nov-23	27-Nov-23	
PRO-EQ-MR17-1030	MR17 - Purchase Order - Container 40' ISO for Water treatment system	10d	1d	23-Feb-24 A	23-Feb-24 A	28-Dec-23	11-Jan-24	
PRO-EQ-MR17-1040	MR17 - Manufacturing & Ex-Works - Container 40' ISO for Water treatment system	231d	238d	23-Feb-24 A	31-Oct-24	12-Jan-24	24-Jul-24	49d
PRO-EQ-MR17-1060	MR17 - Transportation &Yard Delivery - Container 40' ISO for Water treatment system	5d	5d	27-Oct-24	31-Oct-24	25-Jul-24	29-Jul-24	84d
JB with disconnector for Temporary Generator		178d	111d	14-Jun-24 A	22-Oct-24 A	08-Jan-24	27-Jul-24	
PRO-EQ-MR18-1000	MR18 - Request for Quotation - JB with disconnector for Temporary Generator	1d	2d	14-Jun-24 A	17-Jun-24 A	08-Jan-24	08-Jan-24	
PRO-EQ-MR18-1070	MR18 - MR Issued - JB with disconnector for Temporary Generator	0d	0d	14-Jun-24 A		08-Jan-24		
PRO-EQ-MR18-1080	MR18 - Vendor Quotation - JB with disconnector for Temporary Generator	9d	4d	18-Jun-24 A	21-Jun-24 A	09-Jan-24	19-Jan-24	
PRO-EQ-MR18-1090	MR18 - Vendor Evaluation - JB with disconnector for Temporary Generator	15d	16d	21-Jun-24 A	12-Jul-24 A	22-Jan-24	09-Feb-24	
PRO-EQ-MR18-1030	MR18 - Purchase Order - JB with disconnector for Temporary Generator	10d	1d	19-Jul-24 A	19-Jul-24 A	12-Feb-24	23-Feb-24	
PRO-EQ-MR18-1040	MR18 - Manufacturing & Ex-Works - JB with disconnector for Temporary Generator	130d	82d	19-Jul-24 A	22-Oct-24 A	24-Feb-24	22-Jul-24	
PRO-EQ-MR18-1060	MR18 - Transportation &Yard Delivery - JB with disconnector for Temporary Generator	5d	3d	20-Oct-24 A	22-Oct-24 A	23-Jul-24	27-Jul-24	
SDV & BDV		261d	239d	15-Nov-23 A	30-Aug-24 A	14-Nov-23	01-Oct-24	
PRO-EQ-MR19-1000	MR19 - Request for Quotation - SDV & BDV	1d	2d	15-Nov-23 A	16-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-EQ-MR19-1070	MR19 - MR Issued - SDV & BDV	0d	0d	15-Nov-23 A		14-Nov-23		
PRO-EQ-MR19-1080	MR19 - Vendor Quotation - SDV & BDV	9d	9d	17-Nov-23 A	29-Nov-23 A	15-Nov-23	27-Nov-23	
PRO-EQ-MR19-1030	MR19 - Purchase Order - SDV & BDV	10d	1d	01-Feb-24 A	01-Feb-24 A	18-Dec-23	03-Jan-24	
PRO-EQ-MR19-1040	MR19 - Manufacturing & Ex-Works - SDV & BDV	209d	198d	01-Feb-24 A	30-Aug-24 A	07-Jan-24	26-Sep-24	
PRO-EQ-MR19-1060	MR19 - Transportation &Yard Delivery - SDV & BDV	5d	5d	26-Aug-24 A	30-Aug-24 A	27-Sep-24	01-Oct-24	
Actuated Control Valves		286d	291d	21-Nov-23 A	06-Nov-24	27-Nov-23	30-Sep-24	86d
PRO-EQ-MR19-1090	MR19 - Request for Quotation - Actuated Control Valves	1d	1d	21-Nov-23 A	21-Nov-23 A	27-Nov-23	27-Nov-23	
PRO-EQ-MR19-1100	MR19 - MR Issued - Actuated Control Valves	0d	0d	21-Nov-23 A		27-Nov-23		
PRO-EQ-MR19-1110	MR19 - Vendor Quotation - Actuated Control Valves	9d	11d	22-Nov-23 A	06-Dec-23 A	28-Nov-23	11-Dec-23	
PRO-EQ-MR19-1130	MR19 - Purchase Order - Actuated Control Valves	10d	1d	05-Apr-24 A	05-Apr-24 A	02-Jan-24	15-Jan-24	
PRO-EQ-MR19-1140	MR19 - Manufacturing & Ex-Works - Actuated Control Valves	151d	197d	05-Apr-24 A	01-Nov-24	16-Jan-24	25-Sep-24	18d
PRO-EQ-MR19-1160	MR19 - Transportation &Yard Delivery - Actuated Control Valves	5d	5d	02-Nov-24	06-Nov-24	26-Sep-24	30-Sep-24	100d
Pressure Safety Valves		213d	230d	12-Dec-23 A	14-Sep-24 A	27-Nov-23	30-Sep-24	
PRO-EQ-MR19-1170	MR19 - Request for Quotation - Pressure Safety Valves	1d	1d	12-Dec-23 A	12-Dec-23 A	27-Nov-23	27-Nov-23	
PRO-EQ-MR19-1180	MR19 - MR Issued - Pressure Safety Valves	0d	0d	12-Dec-23 A		27-Nov-23		
PRO-EQ-MR19-1190	MR19 - Vendor Quotation - Pressure Safety Valves	9d	9d	12-Dec-23 A	22-Dec-23 A	28-Nov-23	11-Dec-23	

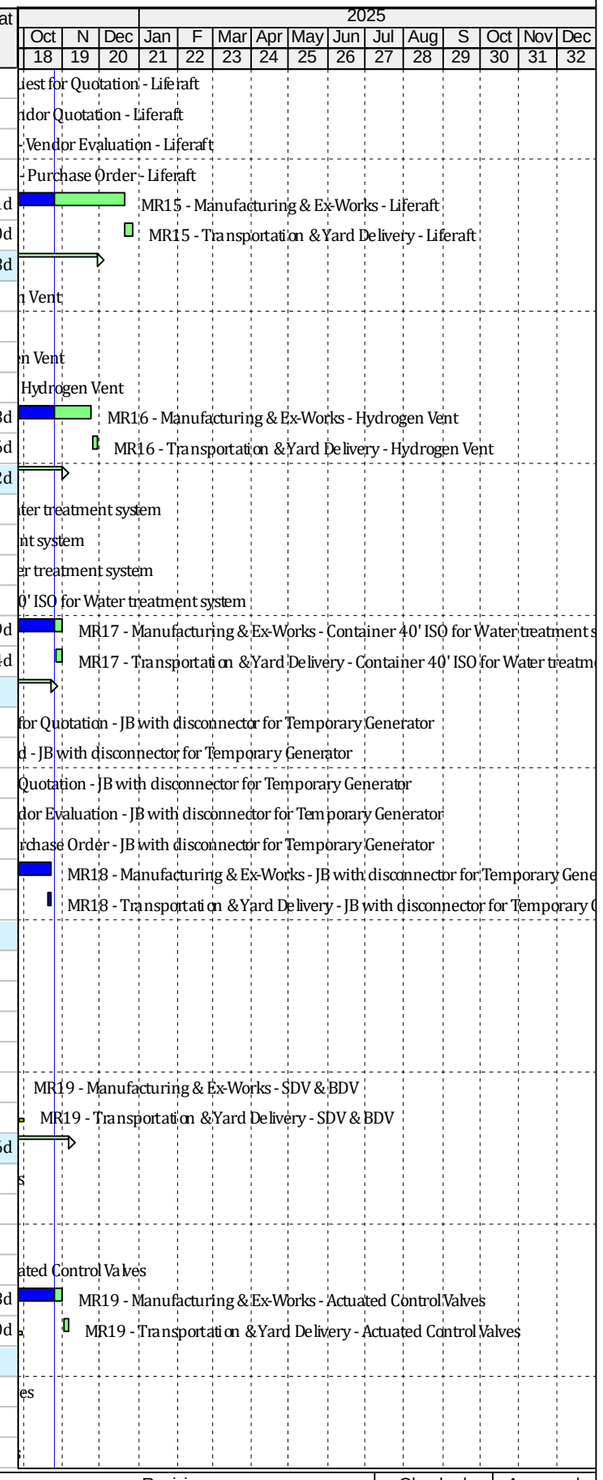

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-EQ-MR19-1210	MR19 - Purchase Order - Pressure Safety Valves	10d	51d	23-Dec-23 A	07-Mar-24 A	02-Jan-24	15-Jan-24	
PRO-EQ-MR19-1220	MR19 - Manufacturing & Ex-Works - Pressure Safety Valves	169d	178d	07-Mar-24 A	14-Sep-24 A	16-Jan-24	25-Sep-24	
PRO-EQ-MR19-1240	MR19 - Transportation & Yard Delivery - Pressure Safety Valves	5d	33d	12-Aug-24 A	14-Sep-24 A	26-Sep-24	30-Sep-24	
Nav. Aids & anti collision system		225d	230d	26-Jan-24 A	25-Oct-24 A	04-Dec-23	11-Jul-24	
PRO-EQ-MR20-1000	MR20 - Request for Quotation - Nav. Aids & anti collision system (incl. AC UPS)	1d	11d	26-Jan-24 A	09-Feb-24 A	04-Dec-23	04-Dec-23	
PRO-EQ-MR20-1070	MR20 - MR Issued - Nav. Aids & anti collision system (incl. AC UPS)	0d	0d	26-Jan-24 A		04-Dec-23		
PRO-EQ-MR20-1080	MR20 - Vendor Quotation - Nav. Aids & anti collision system (incl. AC UPS)	9d	8d	09-Feb-24 A	20-Feb-24 A	05-Dec-23	18-Dec-23	
PRO-EQ-MR20-1030	MR20 - Purchase Order - Nav. Aids & anti collision system (incl. AC UPS)	10d	1d	11-Apr-24 A	11-Apr-24 A	10-Jan-24	23-Jan-24	
PRO-EQ-MR20-1040	MR20 - Manufacturing & Ex-Works - Nav. Aids & anti collision system (incl. AC UPS)	113d	183d	12-Apr-24 A	25-Oct-24 A	24-Jan-24	06-Jul-24	
PRO-EQ-MR20-1060	MR20 - Transportation & Yard Delivery - Nav. Aids & anti collision system (incl. AC UPS)	5d	1d	25-Oct-24 A	25-Oct-24 A	07-Jul-24	11-Jul-24	
Bulk Material - Steel		373d	421d	25-Aug-23 A	15-Jan-25	21-Sep-23	04-Nov-24	71d
Primary Structures - Plate Girders		77d	133d	25-Aug-23 A	02-Feb-24 A	21-Sep-23	16-Dec-23	
PRO-BLK-MR21-1060	MR21 - MTO Issued - Primary Structures - Plate Girders	0d	0d	25-Aug-23 A		21-Sep-23		
PRO-BLK-MR21-1000	MR21 - Request for Quotation - Primary Structures - Plate Girders	1d	2d	28-Aug-23 A	29-Aug-23 A	21-Sep-23	21-Sep-23	
PRO-BLK-MR21-1070	MR21 - Vendor Quotation - Primary Structures - Plate Girders	9d	2d	29-Aug-23 A	30-Aug-23 A	22-Sep-23	04-Oct-23	
PRO-BLK-MR21-1140	MR21 - Vendor Evaluation - Primary Structures - Plate Girders	8d	5d	01-Sep-23 A	07-Sep-23 A	05-Oct-23	16-Oct-23	
PRO-BLK-MR21-1030	MR21 - Purchase Order - Primary Structures - Plate Girders	10d	5d	04-Sep-23 A	08-Sep-23 A	17-Oct-23	30-Oct-23	
PRO-BLK-MR21-1040	MR21 - Manufacturing & Ex-Works - Primary Structures - Plate Girders	42d	132d	11-Sep-23 A	02-Feb-24 A	31-Oct-23	11-Dec-23	
PRO-BLK-MR21-1050	MR21 - Transportation & Yard Delivery - Primary Structures - Plate Girders	5d	82d	08-Nov-23 A	02-Feb-24 A	12-Dec-23	16-Dec-23	
Primary Structures - Nodes		107d	25d	10-Oct-23 A	08-Nov-23 A	21-Sep-23	20-Dec-23	
PRO-BLK-MR21-1090	MR21 - MTO Issued - Primary Structures - Plates for Nodes	0d	0d	10-Oct-23 A		21-Sep-23		
PRO-BLK-MR21-1080	MR21 - Request for Quotation - Primary Structures - Plates for Nodes	1d	2d	11-Oct-23 A	12-Oct-23 A	21-Sep-23	21-Sep-23	
PRO-BLK-MR21-1100	MR21 - Vendor Quotation - Primary Structures - Plates for Nodes	9d	2d	12-Oct-23 A	13-Oct-23 A	22-Sep-23	04-Oct-23	
PRO-BLK-MR21-1110	MR21 - Purchase Order - Primary Structures - Plates for Nodes	10d	2d	16-Oct-23 A	17-Oct-23 A	17-Oct-23	30-Oct-23	
PRO-BLK-MR21-1150	MR21 - Vendor Evaluation - Primary Structures - Plates for Nodes	8d	2d	16-Oct-23 A	17-Oct-23 A	05-Oct-23	16-Oct-23	
PRO-BLK-MR21-1120	MR21 - Manufacturing & Ex-Works - Primary Structures - Plates for Nodes	46d	21d	19-Oct-23 A	08-Nov-23 A	31-Oct-23	15-Dec-23	
PRO-BLK-MR21-1130	MR21 - Transportation & Yard Delivery - Primary Structures - Plates for Nodes	5d	1d	08-Nov-23 A	08-Nov-23 A	16-Dec-23	20-Dec-23	
Primary Structures - Seamless Pipe (column)		97d	53d	26-Sep-23 A	27-Nov-23 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR22-1000	MR22 - Request for Quotation - Primary Structures - Seamless Pipe (column)	1d	1d	26-Sep-23 A	26-Sep-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR22-1060	MR22 - MTO Issued - Primary Structures - Seamless Pipe (column)	0d	0d	26-Sep-23 A		30-Oct-23		
PRO-BLK-MR22-1070	MR22 - Vendor Quotation - Primary Structures - Seamless Pipe (column)	9d	5d	27-Sep-23 A	03-Oct-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR22-1080	MR22 - Vendor Evaluation - Primary Structures - Seamless Pipe (column)	10d	8d	04-Oct-23 A	13-Oct-23 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR22-1030	MR22 - Purchase Order - Primary Structures - Seamless Pipe (column)	10d	5d	23-Oct-23 A	27-Oct-23 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR22-1040	MR22 - Manufacturing & Ex-Works - Primary Structures - Seamless Pipe (column)	76d	29d	30-Oct-23 A	27-Nov-23 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR22-1050	MR22 - Transportation & Yard Delivery - Primary Structures - Seamless Pipe (column)	5d	1d	27-Nov-23 A	27-Nov-23 A	25-Jan-24	29-Jan-24	
Primary Structures - Rolled Pipe (column)		74d	53d	10-Oct-23 A	12-Dec-23 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR23-1060	MR23 - MTO Issued - Primary Structures - Rolled Pipe (column)	0d	0d	10-Oct-23 A		30-Oct-23		
PRO-BLK-MR23-1000	MR23 - Request for Quotation - Primary Structures - Rolled Pipe (column)	1d	2d	11-Oct-23 A	12-Oct-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR23-1070	MR23 - Vendor Quotation - Primary Structures - Rolled Pipe (column)	9d	2d	12-Oct-23 A	13-Oct-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR23-1030	MR23 - Purchase Order - Primary Structures - Rolled Pipe (column)	10d	2d	16-Oct-23 A	17-Oct-23 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR23-1080	MR23 - Vendor Evaluation - Primary Structures - Rolled Pipe (column)	10d	2d	16-Oct-23 A	17-Oct-23 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR23-1040	MR23 - Manufacturing & Ex-Works - Primary Structures - Rolled Pipe (column)	30d	56d	18-Oct-23 A	12-Dec-23 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR23-1050	MR23 - Transportation & Yard Delivery - Primary Structures - Rolled Pipe (column)	5d	34d	08-Nov-23 A	12-Dec-23 A	25-Jan-24	29-Jan-24	
Primary Structures - Seamless Pipe (bracing)		97d	53d	26-Sep-23 A	27-Nov-23 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR24-1000	MR24 - Request for Quotation - Primary Structures - Seamless Pipe (bracing)	1d	1d	26-Sep-23 A	26-Sep-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR24-1060	MR24 - MTO Issued - Primary Structures - Seamless Pipe (bracing)	0d	0d	26-Sep-23 A		30-Oct-23		

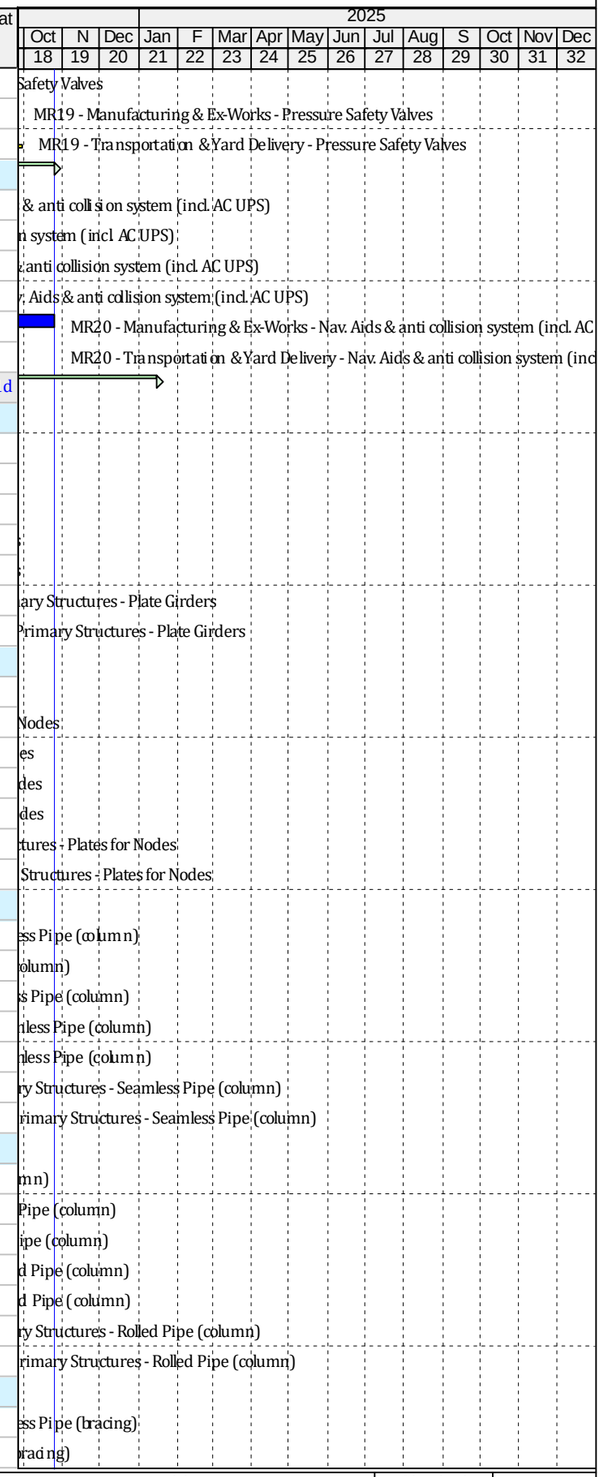

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR24-1070	MR24 - Vendor Quotation - Primary Structures - Seamless Pipe (bracing)	9d	5d	27-Sep-23 A	03-Oct-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR24-1080	MR24 - Vendor Evaluation - Primary Structures - Seamless Pipe (bracing)	10d	8d	04-Oct-23 A	13-Oct-23 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR24-1030	MR24 - Purchase Order - Primary Structures - Seamless Pipe (bracing)	10d	5d	23-Oct-23 A	27-Oct-23 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR24-1040	MR24 - Manufacturing & Ex-Works - Primary Structures - Seamless Pipe (bracing)	76d	29d	30-Oct-23 A	27-Nov-23 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR24-1050	MR24 - Transportation & Yard Delivery - Primary Structures - Seamless Pipe (bracing)	5d	1d	27-Nov-23 A	27-Nov-23 A	25-Jan-24	29-Jan-24	
Primary Structures - Rolled Pipe (bracing)		86d	41d	10-Oct-23 A	27-Nov-23 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR25-1000	MR25 - Request for Quotation - Primary Structures - Rolled Pipe (bracing)	1d	3d	10-Oct-23 A	12-Oct-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR25-1060	MR25 - MTO Issued - Primary Structures - Rolled Pipe (bracing)	0d	0d	10-Oct-23 A		30-Oct-23		
PRO-BLK-MR25-1070	MR25 - Vendor Quotation - Primary Structures - Rolled Pipe (bracing)	9d	2d	12-Oct-23 A	13-Oct-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR25-1030	MR25 - Purchase Order - Primary Structures - Rolled Pipe (bracing)	10d	2d	16-Oct-23 A	17-Oct-23 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR25-1080	MR25 - Vendor Evaluation - Primary Structures - Rolled Pipe (bracing)	10d	2d	16-Oct-23 A	17-Oct-23 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR25-1040	MR25 - Manufacturing & Ex-Works - Primary Structures - Rolled Pipe (bracing)	30d	41d	18-Oct-23 A	27-Nov-23 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR25-1050	MR25 - Transportation & Yard Delivery - Primary Structures - Rolled Pipe (bracing)	5d	1d	27-Nov-23 A	27-Nov-23 A	25-Jan-24	29-Jan-24	
Transition Piece - Box Girders		199d	128d	21-Nov-23 A	26-Apr-24 A	10-Apr-24	04-Sep-24	
PRO-BLK-MR33-1000	MR33 - Request for Quotation - Transition Piece - Box Girders	1d	1d	21-Nov-23 A	21-Nov-23 A	10-Apr-24	10-Apr-24	
PRO-BLK-MR33-1060	MR33 - MTO Issued - Transition Piece - Box Girders	0d	0d	21-Nov-23 A		10-Apr-24		
PRO-BLK-MR33-1070	MR33 - Vendor Quotation - Transition Piece - Box Girders	9d	4d	22-Nov-23 A	27-Nov-23 A	11-Apr-24	23-Apr-24	
PRO-BLK-MR33-1080	MR33 - Vendor Evaluation - Transition Piece - Box Girders	10d	33d	27-Nov-23 A	16-Jan-24 A	24-Apr-24	09-May-24	
PRO-BLK-MR33-1030	MR33 - Purchase Order - Transition Piece - Box Girders	10d	1d	16-Jan-24 A	16-Jan-24 A	10-May-24	23-May-24	
PRO-BLK-MR33-1040	MR33 - Manufacturing & Ex-Works - Transition Piece - Box Girders	205d	102d	16-Jan-24 A	26-Apr-24 A	24-May-24	30-Aug-24	
PRO-BLK-MR33-1050	MR33 - Transportation & Yard Delivery - Transition Piece - Box Girders	5d	40d	15-Mar-24 A	26-Apr-24 A	31-Aug-24	04-Sep-24	
Upper Grillage		89d	56d	09-Feb-24 A	16-Apr-24 A	16-Oct-23	14-Jan-24	
PRO-BLK-MR45-1000	MR45 - Request for Quotation - Upper Grillage	1d	1d	09-Feb-24 A	09-Feb-24 A	16-Oct-23	16-Oct-23	
PRO-BLK-MR45-1060	MR45 - MTO Issued - Upper Grillage	0d	0d	09-Feb-24 A		16-Oct-23		
PRO-BLK-MR45-1070	MR45 - Vendor Quotation - Upper Grillage	9d	11d	09-Feb-24 A	23-Feb-24 A	17-Oct-23	27-Oct-23	
PRO-BLK-MR45-1030	MR45 - Purchase Order - Upper Grillage	10d	1d	23-Feb-24 A	23-Feb-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR45-1080	MR45 - Vendor Evaluation - Upper Grillage	10d	1d	23-Feb-24 A	23-Feb-24 A	30-Oct-23	13-Nov-23	
PRO-BLK-MR45-1040	MR45 - Manufacturing & Ex-Works - Upper Grillage	30d	52d	25-Feb-24 A	16-Apr-24 A	28-Nov-23	09-Jan-24	
PRO-BLK-MR45-1050	MR45 - Transportation & Yard Delivery - Upper Grillage	5d	1d	16-Apr-24 A	16-Apr-24 A	10-Jan-24	14-Jan-24	
Rigging Platform		87d	101d	13-May-24 A	08-Sep-24 A	13-May-24	08-Sep-24	
PRO-BLK-MR47-1000	MR47 - Request for Quotation - Rigging Platform - DELETED	1d	1d	13-May-24 A	13-May-24 A	13-May-24	13-May-24	
PRO-BLK-MR47-1060	MR47 - MTO Issued - Rigging Platform - DELETED	0d	0d	13-May-24 A		13-May-24		
PRO-BLK-MR47-1070	MR47 - Vendor Quotation - Rigging Platform - DELETED	9d	9d	14-May-24 A	24-May-24 A	14-May-24	24-May-24	
PRO-BLK-MR47-1010	MR47 - Vendor Evaluation - Rigging Platform - DELETED	10d	10d	27-May-24 A	07-Jun-24 A	27-May-24	07-Jun-24	
PRO-BLK-MR47-1030	MR47 - Purchase Order - Rigging Platform - DELETED	10d	10d	10-Jun-24 A	21-Jun-24 A	10-Jun-24	21-Jun-24	
PRO-BLK-MR47-1040	MR47 - Manufacturing & Ex-Works - Rigging Platform - TO BE DELETED	60d	60d	22-Jun-24 A	03-Sep-24 A	22-Jun-24	03-Sep-24	
PRO-BLK-MR47-1050	MR47 - Transportation & Yard Delivery - Rigging Platform - TO BE DELETED	5d	5d	04-Sep-24 A	08-Sep-24 A	04-Sep-24	08-Sep-24	
Secondary Structures - Cones		43d	66d	30-Oct-23 A	21-Jan-24 A	30-Oct-23	21-Jan-24	
PRO-BLK-MR26-1000	MR26 - Request for Quotation - Secondary Structures - Cones - DELETED	1d	1d	30-Oct-23 A	30-Oct-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR26-1060	MR26 - MTO Issued - Secondary Structures - Cones - DELETED	0d	0d	30-Oct-23 A		30-Oct-23		
PRO-BLK-MR26-1070	MR26 - Vendor Quotation - Secondary Structures - Cones - DELETED	9d	9d	31-Oct-23 A	13-Nov-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR26-1080	MR26 - Vendor Evaluation - Secondary Structures - Cones - DELETED	5d	5d	14-Nov-23 A	20-Nov-23 A	14-Nov-23	20-Nov-23	
PRO-BLK-MR26-1030	MR26 - Purchase Order - Secondary Structures - Cones - DELETED	10d	23d	21-Nov-23 A	25-Dec-23 A	21-Nov-23	04-Dec-23	
PRO-BLK-MR26-1040	MR26 - Manufacturing & Ex-Works - Secondary Structures - Cones - DELETED	10d	10d	25-Dec-23 A	16-Jan-24 A	05-Dec-23	16-Jan-24	
PRO-BLK-MR26-1050	MR26 - Transportation & Yard Delivery - Secondary Structures - Cones - DELETED	5d	6d	16-Jan-24 A	21-Jan-24 A	17-Jan-24	21-Jan-24	
Secondary Structures - Beams		116d	134d	26-Sep-23 A	06-Mar-24 A	30-Oct-23	21-Jan-24	

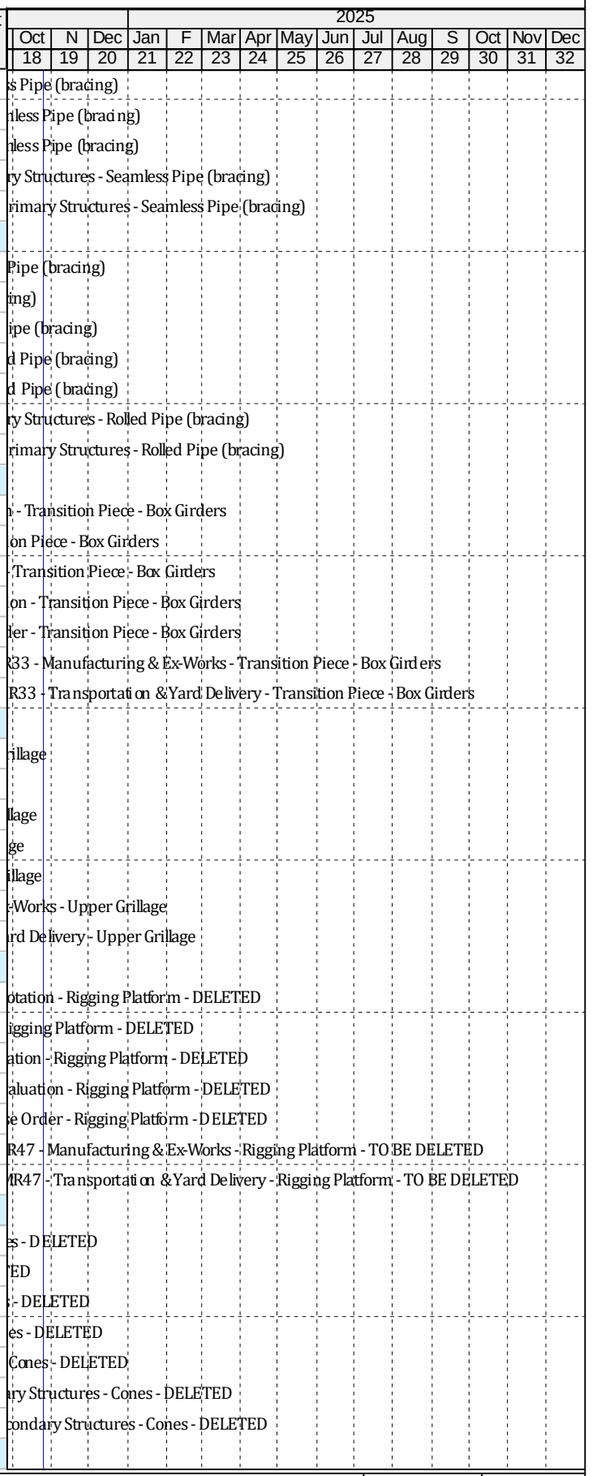

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR27-1000	MR27 - Request for Quotation - Secondary Structures - Beams	1d	1d	26-Sep-23 A	26-Sep-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR27-1060	MR27 - MTO Issued - Secondary Structures - Beams	0d	0d	26-Sep-23 A		30-Oct-23		
PRO-BLK-MR27-1070	MR27 - Vendor Quotation - Secondary Structures - Beams	9d	3d	27-Sep-23 A	29-Sep-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR27-1080	MR27 - Vendor Evaluation - Secondary Structures - Beams	5d	15d	02-Oct-23 A	20-Oct-23 A	14-Nov-23	20-Nov-23	
PRO-BLK-MR27-1030	MR27 - Purchase Order - Secondary Structures - Beams	10d	7d	23-Oct-23 A	31-Oct-23 A	21-Nov-23	04-Dec-23	
PRO-BLK-MR27-1040	MR27 - Manufacturing & Ex-Works - Secondary Structures - Beams	30d	113d	02-Nov-23 A	06-Mar-24 A	05-Dec-23	16-Jan-24	
PRO-BLK-MR27-1050	MR27 - Transportation &Yard Delivery - Secondary Structures - Beams	26d	73d	21-Dec-23 A	06-Mar-24 A	17-Jan-24	21-Jan-24	
Secondary Structures - Structural Plates		71d	26d	20-Nov-23 A	20-Dec-23 A	30-Oct-23	14-Jan-24	
PRO-BLK-MR28-1000	MR28 - Request for Quotation - Secondary Structures - Structural Plates	1d	1d	20-Nov-23 A	20-Nov-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR28-1060	MR28 - MTO Issued - Secondary Structures - Structural Plates	0d	0d	20-Nov-23 A		30-Oct-23		
PRO-BLK-MR28-1070	MR28 - Vendor Quotation - Secondary Structures - Structural Plates	9d	5d	21-Nov-23 A	27-Nov-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR28-1030	MR28 - Purchase Order - Secondary Structures - Structural Plates	10d	4d	27-Nov-23 A	30-Nov-23 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR28-1040	MR28 - Manufacturing & Ex-Works - Secondary Structures - Structural Plates	30d	21d	30-Nov-23 A	20-Dec-23 A	28-Nov-23	09-Jan-24	
PRO-BLK-MR28-1050	MR28 - Transportation &Yard Delivery - Secondary Structures - Structural Plates	5d	8d	13-Dec-23 A	20-Dec-23 A	10-Jan-24	14-Jan-24	
Secondary Structures - Racks		72d	39d	08-Jan-24 A	21-Feb-24 A	30-Oct-23	21-Jan-24	
PRO-BLK-MR29-1000	MR29 - Request for Quotation - Secondary Structures - Racks	1d	8d	08-Jan-24 A	17-Jan-24 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR29-1060	MR29 - MTO Issued - Secondary Structures - Racks	0d	0d	08-Jan-24 A		30-Oct-23		
PRO-BLK-MR29-1070	MR29 - Vendor Quotation - Secondary Structures - Racks	9d	15d	08-Jan-24 A	26-Jan-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR29-1030	MR29 - Purchase Order - Secondary Structures - Racks	10d	1d	26-Jan-24 A	26-Jan-24 A	21-Nov-23	04-Dec-23	
PRO-BLK-MR29-1040	MR29 - Manufacturing & Ex-Works - Secondary Structures - Racks	30d	27d	26-Jan-24 A	21-Feb-24 A	05-Dec-23	16-Jan-24	
PRO-BLK-MR29-1080	MR29 - Vendor Evaluation - Secondary Structures - Racks	5d	1d	26-Jan-24 A	26-Jan-24 A	14-Nov-23	20-Nov-23	
PRO-BLK-MR29-1050	MR29 - Transportation &Yard Delivery - Secondary Structures - Racks	5d	1d	21-Feb-24 A	21-Feb-24 A	17-Jan-24	21-Jan-24	
Caissons - Seamless Pipe and plates		98d	120d	12-Jun-24 A	30-Oct-24	10-May-24	25-Jul-24	32d
PRO-BLK-MR30-1000	MR30 - Request for Quotation - Caissons - Seamless Pipe and plates	1d	1d	12-Jun-24 A	12-Jun-24 A	10-May-24	10-May-24	
PRO-BLK-MR30-1060	MR30 - MTO Issued - Caissons - Seamless Pipe and plates	0d	0d	12-Jun-24 A		10-May-24		
PRO-BLK-MR30-1070	MR30 - Vendor Quotation - Caissons - Seamless Pipe and plates	9d	3d	13-Jun-24 A	17-Jun-24 A	13-May-24	23-May-24	
PRO-BLK-MR30-1080	MR30 - Vendor Evaluation - Caissons - Seamless Pipe and plates	10d	21d	18-Jun-24 A	16-Jul-24 A	24-May-24	06-Jun-24	
PRO-BLK-MR30-1030	MR30 - Purchase Order - Caissons - Seamless Pipe and plates	10d	1d	16-Jul-24 A	16-Jul-24 A	07-Jun-24	20-Jun-24	
PRO-BLK-MR30-1040	MR30 - Manufacturing & Ex-Works - Caissons - Seamless Pipe and plates	30d	92d	17-Jul-24 A	30-Oct-24	21-Jun-24	20-Jul-24	38d
PRO-BLK-MR30-1050	MR30 - Transportation &Yard Delivery - Caissons - Seamless Pipe and plates	5d	45d	16-Sep-24 A	30-Oct-24	21-Jul-24	25-Jul-24	37d
Caissons - Cones		64d	66d	10-May-24 A	25-Jul-24 A	10-May-24	25-Jul-24	
PRO-BLK-MR31-1000	MR31 - Request for Quotation - Caissons - Cones - DELETED	1d	1d	10-May-24 A	10-May-24 A	10-May-24	10-May-24	
PRO-BLK-MR31-1060	MR31 - MTO Issued - Caissons - Cones - DELETED	0d	0d	10-May-24 A		10-May-24		
PRO-BLK-MR31-1070	MR31 - Vendor Quotation - Caissons - Cones - DELETED	9d	9d	13-May-24 A	23-May-24 A	13-May-24	23-May-24	
PRO-BLK-MR31-1080	MR31 - Vendor Evaluation - Caissons - Cones - DELETED	10d	10d	24-May-24 A	06-Jun-24 A	24-May-24	06-Jun-24	
PRO-BLK-MR31-1030	MR31 - Purchase Order - Caissons - Cones - DELETED	10d	10d	07-Jun-24 A	20-Jun-24 A	07-Jun-24	20-Jun-24	
PRO-BLK-MR31-1040	MR31 - Manufacturing & Ex-Works - Caissons - Cones - DELETED	30d	30d	21-Jun-24 A	20-Jul-24 A	21-Jun-24	20-Jul-24	
PRO-BLK-MR31-1050	MR31 - Transportation &Yard Delivery - Caissons - Cones - DELETED	5d	5d	21-Jul-24 A	25-Jul-24 A	21-Jul-24	25-Jul-24	
Caissons - Supports		98d	120d	12-Jun-24 A	30-Oct-24	10-May-24	25-Jul-24	31d
PRO-BLK-MR32-1000	MR32 - Request for Quotation - Caissons - Supports	1d	1d	12-Jun-24 A	12-Jun-24 A	10-May-24	10-May-24	
PRO-BLK-MR32-1060	MR32 - MTO Issued - Caissons - Supports	0d	0d	12-Jun-24 A		10-May-24		
PRO-BLK-MR32-1070	MR32 - Vendor Quotation - Caissons - Supports	9d	3d	13-Jun-24 A	17-Jun-24 A	13-May-24	23-May-24	
PRO-BLK-MR32-1080	MR32 - Vendor Evaluation - Caissons - Supports	10d	21d	18-Jun-24 A	16-Jul-24 A	24-May-24	06-Jun-24	
PRO-BLK-MR32-1030	MR32 - Purchase Order - Caissons - Supports	10d	1d	16-Jul-24 A	16-Jul-24 A	07-Jun-24	20-Jun-24	
PRO-BLK-MR32-1040	MR32 - Manufacturing & Ex-Works - Caissons - Supports	30d	92d	17-Jul-24 A	30-Oct-24	21-Jun-24	20-Jul-24	37d
PRO-BLK-MR32-1050	MR32 - Transportation &Yard Delivery - Caissons - Supports	5d	45d	16-Sep-24 A	30-Oct-24	21-Jul-24	25-Jul-24	36d

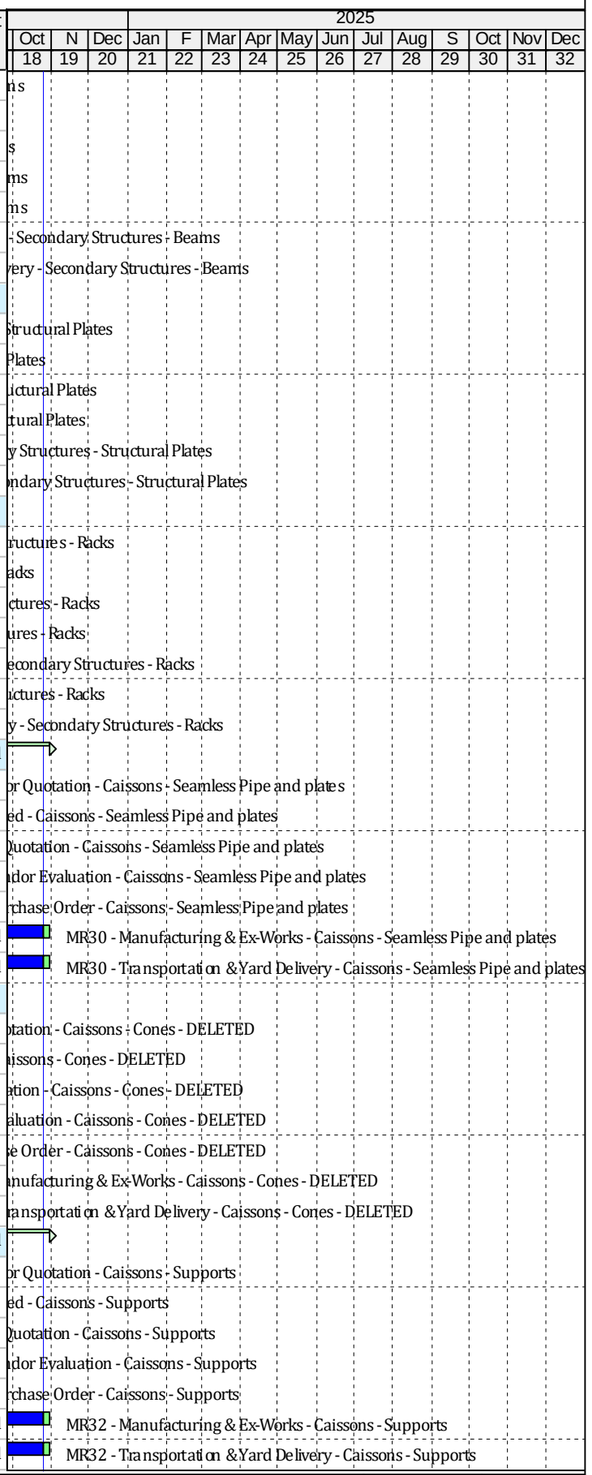

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Transition Piece - Rolled Pipe and plates		317d	128d	21-Nov-23 A	26-Apr-24 A	10-Apr-24	04-Sep-24	
PRO-BLK-MR34-1000	MR34 - Request for Quotation - Transition Piece - Rolled Pipe and plates	1d	1d	21-Nov-23 A	21-Nov-23 A	10-Apr-24	10-Apr-24	
PRO-BLK-MR34-1060	MR34 - MTO Issued - Transition Piece - Rolled Pipe and plates	0d	0d	21-Nov-23 A		10-Apr-24		
PRO-BLK-MR34-1070	MR34 - Vendor Quotation - Transition Piece - Rolled Pipe and plates	9d	4d	22-Nov-23 A	27-Nov-23 A	11-Apr-24	23-Apr-24	
PRO-BLK-MR34-1080	MR34 - Vendor Evaluation - Transition Piece - Rolled Pipe and plates	10d	33d	27-Nov-23 A	16-Jan-24 A	24-Apr-24	09-May-24	
PRO-BLK-MR34-1030	MR34 - Purchase Order - Transition Piece - Rolled Pipe and plates	10d	1d	16-Jan-24 A	16-Jan-24 A	10-May-24	23-May-24	
PRO-BLK-MR34-1040	MR34 - Manufacturing & Ex-Works - Transition Piece - Rolled Pipe and plates	205d	102d	16-Jan-24 A	26-Apr-24 A	24-May-24	30-Aug-24	
PRO-BLK-MR34-1050	MR34 - Transportation & Yard Delivery - Transition Piece - Rolled Pipe and plates	5d	40d	15-Mar-24 A	26-Apr-24 A	31-Aug-24	04-Sep-24	
Transition Piece - Flange, cap, padeyes, bolts, stairs and door		283d	287d	21-Nov-23 A	31-Oct-24	10-Apr-24	25-Aug-24	4d
PRO-BLK-MR35-1000	MR35 - Request for Quotation - Transition Piece - Flange, cap, padeyes, bolts, stairs and door	1d	196d	21-Nov-23 A	02-Sep-24 A	10-Apr-24	10-Apr-24	
PRO-BLK-MR35-1060	MR35 - MTO Issued - Transition Piece - Flange, cap, padeyes, bolts, stairs and door	0d	0d	21-Nov-23 A		10-Apr-24		
PRO-BLK-MR35-1070	MR35 - Vendor Quotation - Transition Piece - Flange, cap, padeyes, bolts, stairs and door	9d	201d	22-Nov-23 A	10-Sep-24 A	11-Apr-24	23-Apr-24	
PRO-BLK-MR35-1080	MR35 - Vendor Evaluation - Transition Piece - Flange, cap, padeyes, bolts, stairs and door	10d	52d	01-Dec-23 A	16-Feb-24 A	24-Apr-24	09-May-24	
PRO-BLK-MR35-1030	MR35 - Purchase Order - Transition Piece - Flange, cap, padeyes, bolts, stairs and door	10d	143d	16-Feb-24 A	10-Sep-24 A	10-May-24	23-May-24	
PRO-BLK-MR35-1040	MR35 - Manufacturing & Ex-Works - Transition Piece - Flange, cap, padeyes, bolts, stairs and door	173d	245d	16-Feb-24 A	31-Oct-24	24-May-24	20-Aug-24	5d
PRO-BLK-MR35-1050	MR35 - Transportation & Yard Delivery - Transition Piece - Flange, cap, padeyes, bolts, stairs and door	5d	253d	16-Feb-24 A	31-Oct-24	21-Aug-24	25-Aug-24	5d
Equipment Supports		76d	49d	22-Mar-24 A	22-May-24 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR36-1000	MR36 - Request for Quotation - Equipment Supports	1d	1d	22-Mar-24 A	22-Mar-24 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR36-1060	MR36 - MTO Issued - Equipment Supports	0d	0d	22-Mar-24 A		30-Oct-23		
PRO-BLK-MR36-1070	MR36 - Vendor Quotation - Equipment Supports	9d	1d	23-Mar-24 A	25-Mar-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR36-1030	MR36 - Purchase Order - Equipment Supports	10d	1d	25-Mar-24 A	25-Mar-24 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR36-1080	MR36 - Vendor Evaluation - Equipment Supports	10d	1d	25-Mar-24 A	25-Mar-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR36-1040	MR36 - Manufacturing & Ex-Works - Equipment Supports	30d	58d	26-Mar-24 A	22-May-24 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR36-1050	MR36 - Transportation & Yard Delivery - Equipment Supports	5d	1d	22-May-24 A	22-May-24 A	25-Jan-24	29-Jan-24	
Access Platform		64d	53d	13-Dec-23 A	16-Feb-24 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR37-1000	MR37 - Request for Quotation - Access Platform	1d	1d	13-Dec-23 A	13-Dec-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR37-1060	MR37 - MTO Issued - Access Platform	0d	0d	13-Dec-23 A		30-Oct-23		
PRO-BLK-MR37-1070	MR37 - Vendor Quotation - Access Platform	9d	19d	13-Dec-23 A	11-Jan-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR37-1080	MR37 - Vendor Evaluation - Access Platform	10d	4d	11-Jan-24 A	16-Jan-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR37-1030	MR37 - Purchase Order - Access Platform	10d	1d	16-Jan-24 A	16-Jan-24 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR37-1040	MR37 - Manufacturing & Ex-Works - Access Platform	30d	32d	16-Jan-24 A	16-Feb-24 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR37-1050	MR37 - Transportation & Yard Delivery - Access Platform	5d	1d	16-Feb-24 A	16-Feb-24 A	25-Jan-24	29-Jan-24	
Hatches		63d	73d	30-Oct-23 A	29-Jan-24 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR38-1000	MR38 - Request for Quotation - Hatches - deleted	1d	1d	30-Oct-23 A	30-Oct-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR38-1060	MR38 - MTO Issued - Hatches - deleted	0d	0d	30-Oct-23 A		30-Oct-23		
PRO-BLK-MR38-1070	MR38 - Vendor Quotation - Hatches - deleted	9d	9d	31-Oct-23 A	13-Nov-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR38-1080	MR38 - Vendor Evaluation - Hatches - deleted	10d	10d	14-Nov-23 A	27-Nov-23 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR38-1030	MR38 - Purchase Order - Hatches - deleted	10d	10d	28-Nov-23 A	12-Dec-23 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR38-1040	MR38 - Manufacturing & Ex-Works - Hatches - deleted	30d	30d	13-Dec-23 A	24-Jan-24 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR38-1050	MR38 - Transportation & Yard Delivery - Hatches - deleted	5d	5d	25-Jan-24 A	29-Jan-24 A	25-Jan-24	29-Jan-24	
Lifting Padeyes		174d	25d	10-Oct-23 A	08-Nov-23 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR39-1000	MR39 - Request for Quotation - Lifting Padeyes	1d	3d	10-Oct-23 A	12-Oct-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR39-1060	MR39 - MTO Issued - Lifting Padeyes	0d	0d	10-Oct-23 A		30-Oct-23		
PRO-BLK-MR39-1070	MR39 - Vendor Quotation - Lifting Padeyes	9d	2d	12-Oct-23 A	13-Oct-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR39-1080	MR39 - Vendor Evaluation - Lifting Padeyes	10d	3d	13-Oct-23 A	17-Oct-23 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR39-1030	MR39 - Purchase Order - Lifting Padeyes	10d	1d	17-Oct-23 A	17-Oct-23 A	28-Nov-23	12-Dec-23	

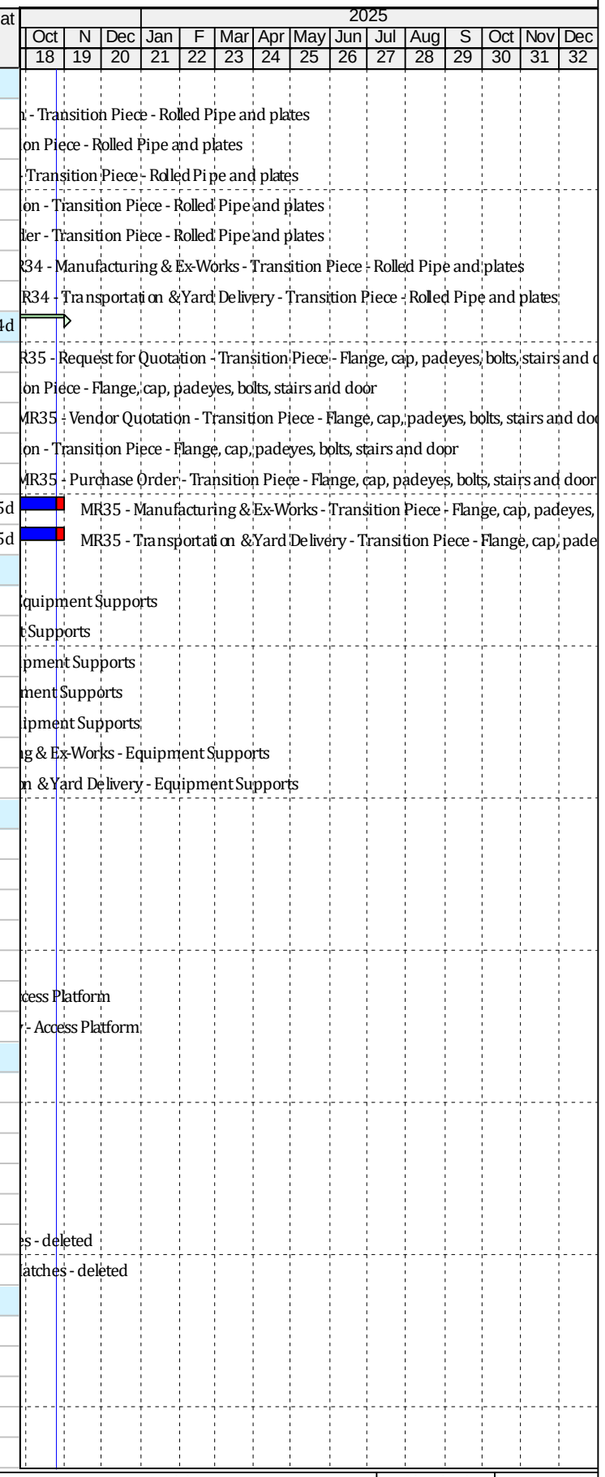

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR39-1040	MR39 - Manufacturing & Ex-Works - Lifting Padeyes	30d	23d	17-Oct-23 A	08-Nov-23 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR39-1050	MR39 - Transportation & Yard Delivery - Lifting Padeyes	5d	1d	08-Nov-23 A	08-Nov-23 A	25-Jan-24	29-Jan-24	
Walkways		128d	69d	13-Dec-23 A	06-Mar-24 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR40-1000	MR40 - Request for Quotation - Walkways	1d	1d	13-Dec-23 A	13-Dec-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR40-1060	MR40 - MTO Issued - Walkways	0d	0d	13-Dec-23 A		30-Oct-23		
PRO-BLK-MR40-1070	MR40 - Vendor Quotation - Walkways	9d	19d	13-Dec-23 A	11-Jan-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR40-1080	MR40 - Vendor Evaluation - Walkways	10d	4d	11-Jan-24 A	16-Jan-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR40-1030	MR40 - Purchase Order - Walkways	10d	1d	16-Jan-24 A	16-Jan-24 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR40-1040	MR40 - Manufacturing & Ex-Works - Walkways	30d	51d	16-Jan-24 A	06-Mar-24 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR40-1050	MR40 - Transportation & Yard Delivery - Walkways	5d	38d	29-Jan-24 A	06-Mar-24 A	25-Jan-24	29-Jan-24	
Gratings		111d	113d	19-Jan-24 A	03-Jun-24 A	30-Oct-23	29-Jan-24	
PRO-BLK-MR41-1000	MR41 - Request for Quotation - Gratings	1d	1d	19-Jan-24 A	19-Jan-24 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR41-1060	MR41 - MTO Issued - Gratings	0d	0d	19-Jan-24 A		30-Oct-23		
PRO-BLK-MR41-1070	MR41 - Vendor Quotation - Gratings	9d	7d	19-Jan-24 A	29-Jan-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR41-1080	MR41 - Vendor Evaluation - Gratings	10d	8d	29-Jan-24 A	07-Feb-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR41-1030	MR41 - Purchase Order - Gratings	10d	1d	07-Feb-24 A	07-Feb-24 A	28-Nov-23	12-Dec-23	
PRO-BLK-MR41-1040	MR41 - Manufacturing & Ex-Works - Gratings	30d	118d	07-Feb-24 A	03-Jun-24 A	13-Dec-23	24-Jan-24	
PRO-BLK-MR41-1050	MR41 - Transportation & Yard Delivery - Gratings	5d	99d	21-Feb-24 A	03-Jun-24 A	25-Jan-24	29-Jan-24	
Handrails		68d	67d	17-Jan-24 A	05-Apr-24 A	30-Oct-23	21-Jan-24	
PRO-BLK-MR42-1000	MR42 - Request for Quotation - Handrails	1d	1d	17-Jan-24 A	17-Jan-24 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR42-1060	MR42 - MTO Issued - Handrails	0d	0d	17-Jan-24 A		30-Oct-23		
PRO-BLK-MR42-1070	MR42 - Vendor Quotation - Handrails	9d	7d	17-Jan-24 A	25-Jan-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR42-1030	MR42 - Purchase Order - Handrails	5d	1d	25-Jan-24 A	25-Jan-24 A	28-Nov-23	04-Dec-23	
PRO-BLK-MR42-1040	MR42 - Manufacturing & Ex-Works - Handrails	30d	72d	25-Jan-24 A	05-Apr-24 A	05-Dec-23	16-Jan-24	
PRO-BLK-MR42-1080	MR42 - Vendor Evaluation - Handrails	10d	1d	25-Jan-24 A	25-Jan-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR42-1050	MR42 - Transportation & Yard Delivery - Handrails	5d	1d	05-Apr-24 A	05-Apr-24 A	17-Jan-24	21-Jan-24	
Ladders		178d	30d	13-Dec-23 A	21-Jan-24 A	30-Oct-23	21-Jan-24	
PRO-BLK-MR43-1000	MR43 - Request for Quotation - Ladders - DELETED	1d	1d	13-Dec-23 A	13-Dec-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR43-1060	MR43 - MTO Issued - Ladders	0d	0d	13-Dec-23 A		30-Oct-23		
PRO-BLK-MR43-1070	MR43 - Vendor Quotation - Ladders - DELETED	9d	22d	13-Dec-23 A	16-Jan-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR43-1080	MR43 - Vendor Evaluation - Ladders	10d	4d	11-Jan-24 A	16-Jan-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR43-1030	MR43 - Purchase Order - Ladders - DELETED	5d	1d	16-Jan-24 A	16-Jan-24 A	28-Nov-23	04-Dec-23	
PRO-BLK-MR43-1040	MR43 - Manufacturing & Ex-Works - Ladders - DELETED	30d	1d	16-Jan-24 A	16-Jan-24 A	05-Dec-23	16-Jan-24	
PRO-BLK-MR43-1050	MR43 - Transportation & Yard Delivery - Ladders	5d	5d	17-Jan-24 A	21-Jan-24 A	17-Jan-24	21-Jan-24	
Stairs		78d	53d	13-Dec-23 A	16-Feb-24 A	30-Oct-23	21-Jan-24	
PRO-BLK-MR44-1000	MR44 - Request for Quotation - Stairs	1d	1d	13-Dec-23 A	13-Dec-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR44-1060	MR44 - MTO Issued - Stairs	0d	0d	13-Dec-23 A		30-Oct-23		
PRO-BLK-MR44-1070	MR44 - Vendor Quotation - Stairs	9d	19d	13-Dec-23 A	11-Jan-24 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR44-1080	MR44 - Vendor Evaluation - Stairs	10d	4d	11-Jan-24 A	16-Jan-24 A	14-Nov-23	27-Nov-23	
PRO-BLK-MR44-1030	MR44 - Purchase Order - Stairs	5d	1d	16-Jan-24 A	16-Jan-24 A	28-Nov-23	04-Dec-23	
PRO-BLK-MR44-1040	MR44 - Manufacturing & Ex-Works - Stairs	30d	32d	16-Jan-24 A	16-Feb-24 A	05-Dec-23	16-Jan-24	
PRO-BLK-MR44-1050	MR44 - Transportation & Yard Delivery - Stairs	5d	1d	16-Feb-24 A	16-Feb-24 A	17-Jan-24	21-Jan-24	
Lower Grillage & Seafastening Beams		85d	333d	07-Dec-23 A	15-Jan-25	26-Jul-24	04-Nov-24	21d
PRO-BLK-MR46-1000	MR46 - Request for Quotation - Lower Grillage & Seafastening - Beams	1d	224d	07-Dec-23 A	28-Oct-24	26-Jul-24	26-Jul-24	53d
PRO-BLK-MR46-1060	MR46 - MTO Issued - Lower Grillage & Seafastening - Beams	0d	0d	07-Dec-23 A		26-Jul-24		
PRO-BLK-MR46-1070	MR46 - Vendor Quotation - Lower Grillage & Seafastening - Beams	9d	227d	07-Dec-23 A	30-Oct-24	29-Jul-24	08-Aug-24	53d

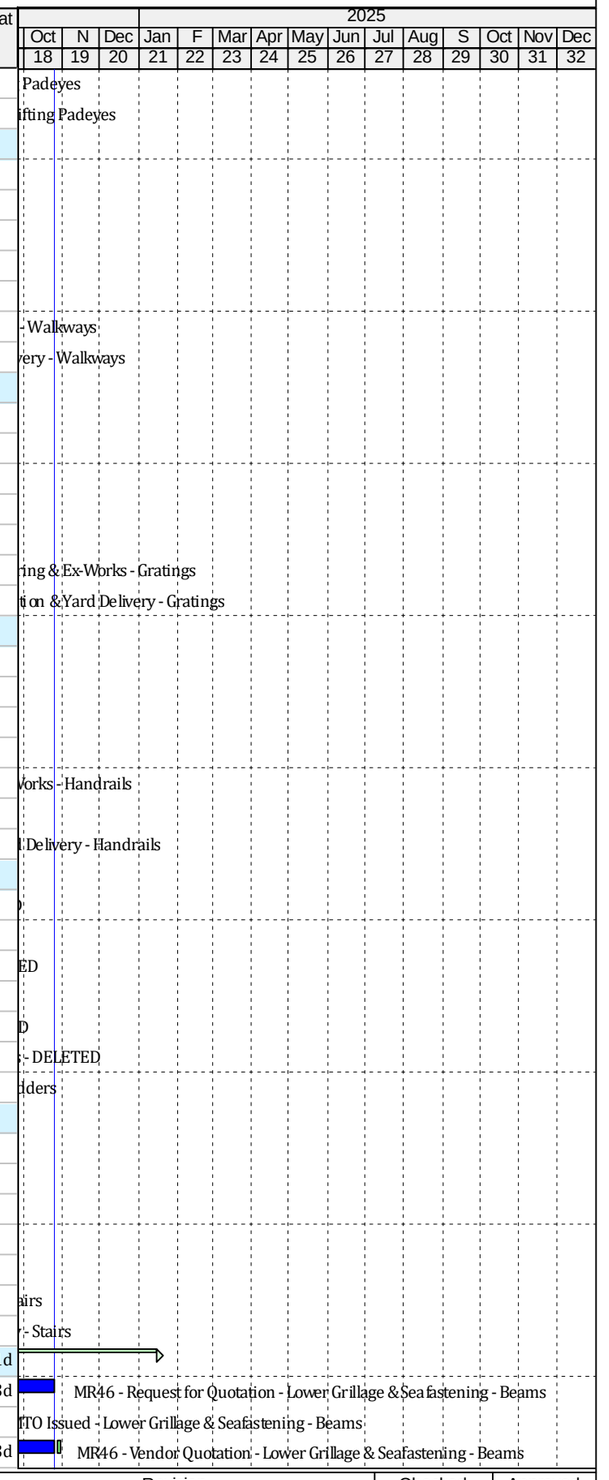

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR46-1080	MR46 - Vendor Evaluation - Lower Grillage & Seafastening - Beams	10d	2d	13-Dec-23 A	14-Dec-23 A	09-Aug-24	23-Aug-24	
PRO-BLK-MR46-1030	MR46 - Purchase Order - Lower Grillage & Seafastening - Beams	5d	222d	14-Dec-23 A	29-Oct-24	26-Aug-24	30-Aug-24	53d
PRO-BLK-MR46-1040	MR46 - Manufacturing & Ex-Works - Lower Grillage & Seafastening - Beams	60d	359d	14-Dec-23 A	15-Jan-25	31-Aug-24	29-Oct-24	25d
PRO-BLK-MR46-1050	MR46 - Transportation & Yard Delivery - Lower Grillage & Seafastening - Beams	5d	346d	24-Jan-24 A	15-Jan-25	30-Oct-24	04-Nov-24	25d
Bulk Material - Piping & Valves		259d	306d	28-Nov-23 A	01-Dec-24	14-Nov-23	21-Sep-24	65d
Piping - Carbon Steel		124d	85d	08-Feb-24 A	21-May-24 A	08-Jan-24	25-May-24	
PRO-BLK-MR48-1000	MR48 - Request for Quotation - Piping Carbon Steel	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR48-1060	MR48 - MR Issued - Piping Carbon Steel	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR48-1070	MR48 - Vendor Quotation - Piping Carbon Steel	9d	5d	15-Mar-24 A	21-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR48-1030	MR48 - Purchase Order - Piping Carbon Steel	4d	1d	22-Apr-24 A	22-Apr-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR48-1040	MR48 - Manufacturing & Ex-Works - Piping Carbon Steel	54d	29d	22-Apr-24 A	20-May-24 A	21-Feb-24	20-May-24	
PRO-BLK-MR48-1050	MR48 - Transportation & Yard Delivery - Piping Carbon Steel	5d	1d	21-May-24 A	21-May-24 A	21-May-24	25-May-24	
Fittings & Flanges Carbon Steel		134d	132d	08-Feb-24 A	15-Jul-24 A	08-Jan-24	25-May-24	
PRO-BLK-MR49-1000	MR49 - Request for Quotation - Fittings & Flanges Carbon Steel	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR49-1060	MR49 - MR/MTO Issued - Fittings & Flanges Carbon Steel	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR49-1070	MR49 - Vendor Quotation - Fittings & Flanges Carbon Steel	9d	10d	15-Mar-24 A	28-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR49-1030	MR49 - Purchase Order - Fittings & Flanges Carbon Steel	10d	1d	26-Apr-24 A	26-Apr-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR49-1040	MR49 - Manufacturing & Ex-Works - Fittings & Flanges Carbon Steel	58d	81d	26-Apr-24 A	15-Jul-24 A	21-Feb-24	20-May-24	
PRO-BLK-MR49-1050	MR49 - Transportation & Yard Delivery - Fittings & Flanges Carbon Steel	5d	43d	03-Jun-24 A	15-Jul-24 A	21-May-24	25-May-24	
Forged Fittings - Carbon Steel		124d	116d	08-Jan-24 A	25-May-24 A	08-Jan-24	25-May-24	
PRO-BLK-MR80-1000	MR80 - Request for Quotation - Forged Fittings Carbon Steel - deleted	1d	1d	08-Jan-24 A	08-Jan-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR80-1010	MR80 - MR/MTO Issued - Forged Fittings Carbon Steel - deleted	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR80-1020	MR80 - Vendor Quotation - Forged Fittings Carbon Steel - deleted	9d	9d	09-Jan-24 A	19-Jan-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR80-1040	MR80 - Purchase Order - Forged Fittings Carbon Steel - deleted	10d	10d	07-Feb-24 A	20-Feb-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR80-1050	MR80 - Manufacturing & Ex-Works - Forged Fittings Carbon Steel - deleted	59d	91d	20-Feb-24 A	20-May-24 A	21-Feb-24	20-May-24	
PRO-BLK-MR80-1060	MR80 - Transportation & Yard Delivery - Forged Fittings Carbon Steel - deleted	5d	5d	21-May-24 A	25-May-24 A	21-May-24	25-May-24	
BW Fittings - Carbon Steel		141d	96d	08-Feb-24 A	03-Jun-24 A	08-Jan-24	25-May-24	
PRO-BLK-MR81-1000	MR81 - Request for Quotation - BW Fittings Carbon Steel	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR81-1010	MR81 - MR/MTO Issued - BW Fittings Carbon Steel	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR81-1020	MR81 - Vendor Quotation - BW Fittings Carbon Steel	9d	9d	15-Mar-24 A	27-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR81-1040	MR81 - Purchase Order - BW Fittings Carbon Steel	10d	1d	26-Apr-24 A	26-Apr-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR81-1050	MR81 - Manufacturing & Ex-Works - BW Fittings Carbon Steel	58d	39d	26-Apr-24 A	03-Jun-24 A	21-Feb-24	20-May-24	
PRO-BLK-MR81-1060	MR81 - Transportation & Yard Delivery - BW Fittings Carbon Steel	5d	1d	03-Jun-24 A	03-Jun-24 A	21-May-24	25-May-24	
Piping - Stainless Steel		155d	96d	08-Feb-24 A	03-Jun-24 A	08-Jan-24	07-Jun-24	
PRO-BLK-MR50-1000	MR50 - Request for Quotation - Piping Stainless Steel	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR50-1060	MR50 - MR/MTO Issued - Piping Stainless Steel	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR50-1070	MR50 - Vendor Quotation - Piping Stainless Steel	9d	9d	15-Mar-24 A	27-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR50-1080	MR50 - Vendor Evaluation - Piping Stainless Steel	15d	18d	27-Mar-24 A	22-Apr-24 A	22-Jan-24	09-Feb-24	
PRO-BLK-MR50-1030	MR50 - Purchase Order - Piping Stainless Steel	10d	1d	22-Apr-24 A	22-Apr-24 A	12-Feb-24	23-Feb-24	
PRO-BLK-MR50-1040	MR50 - Manufacturing & Ex-Works - Piping Stainless Steel	67d	43d	22-Apr-24 A	03-Jun-24 A	24-Feb-24	02-Jun-24	
PRO-BLK-MR50-1050	MR50 - Transportation & Yard Delivery - Piping Stainless Steel	5d	1d	03-Jun-24 A	03-Jun-24 A	03-Jun-24	07-Jun-24	
Fittings & Flanges - Stainless Steel		155d	109d	08-Feb-24 A	18-Jun-24 A	08-Jan-24	07-Jun-24	
PRO-BLK-MR51-1000	MR51 - Request for Quotation - Fittings & Flanges Stainless Steel	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR51-1060	MR51 - MR/MTO Issued - Fittings & Flanges Stainless Steel	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR51-1070	MR51 - Vendor Quotation - Fittings & Flanges Stainless Steel	9d	10d	15-Mar-24 A	28-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR51-1080	MR51 - Vendor Evaluation - Fittings & Flanges Stainless Steel	15d	16d	29-Mar-24 A	22-Apr-24 A	22-Jan-24	09-Feb-24	

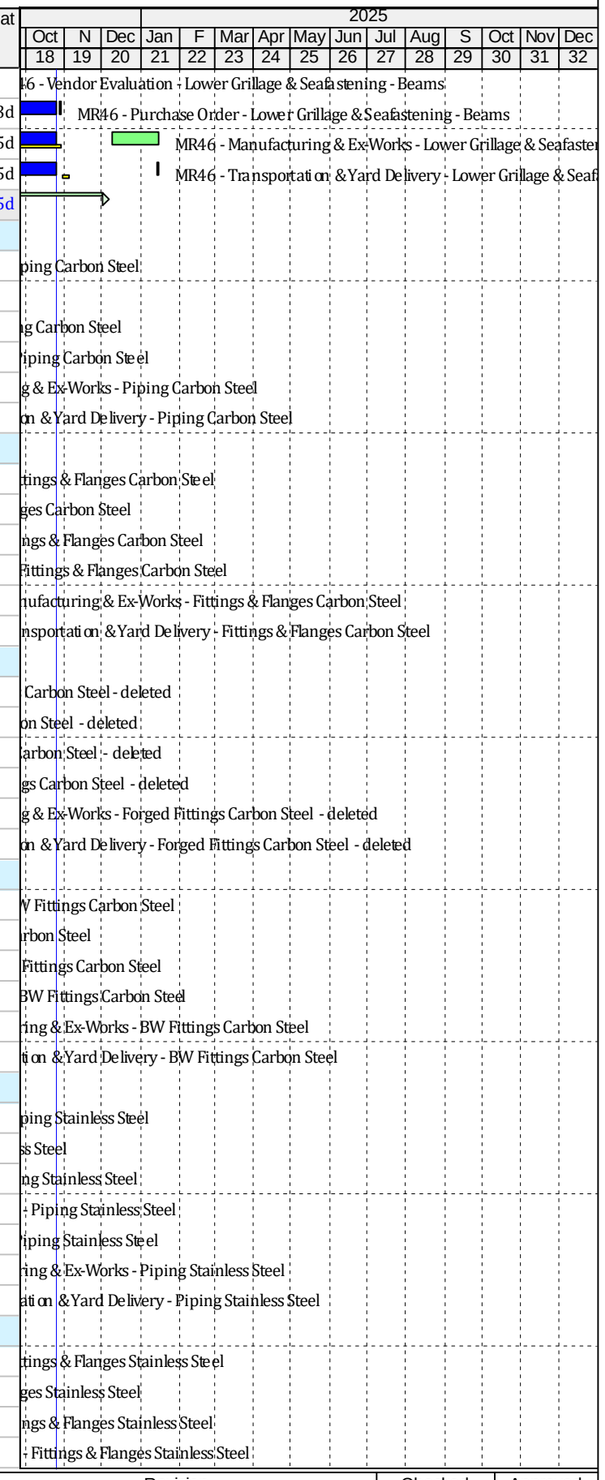

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR51-1030	MR51 - Purchase Order - Fittings & Flanges Stainless Steel	10d	1d	22-Apr-24 A	22-Apr-24 A	12-Feb-24	23-Feb-24	
PRO-BLK-MR51-1040	MR51 - Manufacturing & Ex-Works - Fittings & Flanges Stainless Steel	67d	58d	22-Apr-24 A	18-Jun-24 A	24-Feb-24	02-Jun-24	
PRO-BLK-MR51-1050	MR51 - Transportation & Yard Delivery - Fittings & Flanges Stainless Steel	5d	2d	17-Jun-24 A	18-Jun-24 A	03-Jun-24	07-Jun-24	
Piping - Super Duplex		172d	96d	08-Feb-24 A	03-Jun-24 A	08-Jan-24	24-Jun-24	
PRO-BLK-MR79-1000	MR79 - Request for Quotation - Piping Super Duplex	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR79-1060	MR79 - MR/MTO Issued - Piping Super Duplex	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR79-1070	MR79 - Vendor Quotation - Piping Super Duplex	9d	9d	15-Mar-24 A	27-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR79-1030	MR79 - Purchase Order - Piping Super Duplex	10d	1d	22-Apr-24 A	22-Apr-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR79-1040	MR79 - Manufacturing & Ex-Works - Piping Super Duplex	90d	43d	22-Apr-24 A	03-Jun-24 A	21-Feb-24	19-Jun-24	
PRO-BLK-MR79-1050	MR79 - Transportation & Yard Delivery - Piping Super Duplex	5d	1d	03-Jun-24 A	03-Jun-24 A	20-Jun-24	24-Jun-24	
Fittings & Flanges Super Duplex		172d	153d	08-Feb-24 A	08-Aug-24 A	08-Jan-24	24-Jun-24	
PRO-BLK-MR52-1000	MR52 - Request for Quotation - Fittings & Flanges Super Duplex	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR52-1060	MR52 - MR/MTO Issued - Fittings & Flanges Super Duplex	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR52-1070	MR52 - Vendor Quotation - Fittings & Flanges Super Duplex	9d	10d	15-Mar-24 A	28-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR52-1030	MR52 - Purchase Order - Fittings & Flanges Super Duplex	10d	1d	26-Apr-24 A	26-Apr-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR52-1040	MR52 - Manufacturing & Ex-Works - Fittings & Flanges Super Duplex	90d	101d	26-Apr-24 A	08-Aug-24 A	21-Feb-24	19-Jun-24	
PRO-BLK-MR52-1050	MR52 - Transportation & Yard Delivery - Fittings & Flanges Super Duplex	5d	25d	15-Jul-24 A	08-Aug-24 A	20-Jun-24	24-Jun-24	
Forged Fittings - Super Duplex & SS		172d	136d	08-Feb-24 A	19-Jul-24 A	08-Jan-24	24-Jun-24	
PRO-BLK-MR82-1000	MR82 - Request for Quotation - Forged Fittings Super Duplex & SS	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR82-1010	MR82 - MR/MTO Issued - Forged Fittings Super Duplex & SS	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR82-1020	MR82 - Vendor Quotation - Forged Fittings Super Duplex & SS	9d	9d	15-Mar-24 A	27-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR82-1040	MR82 - Purchase Order - Forged Fittings Super Duplex & SS	10d	1d	26-Apr-24 A	26-Apr-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR82-1050	MR82 - Manufacturing & Ex-Works - Forged Fittings Super Duplex & SS	90d	85d	26-Apr-24 A	19-Jul-24 A	21-Feb-24	19-Jun-24	
PRO-BLK-MR82-1060	MR82 - Transportation & Yard Delivery - Forged Fittings Super Duplex & SS	5d	1d	19-Jul-24 A	19-Jul-24 A	20-Jun-24	24-Jun-24	
BW Fittings - Super Duplex & SS		172d	136d	08-Feb-24 A	19-Jul-24 A	08-Jan-24	24-Jun-24	
PRO-BLK-MR83-1000	MR83 - Request for Quotation - BW Fittings Super Duplex & SS	1d	27d	08-Feb-24 A	15-Mar-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR83-1010	MR83 - MR/MTO Issued - BW Fittings Super Duplex & SS	0d	0d	08-Feb-24 A		08-Jan-24		
PRO-BLK-MR83-1020	MR83 - Vendor Quotation - BW Fittings Super Duplex & SS	9d	10d	15-Mar-24 A	28-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR83-1040	MR83 - Purchase Order - BW Fittings Super Duplex & SS	10d	1d	26-Apr-24 A	26-Apr-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR83-1050	MR83 - Manufacturing & Ex-Works - BW Fittings Super Duplex & SS	90d	85d	26-Apr-24 A	19-Jul-24 A	21-Feb-24	19-Jun-24	
PRO-BLK-MR83-1060	MR83 - Transportation & Yard Delivery - BW Fittings Super Duplex & SS	5d	47d	03-Jun-24 A	19-Jul-24 A	20-Jun-24	24-Jun-24	
Gaskets		170d	130d	08-Feb-24 A	12-Jul-24 A	26-Feb-24	14-Jul-24	
PRO-BLK-MR53-1000	MR53 - Request for Quotation - Gaskets	1d	27d	08-Feb-24 A	15-Mar-24 A	26-Feb-24	26-Feb-24	
PRO-BLK-MR53-1060	MR53 - MR/MTO Issued - Gaskets	0d	0d	08-Feb-24 A		26-Feb-24		
PRO-BLK-MR53-1070	MR53 - Vendor Quotation - Gaskets	15d	10d	15-Mar-24 A	28-Mar-24 A	27-Feb-24	08-Mar-24	
PRO-BLK-MR53-1030	MR53 - Purchase Order - Gaskets	10d	1d	26-Apr-24 A	26-Apr-24 A	27-Mar-24	10-Apr-24	
PRO-BLK-MR53-1040	MR53 - Manufacturing & Ex-Works - Gaskets	87d	78d	26-Apr-24 A	12-Jul-24 A	11-Apr-24	09-Jul-24	
PRO-BLK-MR53-1050	MR53 - Transportation & Yard Delivery - Gaskets	5d	1d	12-Jul-24 A	12-Jul-24 A	10-Jul-24	14-Jul-24	
Studs & Bolts		175d	165d	08-Feb-24 A	23-Aug-24 A	22-Jan-24	17-Jul-24	
PRO-BLK-MR84-1000	MR84 - Request for Quotation - Studs & Bolts	1d	27d	08-Feb-24 A	15-Mar-24 A	22-Jan-24	22-Jan-24	
PRO-BLK-MR84-1010	MR84 - MR/MTO Issued - Studs & Bolts	0d	0d	08-Feb-24 A		22-Jan-24		
PRO-BLK-MR84-1020	MR84 - Vendor Quotation - Studs & Bolts	9d	10d	15-Mar-24 A	28-Mar-24 A	23-Jan-24	02-Feb-24	
PRO-BLK-MR84-1040	MR84 - Purchase Order - Studs & Bolts	10d	1d	26-Apr-24 A	26-Apr-24 A	21-Feb-24	05-Mar-24	
PRO-BLK-MR84-1050	MR84 - Manufacturing & Ex-Works - Studs & Bolts	93d	106d	26-Apr-24 A	23-Aug-24 A	06-Mar-24	12-Jul-24	
PRO-BLK-MR84-1060	MR84 - Transportation & Yard Delivery - Studs & Bolts	5d	1d	23-Aug-24 A	23-Aug-24 A	13-Jul-24	17-Jul-24	
Manual Valves - Ball		258d	281d	28-Nov-23 A	01-Nov-24	14-Nov-23	21-Sep-24	63d

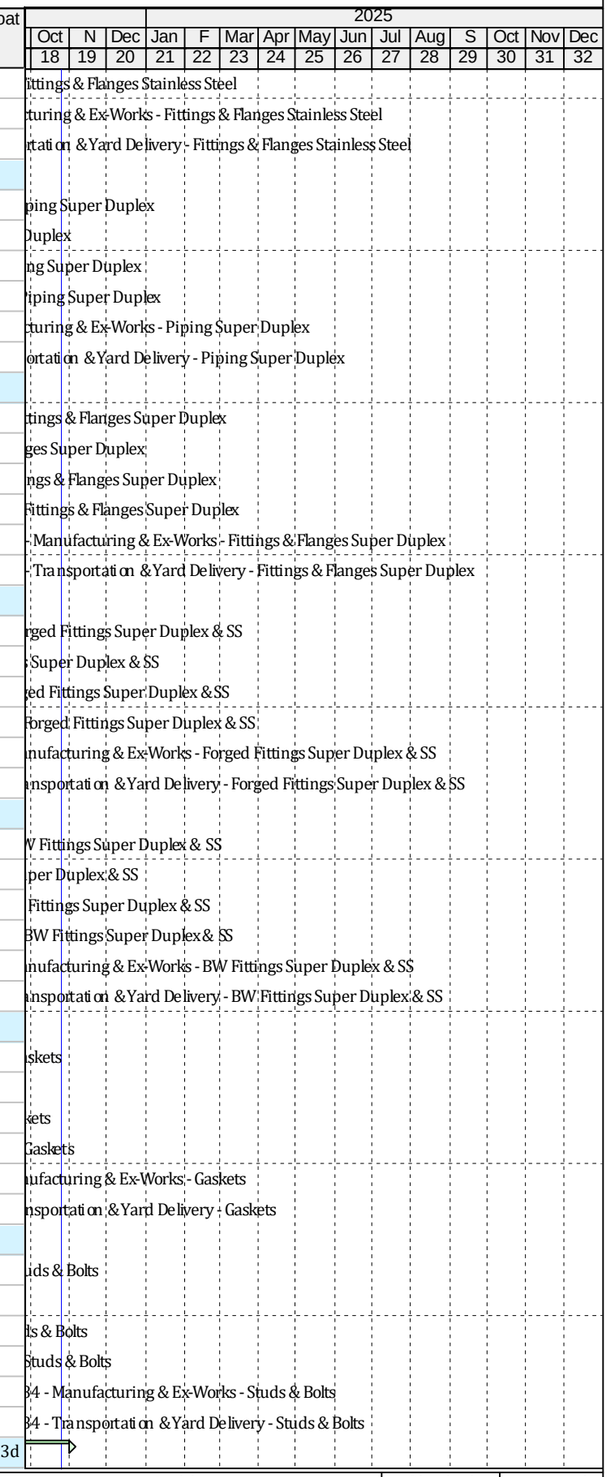

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR54-1000	MR54 - Request for Quotation - Manual Valves - Ball	1d	1d	28-Nov-23 A	28-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-BLK-MR54-1060	MR54 - MR Issued - Manual Valves - Ball	0d	0d	28-Nov-23 A		14-Nov-23		
PRO-BLK-MR54-1070	MR54 - Vendor Quotation - Manual Valves - Ball	9d	6d	28-Nov-23 A	05-Dec-23 A	15-Nov-23	27-Nov-23	
PRO-BLK-MR54-1030	MR54 - Purchase Order - Manual Valves - Ball	10d	1d	16-Apr-24 A	16-Apr-24 A	18-Dec-23	03-Jan-24	
PRO-BLK-MR54-1040	MR54 - Manufacturing & Ex-Works - Manual Valves - Ball	136d	186d	16-Apr-24 A	01-Nov-24	07-Jan-24	16-Sep-24	66d
PRO-BLK-MR54-1050	MR54 - Transportation &Yard Delivery - Manual Valves - Ball	5d	21d	11-Oct-24 A	31-Oct-24	17-Sep-24	21-Sep-24	74d
Manual Valves - Check, Gate and Globe		259d	281d	28-Nov-23 A	31-Oct-24	14-Nov-23	21-Sep-24	90d
PRO-BLK-MR85-1000	MR85 - Request for Quotation - Manual Valves - Check, Gate & Globe	1d	2d	28-Nov-23 A	29-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-BLK-MR85-1010	MR85 - MR Issued - Manual Valves - Check, Gate & Globe	0d	0d	28-Nov-23 A		14-Nov-23		
PRO-BLK-MR85-1020	MR85 - Vendor Quotation - Manual Valves - Check, Gate & Globe	9d	5d	29-Nov-23 A	05-Dec-23 A	15-Nov-23	27-Nov-23	
PRO-BLK-MR85-1040	MR85 - Purchase Order - Manual Valves - Check, Gate & Globe	10d	1d	16-Apr-24 A	16-Apr-24 A	18-Dec-23	03-Jan-24	
PRO-BLK-MR85-1050	MR85 - Manufacturing & Ex-Works - Manual Valves - Check, Gate & Globe	136d	180d	16-Apr-24 A	26-Oct-24	07-Jan-24	16-Sep-24	98d
PRO-BLK-MR85-1060	MR85 - Transportation &Yard Delivery - Manual Valves - Check, Gate & Globe	5d	5d	27-Oct-24	31-Oct-24	17-Sep-24	21-Sep-24	105d
Manual Valves - DBB & SBB		239d	280d	28-Nov-23 A	30-Oct-24	14-Nov-23	21-Sep-24	64d
PRO-BLK-MR86-1000	MR86 - Request for Quotation - Manual Valves - DBB & SBB	1d	2d	28-Nov-23 A	29-Nov-23 A	14-Nov-23	14-Nov-23	
PRO-BLK-MR86-1010	MR86 - MR Issued - Manual Valves - DBB & SBB	0d	0d	28-Nov-23 A		14-Nov-23		
PRO-BLK-MR86-1020	MR86 - Vendor Quotation - Manual Valves - DBB & SBB	9d	5d	29-Nov-23 A	05-Dec-23 A	15-Nov-23	27-Nov-23	
PRO-BLK-MR86-1040	MR86 - Purchase Order - Manual Valves - DBB & SBB	10d	1d	16-Apr-24 A	16-Apr-24 A	18-Dec-23	03-Jan-24	
PRO-BLK-MR86-1050	MR86 - Manufacturing & Ex-Works - Manual Valves - DBB & SBB	127d	181d	16-Apr-24 A	27-Oct-24	07-Jan-24	16-Sep-24	71d
PRO-BLK-MR86-1060	MR86 - Transportation &Yard Delivery - Manual Valves - DBB & SBB	5d	20d	11-Oct-24 A	30-Oct-24	17-Sep-24	21-Sep-24	75d
Flame Arresters & Bird Screen		201d	187d	17-Jan-24 A	27-Aug-24 A	17-Jan-24	27-Aug-24	
PRO-BLK-MR87-1000	MR87 - Request for Quotation - Flame Arresters & Bird Screen - DELETED	1d	1d	17-Jan-24 A	17-Jan-24 A	17-Jan-24	17-Jan-24	
PRO-BLK-MR87-1010	MR87 - MR/MTO Issued - Flame Arresters & Bird Screen - DELETED	0d	0d	17-Jan-24 A		17-Jan-24		
PRO-BLK-MR87-1020	MR87 - Vendor Quotation - Flame Arresters & Bird Screen - DELETED	9d	9d	18-Jan-24 A	30-Jan-24 A	18-Jan-24	30-Jan-24	
PRO-BLK-MR87-1040	MR87 - Purchase Order - Flame Arresters & Bird Screen - DELETED	10d	11d	16-Feb-24 A	01-Mar-24 A	19-Feb-24	01-Mar-24	
PRO-BLK-MR87-1050	MR87 - Manufacturing & Ex-Works - Flame Arresters & Bird Screen - DELETED	160d	160d	02-Mar-24 A	22-Aug-24 A	02-Mar-24	22-Aug-24	
PRO-BLK-MR87-1060	MR87 - Transportation &Yard Delivery - Flame Arresters & Bird Screen - DELETED	5d	5d	23-Aug-24 A	27-Aug-24 A	23-Aug-24	27-Aug-24	
Y Strainers		171d	176d	08-Jan-24 A	03-Aug-24 A	08-Jan-24	03-Aug-24	
PRO-BLK-MR88-1000	MR88 - Request for Quotation - Y-Strainers - DELETED	1d	1d	08-Jan-24 A	08-Jan-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR88-1010	MR88 - MR/MTO Issued - Y-Strainers - DELETED	0d	0d	08-Jan-24 A		08-Jan-24		
PRO-BLK-MR88-1020	MR88 - Vendor Quotation - Y-Strainers - DELETED	9d	9d	09-Jan-24 A	19-Jan-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR88-1040	MR88 - Purchase Order - Y-Strainers - DELETED	10d	10d	07-Feb-24 A	20-Feb-24 A	07-Feb-24	20-Feb-24	
PRO-BLK-MR88-1050	MR88 - Manufacturing & Ex-Works - Y-Strainers - DELETED	160d	160d	21-Feb-24 A	29-Jul-24 A	21-Feb-24	29-Jul-24	
PRO-BLK-MR88-1060	MR88 - Transportation &Yard Delivery - Y-Strainers - DELETED	5d	5d	30-Jul-24 A	03-Aug-24 A	30-Jul-24	03-Aug-24	
Expansion Joints		117d	178d	20-Dec-23 A	23-Jul-24 A	20-Dec-23	23-Jul-24	
PRO-BLK-MR89-1000	MR89 - Request for Quotation - Expansion Joints - DELETED	1d	1d	20-Dec-23 A	20-Dec-23 A	20-Dec-23	20-Dec-23	
PRO-BLK-MR89-1010	MR89 - MR/MTO Issued - Expansion Joints - DELETED	0d	0d	20-Dec-23 A		20-Dec-23		
PRO-BLK-MR89-1020	MR89 - Vendor Quotation - Expansion Joints - DELETED	9d	9d	21-Dec-23 A	05-Jan-24 A	21-Dec-23	05-Jan-24	
PRO-BLK-MR89-1070	MR89 - Vendor Evaluation - Expansion Joints - DELETED	15d	15d	08-Jan-24 A	26-Jan-24 A	08-Jan-24	26-Jan-24	
PRO-BLK-MR89-1040	MR89 - Purchase Order - Expansion Joints - DELETED	10d	10d	29-Jan-24 A	09-Feb-24 A	29-Jan-24	09-Feb-24	
PRO-BLK-MR89-1050	MR89 - Manufacturing & Ex-Works - Expansion Joints - DELETED	75d	160d	10-Feb-24 A	18-Jul-24 A	10-Feb-24	18-Jul-24	
PRO-BLK-MR89-1060	MR89 - Transportation &Yard Delivery - Expansion Joints - DELETED	5d	5d	19-Jul-24 A	23-Jul-24 A	19-Jul-24	23-Jul-24	
Piping supports (incl. Spring Supports, if any)		126d	163d	23-May-24 A	01-Dec-24	29-Feb-24	09-Aug-24	43d
PRO-BLK-MR56-1000	MR56 - Request for Quotation - Piping supports	1d	1d	23-May-24 A	23-May-24 A	29-Feb-24	29-Feb-24	
PRO-BLK-MR56-1060	MR56 - MR/MTO Issued - Piping supports	0d	0d	23-May-24 A		29-Feb-24		
PRO-BLK-MR56-1070	MR56 - Vendor Quotation - Piping supports	8d	3d	24-May-24 A	28-May-24 A	01-Mar-24	13-Mar-24	

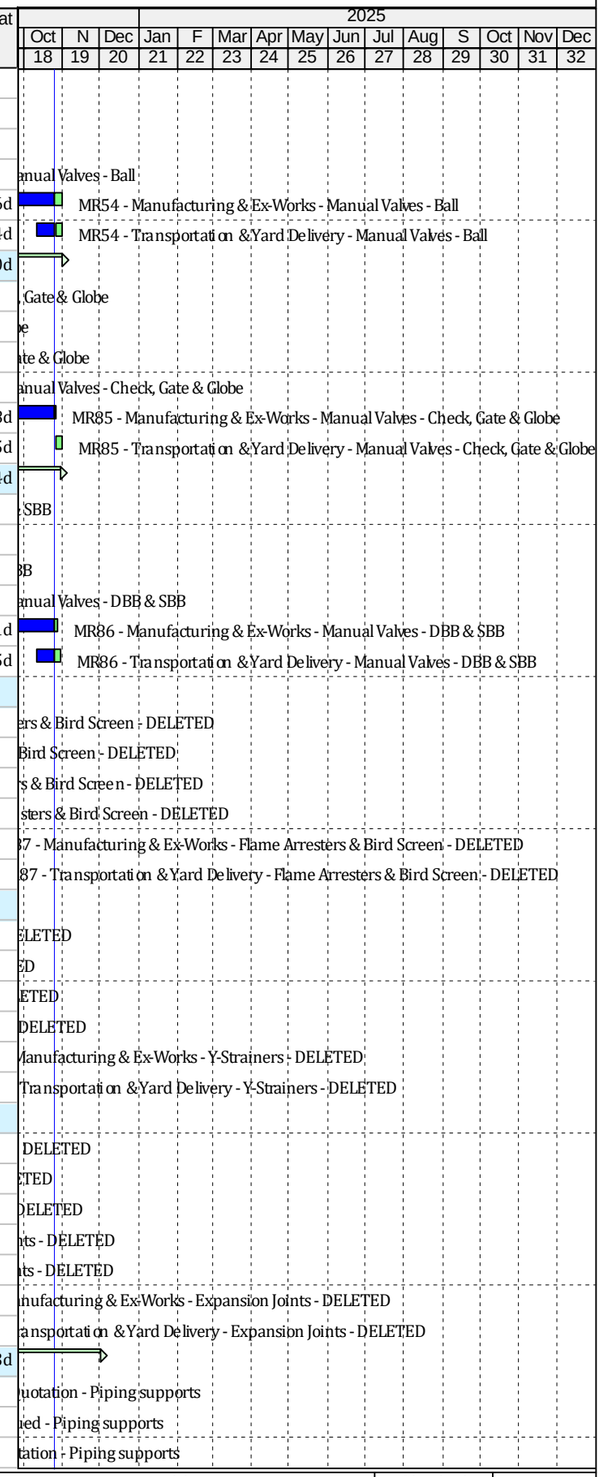

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR56-1030	MR56 - Purchase Order - Piping supports	10d	1d	29-May-24 A	29-May-24 A	14-Mar-24	27-Mar-24	
PRO-BLK-MR56-1040	MR56 - Manufacturing & Ex-Works - Piping supports	60d	172d	30-May-24 A	01-Dec-24	28-Mar-24	04-Aug-24	41d
PRO-BLK-MR56-1050	MR56 - Transportation & Yard Delivery - Piping supports	5d	76d	16-Sep-24 A	01-Dec-24	05-Aug-24	09-Aug-24	49d
Bulk Material - Electrical, Instrumentation, Control		317d	384d	20-Nov-23 A	26-Feb-25	10-Nov-23	27-Nov-24	204d
Cable Trays and Ladder		85d	140d	15-Mar-24 A	30-Aug-24 A	15-Feb-24	01-Aug-24	
PRO-BLK-MR57-1000	MR57 - Request for Quotation - Cable Trays and Ladder	1d	21d	15-Mar-24 A	15-Apr-24 A	15-Feb-24	15-Feb-24	
PRO-BLK-MR57-1060	MR57 - MR Issued - Cable Trays and Ladder	0d	0d	15-Mar-24 A		15-Feb-24		
PRO-BLK-MR57-1070	MR57 - Vendor Quotation - Cable Trays and Ladder	9d	9d	15-Apr-24 A	26-Apr-24 A	16-Feb-24	28-Feb-24	
PRO-BLK-MR57-1030	MR57 - Purchase Order - Cable Trays and Ladder	10d	1d	05-Jun-24 A	05-Jun-24 A	18-Mar-24	29-Mar-24	
PRO-BLK-MR57-1040	MR57 - Manufacturing & Ex-Works - Cable Trays and Ladder	10d	72d	06-Jun-24 A	30-Aug-24 A	30-Mar-24	27-Jul-24	
PRO-BLK-MR57-1050	MR57 - Transportation & Yard Delivery - Cable Trays and Ladder	5d	49d	12-Jul-24 A	30-Aug-24 A	28-Jul-24	01-Aug-24	
Instrument & Telecom Cable Trays		150d	140d	15-Mar-24 A	30-Aug-24 A	05-Feb-24	22-Jul-24	
PRO-BLK-MR59-1080	MR59 - Request for Quotation - Instrument and Telecom Cable Trays	1d	21d	15-Mar-24 A	15-Apr-24 A	05-Feb-24	05-Feb-24	
PRO-BLK-MR59-1090	MR59 - MR Issued - Instrument and Telecom Cable Trays	0d	0d	15-Mar-24 A		05-Feb-24		
PRO-BLK-MR59-1100	MR59 - Vendor Quotation - Instrument and Telecom Cable Trays	9d	8d	15-Apr-24 A	24-Apr-24 A	06-Feb-24	16-Feb-24	
PRO-BLK-MR59-1120	MR59 - Purchase Order - Instrument and Telecom Cable Trays	10d	1d	05-Jun-24 A	05-Jun-24 A	06-Mar-24	19-Mar-24	
PRO-BLK-MR59-1130	MR59 - Manufacturing & Ex-Works - Instrument and Telecom Cable Trays	93d	72d	06-Jun-24 A	30-Aug-24 A	20-Mar-24	17-Jul-24	
PRO-BLK-MR59-1140	MR59 - Transportation & Yard Delivery - Instrument and Telecom Cable Trays	5d	46d	15-Jul-24 A	30-Aug-24 A	18-Jul-24	22-Jul-24	
Electrical HV Cables		277d	289d	15-Mar-24 A	26-Feb-25	31-Jan-24	04-Sep-24	3d
PRO-BLK-MR58-1000	MR58 - Request for Quotation - Electrical HV Cables	1d	4d	15-Mar-24 A	20-Mar-24 A	31-Jan-24	31-Jan-24	
PRO-BLK-MR58-1060	MR58 - MR Issued - Electrical HV Cables	0d	0d	15-Mar-24 A		31-Jan-24		
PRO-BLK-MR58-1070	MR58 - Vendor Quotation - Electrical HV Cables	9d	68d	20-Mar-24 A	26-Jun-24 A	01-Feb-24	13-Feb-24	
PRO-BLK-MR58-1220	MR58 - Vendor Evaluation - Electrical HV Cables	15d	70d	27-Jun-24 A	04-Oct-24 A	14-Feb-24	05-Mar-24	
PRO-BLK-MR58-1030	MR58 - Purchase Order - Electrical HV Cables	5d	1d	04-Oct-24 A	04-Oct-24 A	06-Mar-24	19-Mar-24	
PRO-BLK-MR58-1040	MR58 - Manufacturing & Ex-Works - Electrical HV Cables	125d	125d	07-Oct-24 A	21-Feb-25	20-Mar-24	30-Aug-24	4d
PRO-BLK-MR58-1050	MR58 - Transportation & Yard Delivery - Electrical HV Cables	5d	5d	22-Feb-25	26-Feb-25	31-Aug-24	04-Sep-24	4d
Electrical MV Cables		165d	113d	15-Mar-24 A	29-Jul-24 A	31-Jan-24	04-Sep-24	
PRO-BLK-MR58-1080	MR58 - Request for Quotation - Electrical MV Cables	1d	4d	15-Mar-24 A	20-Mar-24 A	31-Jan-24	31-Jan-24	
PRO-BLK-MR58-1090	MR58 - MR Issued - Electrical MV Cables	0d	0d	15-Mar-24 A		31-Jan-24		
PRO-BLK-MR58-1100	MR58 - Vendor Quotation - Electrical MV Cables	9d	7d	20-Mar-24 A	28-Mar-24 A	01-Feb-24	13-Feb-24	
PRO-BLK-MR58-1230	MR58 - Vendor Evaluation - Electrical MV Cables	15d	47d	29-Mar-24 A	06-Jun-24 A	14-Feb-24	05-Mar-24	
PRO-BLK-MR58-1120	MR58 - Purchase Order - Electrical MV Cables	10d	0d	06-Jun-24 A	06-Jun-24 A	06-Mar-24	19-Mar-24	
PRO-BLK-MR58-1130	MR58 - Manufacturing & Ex-Works - Electrical MV Cables	77d	54d	06-Jun-24 A	29-Jul-24 A	20-Mar-24	30-Aug-24	
PRO-BLK-MR58-1140	MR58 - Transportation & Yard Delivery - Electrical MV Cables	5d	1d	29-Jul-24 A	29-Jul-24 A	31-Aug-24	04-Sep-24	
Electrical LV Cables		150d	164d	15-Mar-24 A	27-Sep-24 A	06-Feb-24	16-Sep-24	
PRO-BLK-MR58-1150	MR58 - Request for Quotation - Electrical LV Cables	1d	4d	15-Mar-24 A	20-Mar-24 A	06-Feb-24	06-Feb-24	
PRO-BLK-MR58-1160	MR58 - MR Issued - Electrical LV Cables	0d	0d	15-Mar-24 A		06-Feb-24		
PRO-BLK-MR58-1170	MR58 - Vendor Quotation - Electrical LV Cables	9d	7d	20-Mar-24 A	28-Mar-24 A	07-Feb-24	19-Feb-24	
PRO-BLK-MR58-1190	MR58 - Purchase Order - Electrical LV Cables	10d	1d	06-Jun-24 A	06-Jun-24 A	08-Mar-24	21-Mar-24	
PRO-BLK-MR58-1200	MR58 - Manufacturing & Ex-Works - Electrical LV Cables	92d	100d	06-Jun-24 A	27-Sep-24 A	22-Mar-24	11-Sep-24	
PRO-BLK-MR58-1210	MR58 - Transportation & Yard Delivery - Electrical LV Cables	5d	60d	29-Jul-24 A	27-Sep-24 A	12-Sep-24	16-Sep-24	
Instrumental cables		183d	106d	25-Mar-24 A	30-Jul-24 A	21-Feb-24	24-Sep-24	
PRO-BLK-MR59-1000	MR59 - Request for Quotation - Instrumental cables	1d	2d	25-Mar-24 A	26-Mar-24 A	21-Feb-24	21-Feb-24	
PRO-BLK-MR59-1060	MR59 - MR Issued - Instrumental cables	0d	0d	25-Mar-24 A		21-Feb-24		
PRO-BLK-MR59-1070	MR59 - Vendor Quotation - Instrumental cables	9d	3d	26-Mar-24 A	28-Mar-24 A	22-Feb-24	05-Mar-24	
PRO-BLK-MR59-1030	MR59 - Purchase Order - Instrumental cables	10d	1d	10-Jun-24 A	10-Jun-24 A	25-Mar-24	08-Apr-24	

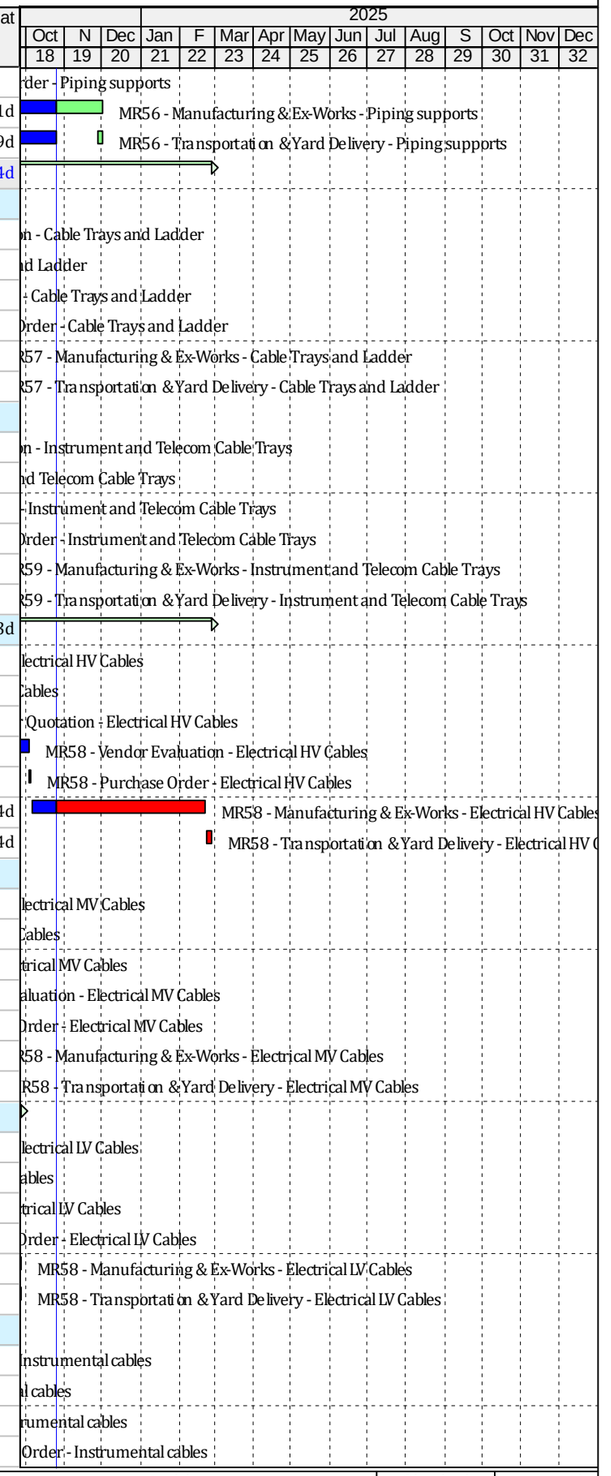

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR59-1040	MR59 - Manufacturing & Ex-Works - Instrumental cables	122d	50d	11-Jun-24 A	30-Jul-24 A	09-Apr-24	19-Sep-24	
PRO-BLK-MR59-1050	MR59 - Transportation & Yard Delivery - Instrumental cables	5d	0d	30-Jul-24 A	30-Jul-24 A	20-Sep-24	24-Sep-24	
Telecom cables		107d	81d	26-Apr-24 A	30-Jul-24 A	09-Feb-24	05-Oct-24	
PRO-BLK-MR60-1000	MR60 - Request for Quotation - Telecom cables - DELETED	1d	1d	26-Apr-24 A	26-Apr-24 A	09-Feb-24	09-Feb-24	
PRO-BLK-MR60-1060	MR60 - MR Issued - Telecom cables - DELETED	0d	0d	26-Apr-24 A		09-Feb-24		
PRO-BLK-MR60-1070	MR60 - Vendor Quotation - Telecom cables - DELETED	9d	9d	29-Apr-24 A	10-May-24 A	12-Feb-24	22-Feb-24	
PRO-BLK-MR60-1030	MR60 - Purchase Order - Telecom cables - DELETED	10d	10d	13-May-24 A	24-May-24 A	12-Mar-24	25-Mar-24	
PRO-BLK-MR60-1040	MR60 - Manufacturing & Ex-Works - Telecom cables - TO BE DELETED	86d	67d	25-May-24 A	30-Jul-24 A	26-Mar-24	30-Sep-24	
PRO-BLK-MR60-1050	MR60 - Transportation & Yard Delivery - Telecom cables - TO BE DELETED	5d	1d	30-Jul-24 A	30-Jul-24 A	01-Oct-24	05-Oct-24	
Earthing Cables		157d	113d	15-Mar-24 A	29-Jul-24 A	28-Dec-23	27-Aug-24	
PRO-BLK-MR61-1000	MR61 - Request for Quotation - Earthing Cables	1d	4d	15-Mar-24 A	20-Mar-24 A	28-Dec-23	28-Dec-23	
PRO-BLK-MR61-1060	MR61 - MR Issued - Earthing Cables	0d	0d	15-Mar-24 A		28-Dec-23		
PRO-BLK-MR61-1070	MR61 - Vendor Quotation - Earthing Cables	9d	7d	20-Mar-24 A	28-Mar-24 A	29-Dec-23	11-Jan-24	
PRO-BLK-MR61-1080	MR61 - Vendor Evaluation - Earthing Cables	15d	47d	29-Mar-24 A	06-Jun-24 A	12-Jan-24	01-Feb-24	
PRO-BLK-MR61-1030	MR61 - Purchase Order - Earthing Cables	10d	1d	06-Jun-24 A	06-Jun-24 A	02-Feb-24	15-Feb-24	
PRO-BLK-MR61-1040	MR61 - Manufacturing & Ex-Works - Earthing Cables	69d	54d	06-Jun-24 A	29-Jul-24 A	16-Feb-24	22-Aug-24	
PRO-BLK-MR61-1050	MR61 - Transportation & Yard Delivery - Earthing Cables	5d	1d	29-Jul-24 A	29-Jul-24 A	23-Aug-24	27-Aug-24	
Earthing accessories		97d	177d	13-Mar-24 A	10-Oct-24 A	11-Jan-24	18-Jun-24	
PRO-BLK-MR62-1060	MR62 - MR Issued - Earthing accessories	0d	0d	13-Mar-24 A		11-Jan-24		
PRO-BLK-MR62-1000	MR62 - Request for Quotation - Earthing accessories	1d	88d	14-Mar-24 A	19-Jul-24 A	11-Jan-24	11-Jan-24	
PRO-BLK-MR62-1070	MR62 - Vendor Quotation - Earthing accessories	9d	20d	20-Jul-24 A	19-Aug-24 A	12-Jan-24	24-Jan-24	
PRO-BLK-MR62-1030	MR62 - Purchase Order - Earthing accessories	10d	22d	20-Aug-24 A	18-Sep-24 A	25-Jan-24	07-Feb-24	
PRO-BLK-MR62-1040	MR62 - Manufacturing & Ex-Works - Earthing accessories	62d	22d	19-Sep-24 A	10-Oct-24 A	15-Feb-24	13-Jun-24	
PRO-BLK-MR62-1050	MR62 - Transportation & Yard Delivery - Earthing accessories	5d	4d	07-Oct-24 A	10-Oct-24 A	14-Jun-24	18-Jun-24	
Heat Tracing		113d	111d	24-Jun-24 A	31-Oct-24	23-Jan-24	09-Aug-24	77d
PRO-BLK-MR90-1000	MR90 - Request for Quotation - Heat Tracing	1d	3d	24-Jun-24 A	26-Jun-24 A	23-Jan-24	23-Jan-24	
PRO-BLK-MR90-1010	MR90 - MR Issued - Heat Tracing	0d	0d	24-Jun-24 A		23-Jan-24		
PRO-BLK-MR90-1020	MR90 - Vendor Quotation - Heat Tracing	9d	13d	26-Jun-24 A	12-Jul-24 A	24-Jan-24	05-Feb-24	
PRO-BLK-MR90-1040	MR90 - Purchase Order - Heat Tracing	10d	1d	08-Aug-24 A	08-Aug-24 A	23-Feb-24	07-Mar-24	
PRO-BLK-MR90-1050	MR90 - Manufacturing & Ex-Works - Heat Tracing	78d	69d	09-Aug-24 A	26-Oct-24	08-Mar-24	04-Aug-24	83d
PRO-BLK-MR90-1060	MR90 - Transportation & Yard Delivery - Heat Tracing	5d	5d	27-Oct-24	31-Oct-24	05-Aug-24	09-Aug-24	90d
Cable Glands		122d	120d	15-Apr-24 A	04-Sep-24 A	15-Feb-24	01-Aug-24	
PRO-BLK-MR63-1000	MR63 - Request for Quotation - Cable Glands	1d	1d	15-Apr-24 A	15-Apr-24 A	15-Feb-24	15-Feb-24	
PRO-BLK-MR63-1060	MR63 - MR Issued - Cable Glands	0d	0d	15-Apr-24 A		15-Feb-24		
PRO-BLK-MR63-1070	MR63 - Vendor Quotation - Cable Glands	9d	47d	16-Apr-24 A	21-Jun-24 A	16-Feb-24	28-Feb-24	
PRO-BLK-MR63-1030	MR63 - Purchase Order - Cable Glands	10d	1d	19-Jul-24 A	19-Jul-24 A	18-Mar-24	29-Mar-24	
PRO-BLK-MR63-1040	MR63 - Manufacturing & Ex-Works - Cable Glands	73d	33d	20-Jul-24 A	04-Sep-24 A	30-Mar-24	27-Jul-24	
PRO-BLK-MR63-1050	MR63 - Transportation & Yard Delivery - Cable Glands	5d	1d	04-Sep-24 A	04-Sep-24 A	28-Jul-24	01-Aug-24	
Connections & Terminations		240d	172d	21-Feb-24 A	13-Sep-24 A	23-Feb-24	26-Aug-24	
PRO-BLK-MR63-1080	MR63 - Request for Quotation - Connections & Terminations	1d	59d	21-Feb-24 A	16-May-24 A	23-Feb-24	23-Feb-24	
PRO-BLK-MR63-1090	MR63 - MR Issued - Connections & Terminations	0d	0d	21-Feb-24 A		23-Feb-24		
PRO-BLK-MR63-1100	MR63 - Vendor Quotation - Connections & Terminations	9d	19d	17-May-24 A	12-Jun-24 A	26-Feb-24	07-Mar-24	
PRO-BLK-MR63-1120	MR63 - Purchase Order - Connections & Terminations	10d	38d	13-Jun-24 A	05-Aug-24 A	26-Mar-24	09-Apr-24	
PRO-BLK-MR63-1130	MR63 - Manufacturing & Ex-Works - Connections & Terminations	107d	21d	06-Aug-24 A	08-Sep-24 A	10-Apr-24	21-Aug-24	
PRO-BLK-MR63-1140	MR63 - Transportation & Yard Delivery - Connections & Terminations	5d	5d	09-Sep-24 A	13-Sep-24 A	22-Aug-24	26-Aug-24	
Junction Boxes		107d	182d	01-Mar-24 A	04-Oct-24 A	28-Dec-23	16-Jun-24	

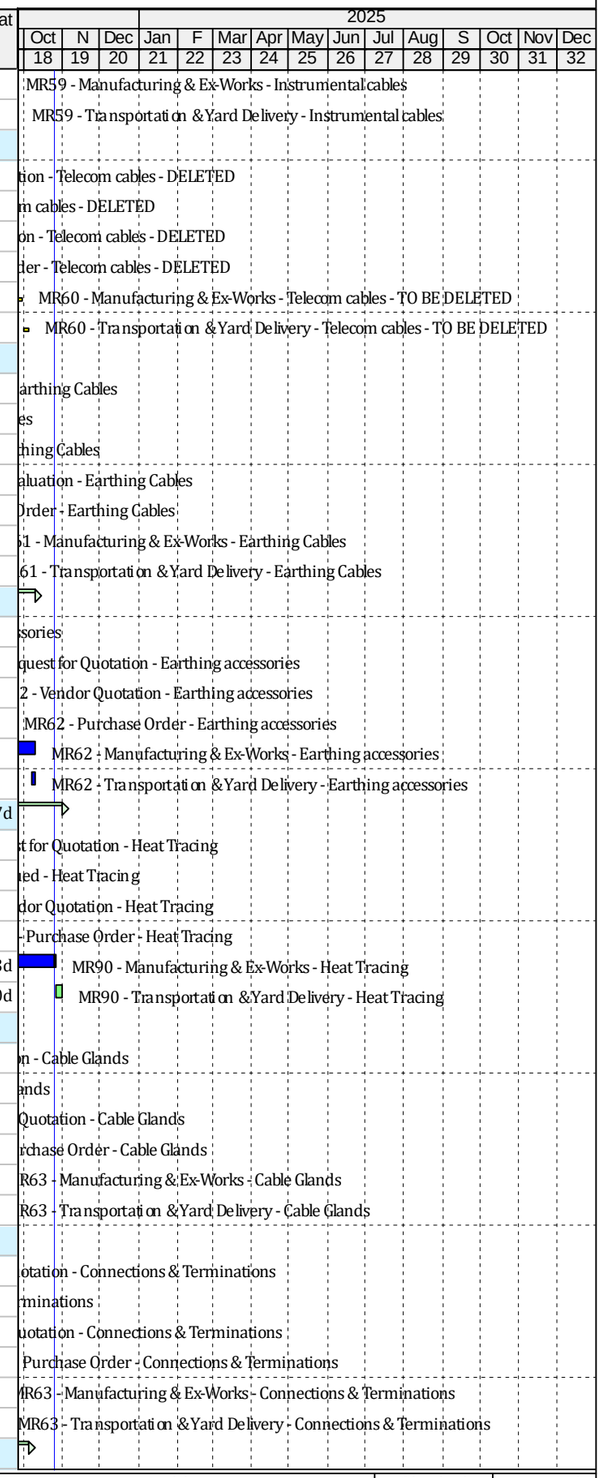

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR64-1000	MR64 - Request for Quotation - Junction Boxes	1d	1d	01-Mar-24 A	01-Mar-24 A	28-Dec-23	28-Dec-23	
PRO-BLK-MR64-1060	MR64 - MR Issued - Junction Boxes	0d	0d	01-Mar-24 A		28-Dec-23		
PRO-BLK-MR64-1070	MR64 - Vendor Quotation - Junction Boxes	9d	77d	02-Mar-24 A	21-Jun-24 A	29-Dec-23	11-Jan-24	
PRO-BLK-MR64-1030	MR64 - Purchase Order - Junction Boxes	10d	5d	15-Jul-24 A	19-Jul-24 A	30-Jan-24	12-Feb-24	
PRO-BLK-MR64-1040	MR64 - Manufacturing & Ex-Works - Junction Boxes	62d	61d	20-Jul-24 A	02-Oct-24 A	13-Feb-24	11-Jun-24	
PRO-BLK-MR64-1050	MR64 - Transportation & Yard Delivery - Junction Boxes	5d	2d	03-Oct-24 A	04-Oct-24 A	12-Jun-24	16-Jun-24	
MCT		47d	99d	08-Mar-24 A	05-Jul-24 A	23-Feb-24	13-Jul-24	
PRO-BLK-MR65-1060	MR65 - MR Issued - MCT	0d	0d	08-Mar-24 A		23-Feb-24		
PRO-BLK-MR65-1000	MR65 - Request for Quotation - MCT	1d	1d	15-May-24 A	15-May-24 A	23-Feb-24	23-Feb-24	
PRO-BLK-MR65-1070	MR65 - Vendor Quotation - MCT	9d	6d	16-May-24 A	23-May-24 A	26-Feb-24	07-Mar-24	
PRO-BLK-MR65-1030	MR65 - Purchase Order - MCT	10d	3d	23-May-24 A	27-May-24 A	26-Mar-24	09-Apr-24	
PRO-BLK-MR65-1040	MR65 - Manufacturing & Ex-Works - MCT	33d	39d	28-May-24 A	05-Jul-24 A	10-Apr-24	08-Jul-24	
PRO-BLK-MR65-1050	MR65 - Transportation & Yard Delivery - MCT	5d	1d	05-Jul-24 A	05-Jul-24 A	09-Jul-24	13-Jul-24	
Instrument & Telecom MCT		114d	45d	15-May-24 A	05-Jul-24 A	09-Feb-24	28-Jun-24	
PRO-BLK-MR59-1150	MR59 - Request for Quotation - Instrument and Telecom MCTs	1d	1d	15-May-24 A	15-May-24 A	09-Feb-24	09-Feb-24	
PRO-BLK-MR59-1160	MR59 - MR Issued - Instrument and Telecom MCTs	0d	0d	15-May-24 A		09-Feb-24		
PRO-BLK-MR59-1170	MR59 - Vendor Quotation - Instrument and Telecom MCTs	9d	7d	15-May-24 A	23-May-24 A	12-Feb-24	22-Feb-24	
PRO-BLK-MR59-1190	MR59 - Purchase Order - Instrument and Telecom MCTs	10d	2d	24-May-24 A	27-May-24 A	12-Mar-24	25-Mar-24	
PRO-BLK-MR59-1200	MR59 - Manufacturing & Ex-Works - Instrument and Telecom MCTs	90d	39d	28-May-24 A	05-Jul-24 A	26-Mar-24	23-Jun-24	
PRO-BLK-MR59-1210	MR59 - Transportation & Yard Delivery - Instrument and Telecom MCTs	1d	1d	05-Jul-24 A	05-Jul-24 A	24-Jun-24	28-Jun-24	
Instrument Junction Boxes		226d	116d	15-Apr-24 A	30-Aug-24 A	27-Nov-23	13-Jul-24	
PRO-BLK-MR59-1290	MR59 - Request for Quotation - Instrument Junction Boxes	1d	1d	15-Apr-24 A	15-Apr-24 A	27-Nov-23	27-Nov-23	
PRO-BLK-MR59-1300	MR59 - MR Issued - Instrument Junction Boxes	0d	0d	15-Apr-24 A		27-Nov-23		
PRO-BLK-MR59-1310	MR59 - Vendor Quotation - Instrument Junction Boxes	9d	3d	15-Apr-24 A	17-Apr-24 A	28-Nov-23	11-Dec-23	
PRO-BLK-MR59-1330	MR59 - Purchase Order - Instrument Junction Boxes	10d	1d	26-Jun-24 A	26-Jun-24 A	02-Jan-24	15-Jan-24	
PRO-BLK-MR59-1340	MR59 - Manufacturing & Ex-Works - Instrument Junction Boxes	156d	46d	27-Jun-24 A	26-Aug-24 A	16-Jan-24	08-Jul-24	
PRO-BLK-MR59-1350	MR59 - Transportation & Yard Delivery - Instrument Junction Boxes	5d	5d	26-Aug-24 A	30-Aug-24 A	09-Jul-24	13-Jul-24	
Instrument Cable Glands & Accessories		232d	120d	15-Apr-24 A	04-Sep-24 A	15-Feb-24	09-Oct-24	
PRO-BLK-MR59-1220	MR59 - Request for Quotation - Instrument Cable Glands and Accessory	1d	1d	15-Apr-24 A	15-Apr-24 A	15-Feb-24	15-Feb-24	
PRO-BLK-MR59-1230	MR59 - MR Issued - Instrument Cable Glands and Accessory	0d	0d	15-Apr-24 A		15-Feb-24		
PRO-BLK-MR59-1240	MR59 - Vendor Quotation - Instrument Cable Glands and Accessory	9d	23d	15-Apr-24 A	17-May-24 A	16-Feb-24	28-Feb-24	
PRO-BLK-MR59-1260	MR59 - Purchase Order - Instrument Cable Glands and Accessory	10d	1d	19-Jul-24 A	19-Jul-24 A	18-Mar-24	29-Mar-24	
PRO-BLK-MR59-1270	MR59 - Manufacturing & Ex-Works - Instrument Cable Glands and Accessory	151d	33d	20-Jul-24 A	04-Sep-24 A	30-Mar-24	04-Oct-24	
PRO-BLK-MR59-1280	MR59 - Transportation & Yard Delivery - Instrument Cable Glands and Accessory	5d	1d	04-Sep-24 A	04-Sep-24 A	05-Oct-24	09-Oct-24	
Floor penetration for GIS & MV cables		57d	18d	20-Nov-23 A	11-Dec-23 A	10-Nov-23	10-Apr-24	
PRO-BLK-MR66-1000	MR66 - Request for Quotation - Floor penetration for GIS & MV cables	1d	1d	20-Nov-23 A	20-Nov-23 A	10-Nov-23	10-Nov-23	
PRO-BLK-MR66-1060	MR66 - MR Issued - Floor penetration for GIS & MV cables	0d	0d	20-Nov-23 A		10-Nov-23		
PRO-BLK-MR66-1070	MR66 - Vendor Quotation - Floor penetration for GIS & MV cables	9d	5d	21-Nov-23 A	27-Nov-23 A	13-Nov-23	23-Nov-23	
PRO-BLK-MR66-1010	MR66 - Vendor Evaluation - Floor penetration for GIS & MV cables	15d	3d	28-Nov-23 A	30-Nov-23 A	24-Nov-23	15-Dec-23	
PRO-BLK-MR66-1030	MR66 - Purchase Order - Floor penetration for GIS & MV cables	10d	1d	30-Nov-23 A	30-Nov-23 A	18-Dec-23	03-Jan-24	
PRO-BLK-MR66-1040	MR66 - Manufacturing & Ex-Works - Floor penetration for GIS & MV cables	13d	11d	01-Dec-23 A	11-Dec-23 A	07-Jan-24	05-Apr-24	
PRO-BLK-MR66-1050	MR66 - Transportation & Yard Delivery - Floor penetration for GIS & MV cables	5d	1d	11-Dec-23 A	11-Dec-23 A	06-Apr-24	10-Apr-24	
Lighting Fixtures		121d	146d	22-Mar-24 A	13-Sep-24 A	28-Dec-23	31-Jul-24	
PRO-BLK-MR67-1060	MR67 - MR Issued - Lighting Fixtures	0d	0d	22-Mar-24 A		28-Dec-23		
PRO-BLK-MR67-1000	MR67 - Request for Quotation - Lighting Fixtures	1d	1d	02-May-24 A	02-May-24 A	28-Dec-23	28-Dec-23	
PRO-BLK-MR67-1070	MR67 - Vendor Quotation - Lighting Fixtures	9d	7d	02-May-24 A	10-May-24 A	29-Dec-23	11-Jan-24	

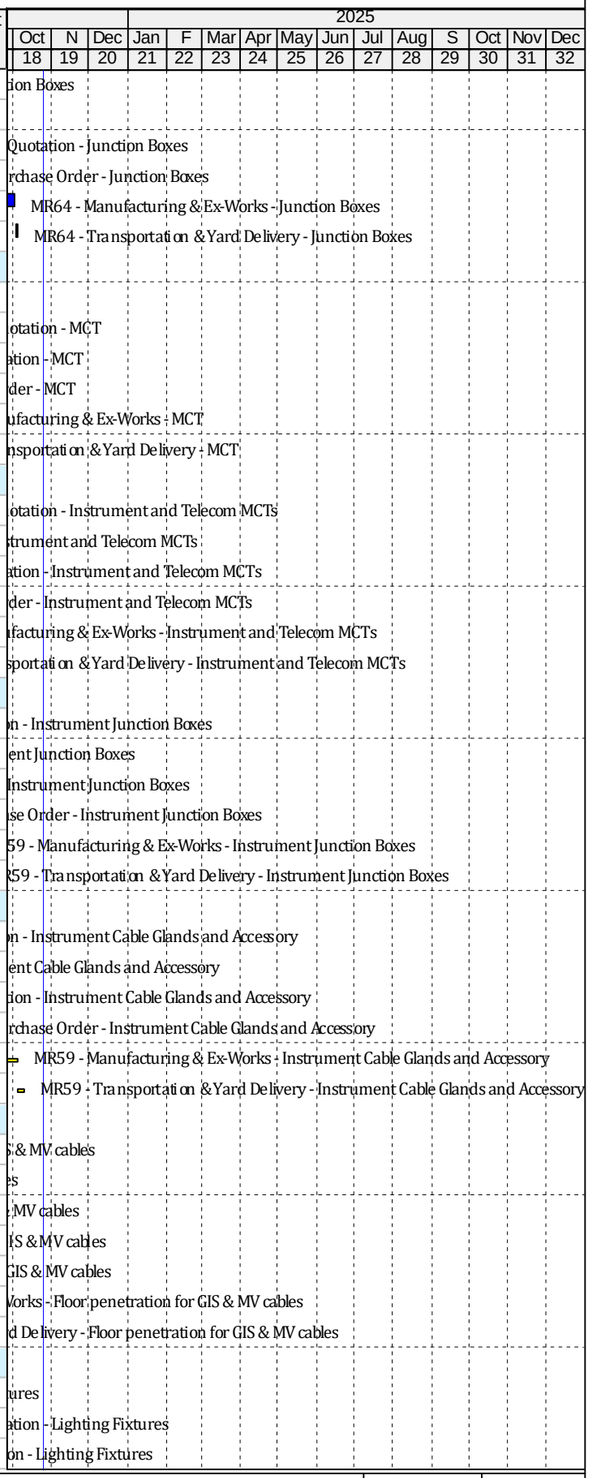

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR67-1030	MR67 - Purchase Order - Lighting Fixtures	10d	1d	25-Jun-24 A	25-Jun-24 A	30-Jan-24	12-Feb-24	
PRO-BLK-MR67-1040	MR67 - Manufacturing & Ex-Works - Lighting Fixtures	70d	66d	26-Jun-24 A	13-Sep-24 A	13-Feb-24	26-Jul-24	
PRO-BLK-MR67-1050	MR67 - Transportation & Yard Delivery - Lighting Fixtures	5d	1d	13-Sep-24 A	13-Sep-24 A	27-Jul-24	31-Jul-24	
Small Power Sockets		93d	182d	01-Mar-24 A	04-Oct-24 A	02-Jan-24	07-Aug-24	
PRO-BLK-MR91-1000	MR91 - Request for Quotation - Small Power Sockets	1d	1d	01-Mar-24 A	01-Mar-24 A	02-Jan-24	02-Jan-24	
PRO-BLK-MR91-1010	MR91 - MR Issued - Small Power Sockets	0d	0d	01-Mar-24 A		02-Jan-24		
PRO-BLK-MR91-1020	MR91 - Vendor Quotation - Small Power Sockets	9d	77d	02-Mar-24 A	21-Jun-24 A	03-Jan-24	15-Jan-24	
PRO-BLK-MR91-1070	MR91 - Vendor Evaluation - Small Power Sockets	15d	20d	22-Jun-24 A	19-Jul-24 A	16-Jan-24	05-Feb-24	
PRO-BLK-MR91-1040	MR91 - Purchase Order - Small Power Sockets	10d	1d	19-Jul-24 A	19-Jul-24 A	06-Feb-24	19-Feb-24	
PRO-BLK-MR91-1050	MR91 - Manufacturing & Ex-Works - Small Power Sockets	60d	61d	20-Jul-24 A	02-Oct-24 A	20-Feb-24	02-Aug-24	
PRO-BLK-MR91-1060	MR91 - Transportation & Yard Delivery - Small Power Sockets	5d	2d	03-Oct-24 A	04-Oct-24 A	03-Aug-24	07-Aug-24	
Pressure, Temperature and Diff. Pressure Level Transmitters		239d	173d	17-Jan-24 A	09-Aug-24 A	04-Jan-24	02-Oct-24	
PRO-BLK-MR68-1080	MR68 - Request for Quotation - Pressure, Temperature and Diff. Pressure Level Transmitters	1d	1d	17-Jan-24 A	17-Jan-24 A	04-Jan-24	04-Jan-24	
PRO-BLK-MR68-1090	MR68 - MR Issued - Pressure, Temperature and Diff. Pressure Level Transmitters	0d	0d	17-Jan-24 A		04-Jan-24		
PRO-BLK-MR68-1100	MR68 - Vendor Quotation - Pressure, Temperature and Diff. Pressure Level Transmitters	9d	12d	17-Jan-24 A	01-Feb-24 A	05-Jan-24	17-Jan-24	
PRO-BLK-MR68-1120	MR68 - Purchase Order - Pressure, Temperature and Diff. Pressure Level Transmitters	10d	50d	02-Mar-24 A	15-May-24 A	05-Feb-24	16-Feb-24	
PRO-BLK-MR68-1130	MR68 - Manufacturing & Ex-Works - Pressure, Temperature and Diff. Pressure Level Transmitters	137d	81d	16-May-24 A	09-Aug-24 A	17-Feb-24	27-Sep-24	
PRO-BLK-MR68-1140	MR68 - Transportation & Yard Delivery - Pressure, Temperature and Diff. Pressure Level Transmitters	5d	1d	09-Aug-24 A	09-Aug-24 A	28-Sep-24	02-Oct-24	
Radar Level Transmitters		167d	173d	17-Jan-24 A	09-Aug-24 A	04-Jan-24	02-Oct-24	
PRO-BLK-MR68-1150	MR68 - Request for Quotation - Radar Level Transmitters	1d	1d	17-Jan-24 A	17-Jan-24 A	04-Jan-24	04-Jan-24	
PRO-BLK-MR68-1160	MR68 - MR Issued - Radar Level Transmitters	0d	0d	17-Jan-24 A		04-Jan-24		
PRO-BLK-MR68-1170	MR68 - Vendor Quotation - Radar Level Transmitters	9d	12d	17-Jan-24 A	01-Feb-24 A	05-Jan-24	17-Jan-24	
PRO-BLK-MR68-1190	MR68 - Purchase Order - Radar Level Transmitters	10d	71d	02-Feb-24 A	15-May-24 A	05-Feb-24	16-Feb-24	
PRO-BLK-MR68-1200	MR68 - Manufacturing & Ex-Works - Radar Level Transmitters	137d	81d	16-May-24 A	09-Aug-24 A	17-Feb-24	27-Sep-24	
PRO-BLK-MR68-1210	MR68 - Transportation & Yard Delivery - Radar Level Transmitters	5d	1d	09-Aug-24 A	09-Aug-24 A	28-Sep-24	02-Oct-24	
Variable Area Flow Transmitters and Flow gauges		220d	199d	26-Feb-24 A	19-Oct-24 A	04-Jan-24	02-Oct-24	
PRO-BLK-MR68-1220	MR68 - Request for Quotation - Variable Area Flow Transmitters and Flow gauges	1d	1d	26-Feb-24 A	26-Feb-24 A	04-Jan-24	04-Jan-24	
PRO-BLK-MR68-1240	MR68 - Vendor Quotation - Variable Area Flow Transmitters and Flow gauges	9d	5d	26-Feb-24 A	01-Mar-24 A	05-Jan-24	17-Jan-24	
PRO-BLK-MR68-1230	MR68 - MR Issued - Variable Area Flow Transmitters and Flow gauges	0d	0d	28-Feb-24 A		04-Jan-24		
PRO-BLK-MR68-1260	MR68 - Purchase Order - Variable Area Flow Transmitters and Flow gauges	10d	1d	15-Apr-24 A	15-Apr-24 A	05-Feb-24	16-Feb-24	
PRO-BLK-MR68-1270	MR68 - Manufacturing & Ex-Works - Variable Area Flow Transmitters and Flow gauges	169d	174d	15-Apr-24 A	19-Oct-24 A	17-Feb-24	27-Sep-24	
PRO-BLK-MR68-1280	MR68 - Transportation & Yard Delivery - Variable Area Flow Transmitters and Flow gauges	5d	5d	15-Oct-24 A	19-Oct-24 A	28-Sep-24	02-Oct-24	
Ultrasonic Flow Transmitters		216d	237d	18-Mar-24 A	27-Dec-24	04-Jan-24	02-Oct-24	55d
PRO-BLK-MR68-1290	MR68 - Request for Quotation - Ultrasonic Flow Transmitters	1d	3d	18-Mar-24 A	20-Mar-24 A	04-Jan-24	04-Jan-24	
PRO-BLK-MR68-1300	MR68 - MR Issued - Ultrasonic Flow Transmitters	0d	0d	18-Mar-24 A		04-Jan-24		
PRO-BLK-MR68-1310	MR68 - Vendor Quotation - Ultrasonic Flow Transmitters	9d	8d	20-Mar-24 A	29-Mar-24 A	05-Jan-24	17-Jan-24	
PRO-BLK-MR68-1330	MR68 - Purchase Order - Ultrasonic Flow Transmitters	10d	1d	28-Jun-24 A	28-Jun-24 A	05-Feb-24	16-Feb-24	
PRO-BLK-MR68-1340	MR68 - Manufacturing & Ex-Works - Ultrasonic Flow Transmitters	144d	162d	28-Jun-24 A	20-Dec-24	17-Feb-24	27-Sep-24	56d
PRO-BLK-MR68-1350	MR68 - Transportation & Yard Delivery - Ultrasonic Flow Transmitters	5d	5d	21-Dec-24	27-Dec-24	28-Sep-24	02-Oct-24	65d
Flow Gauges		171d	201d	28-Feb-24 A	24-Oct-24 A	04-Jan-24	02-Oct-24	
PRO-BLK-MR68-1360	MR68 - Request for Quotation - Flow Gauges	1d	1d	28-Feb-24 A	28-Feb-24 A	04-Jan-24	04-Jan-24	
PRO-BLK-MR68-1370	MR68 - MR Issued - Flow Gauges	0d	0d	28-Feb-24 A		04-Jan-24		
PRO-BLK-MR68-1380	MR68 - Vendor Quotation - Flow Gauges	9d	3d	28-Feb-24 A	01-Mar-24 A	05-Jan-24	17-Jan-24	
PRO-BLK-MR68-1390	MR68 - Purchase Order - Flow Gauges	10d	31d	01-Mar-24 A	15-Apr-24 A	05-Feb-24	16-Feb-24	
PRO-BLK-MR68-1400	MR68 - Manufacturing & Ex-Works - Flow Gauges	156d	179d	15-Apr-24 A	24-Oct-24 A	17-Feb-24	27-Sep-24	
PRO-BLK-MR68-1410	MR68 - Transportation & Yard Delivery - Flow Gauges	5d	5d	20-Oct-24 A	24-Oct-24 A	28-Sep-24	02-Oct-24	

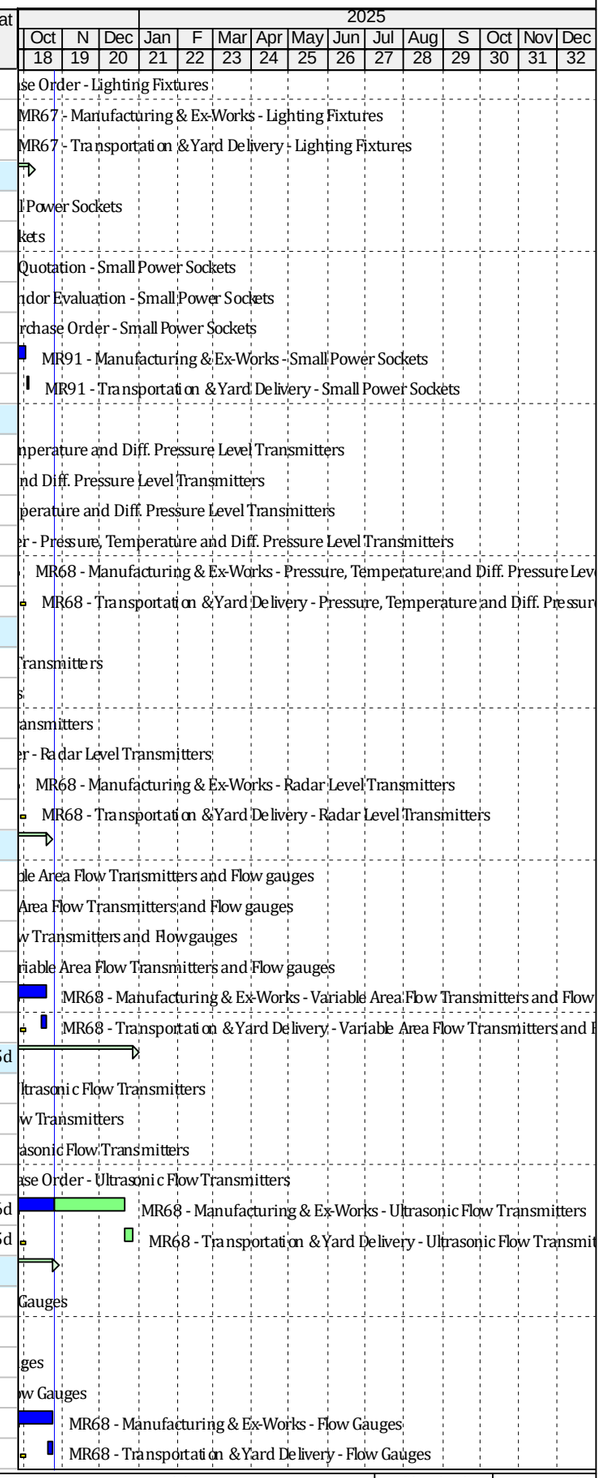

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
F&G Detectors		256d	198d	05-Feb-24 A	27-Sep-24 A	15-Dec-23	27-Nov-24	
PRO-BLK-MR92-1000	MR92 - Request for Quotation - F&G Detectors	1d	1d	05-Feb-24 A	05-Feb-24 A	15-Dec-23	15-Dec-23	
PRO-BLK-MR92-1010	MR92 - MR Issued - F&G Detectors	0d	0d	05-Feb-24 A		15-Dec-23		
PRO-BLK-MR92-1020	MR92 - Vendor Quotation - F&G Detectors	9d	10d	05-Feb-24 A	16-Feb-24 A	18-Dec-23	02-Jan-24	
PRO-BLK-MR92-1040	MR92 - Purchase Order - F&G Detectors	10d	44d	16-Feb-24 A	18-Apr-24 A	22-Jan-24	02-Feb-24	
PRO-BLK-MR92-1050	MR92 - Manufacturing & Ex-Works - F&G Detectors	197d	149d	18-Apr-24 A	27-Sep-24 A	03-Feb-24	22-Nov-24	
PRO-BLK-MR92-1060	MR92 - Transportation & Yard Delivery - F&G Detectors	5d	1d	27-Sep-24 A	27-Sep-24 A	23-Nov-24	27-Nov-24	
Dew Point Analyzer		187d	222d	04-Jan-24 A	25-Sep-24 A	04-Jan-24	30-Jul-24	
PRO-BLK-MR93-1000	MR93 - Request for Quotation - Dew Point Analyzer - deleted	1d	1d	04-Jan-24 A	04-Jan-24 A	04-Jan-24	04-Jan-24	
PRO-BLK-MR93-1010	MR93 - MR Issued - Dew Point Analyzer - deleted	0d	0d	04-Jan-24 A		04-Jan-24		
PRO-BLK-MR93-1020	MR93 - Vendor Quotation - Dew Point Analyzer - deleted	9d	9d	05-Jan-24 A	17-Jan-24 A	05-Jan-24	17-Jan-24	
PRO-BLK-MR93-1040	MR93 - Purchase Order - Dew Point Analyzer - deleted	10d	10d	05-Feb-24 A	16-Feb-24 A	05-Feb-24	16-Feb-24	
PRO-BLK-MR93-1050	MR93 - Manufacturing & Ex-Works - Dew Point Analyzer - deleted	160d	160d	17-Feb-24 A	25-Jul-24 A	17-Feb-24	25-Jul-24	
PRO-BLK-MR93-1060	MR93 - Transportation & Yard Delivery - Dew Point Analyzer - deleted	5d	61d	26-Jul-24 A	25-Sep-24 A	26-Jul-24	30-Jul-24	
Orifice		115d	132d	16-Jul-24 A	18-Dec-24	20-Dec-23	23-Sep-24	260d
PRO-BLK-MR94-1000	MR94 - Request for Quotation - Restriction Orifice	1d	4d	16-Jul-24 A	19-Jul-24 A	20-Dec-23	20-Dec-23	
PRO-BLK-MR94-1010	MR94 - MR Issued - Restriction Orifice	0d	0d	16-Jul-24 A		20-Dec-23		
PRO-BLK-MR94-1020	MR94 - Vendor Quotation - Restriction Orifice	9d	12d	19-Jul-24 A	05-Aug-24 A	21-Dec-23	05-Jan-24	
PRO-BLK-MR94-1040	MR94 - Purchase Order - Restriction Orifice	10d	1d	27-Aug-24 A	27-Aug-24 A	25-Jan-24	07-Feb-24	
PRO-BLK-MR94-1050	MR94 - Manufacturing & Ex-Works - Restriction Orifice	70d	108d	28-Aug-24 A	13-Dec-24	08-Feb-24	18-Sep-24	288d
PRO-BLK-MR94-1060	MR94 - Transportation & Yard Delivery - Restriction Orifice	5d	5d	14-Dec-24	18-Dec-24	19-Sep-24	23-Sep-24	306d
Tubing		157d	148d	27-Mar-24 A	20-Sep-24 A	09-Feb-24	20-Sep-24	
PRO-BLK-MR69-1000	MR69 - Request for Quotation - Tubing	1d	13d	27-Mar-24 A	15-Apr-24 A	09-Feb-24	09-Feb-24	
PRO-BLK-MR69-1060	MR69 - MR Issued - Tubing	0d	0d	27-Mar-24 A		09-Feb-24		
PRO-BLK-MR69-1070	MR69 - Vendor Quotation - Tubing	9d	10d	15-Apr-24 A	29-Apr-24 A	12-Feb-24	22-Feb-24	
PRO-BLK-MR69-1040	MR69 - Manufacturing & Ex-Works - Tubing	146d	138d	22-Apr-24 A	20-Sep-24 A	26-Mar-24	15-Sep-24	
PRO-BLK-MR69-1050	MR69 - Transportation & Yard Delivery - Tubing	5d	148d	22-Apr-24 A	20-Sep-24 A	16-Sep-24	20-Sep-24	
PRO-BLK-MR69-1030	MR69 - Purchase Order - Tubing	10d	45d	29-Apr-24 A	01-Jul-24 A	12-Mar-24	25-Mar-24	
E&I supports (incl. Bulk Material)		138d	93d	30-Jan-24 A	21-May-24 A	08-Jan-24	27-Jun-24	
PRO-BLK-MR70-1000	MR70 - Request for Quotation - E&I supports	1d	1d	30-Jan-24 A	30-Jan-24 A	08-Jan-24	08-Jan-24	
PRO-BLK-MR70-1060	MR70 - MR Issued - E&I supports	0d	0d	30-Jan-24 A		08-Jan-24		
PRO-BLK-MR70-1070	MR70 - Vendor Quotation - E&I supports	9d	28d	30-Jan-24 A	07-Mar-24 A	09-Jan-24	19-Jan-24	
PRO-BLK-MR70-1030	MR70 - Purchase Order - E&I supports	10d	1d	07-Mar-24 A	07-Mar-24 A	12-Feb-24	23-Feb-24	
PRO-BLK-MR70-1040	MR70 - Manufacturing & Ex-Works - E&I supports	69d	76d	07-Mar-24 A	21-May-24 A	24-Feb-24	22-Jun-24	
PRO-BLK-MR70-1080	MR70 - Vendor Evaluation - E&I supports	15d	1d	07-Mar-24 A	07-Mar-24 A	22-Jan-24	09-Feb-24	
PRO-BLK-MR70-1050	MR70 - Transportation & Yard Delivery - E&I supports	5d	1d	21-May-24 A	21-May-24 A	23-Jun-24	27-Jun-24	
Bulk Material - Insulation & Coating		248d	293d	17-Nov-23 A	05-Nov-24	18-Dec-23	24-Aug-24	84d
Painting for Structures		61d	100d	17-Nov-23 A	18-Mar-24 A	18-Dec-23	21-Feb-24	
PRO-BLK-MR71-1000	MR71 - Request for Quotation - Painting for Structures	1d	8d	17-Nov-23 A	28-Nov-23 A	18-Dec-23	18-Dec-23	
PRO-BLK-MR71-1060	MR71 - MR Issued - Painting for Structures	0d	0d	17-Nov-23 A		18-Dec-23		
PRO-BLK-MR71-1070	MR71 - Vendor Quotation - Painting for Structures	9d	18d	28-Nov-23 A	22-Dec-23 A	19-Dec-23	03-Jan-24	
PRO-BLK-MR71-1030	MR71 - Purchase Order - Painting for Structures	10d	29d	22-Dec-23 A	05-Feb-24 A	04-Jan-24	17-Jan-24	
PRO-BLK-MR71-1040	MR71 - Manufacturing & Ex-Works - Painting for Structures	27d	43d	05-Feb-24 A	18-Mar-24 A	18-Jan-24	16-Feb-24	
PRO-BLK-MR71-1050	MR71 - Transportation & Yard Delivery - Painting for Structures	5d	15d	04-Mar-24 A	18-Mar-24 A	17-Feb-24	21-Feb-24	
Painting for Piping		98d	42d	03-May-24 A	20-Jun-24 A	15-Mar-24	17-May-24	
PRO-BLK-MR72-1000	MR72 - Request for Quotation - Painting for Piping	1d	2d	03-May-24 A	06-May-24 A	15-Mar-24	15-Mar-24	

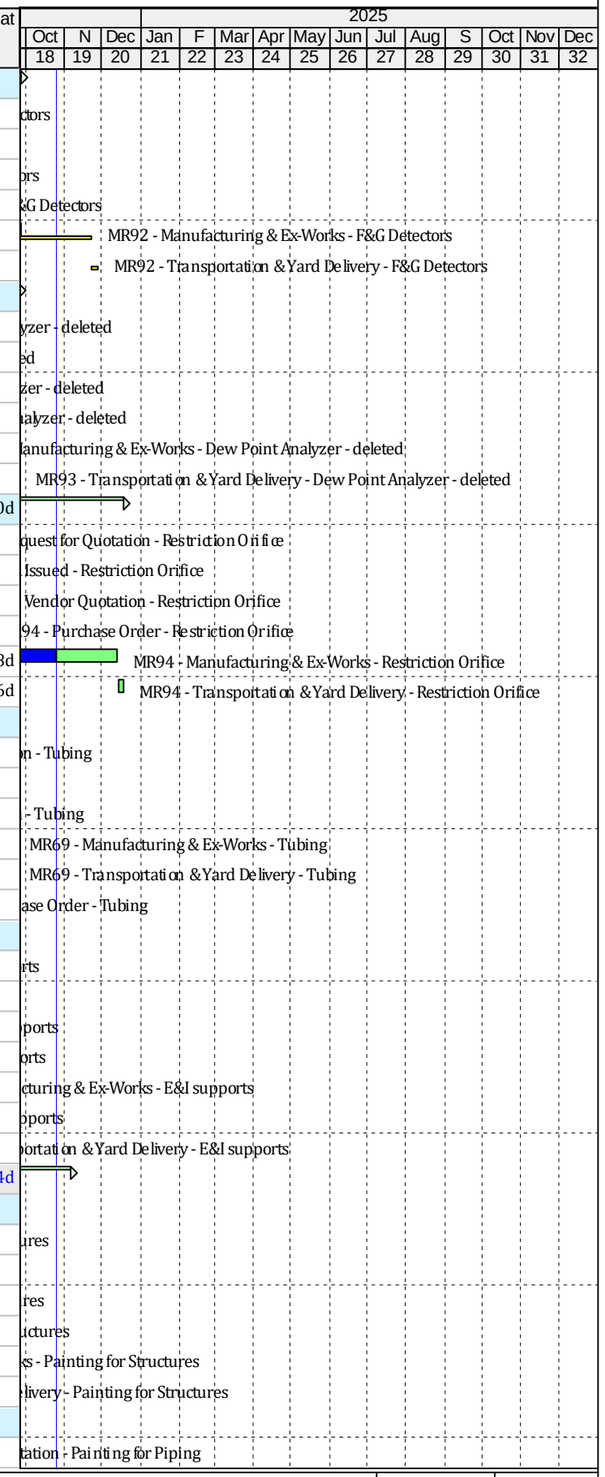


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR72-1070	MR72 - MR Issued - Painting for Piping	0d	0d	03-May-24 A		15-Mar-24		
PRO-BLK-MR72-1060	MR72 - Vendor Quotation - Painting for Piping	9d	33d	06-May-24 A	19-Jun-24 A	18-Mar-24	28-Mar-24	
PRO-BLK-MR72-1030	MR72 - Purchase Order - Painting for Piping	10d	1d	19-Jun-24 A	19-Jun-24 A	29-Mar-24	12-Apr-24	
PRO-BLK-MR72-1040	MR72 - Manufacturing & Ex-Works - Painting for Piping	30d	1d	20-Jun-24 A	20-Jun-24 A	13-Apr-24	12-May-24	
PRO-BLK-MR72-1050	MR72 - Transportation & Yard Delivery - Painting for Piping	5d	1d	20-Jun-24 A	20-Jun-24 A	13-May-24	17-May-24	
Insulation		136d	106d	03-Jul-24 A	05-Nov-24	15-Mar-24	24-Aug-24	84d
PRO-BLK-MR73-1000	MR73 - Request for Quotation - Insulation	1d	1d	03-Jul-24 A	03-Jul-24 A	15-Mar-24	15-Mar-24	
PRO-BLK-MR73-1060	MR73 - MR Issued - Insulation	0d	0d	03-Jul-24 A		15-Mar-24		
PRO-BLK-MR73-1070	MR73 - Vendor Quotation - Insulation	9d	7d	04-Jul-24 A	12-Jul-24 A	18-Mar-24	28-Mar-24	
PRO-BLK-MR73-1010	MR73 - Vendor Evaluation - Insulation	15d	9d	13-Jul-24 A	25-Jul-24 A	29-Mar-24	19-Apr-24	
PRO-BLK-MR73-1030	MR73 - Purchase Order - Insulation	10d	1d	25-Jul-24 A	25-Jul-24 A	22-Apr-24	07-May-24	
PRO-BLK-MR73-1040	MR73 - Manufacturing & Ex-Works - Insulation	90d	83d	26-Jul-24 A	30-Oct-24	08-May-24	19-Aug-24	91d
PRO-BLK-MR73-1050	MR73 - Transportation & Yard Delivery - Insulation	5d	5d	31-Oct-24	05-Nov-24	20-Aug-24	24-Aug-24	98d
All Other Material		366d	387d	13-Nov-23 A	22-Feb-25	30-Oct-23	28-Nov-24	4d
Safety Signs		97d	99d	25-Oct-24 A	22-Feb-25	14-Jun-24	24-Oct-24	4d
PRO-BLK-MR74-1060	MR74 - MR Issued - Safety Signs	0d	0d	25-Oct-24 A		14-Jun-24		
PRO-BLK-MR74-1000	MR74 - Request for Quotation - Safety Signs	1d	1d	28-Oct-24	28-Oct-24	14-Jun-24	14-Jun-24	4d
PRO-BLK-MR74-1070	MR74 - Vendor Quotation - Safety Signs	9d	9d	29-Oct-24	11-Nov-24	17-Jun-24	27-Jun-24	4d
PRO-BLK-MR74-1010	MR74 - Technical Bid Evaluation - Safety Signs - IFA	15d	15d	12-Nov-24	02-Dec-24	28-Jun-24	18-Jul-24	4d
PRO-BLK-MR74-1030	MR74 - Purchase Order - Safety Signs	10d	10d	03-Dec-24	16-Dec-24	19-Jul-24	01-Aug-24	4d
PRO-BLK-MR74-1040	MR74 - Manufacturing & Ex-Works - Safety Signs	55d	55d	17-Dec-24	22-Feb-25	02-Aug-24	19-Oct-24	5d
PRO-BLK-MR74-1050	MR74 - Transportation & Yard Delivery - Safety Signs	5d	5d	18-Feb-25	22-Feb-25	20-Oct-24	24-Oct-24	5d
Safety Equipment		104d	127d	03-Jul-24 A	29-Nov-24	14-Jun-24	24-Oct-24	73d
PRO-BLK-MR75-1060	MR75 - MR Issued - Safety Equipment	0d	0d	03-Jul-24 A		14-Jun-24		
PRO-BLK-MR75-1000	MR75 - Request for Quotation - Safety Equipment	1d	1d	11-Jul-24 A	11-Jul-24 A	14-Jun-24	14-Jun-24	
PRO-BLK-MR75-1070	MR75 - Vendor Quotation - Safety Equipment	9d	5d	12-Jul-24 A	18-Jul-24 A	17-Jun-24	27-Jun-24	
PRO-BLK-MR75-1010	MR75 - Technical Bid Evaluation - Safety Equipment - IFA	15d	15d	19-Jul-24 A	08-Aug-24 A	28-Jun-24	18-Jul-24	
PRO-BLK-MR75-1030	MR75 - Purchase Order - Safety Equipment	10d	1d	08-Aug-24 A	08-Aug-24 A	19-Jul-24	01-Aug-24	
PRO-BLK-MR75-1040	MR75 - Manufacturing & Ex-Works - Safety Equipment	65d	98d	09-Aug-24 A	24-Nov-24	02-Aug-24	19-Oct-24	77d
PRO-BLK-MR75-1050	MR75 - Transportation & Yard Delivery - Safety Equipment	5d	5d	25-Nov-24	29-Nov-24	20-Oct-24	24-Oct-24	85d
Firefighting Equipment		114d	127d	03-Jul-24 A	29-Nov-24	14-Jun-24	24-Oct-24	73d
PRO-BLK-MR76-1060	MR76 - MR Issued - Firefighting Equipment	0d	0d	03-Jul-24 A		14-Jun-24		
PRO-BLK-MR76-1000	MR76 - Request for Quotation - Firefighting Equipment	1d	1d	11-Jul-24 A	11-Jul-24 A	14-Jun-24	14-Jun-24	
PRO-BLK-MR76-1070	MR76 - Vendor Quotation - Firefighting Equipment	9d	5d	12-Jul-24 A	18-Jul-24 A	17-Jun-24	27-Jun-24	
PRO-BLK-MR76-1010	MR76 - Vendor Evaluation - Firefighting Equipment	15d	15d	19-Jul-24 A	08-Aug-24 A	28-Jun-24	18-Jul-24	
PRO-BLK-MR76-1030	MR76 - Purchase Order - Firefighting Equipment	10d	1d	08-Aug-24 A	08-Aug-24 A	19-Jul-24	01-Aug-24	
PRO-BLK-MR76-1040	MR76 - Manufacturing & Ex-Works - Firefighting Equipment	65d	98d	09-Aug-24 A	24-Nov-24	02-Aug-24	19-Oct-24	77d
PRO-BLK-MR76-1050	MR76 - Transportation & Yard Delivery - Firefighting Equipment	5d	5d	25-Nov-24	29-Nov-24	20-Oct-24	24-Oct-24	85d
Nitrogen Generation Package and Nitrogen bottles - Option		274d	293d	15-Nov-23 A	02-Nov-24	30-Oct-23	28-Nov-24	67d
PRO-BLK-MR77-1000	MR77 - Request for Quotation - Nitrogen Generation Package and Nitrogen bottles - Option	1d	1d	15-Nov-23 A	15-Nov-23 A	30-Oct-23	30-Oct-23	
PRO-BLK-MR77-1060	MR77 - MR Issued - Nitrogen Generation Package and Nitrogen bottles - Option	0d	0d	15-Nov-23 A		30-Oct-23		
PRO-BLK-MR77-1070	MR77 - Vendor Quotation - Nitrogen Generation Package and Nitrogen bottles - Option	9d	8d	16-Nov-23 A	27-Nov-23 A	31-Oct-23	13-Nov-23	
PRO-BLK-MR77-1030	MR77 - Purchase Order - Nitrogen Generation Package and Nitrogen bottles - Option	10d	13d	08-Feb-24 A	26-Feb-24 A	01-Dec-23	15-Dec-23	
PRO-BLK-MR77-1040	MR77 - Manufacturing & Ex-Works - Nitrogen Generation Package and Nitrogen bottles - Option	139d	231d	26-Feb-24 A	27-Oct-24	23-Dec-23	23-Nov-24	71d
PRO-BLK-MR77-1050	MR77 - Transportation & Yard Delivery - Nitrogen Generation Package and Nitrogen bottles - Option	5d	5d	28-Oct-24	02-Nov-24	24-Nov-24	28-Nov-24	78d
Mechanical Handling – Monorail - Option		43d	51d	13-Nov-23 A	16-Jan-24 A	13-Nov-23	16-Jan-24	

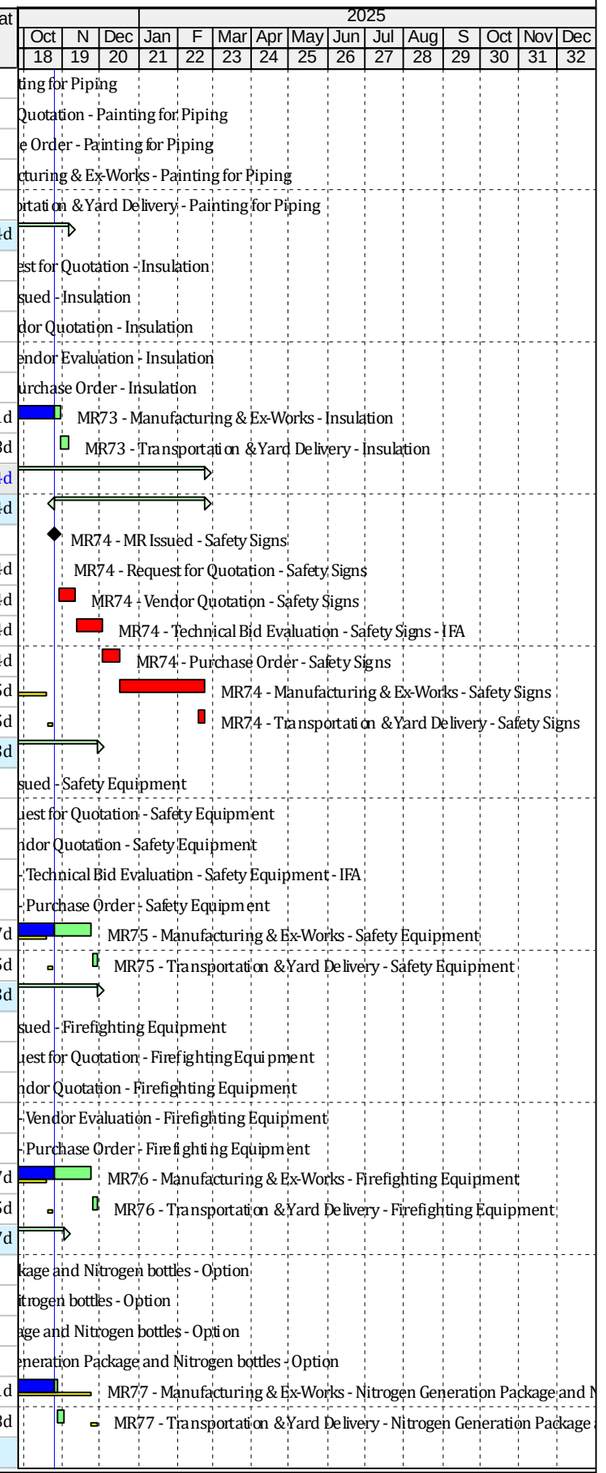

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
PRO-BLK-MR78-1000	MR78 - Request for Quotation - Mechanical Handling – Monorail - Option - DELETED	1d	1d	13-Nov-23 A	13-Nov-23 A	13-Nov-23	13-Nov-23	
PRO-BLK-MR78-1060	MR78 - MR Issued - Mechanical Handling – Monorail - Option - DELETED	0d	0d	13-Nov-23 A		13-Nov-23		
PRO-BLK-MR78-1070	MR78 - Vendor Quotation - Mechanical Handling – Monorail - Option - DELETED	9d	11d	14-Nov-23 A	28-Nov-23 A	14-Nov-23	24-Nov-23	
PRO-BLK-MR78-1080	MR78 - Vendor Evaluation - Mechanical Handling – Monorail - Option - DELETED	10d	10d	27-Nov-23 A	11-Dec-23 A	27-Nov-23	11-Dec-23	
PRO-BLK-MR78-1030	MR78 - Purchase Order - Mechanical Handling – Monorail - Option - DELETED	10d	10d	12-Dec-23 A	27-Dec-23 A	12-Dec-23	27-Dec-23	
PRO-BLK-MR78-1040	MR78 - Manufacturing & Ex-Works - Mechanical Handling – Monorail - Option - DELETED	5d	5d	07-Jan-24 A	11-Jan-24 A	07-Jan-24	11-Jan-24	
PRO-BLK-MR78-1050	MR78 - Transportation &Yard Delivery - Mechanical Handling – Monorail - Option - DELETED	5d	5d	12-Jan-24 A	16-Jan-24 A	12-Jan-24	16-Jan-24	
Fabrication		435d	559d	10-Jul-23 A	16-May-25	27-Dec-23	16-May-25	141d
Onshore Fabrication		408d	511d	10-Jul-23 A	15-Mar-25	27-Dec-23	03-Apr-25	189d
Structural		386d	396d	22-Nov-23 A	14-Mar-25	27-Dec-23	19-Mar-25	190d
CON-STR1010	Steel Structure - Pre-Fabrication - Lower Deck - (Primary & Secondary Steel) - Block 1	68d	148d	02-Dec-23 A	03-Jun-24 A	27-Dec-23	26-Feb-24	
CON-STR1020	Steel Structure - Pre-Fabrication - Lower Deck - (Primary & Secondary Steel) - Block 2	71d	148d	04-Dec-23 A	03-Jun-24 A	04-Jan-24	26-Feb-24	
CON-STR1050	Steel Structure - Pre-Fabrication - Upper Deck - (Primary & Secondary Steel) - Block 1	45d	101d	18-Dec-23 A	19-Apr-24 A	12-Jan-24	26-Feb-24	
CON-STR1080	Steel Structure - Pre-Fabrication - Upper Deck - (Primary & Secondary Steel) - Block 2	51d	95d	18-Dec-23 A	12-Apr-24 A	19-Jan-24	04-Mar-24	
CON-STR1030	Steel Structure - Pre-Fabrication - Upper Grillage	24d	24d	14-Feb-24 A	12-Mar-24 A	14-Feb-24	12-Mar-24	
CON-STR1040	Steel Structure - Pre-Fabrication - Remaining Structure (Stair & Ladders, Hatches, Handrails)	148d	309d	14-Feb-24 A	19-Feb-25	14-Feb-24	17-Jan-25	21d
CON-STR1120	Steel Structure - Pre-Fabrication - Vessel Rack - (Primary & Secondary Steel)	23d	124d	03-Jun-24 A	26-Oct-24	16-Feb-24	18-Mar-24	305d
CON-STR1130	Steel Structure - Pre-Fabrication - Lower Grillage & Sea Fastening	30d	30d	16-Jan-25	19-Feb-25	05-Nov-24	09-Dec-24	21d
Pre-Fabrication		346d	376d	22-Nov-23 A	19-Feb-25	27-Dec-23	22-Jan-25	41d
CON-STR1000	Steel Structure - Pre-Fabrication - Start	0d	0d	22-Nov-23 A		27-Dec-23		
CON-STR1550	Steel Structure - Pre-Fabrication - Transition Piece - Pre-Fabrication - Start	0d	0d	26-Apr-24 A		05-Sep-24		
CON-STR1900	Steel Structure - Pre-Fabrication - Caisson - Pre-Fabrication - Start	0d	0d	25-Jun-24 A		17-Dec-24		
Lower Deck		77d	148d	04-Dec-23 A	03-Jun-24 A	27-Dec-23	26-Feb-24	
Block 1		77d	148d	04-Dec-23 A	03-Jun-24 A	27-Dec-23	26-Feb-24	
CON-STR1320	Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Plate Girders	41d	42d	04-Dec-23 A	26-Jan-24 A	27-Dec-23	25-Jan-24	
CON-STR1330	Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Primary Beams	18d	42d	04-Dec-23 A	26-Jan-24 A	12-Jan-24	01-Feb-24	
CON-STR1340	Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Nodes	24d	54d	04-Dec-23 A	09-Feb-24 A	27-Dec-23	25-Jan-24	
CON-STR1350	Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Secondary Beams	12d	78d	04-Dec-23 A	08-Mar-24 A	25-Jan-24	07-Feb-24	
CON-STR1335	Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Bracings	10d	113d	19-Jan-24 A	03-Jun-24 A	06-Feb-24	26-Feb-24	
CON-STR1790	Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Legs	16d	61d	19-Jan-24 A	29-Mar-24 A	30-Jan-24	19-Feb-24	
CON-STR1360	Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Flooring Plates	15d	7d	23-Feb-24 A	01-Mar-24 A	09-Feb-24	26-Feb-24	
Block 2		77d	148d	04-Dec-23 A	03-Jun-24 A	04-Jan-24	26-Feb-24	
CON-STR1370	Steel Structure - Pre-Fabrication - Lower Deck - Block 2 - Plate Girders	42d	42d	04-Dec-23 A	26-Jan-24 A	04-Jan-24	01-Feb-24	
CON-STR1400	Steel Structure - Pre-Fabrication - Lower Deck - Block 2 - Nodes	24d	54d	04-Dec-23 A	09-Feb-24 A	04-Jan-24	01-Feb-24	
CON-STR1410	Steel Structure - Pre-Fabrication - Lower Deck - Block 2 - Secondary Beams	12d	78d	04-Dec-23 A	08-Mar-24 A	26-Jan-24	08-Feb-24	
CON-STR1380	Steel Structure - Pre-Fabrication - Lower Deck - Block 2 - Primary Beams	18d	18d	19-Jan-24 A	08-Feb-24 A	19-Jan-24	08-Feb-24	
CON-STR1390	Steel Structure - Pre-Fabrication - Lower Deck - Block 2 - Bracings	10d	113d	19-Jan-24 A	03-Jun-24 A	06-Feb-24	26-Feb-24	
CON-STR1800	Steel Structure - Pre-Fabrication - Lower Deck - Block 2 - Legs	18d	31d	19-Jan-24 A	23-Feb-24 A	30-Jan-24	19-Feb-24	
CON-STR1420	Steel Structure - Pre-Fabrication - Lower Deck - Block 2 - Flooring Plates	15d	7d	23-Feb-24 A	01-Mar-24 A	09-Feb-24	26-Feb-24	
Upper Deck		82d	101d	18-Dec-23 A	19-Apr-24 A	12-Jan-24	04-Mar-24	
Block 1		69d	101d	18-Dec-23 A	19-Apr-24 A	12-Jan-24	26-Feb-24	
CON-STR1430	Steel Structure - Pre-Fabrication - Upper Deck - Block 1 - Plate Girders	24d	61d	18-Dec-23 A	01-Mar-24 A	12-Jan-24	08-Feb-24	
CON-STR1460	Steel Structure - Pre-Fabrication - Upper Deck - Block 1 - Nodes	24d	57d	22-Dec-23 A	01-Mar-24 A	12-Jan-24	08-Feb-24	
CON-STR1450	Steel Structure - Pre-Fabrication - Upper Deck - Block 1 - Bracings	18d	33d	19-Jan-24 A	26-Feb-24 A	06-Feb-24	26-Feb-24	
CON-STR1810	Steel Structure - Pre-Fabrication - Upper Deck - Block 1 - Legs	18d	33d	19-Jan-24 A	26-Feb-24 A	30-Jan-24	19-Feb-24	
CON-STR1470	Steel Structure - Pre-Fabrication - Upper Deck - Block 1 - Secondary Beams	12d	65d	02-Feb-24 A	19-Apr-24 A	02-Feb-24	15-Feb-24	

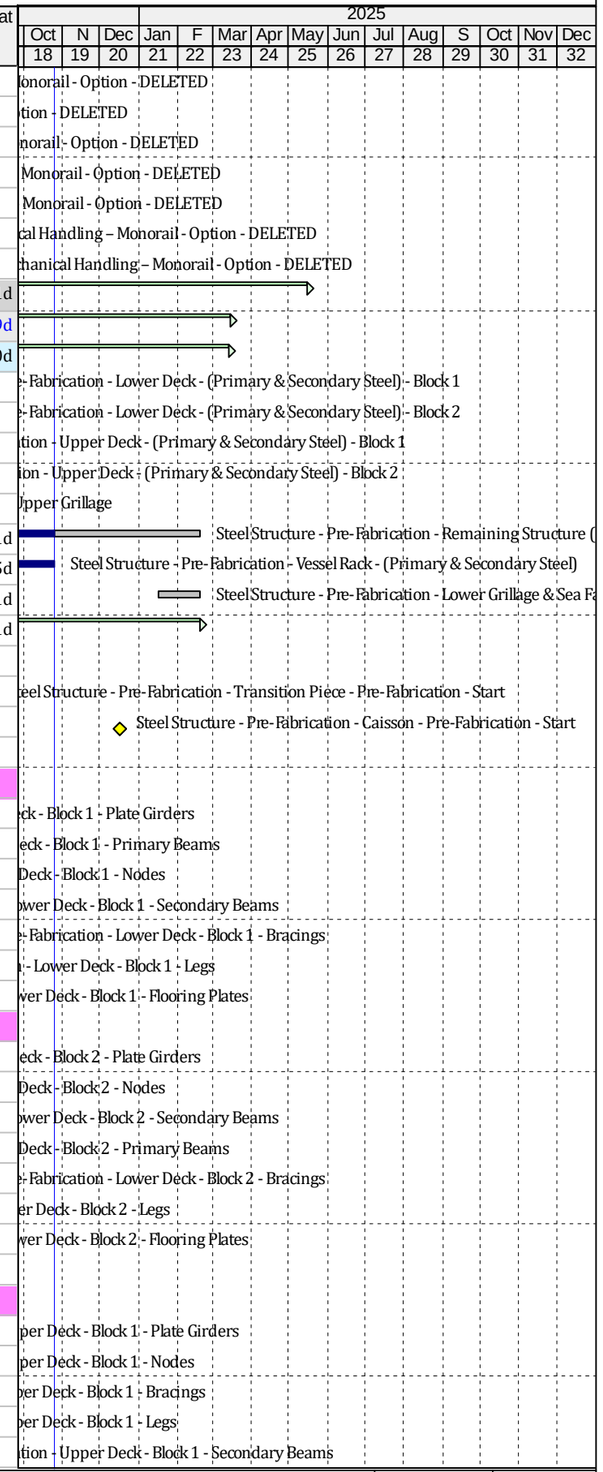

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-STR1440	Steel Structure - Pre-Fabrication - Upper Deck - Block 1 - Primary Beams	19d	13d	09-Feb-24 A	23-Feb-24 A	26-Jan-24	15-Feb-24	
CON-STR1480	Steel Structure - Pre-Fabrication - Upper Deck - Block 1 - Flooring Plates	15d	7d	22-Mar-24 A	29-Mar-24 A	09-Feb-24	26-Feb-24	
Block 2		82d	95d	18-Dec-23 A	12-Apr-24 A	19-Jan-24	04-Mar-24	
CON-STR1490	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Plate Girders	24d	61d	18-Dec-23 A	01-Mar-24 A	19-Jan-24	15-Feb-24	
CON-STR1520	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Nodes	12d	43d	12-Jan-24 A	01-Mar-24 A	19-Jan-24	15-Feb-24	
CON-STR1510	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Bracings	10d	33d	19-Jan-24 A	26-Feb-24 A	06-Feb-24	26-Feb-24	
CON-STR1820	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Legs	10d	31d	19-Jan-24 A	23-Feb-24 A	30-Jan-24	19-Feb-24	
CON-STR1530	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Secondary Beams	12d	59d	02-Feb-24 A	12-Apr-24 A	09-Feb-24	22-Feb-24	
CON-STR1500	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Primary Beams	18d	19d	09-Feb-24 A	01-Mar-24 A	02-Feb-24	22-Feb-24	
CON-STR1880	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Crane Pedestal - DELETED	12d	8d	24-Feb-24 A	04-Mar-24 A	20-Feb-24	04-Mar-24	
CON-STR1540	Steel Structure - Pre-Fabrication - Upper Deck - Block 2 - Flooring Plates	7d	7d	22-Mar-24 A	29-Mar-24 A	09-Feb-24	26-Feb-24	
Vessel Rack		33d	117d	16-Feb-24 A	05-Jul-24 A	16-Feb-24	18-Mar-24	
CON-STR1610	Steel Structure - Pre-Fabrication - Vessel Rack - Block 1 - Plate Girders - DELETED	18d	18d	16-Feb-24 A	07-Mar-24 A	16-Feb-24	07-Mar-24	
CON-STR1640	Steel Structure - Pre-Fabrication - Vessel Rack - Block 1 - Nodes	18d	29d	03-Jun-24 A	05-Jul-24 A	16-Feb-24	07-Mar-24	
CON-STR1650	Steel Structure - Pre-Fabrication - Vessel Rack - Block 1 - Secondary Beams	15d	11d	03-Jun-24 A	14-Jun-24 A	23-Feb-24	11-Mar-24	
CON-STR1630	Steel Structure - Pre-Fabrication - Vessel Rack - Block 1 - Bracings	15d	11d	03-Jun-24 A	14-Jun-24 A	27-Feb-24	14-Mar-24	
CON-STR1620	Steel Structure - Pre-Fabrication - Vessel Rack - Block 1 - Primary Beams	15d	7d	28-Jun-24 A	05-Jul-24 A	01-Mar-24	18-Mar-24	
Miscellaneous Tertiary Structure (Stairs, Hatches etc..)		244d	309d	14-Feb-24 A	19-Feb-25	14-Feb-24	17-Jan-25	41d
CON-STR1680	Steel Structure - Pre-Fabrication - Upper Grillage - DELETED	24d	24d	14-Feb-24 A	12-Mar-24 A	14-Feb-24	12-Mar-24	
CON-STR1720	Steel Structure - Pre-Fabrication - Platform Handrails	24d	35d	23-Feb-24 A	05-Apr-24 A	19-Apr-24	18-May-24	
CON-STR1830	Steel Structure - Pre-Fabrication - Installation Aids	30d	87d	29-Mar-24 A	12-Jul-24 A	10-Dec-24	17-Jan-25	
CON-STR1870	Steel Structure - Pre-Fabrication - Platform Monorails - TO BE DELETED	18d	17d	03-Apr-24 A	23-Apr-24 A	03-Apr-24	23-Apr-24	
CON-STR1660	Steel Structure - Pre-Fabrication - Platform Access Platforms - H2 Vessel Racks Access	30d	202d	05-Apr-24 A	30-Nov-24	11-May-24	14-Jun-24	82d
CON-STR1710	Steel Structure - Pre-Fabrication - Platform Hatches	21d	34d	29-Apr-24 A	07-Jun-24 A	19-Apr-24	15-May-24	
CON-STR1740	Steel Structure - Pre-Fabrication - Equipment Supports	25d	110d	22-May-24 A	27-Sep-24 A	11-Mar-24	09-May-24	
CON-STR1670	Steel Structure - Pre-Fabrication - Platform Stairs & Ladders - Deck	35d	64d	03-Jun-24 A	16-Aug-24 A	30-Apr-24	10-Jun-24	
CON-STR1730	Steel Structure - Pre-Fabrication - Platform Gratings	30d	5d	03-Jun-24 A	07-Jun-24 A	19-Apr-24	25-May-24	
CON-STR1780	Steel Structure - Pre-Fabrication - Platform Piping & E&I Racks	16d	82d	17-Jun-24 A	20-Sep-24 A	16-Mar-24	18-Apr-24	
CON-STR1690	Steel Structure - Pre-Fabrication - Lower Grillage & Sea-Fastening	30d	30d	16-Jan-25	19-Feb-25	05-Nov-24	09-Dec-24	21d
Transition Piece		228d	251d	12-Apr-24 A	07-Feb-25	06-Jul-24	26-Oct-24	51d
CON-STR1580	Steel Structure - Pre-Fabrication - Transition Piece - Nodes	24d	130d	12-Apr-24 A	13-Sep-24 A	05-Sep-24	02-Oct-24	
CON-STR1770	Steel Structure - Pre-Fabrication - Transition Piece - Box Girders	24d	130d	12-Apr-24 A	13-Sep-24 A	05-Sep-24	02-Oct-24	
CON-STR1840	Steel Structure - Pre-Fabrication - Transition Piece - Upper Grillage	30d	50d	16-Apr-24 A	14-Jun-24 A	06-Jul-24	09-Aug-24	
CON-STR1560	Steel Structure - Pre-Fabrication - Transition Piece - Primary Beams	18d	106d	13-May-24 A	13-Sep-24 A	16-Sep-24	05-Oct-24	
CON-STR1570	Steel Structure - Pre-Fabrication - Transition Piece - Bracings	18d	17d	03-Jun-24 A	21-Jun-24 A	19-Sep-24	09-Oct-24	
CON-STR1760	Steel Structure - Pre-Fabrication - Transition Piece - Access Platform	21d	154d	03-Jun-24 A	30-Nov-24	03-Oct-24	26-Oct-24	4d
CON-STR1860	Steel Structure - Pre-Fabrication - Transition Piece - Installation Aids	30d	29d	01-Jul-24 A	02-Aug-24 A	10-Aug-24	14-Sep-24	
CON-STR1600	Steel Structure - Pre-Fabrication - Transition Piece - Flooring Plates	9d	22d	02-Sep-24 A	27-Sep-24 A	07-Oct-24	16-Oct-24	
CON-STR1750	Steel Structure - Pre-Fabrication - Transition Piece - Stairs & Ladders - (DELETED AFTER REVISED SCHEDULE	21d	20d	03-Oct-24 A	25-Oct-24 A	03-Oct-24	26-Oct-24	
CON-STR1850	Steel Structure - Pre-Fabrication - Transition Piece - Lower Grillage & Sea-Fastening	30d	30d	03-Jan-25	07-Feb-25	10-Aug-24	14-Sep-24	51d
Caisson		34d	39d	14-Oct-24 A	28-Nov-24	17-Dec-24	22-Jan-25	30d
CON-STR1890	Steel Structure - Pre-Fabrication - Caisson - Pre- Fabrication	21d	32d	14-Oct-24 A	20-Nov-24	17-Dec-24	14-Jan-25	15d
CON-STR1910	Steel Structure - Pre-Fabrication - Caisson - Pre- Fabrication - Supports	28d	39d	14-Oct-24 A	28-Nov-24	17-Dec-24	22-Jan-25	30d
Assembly		328d	357d	12-Jan-24 A	14-Mar-25	02-Feb-24	19-Feb-25	21d
CON-STR1270	Steel Structure - Assembly - Remaining Structure (Stair & Ladders, Hatches, Handrails)	187d	301d	23-Feb-24 A	19-Feb-25	18-Apr-24	16-Dec-24	21d
Deck		328d	357d	12-Jan-24 A	14-Mar-25	02-Feb-24	04-Jan-25	21d

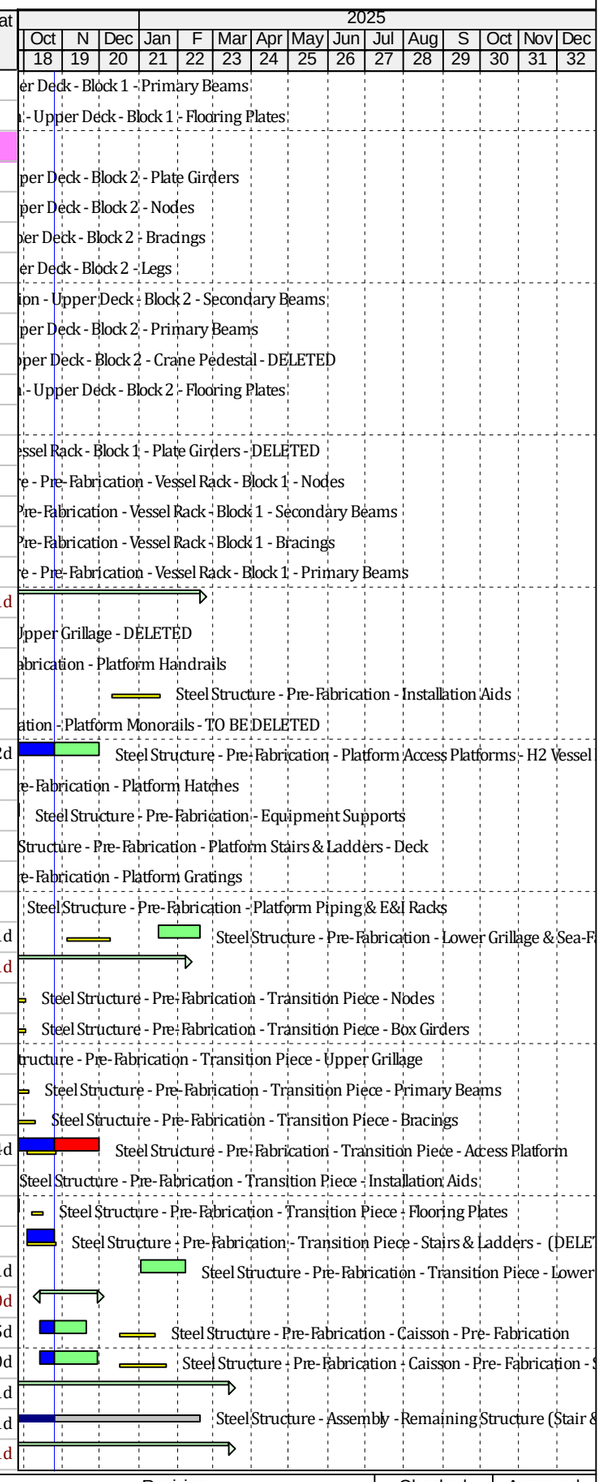


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-STR1110	Steel Structure - Assembly - Lower Deck - (Primary & Secondary Steel) - Block 2	39d	259d	12-Jan-24 A	15-Nov-24	13-Feb-24	28-Mar-24	15d
CON-STR1060	Steel Structure - Assembly - Lower Deck - (Primary & Secondary Steel) - Block 1	39d	247d	26-Jan-24 A	15-Nov-24	02-Feb-24	18-Mar-24	15d
CON-STR1150	Steel Structure - Assembly - Upper Deck - (Primary & Secondary Steel) - Block 1	42d	158d	08-Mar-24 A	13-Sep-24 A	13-Feb-24	03-Apr-24	
CON-STR1180	Steel Structure - Assembly - Upper Deck - (Primary & Secondary Steel) - Block 2	52d	224d	08-Mar-24 A	30-Nov-24	26-Feb-24	29-Apr-24	15d
CON-STR1090	Steel Structure - Assembly - Upper Grillage - Deleted	25d	24d	13-Mar-24 A	11-Apr-24 A	13-Mar-24	11-Apr-24	
CON-STR1240	Steel Structure - Assembly - Vessel Rack - (Primary & Secondary Steel)	24d	124d	08-Jul-24 A	30-Nov-24	19-Mar-24	17-Apr-24	57d
CON-STR1310	Steel Structure - Assembly - Lower Grillage & Sea Fastening	20d	20d	20-Feb-25	14-Mar-25	10-Dec-24	04-Jan-25	21d
Miscellaneous Tertiary Structure (Stairs, Hatches etc..)		99d	236d	23-Feb-24 A	30-Nov-24	19-Apr-24	04-Jul-24	52d
CON-STR1970	Steel Structure - Assembly - Platform Handrails	21d	236d	23-Feb-24 A	30-Nov-24	20-May-24	12-Jun-24	47d
CON-STR1960	Steel Structure - Assembly - Platform Monorails - DELETED	12d	12d	24-Apr-24 A	09-May-24 A	24-Apr-24	09-May-24	
CON-STR1940	Steel Structure - Assembly - Platform Gratings	30d	31d	07-Jun-24 A	12-Jul-24 A	09-May-24	12-Jun-24	
CON-STR1950	Steel Structure - Assembly - Platform Hatches	12d	19d	07-Jun-24 A	28-Jun-24 A	16-May-24	29-May-24	
CON-STR1920	Steel Structure - Assembly - Platform Piping & E&I Racks	21d	82d	17-Jun-24 A	20-Sep-24 A	19-Apr-24	15-May-24	
CON-STR1930	Steel Structure - Assembly - Platform Stairs & Ladders	28d	53d	19-Aug-24 A	18-Oct-24 A	03-Jun-24	04-Jul-24	
Transition Piece		42d	136d	24-Jun-24 A	30-Nov-24	28-Oct-24	16-Dec-24	4d
CON-STR1980	Steel Structure - Assembly - Transition Piece - (Primary & Secondary Steel)	42d	136d	24-Jun-24 A	30-Nov-24	28-Oct-24	16-Dec-24	4d
Caisson		24d	54d	14-Oct-24 A	16-Dec-24	23-Jan-25	19-Feb-25	15d
CON-STR2070	Steel Structure - Assembly - Caissons	24d	54d	14-Oct-24 A	16-Dec-24	23-Jan-25	19-Feb-25	15d
Painting		241d	262d	20-Mar-24 A	30-Jan-25	19-Mar-24	19-Mar-25	39d
CON-STR1100	Steel Structure - Painting - Lower Deck - Block 2	26d	188d	20-Mar-24 A	30-Oct-24	20-Apr-24	22-May-24	15d
CON-STR1070	Steel Structure - Painting - Lower Deck - Block 1	20d	176d	05-Apr-24 A	30-Oct-24	19-Mar-24	19-Apr-24	15d
CON-STR1140	Steel Structure - Painting - Upper Deck - Block 1	20d	157d	29-Apr-24 A	30-Oct-24	23-May-24	21-Jun-24	15d
CON-STR1220	Steel Structure - Painting - Miscellaneous Structure (Stair & Ladders, Hatches, Handrails)	70d	218d	06-May-24 A	21-Jan-25	14-Jun-24	04-Sep-24	47d
CON-STR1160	Steel Structure - Painting - Upper Deck - Block 2	20d	139d	21-May-24 A	30-Oct-24	22-Jun-24	22-Jul-24	15d
CON-STR1210	Steel Structure - Painting - Vessel Rack	20d	116d	24-Jun-24 A	07-Nov-24	23-Jul-24	14-Aug-24	57d
CON-STR2080	Painting Touch-Up	88d	155d	15-Jul-24 A	17-Jan-25			15d
CON-STR1990	Steel Structure - Painting - Transition Piece	48d	48d	02-Dec-24	30-Jan-25	17-Dec-24	14-Feb-25	4d
CON-STR2060	Steel Structure - Painting - Caissons	24d	24d	17-Dec-24	17-Jan-25	20-Feb-25	19-Mar-25	15d
Erection		150d	174d	04-May-24 A	25-Nov-24	13-May-24	20-Sep-24	47d
CON-STR1200	Steel Structure - Erection - Lower Deck - Block 1 - Lifting & Positioning	1d	24d	04-May-24 A	31-May-24 A	23-May-24	23-May-24	
CON-STR1230	Steel Structure - Erection - Lower Deck - Block 2 - Lifting & Positioning	1d	24d	04-May-24 A	31-May-24 A	04-Jun-24	04-Jun-24	
CON-STR1190	Steel Structure - Erection - Start	0d	0d	04-May-24 A		23-May-24		
CON-STR1290	Steel Structure - Erection - Miscellaneous Structure (Stair & Ladders, Hatches, Handrails)	45d	172d	07-May-24 A	25-Nov-24	30-Jul-24	20-Sep-24	47d
CON-STR1170	Steel Structure - Erection - Positioning - Upper Grillage - Deleted	9d	9d	13-May-24 A	22-May-24 A	13-May-24	22-May-24	
CON-STR2010	Steel Structure - Erection - Lower Deck - Block 1 - Welding	9d	19d	13-May-24 A	03-Jun-24 A	24-May-24	03-Jun-24	
CON-STR2020	Steel Structure - Erection - Lower Deck - Block 2 - Welding	15d	11d	27-May-24 A	07-Jun-24 A	05-Jun-24	21-Jun-24	
CON-STR2030	Steel Structure - Erection - Upper Deck - Block 1 - Welding	15d	118d	21-Jun-24 A	07-Nov-24	20-Jul-24	06-Aug-24	15d
CON-STR2040	Steel Structure - Erection - Upper Deck - Block 2 - Welding	15d	118d	21-Jun-24 A	07-Nov-24	08-Aug-24	26-Aug-24	15d
CON-STR3070	Installation of FRP supports and cable trays - Stainless Steel - DELETED	25d	29d	01-Jul-24 A	02-Aug-24 A			
CON-STR1250	Steel Structure - Erection - Upper Deck - Block 1 - Lifting & Positioning	1d	1d	08-Aug-24 A	08-Aug-24 A	19-Jul-24	19-Jul-24	
CON-STR1260	Steel Structure - Erection - Upper Deck - Block 2 - Lifting & Positioning	1d	1d	08-Aug-24 A	08-Aug-24 A	07-Aug-24	07-Aug-24	
CON-STR1590	Steel Structure - Erection - Complete Box Erection	14d	76d	09-Aug-24 A	07-Nov-24			36d
CON-STR1280	Steel Structure - Erection - Vessel Rack - Lifting & Positioning	1d	6d	14-Oct-24 A	19-Oct-24 A	27-Aug-24	27-Aug-24	
CON-STR2050	Steel Structure - Erection - Vessel Rack - Welding	15d	26d	14-Oct-24 A	13-Nov-24	28-Aug-24	13-Sep-24	52d
CON-STR1300	Steel Structure - Erection - Box Complete	0d	0d	20-Nov-24		27-Aug-24		26d
Piping		161d	208d	10-Jun-24 A	13-Feb-25	27-May-24	26-Nov-24	32d

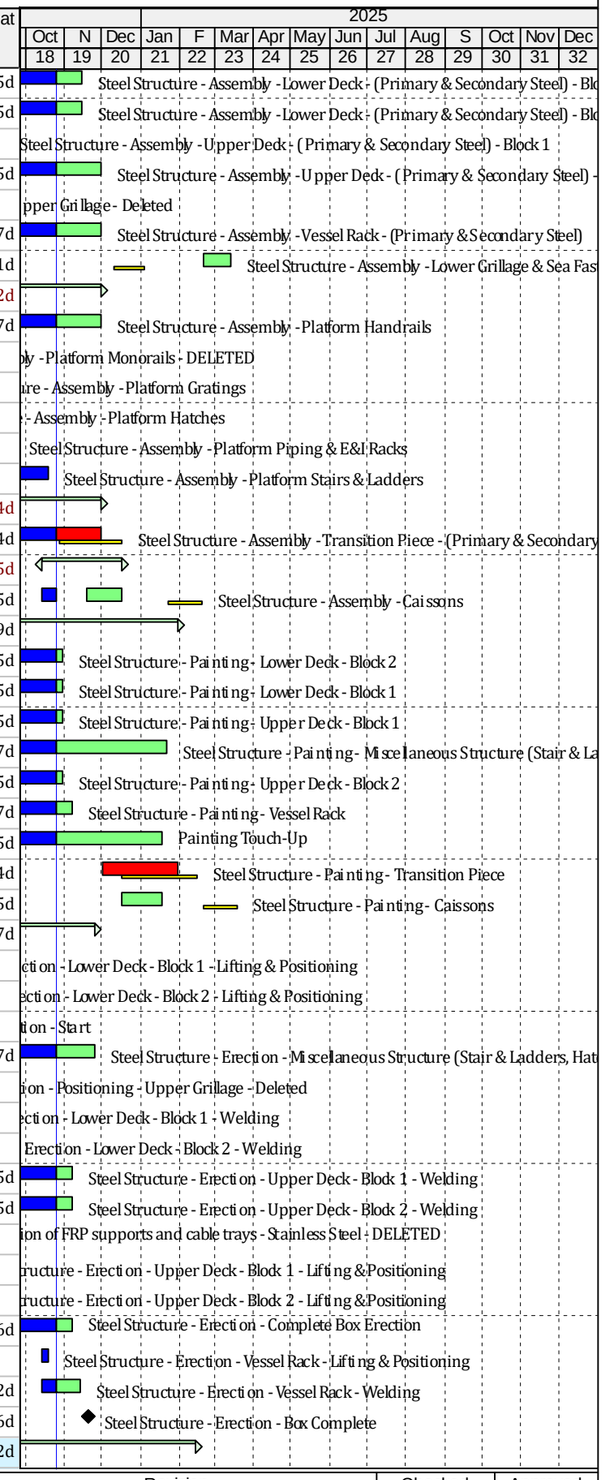

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Pre-Fabrication		82d	135d	10-Jun-24 A	15-Nov-24	27-May-24	29-Jul-24	55d
CON-PIP1100	Piping - Pre-Fabrication - Carbon Steel	30d	135d	10-Jun-24 A	15-Nov-24	27-May-24	29-Jun-24	55d
CON-PIP1110	Piping - Pre-Fabrication - Stainless Steel	30d	76d	19-Aug-24 A	15-Nov-24	08-Jun-24	12-Jul-24	55d
CON-PIP1210	Piping - Pre-Fabrication - Piping Supports	30d	58d	09-Sep-24 A	15-Nov-24	27-May-24	29-Jun-24	55d
CON-PIP1120	Piping - Pre-Fabrication - Super Duplex	30d	46d	23-Sep-24 A	15-Nov-24	25-Jun-24	29-Jul-24	55d
Painting		59d	68d	09-Sep-24 A	27-Nov-24	13-Jun-24	09-Aug-24	55d
CON-PIP1230	Piping - Painting - Piping Supports	20d	68d	09-Sep-24 A	27-Nov-24	01-Jul-24	23-Jul-24	55d
CON-PIP1020	Piping - Painting - Carbon Steel	25d	62d	16-Sep-24 A	27-Nov-24	13-Jun-24	11-Jul-24	55d
CON-PIP1030	Piping - Painting - Stainless Steel	25d	62d	16-Sep-24 A	27-Nov-24	26-Jun-24	24-Jul-24	55d
CON-PIP1050	Piping - Painting - Super Duplex	25d	38d	14-Oct-24 A	27-Nov-24	12-Jul-24	09-Aug-24	55d
Installation		123d	101d	23-Aug-24 A	19-Dec-24	24-Aug-24	26-Nov-24	76d
CON-PIP3110	Piping - Installation - Piping Supports	46d	81d	16-Sep-24 A	19-Dec-24			59d
CON-PIP1205	Start Piping Installation	0d	0d		21-Oct-24 A			
CON-PIP1220	Piping - Installation - Piping Supports Standard	46d	46d	26-Oct-24	19-Dec-24	24-Aug-24	15-Oct-24	59d
Lower Deck		75d	1d	23-Aug-24 A	23-Aug-24 A	24-Aug-24	14-Nov-24	
CON-PIP1060	Piping & Valves - Installation - Lower Deck incl. Pip Supports (DELETED AFTER REVISED SCHEDULE AUGUST 2	40d	1d	23-Aug-24 A	23-Aug-24 A	24-Aug-24	09-Oct-24	
CON-PIP1090	Piping - Hydrotesting - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	19d	1d	23-Aug-24 A	23-Aug-24 A	28-Sep-24	21-Oct-24	
CON-PIP1150	Piping - Insulation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	18d	1d	23-Aug-24 A	23-Aug-24 A	10-Oct-24	02-Nov-24	
CON-PIP1180	Piping - Reinstatement - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	25d	1d	23-Aug-24 A	23-Aug-24 A	16-Oct-24	14-Nov-24	
Upper Deck		119d	1d	23-Aug-24 A	23-Aug-24 A	05-Sep-24	26-Nov-24	
CON-PIP1070	Piping & Valves -Installation - Upper Deck incl. Pip Supports (DELETED AFTER REVISED SCHEDULE AUGUST 2	40d	1d	23-Aug-24 A	23-Aug-24 A	05-Sep-24	21-Oct-24	
CON-PIP1130	Piping - Hydrotesting - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	20d	1d	23-Aug-24 A	23-Aug-24 A	10-Oct-24	02-Nov-24	
CON-PIP1160	Piping - Insulation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	20d	1d	23-Aug-24 A	23-Aug-24 A	22-Oct-24	14-Nov-24	
CON-PIP1190	Piping - Reinstatement - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	25d	1d	23-Aug-24 A	23-Aug-24 A	28-Oct-24	26-Nov-24	
Vessel Rack		84d	1d	23-Aug-24 A	23-Aug-24 A	28-Sep-24	26-Nov-24	
CON-PIP1080	Piping & Valves -Installation - Vessel Rack incl. Pip Supports (DELETED AFTER REVISED SCHEDULE AUGUST	30d	1d	23-Aug-24 A	23-Aug-24 A	28-Sep-24	02-Nov-24	
CON-PIP1140	Piping - Hydrotesting - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	20d	1d	23-Aug-24 A	23-Aug-24 A	16-Oct-24	08-Nov-24	
CON-PIP1170	Piping - Insulation - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	20d	1d	23-Aug-24 A	23-Aug-24 A	22-Oct-24	14-Nov-24	
CON-PIP1200	Piping - Reinstatement - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	25d	1d	23-Aug-24 A	23-Aug-24 A	28-Oct-24	26-Nov-24	
M.16 Sub-System 25-01 | Hydrogen Storage Vessel A (V-25001A)		25d	25d	27-Nov-24	27-Dec-24			66d
CON-PIP1075	Sub-System 25-01 | Piping - Stainless Steel Lines Installation (009, 017, 019, 055, 064, 069)	13d	13d	27-Nov-24	11-Dec-24			66d
CON-PIP1085	Sub-System 25-01 | Piping - HTP LOE	10d	10d	12-Dec-24	23-Dec-24			66d
CON-PIP1105	Sub-System 25-01 | Piping - Hydrotest Pack TP-008	2d	2d	12-Dec-24	13-Dec-24			66d
CON-PIP1065	Sub-System 25-01 | Piping - REINSTAINTEMENT LOE	10d	10d	14-Dec-24	27-Dec-24			66d
CON-PIP1115	Sub-System 25-01 | Piping - Hydrotest Pack TP-014	2d	2d	14-Dec-24	16-Dec-24			66d
CON-PIP1155	Sub-System 25-01 | Piping - Reinstantment After TP-008	2d	2d	14-Dec-24	16-Dec-24			74d
CON-PIP1125	Sub-System 25-01 | Piping - Hydrotest Pack TP-032	2d	2d	17-Dec-24	18-Dec-24			66d
CON-PIP1165	Sub-System 25-01 | Piping - Reinstantment After TP-014	2d	2d	17-Dec-24	18-Dec-24			72d
CON-PIP1135	Sub-System 25-01 | Piping - Hydrotest Pack TP-038	2d	2d	19-Dec-24	20-Dec-24			66d
CON-PIP1175	Sub-System 25-01 | Piping - Reinstantment After TP-032	2d	2d	19-Dec-24	20-Dec-24			70d
CON-PIP1145	Sub-System 25-01 | Piping - Hydrotest Pack TP-052	2d	2d	21-Dec-24	23-Dec-24			66d
CON-PIP1185	Sub-System 25-01 | Piping - Reinstantment After TP-038	2d	2d	21-Dec-24	23-Dec-24			68d
CON-PIP1195	Sub-System 25-01 | Piping - Reinstantment After TP-052	2d	2d	24-Dec-24	27-Dec-24			66d
CON-PIP1095	Sub-System 25-01 | Piping - RFCC	0d	0d		27-Dec-24			66d
M.16 Sub-System 25-02 | Hydrogen Storage Vessel B (V-25001B)		27d	27d	27-Nov-24	30-Dec-24			64d
CON-PIP1240	Sub-System 25-02 | Piping - Lines Installation (010, 050, 070, 071, 072, 090)	15d	15d	27-Nov-24	13-Dec-24			64d

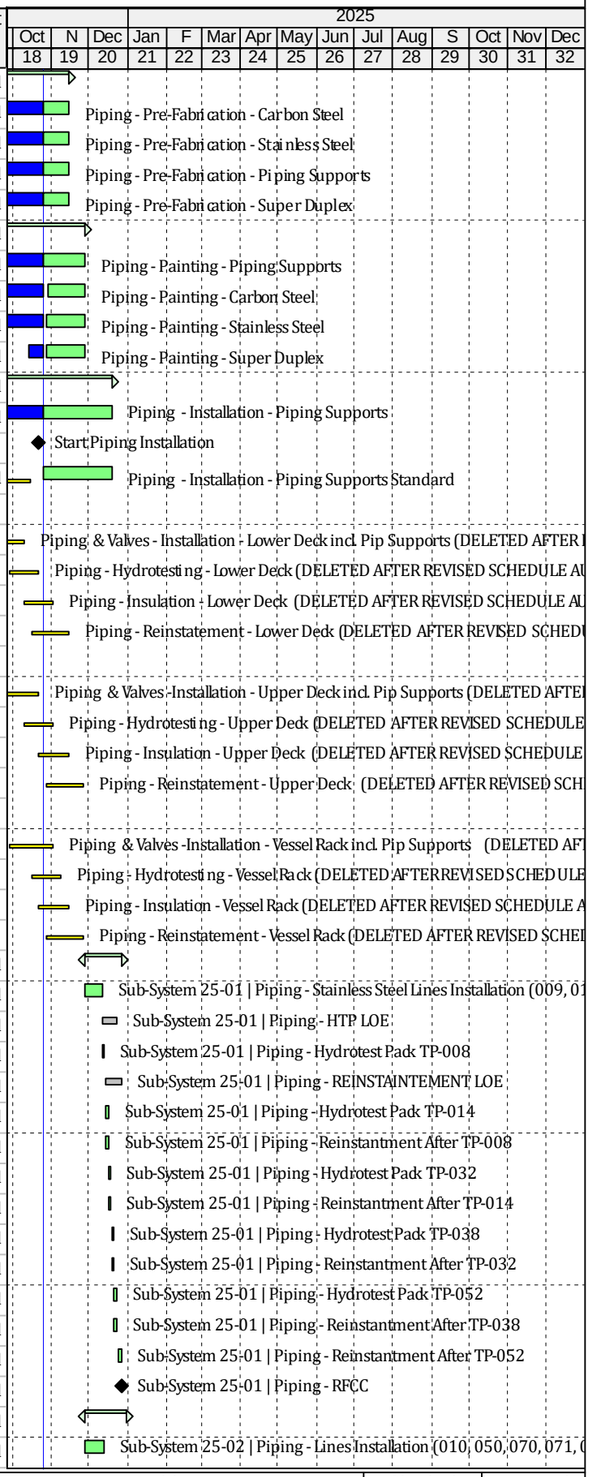

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-PIP1250	Sub-System 25-02 | Piping - Hydrotest Pack LOE	10d	10d	14-Dec-24	27-Dec-24			64d
CON-PIP1990	Sub-System 25-02 | Piping - Hydrotest Pack TP-009	2d	2d	14-Dec-24	16-Dec-24			64d
CON-PIP1260	Sub-System 25-02 | Piping - Reinstantment LOE	10d	10d	17-Dec-24	30-Dec-24			64d
CON-PIP2000	Sub-System 25-02 | Piping - Hydrotest Pack TP-015	2d	2d	17-Dec-24	18-Dec-24			64d
CON-PIP2040	Sub-System 25-02 | Piping - Reinstantment After TP-009	2d	2d	17-Dec-24	18-Dec-24			72d
CON-PIP2010	Sub-System 25-02 | Piping - Hydrotest Pack TP-033	2d	2d	19-Dec-24	20-Dec-24			64d
CON-PIP2050	Sub-System 25-02 | Piping - Reinstantment After TP-015	2d	2d	19-Dec-24	20-Dec-24			70d
CON-PIP2020	Sub-System 25-02 | Piping - Hydrotest Pack TP-039	2d	2d	21-Dec-24	23-Dec-24			64d
CON-PIP2060	Sub-System 25-02 | Piping - Reinstantment After TP-033	2d	2d	21-Dec-24	23-Dec-24			68d
CON-PIP2030	Sub-System 25-02 | Piping - Hydrotest Pack TP-053	2d	2d	24-Dec-24	27-Dec-24			64d
CON-PIP2070	Sub-System 25-02 | Piping - Reinstantment After TP-039	2d	2d	24-Dec-24	27-Dec-24			66d
CON-PIP2080	Sub-System 25-02 | Piping - Reinstantment After TP-053	2d	2d	28-Dec-24	30-Dec-24			64d
CON-PIP1270	Sub-System 25-02 | Piping - RFCC	0d	0d		30-Dec-24			64d
M.16 Sub-System 25-03 | Hydrogen Storage Vessel C (V-25001C)		27d	27d	27-Nov-24	30-Dec-24			64d
CON-PIP1280	Sub-System 25-03 | Piping - Lines Installation (011, 051, 074, 075, 076, 091)	15d	15d	27-Nov-24	13-Dec-24			64d
CON-PIP1290	Sub-System 25-03 | Piping - Hydrotest Pack LOE	10d	10d	14-Dec-24	27-Dec-24			64d
CON-PIP2090	Sub-System 25-03 | Piping - Hydrotest Pack TP-010	2d	2d	14-Dec-24	16-Dec-24			64d
CON-PIP1300	Sub-System 25-03 | Piping - Reinstantment LOE	10d	10d	17-Dec-24	30-Dec-24			64d
CON-PIP2100	Sub-System 25-03 | Piping - Hydrotest Pack TP-016	2d	2d	17-Dec-24	18-Dec-24			64d
CON-PIP2140	Sub-System 25-03 | Piping - Reinstantment After TP-010	2d	2d	17-Dec-24	18-Dec-24			72d
CON-PIP2110	Sub-System 25-03 | Piping - Hydrotest Pack TP-034	2d	2d	19-Dec-24	20-Dec-24			64d
CON-PIP2150	Sub-System 25-03 | Piping - Reinstantment After TP-016	2d	2d	19-Dec-24	20-Dec-24			70d
CON-PIP2120	Sub-System 25-03 | Piping - Hydrotest Pack TP-040	2d	2d	21-Dec-24	23-Dec-24			64d
CON-PIP2160	Sub-System 25-03 | Piping - Reinstantment After TP-034	2d	2d	21-Dec-24	23-Dec-24			68d
CON-PIP2130	Sub-System 25-03 | Piping - Hydrotest Pack TP-054	2d	2d	24-Dec-24	27-Dec-24			64d
CON-PIP2170	Sub-System 25-03 | Piping - Reinstantment After TP-040	2d	2d	24-Dec-24	27-Dec-24			66d
CON-PIP2180	Sub-System 25-03 | Piping - Reinstantment After TP-054	2d	2d	28-Dec-24	30-Dec-24			64d
CON-PIP1310	Sub-System 25-03 | Piping - RFCC	0d	0d		30-Dec-24			64d
M.16 Sub-System 25-04 | Hydrogen Storage Vessel D (V-25001D)		27d	27d	27-Nov-24	30-Dec-24			64d
CON-PIP1320	Sub-System 25-04 | Piping - Lines Installation (012, 052, 078, 079, 080, 092)	15d	15d	27-Nov-24	13-Dec-24			64d
CON-PIP1330	Sub-System 25-04 | Piping - Hydrotest Pack LOE	10d	10d	14-Dec-24	27-Dec-24			64d
CON-PIP2190	Sub-System 25-04 | Piping - Hydrotest Pack TP-011	2d	2d	14-Dec-24	16-Dec-24			64d
CON-PIP1340	Sub-System 25-04 | Piping - Reinstantment LOE	10d	10d	17-Dec-24	30-Dec-24			64d
CON-PIP2200	Sub-System 25-04 | Piping - Hydrotest Pack TP-017	2d	2d	17-Dec-24	18-Dec-24			64d
CON-PIP2240	Sub-System 25-04 | Piping - Reinstantment After TP-011	2d	2d	17-Dec-24	18-Dec-24			72d
CON-PIP2210	Sub-System 25-04 | Piping - Hydrotest Pack TP-035	2d	2d	19-Dec-24	20-Dec-24			64d
CON-PIP2250	Sub-System 25-04 | Piping - Reinstantment After TP-017	2d	2d	19-Dec-24	20-Dec-24			70d
CON-PIP2220	Sub-System 25-04 | Piping - Hydrotest Pack TP-041	2d	2d	21-Dec-24	23-Dec-24			64d
CON-PIP2260	Sub-System 25-04 | Piping - Reinstantment After TP-035	2d	2d	21-Dec-24	23-Dec-24			68d
CON-PIP2230	Sub-System 25-04 | Piping - Hydrotest Pack TP-055	2d	2d	24-Dec-24	27-Dec-24			64d
CON-PIP2270	Sub-System 25-04 | Piping - Reinstantment After TP-041	2d	2d	24-Dec-24	27-Dec-24			66d
CON-PIP2280	Sub-System 25-04 | Piping - Reinstantment After TP-055	2d	2d	28-Dec-24	30-Dec-24			64d
CON-PIP1350	Sub-System 25-04 | Piping - RFCC	0d	0d		30-Dec-24			64d
M.16 Sub-System 25-05 | Hydrogen Storage Vessel E (V-25001E)		27d	27d	27-Nov-24	30-Dec-24			64d
CON-PIP1360	Sub-System 25-05 | Piping - Lines Installation (013, 053, 082, 083, 084, 093)	15d	15d	27-Nov-24	13-Dec-24			64d
CON-PIP1370	Sub-System 25-05 | Piping - Hydrotest Pack LOE	10d	10d	14-Dec-24	27-Dec-24			64d

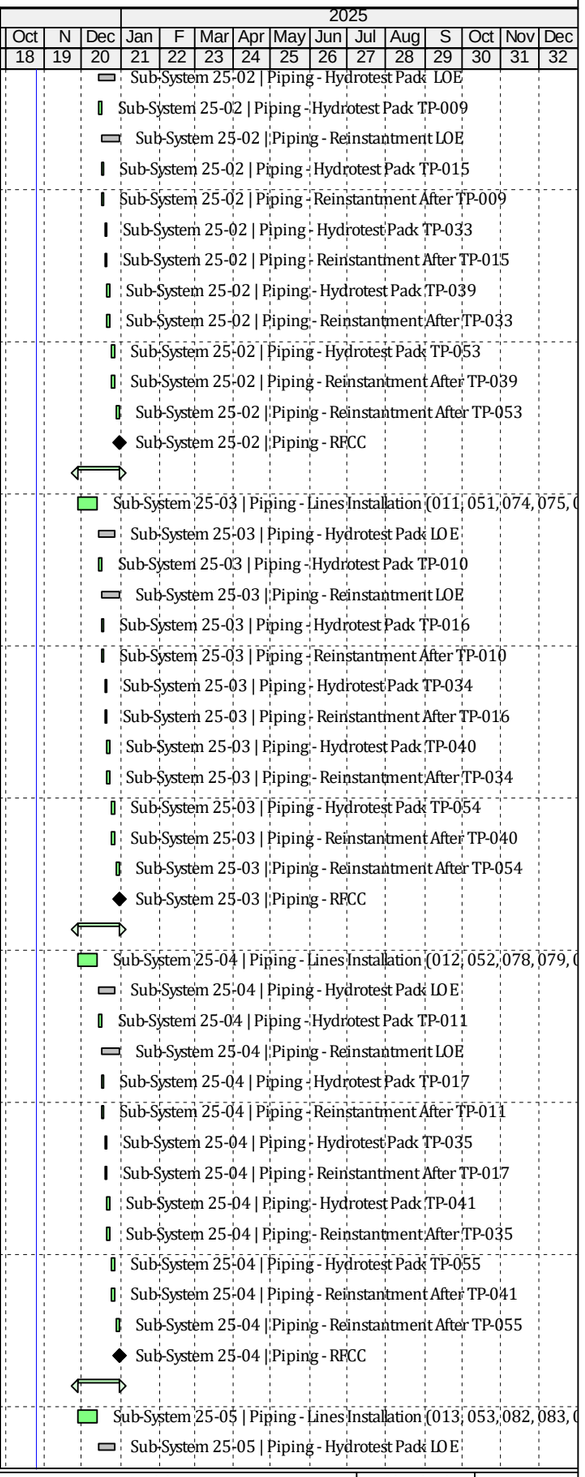

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-PIP2290	Sub-System 25-05 | Piping - Hydrotest Pack TP-012	2d	2d	14-Dec-24	16-Dec-24			64d
CON-PIP1380	Sub-System 25-05 | Piping - Reinstantment LOE	10d	10d	17-Dec-24	30-Dec-24			64d
CON-PIP2300	Sub-System 25-05 | Piping - Hydrotest Pack TP-018	2d	2d	17-Dec-24	18-Dec-24			64d
CON-PIP2340	Sub-System 25-05 | Piping - Reinstantment After TP-012	2d	2d	17-Dec-24	18-Dec-24			72d
CON-PIP2310	Sub-System 25-05 | Piping - Hydrotest Pack TP-036	2d	2d	19-Dec-24	20-Dec-24			64d
CON-PIP2350	Sub-System 25-05 | Piping - Reinstantment After TP-018	2d	2d	19-Dec-24	20-Dec-24			70d
CON-PIP2320	Sub-System 25-05 | Piping - Hydrotest Pack TP-042	2d	2d	21-Dec-24	23-Dec-24			64d
CON-PIP2360	Sub-System 25-05 | Piping - Reinstantment After TP-036	2d	2d	21-Dec-24	23-Dec-24			68d
CON-PIP2330	Sub-System 25-05 | Piping - Hydrotest Pack TP-056	2d	2d	24-Dec-24	27-Dec-24			64d
CON-PIP2370	Sub-System 25-05 | Piping - Reinstantment After TP-042	2d	2d	24-Dec-24	27-Dec-24			66d
CON-PIP2380	Sub-System 25-05 | Piping - Reinstantment After TP-056	2d	2d	28-Dec-24	30-Dec-24			64d
CON-PIP1390	Sub-System 25-05 | Piping - RFCC	0d	0d		30-Dec-24			64d
M.16 Sub-System 25-06 | Hydrogen Storage Vessel F (V-25001F)		26d	26d	27-Nov-24	28-Dec-24			65d
CON-PIP1400	Sub-System 25-06 | Piping - Lines Installation (014, 054, 086, 087, 088, 094)	14d	14d	27-Nov-24	12-Dec-24			65d
CON-PIP1410	Sub-System 25-06 | Piping - Hydrotest Pack LOE	10d	10d	13-Dec-24	24-Dec-24			65d
CON-PIP2390	Sub-System 25-06 | Piping - Hydrotest Pack TP-013	2d	2d	13-Dec-24	14-Dec-24			65d
CON-PIP1420	Sub-System 25-06 | Piping - Reinstantment LOE	10d	10d	16-Dec-24	28-Dec-24			65d
CON-PIP2400	Sub-System 25-06 | Piping - Hydrotest Pack TP-019	2d	2d	16-Dec-24	17-Dec-24			65d
CON-PIP2440	Sub-System 25-06 | Piping - Reinstantment After TP-013	2d	2d	16-Dec-24	17-Dec-24			73d
CON-PIP2410	Sub-System 25-06 | Piping - Hydrotest Pack TP-037	2d	2d	18-Dec-24	19-Dec-24			65d
CON-PIP2450	Sub-System 25-06 | Piping - Reinstantment After TP-019	2d	2d	18-Dec-24	19-Dec-24			71d
CON-PIP2420	Sub-System 25-06 | Piping - Hydrotest Pack TP-043	2d	2d	20-Dec-24	21-Dec-24			65d
CON-PIP2460	Sub-System 25-06 | Piping - Reinstantment After TP-037	2d	2d	20-Dec-24	21-Dec-24			69d
CON-PIP2430	Sub-System 25-06 | Piping - Hydrotest Pack TP-057	2d	2d	23-Dec-24	24-Dec-24			65d
CON-PIP2470	Sub-System 25-06 | Piping - Reinstantment After TP-043	2d	2d	23-Dec-24	24-Dec-24			67d
CON-PIP2480	Sub-System 25-06 | Piping - Reinstantment After TP-057	2d	2d	27-Dec-24	28-Dec-24			65d
CON-PIP1430	Sub-System 25-06 | Piping - RFCC	0d	0d		28-Dec-24			65d
M.18 Sub-System 25-07 | Hydrogen Storage Vessels Header (Intlet)		27d	27d	15-Nov-24	16-Dec-24			70d
CON-PIP1440	Sub-System 25-07 | Piping - Lines Installation (005, 009, 010, 011, 012, 013, 014, 056)	18d	18d	15-Nov-24	05-Dec-24			75d
CON-PIP1450	Sub-System 25-07 | Piping - Hydrotest Pack TP-007	2d	2d	06-Dec-24	07-Dec-24			75d
CON-PIP1460	Sub-System 25-07 | Piping - Reinstantment After TP-007	2d	2d	09-Dec-24	10-Dec-24			75d
CON-PIP1470	Sub-System 25-07 | Piping - RFCC	0d	0d		16-Dec-24			70d
M.15 Sub-System 25-08 | Hydrogen Storage Vessels Header (Outlet)		33d	33d	27-Nov-24	08-Jan-25			53d
CON-PIP1480	Sub-System 25-08 | Piping - Lines Installation (016, 019, 050, 051, 052, 053, 054, 057, 061, 063, 068)	27d	27d	27-Nov-24	30-Dec-24			53d
CON-PIP1490	Sub-System 25-08 | Piping - Hydrotest Pack LOE	4d	4d	31-Dec-24	04-Jan-25			53d
CON-PIP2490	Sub-System 25-08 | Piping - Hydrotest Pack TP-030	2d	2d	31-Dec-24	02-Jan-25			53d
CON-PIP1500	Sub-System 25-08 | Piping - Reinstantment LOE	4d	4d	03-Jan-25	08-Jan-25			53d
CON-PIP2500	Sub-System 25-08 | Piping - Hydrotest Pack TP-031	2d	2d	03-Jan-25	04-Jan-25			53d
CON-PIP2510	Sub-System 25-08 | Piping - Reinstantment After TP-030	2d	2d	03-Jan-25	04-Jan-25			55d
CON-PIP2520	Sub-System 25-08 | Piping - Reinstantment After TP-031	2d	2d	07-Jan-25	08-Jan-25			53d
CON-PIP1510	Sub-System 25-08 | Piping - RFCC	0d	0d		08-Jan-25			53d
M.17 Sub-System 43-00 | Hydrogen Vent Header & Drum System		44d	44d	14-Nov-24	08-Jan-25			53d
CON-PIP1520	Sub-System 43-00 | Piping - Lines Installation LOE	21d	21d	14-Nov-24	07-Dec-24			68d
CON-PIP3050	Sub-System 43-00 | Piping - Lines Installation 1" - (008, 125, 157, 114, 123, 124, 065)	20d	20d	14-Nov-24	06-Dec-24			64d
CON-PIP3060	Sub-System 43-00 | Piping - Lines Installation 2" - (002, 015)	8d	8d	14-Nov-24	22-Nov-24			81d
CON-PIP3070	Sub-System 43-00 | Piping - Lines Installation 3" - (116)	3d	3d	14-Nov-24	16-Nov-24			85d

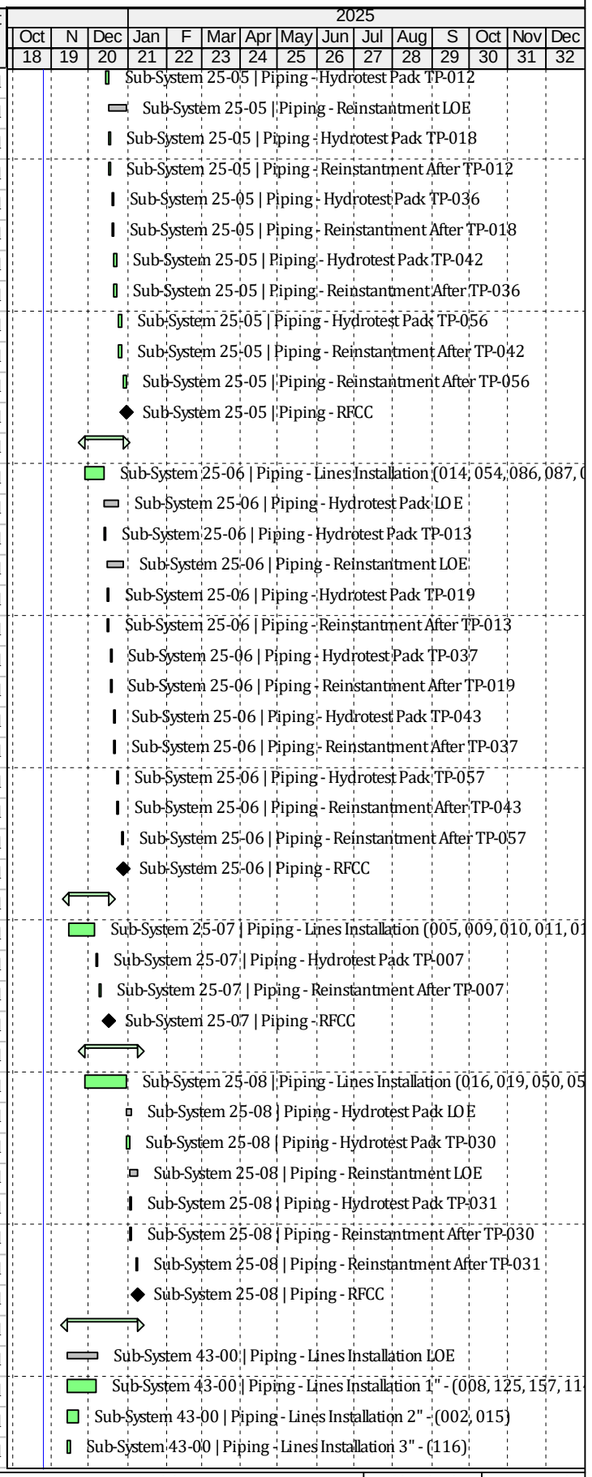

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-PIP3080	Sub-System 43-00 | Piping - Lines Installation 4" - (018, 037, 038, 039, 040, 041)	15d	15d	14-Nov-24	30-Nov-24			74d
CON-PIP3090	Sub-System 43-00 | Piping - Lines Installation 6" - (006, 058, 073, 077, 081, 085, 089)	21d	21d	14-Nov-24	07-Dec-24			68d
CON-PIP3100	Sub-System 43-00 | Piping - Lines Installation 10" - (042, 043, 044)	12d	12d	28-Nov-24	11-Dec-24			65d
CON-PIP1530	Sub-System 43-00 | Piping - Hydrotest Pack LOE	5d	5d	07-Dec-24	12-Dec-24			65d
CON-PIP2530	Sub-System 43-00 | Piping - Hydrotest Pack TP-022	1d	1d	07-Dec-24	07-Dec-24			68d
CON-PIP2560	Sub-System 43-00 | Piping - Hydrotest Pack TP-050	1d	1d	07-Dec-24	07-Dec-24			64d
CON-PIP1540	Sub-System 43-00 | Piping - Reinstantment LOE	23d	23d	09-Dec-24	08-Jan-25			53d
CON-PIP2570	Sub-System 43-00 | Piping - Hydrotest Pack TP-058 TP-064 and TP-065	3d	3d	09-Dec-24	11-Dec-24			64d
CON-PIP2580	Sub-System 43-00 | Piping - Reinstantment After TP-022	1d	1d	09-Dec-24	09-Dec-24			69d
CON-PIP2610	Sub-System 43-00 | Piping - Reinstantment After TP-050	1d	1d	09-Dec-24	09-Dec-24			69d
CON-PIP2540	Sub-System 43-00 | Piping - Hydrotest Pack TP-024	1d	1d	12-Dec-24	12-Dec-24			65d
CON-PIP2550	Sub-System 43-00 | Piping - Hydrotest Pack TP-044	1d	1d	12-Dec-24	12-Dec-24			65d
CON-PIP2620	Sub-System 43-00 | Piping - Reinstantment After TP-058 TP-064 and TP-065	1d	1d	12-Dec-24	12-Dec-24			64d
CON-PIP1920	Sub-System 43-00 | Piping - Insulation	2d	2d	13-Dec-24	14-Dec-24			64d
CON-PIP2590	Sub-System 43-00 | Piping - Reinstantment After TP-024	1d	1d	13-Dec-24	13-Dec-24			65d
CON-PIP2600	Sub-System 43-00 | Piping - Reinstantment After TP-044	1d	1d	13-Dec-24	13-Dec-24			65d
CON-PIP1550	Sub-System 43-00 | Piping - RFCC	0d	0d		19-Dec-24			60d
M.09 Sub-System 50-00 | Seawater Intake System (Lifting Pumps)		26d	26d	07-Dec-24	10-Jan-25			58d
CON-PIP1560	Sub-System 50-00 | Piping - Lines Installation (023, 025, 026, 059, 060, 117, 118, 150, 151, 152, 153, 154, 1!	12d	12d	07-Dec-24	20-Dec-24			53d
CON-PIP1570	Sub-System 50-00 | Piping - Hydrotest Pack LOE	12d	12d	21-Dec-24	08-Jan-25			58d
CON-PIP2670	Sub-System 50-00 | Piping - Hydrotest Pack TP-001	2d	2d	21-Dec-24	23-Dec-24			53d
CON-PIP1580	Sub-System 50-00 | Piping - Reinstantment LOE	12d	12d	24-Dec-24	10-Jan-25			58d
CON-PIP2710	Sub-System 50-00 | Piping - Reinstantment After TP-001	2d	2d	24-Dec-24	27-Dec-24			53d
CON-PIP2720	Sub-System 50-00 | Piping - Reinstantment After TP-028	2d	2d	28-Dec-24	30-Dec-24			53d
CON-PIP2680	Sub-System 50-00 | Piping - Hydrotest Pack TP-028	2d	2d	31-Dec-24	02-Jan-25			53d
CON-PIP2730	Sub-System 50-00 | Piping - Reinstantment After TP-045	2d	2d	31-Dec-24	02-Jan-25			53d
CON-PIP2690	Sub-System 50-00 | Piping - Hydrotest Pack TP-045	2d	2d	03-Jan-25	04-Jan-25			53d
CON-PIP2700	Sub-System 50-00 | Piping - Hydrotest Pack TP-104	2d	2d	07-Jan-25	08-Jan-25			53d
CON-PIP1930	Sub-System 50-00 | Piping - Insulation	2d	2d	09-Jan-25	10-Jan-25			58d
CON-PIP2740	Sub-System 50-00 | Piping - Reinstantment After TP-104	2d	2d	09-Jan-25	10-Jan-25			58d
CON-PIP1590	Sub-System 50-00 | Piping - RFCC	0d	0d		10-Jan-25			58d
M.10 Sub-System 50-10 | Water Desalination Package & Distribution		13d	13d	17-Dec-24	03-Jan-25			49d
CON-PIP1600	Sub-System 50-10 | Piping - Lines Installation (001)	7d	7d	17-Dec-24	24-Dec-24			40d
CON-PIP1610	Sub-System 50-10 | Piping - Hydrotest Pack TP-006	2d	2d	27-Dec-24	28-Dec-24			49d
CON-PIP1940	Sub-System 50-10 | Piping - Insulation	2d	2d	30-Dec-24	31-Dec-24			49d
CON-PIP1620	Sub-System 50-10 | Piping - Reinstantment After TP-006	2d	2d	02-Jan-25	03-Jan-25			49d
CON-PIP1630	Sub-System 50-10 | Piping - RFCC	0d	0d		03-Jan-25			49d
M.10 Sub-System 50-11 | Non-Oxidant Biocide		15d	15d	27-Dec-24	15-Jan-25			40d
CON-PIP1800	Sub-System 50-11| Piping - Lines Installation (021, 022, 024)	9d	9d	27-Dec-24	08-Jan-25			40d
CON-PIP1810	Sub-System 50-11| Piping - Hydrotest Pack TP-002	2d	2d	09-Jan-25	10-Jan-25			40d
CON-PIP1950	Sub-System 50-11| Piping - Insulation	2d	2d	11-Jan-25	13-Jan-25			40d
CON-PIP1820	Sub-System 50-11| Piping - Reinstantment After TP-002	2d	2d	14-Jan-25	15-Jan-25			40d
CON-PIP1830	Sub-System 50-11| Piping - RFCC	0d	0d		15-Jan-25			40d
M.12 Sub-System 55-00 | WasteWater Disposal		61d	95d	21-Oct-24 A	13-Feb-25			22d
CON-PIP1640	Sub-System 55-00 | Piping - Lines Installation (003, 027, 028, 033, 098, 099, 100, 121, 156)	14d	78d	21-Oct-24 A	24-Jan-25			22d
CON-PIP1650	Sub-System 55-00 | Piping - Hydrotest Pack LOE	10d	10d	25-Jan-25	05-Feb-25			22d

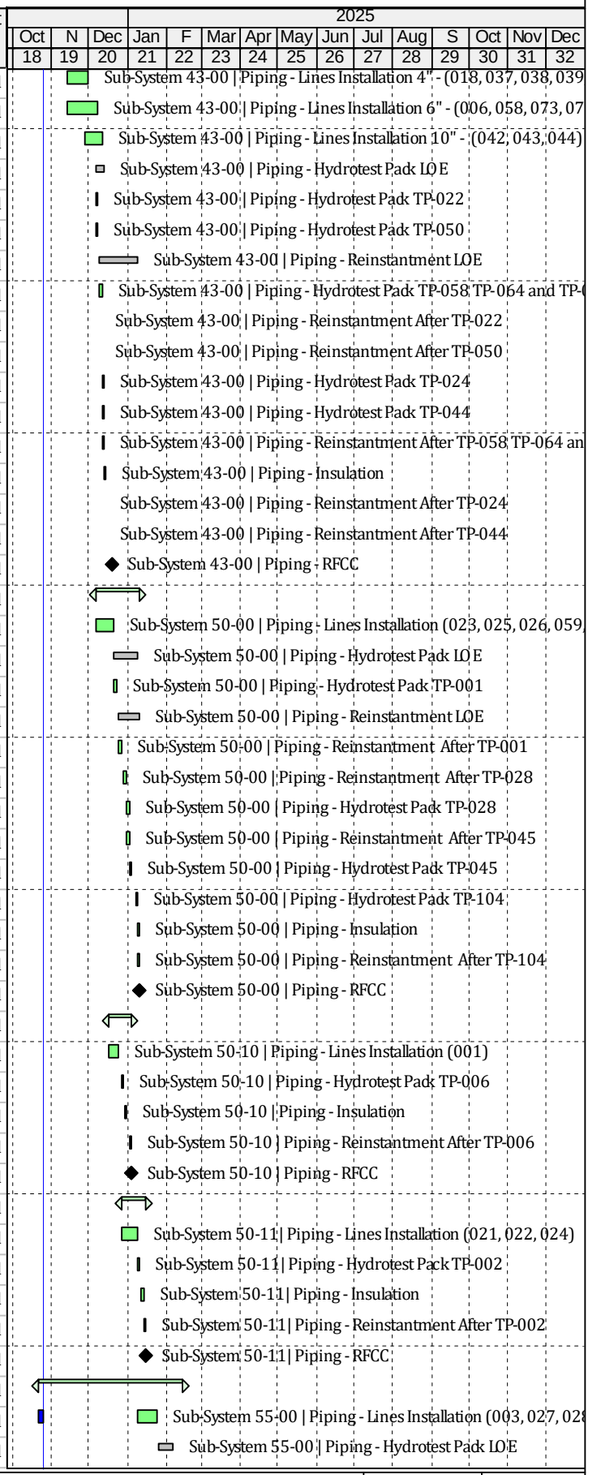


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-PIP2630	Sub-System 55-00 | Piping - Hydrotest Pack TP-004	2d	2d	25-Jan-25	27-Jan-25			22d
CON-PIP1660	Sub-System 55-00 | Piping - Reinstantment LOE	10d	10d	28-Jan-25	07-Feb-25			22d
CON-PIP2640	Sub-System 55-00 | Piping - Hydrotest Pack TP-005	2d	2d	28-Jan-25	29-Jan-25			22d
CON-PIP2760	Sub-System 55-00 | Piping - Reinstantment After TP-004	2d	2d	28-Jan-25	29-Jan-25			30d
CON-PIP2650	Sub-System 55-00 | Piping - Hydrotest Pack TP-026	2d	2d	30-Jan-25	31-Jan-25			22d
CON-PIP2770	Sub-System 55-00 | Piping - Reinstantment After TP-005	2d	2d	30-Jan-25	31-Jan-25			28d
CON-PIP2660	Sub-System 55-00 | Piping - Hydrotest Pack TP-100 and TP-060	2d	2d	01-Feb-25	03-Feb-25			22d
CON-PIP2780	Sub-System 55-00 | Piping - Reinstantment After TP-026	2d	2d	01-Feb-25	03-Feb-25			26d
CON-PIP2750	Sub-System 55-00 | Piping - Hydrotest Pack TP-101 TP-061-TP-062	2d	2d	04-Feb-25	05-Feb-25			22d
CON-PIP2790	Sub-System 55-00 | Piping - Reinstantment After TP-100	2d	2d	04-Feb-25	05-Feb-25			24d
CON-PIP2800	Sub-System 55-00 | Piping - Reinstantment After TP-101	2d	2d	06-Feb-25	07-Feb-25			22d
CON-PIP1960	Sub-System 55-00 | Piping - Insulation	5d	5d	08-Feb-25	13-Feb-25			22d
CON-PIP1670	Sub-System 55-00 | Piping - RFCC	0d	0d		13-Feb-25			22d
M.13 Sub-System 55-01 | WasteWater Brine Discharge System		46d	46d	17-Dec-24	12-Feb-25			25d
CON-PIP1680	Sub-System 55-01 | Piping - Lines Installation (004, 007, 029, 030, 031, 032, 158)	34d	34d	17-Dec-24	29-Jan-25			25d
CON-PIP1690	Sub-System 55-01 | Piping - Hydrotest Pack LOE	10d	10d	30-Jan-25	10-Feb-25			25d
CON-PIP2810	Sub-System 55-01 | Piping - Hydrotest Pack TP-003	2d	2d	30-Jan-25	31-Jan-25			25d
CON-PIP1700	Sub-System 55-01 | Piping - Reinstantment LOE	10d	10d	01-Feb-25	12-Feb-25			25d
CON-PIP2820	Sub-System 55-01 | Piping - Hydrotest Pack TP-021	2d	2d	01-Feb-25	03-Feb-25			25d
CON-PIP2850	Sub-System 55-01 | Piping - Reinstantment After TP-003	2d	2d	01-Feb-25	03-Feb-25			31d
CON-PIP2830	Sub-System 55-01 | Piping - Hydrotest Pack TP-046	2d	2d	04-Feb-25	05-Feb-25			25d
CON-PIP2860	Sub-System 55-01 | Piping - Reinstantment After TP-021	2d	2d	04-Feb-25	05-Feb-25			29d
CON-PIP2840	Sub-System 55-01 | Piping - Hydrotest Pack TP-103	2d	2d	06-Feb-25	07-Feb-25			25d
CON-PIP2870	Sub-System 55-01 | Piping - Reinstantment After TP-046	2d	2d	06-Feb-25	07-Feb-25			27d
CON-PIP2880	Sub-System 55-01 | Piping - Reinstantment After TP-103	2d	2d	08-Feb-25	10-Feb-25			25d
CON-PIP1970	Sub-System 55-01 | Piping - Insulation	2d	2d	11-Feb-25	12-Feb-25			25d
CON-PIP1710	Sub-System 55-01 | Piping - RFCC	0d	0d		12-Feb-25			25d
M.05 Sub-System 63-00 | Instrument Air Package (A-63000)		26d	26d	31-Oct-24	30-Nov-24			64d
CON-PIP1840	Sub-System 63-00 | Piping - Lines Installation (032, 036, 127)	18d	18d	31-Oct-24	21-Nov-24			64d
CON-PIP1850	Sub-System 63-00 | Piping - Hydrotest Pack LOE	4d	4d	22-Nov-24	26-Nov-24			66d
CON-PIP2890	Sub-System 63-00 | Piping - Hydrotest Pack TP-025	2d	2d	22-Nov-24	23-Nov-24			64d
CON-PIP1860	Sub-System 63-00 | Piping - Reinstantment LOE	4d	4d	25-Nov-24	28-Nov-24			64d
CON-PIP2900	Sub-System 63-00 | Piping - Hydrotest Pack TP-059	2d	2d	25-Nov-24	26-Nov-24			64d
CON-PIP2910	Sub-System 63-00 | Piping - Reinstantment After TP-025	2d	2d	25-Nov-24	26-Nov-24			66d
CON-PIP2920	Sub-System 63-00 | Piping - Reinstantment After TP-059	2d	2d	27-Nov-24	28-Nov-24			64d
CON-PIP1980	Sub-System 63-00 | Piping - Insulation	2d	2d	29-Nov-24	30-Nov-24			64d
CON-PIP1870	Sub-System 63-00 | Piping - RFCC	0d	0d		30-Nov-24			64d
M.07 Sub-System 63-30 | Instrument Air Network		38d	42d	14-Oct-24 A	02-Dec-24			68d
CON-PIP1720	Sub-System 63-30 | Piping - Lines Installation (16 Lines)	38d	38d	14-Oct-24 A	27-Nov-24			68d
CON-PIP1730	Sub-System 63-30 | Piping - Hydrotest Pack TP-027	2d	2d	28-Nov-24	29-Nov-24			68d
CON-PIP1740	Sub-System 63-30 | Piping - Reinstantment After TP-027	2d	2d	30-Nov-24	02-Dec-24			68d
CON-PIP1750	Sub-System 63-30 | Piping - RFCC	0d	0d		02-Dec-24			68d
M.06 Sub-System 64-00 | Nitrogen Generator Package (U-6400)		14d	14d	15-Nov-24	30-Nov-24			71d
CON-PIP1880	Sub-System 64-00 | Piping - Lines Installation (066, 102, 120, 126)	8d	8d	15-Nov-24	23-Nov-24			71d
CON-PIP1890	Sub-System 64-00 | Piping - Hydrotest Pack LOE	4d	4d	25-Nov-24	28-Nov-24			71d
CON-PIP2930	Sub-System 64-00 | Piping - Hydrotest Pack TP-029 and TP-063	2d	2d	25-Nov-24	26-Nov-24			71d

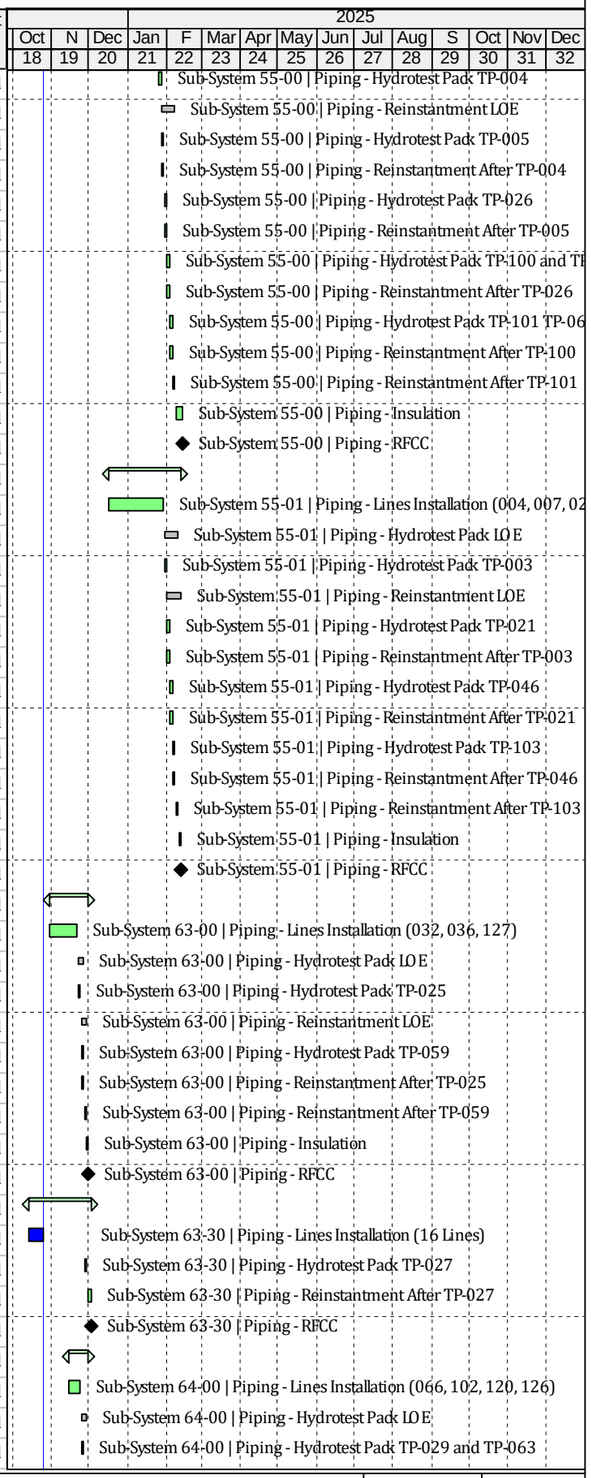


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-PIP1900	Sub-System 64-00 | Piping - Reinstantment LOE	4d	4d	27-Nov-24	30-Nov-24			71d
CON-PIP2940	Sub-System 64-00 | Piping - Hydrotest Pack TP-049	2d	2d	27-Nov-24	28-Nov-24			71d
CON-PIP2950	Sub-System 64-00 | Piping - Reinstantment After TP-029	2d	2d	27-Nov-24	28-Nov-24			73d
CON-PIP2960	Sub-System 64-00 | Piping - Reinstantment After TP-049	2d	2d	29-Nov-24	30-Nov-24			71d
CON-PIP1910	Sub-System 64-00 | Piping - RFCC	0d	0d		30-Nov-24			71d
M.08 Sub-System 64-10 | Nitrogen Distribution Network		38d	38d	29-Oct-24	12-Dec-24			66d
CON-PIP1760	Sub-System 64-10 | Piping - Lines Installation (020, 034, 035, 045, 046, 047, 048, 049, 062, 064 to 067, 090 t	16d	16d	29-Oct-24	16-Nov-24			66d
CON-PIP1770	Sub-System 64-10 | Piping - Hydrotest Pack LOE	20d	20d	18-Nov-24	10-Dec-24			66d
CON-PIP2970	Sub-System 64-10 | Piping - Hydrotest Pack TP-020	5d	5d	18-Nov-24	22-Nov-24			66d
CON-PIP1780	Sub-System 64-10 | Piping - Reinstantment LOE	17d	17d	23-Nov-24	12-Dec-24			66d
CON-PIP2980	Sub-System 64-10 | Piping - Hydrotest Pack TP-023	5d	5d	23-Nov-24	28-Nov-24			66d
CON-PIP3010	Sub-System 64-10 | Piping - Reinstantment After TP-020	2d	2d	23-Nov-24	25-Nov-24			81d
CON-PIP2990	Sub-System 64-10 | Piping - Hydrotest Pack TP-047	5d	5d	29-Nov-24	04-Dec-24			66d
CON-PIP3020	Sub-System 64-10 | Piping - Reinstantment After TP-023	2d	2d	29-Nov-24	30-Nov-24			76d
CON-PIP3000	Sub-System 64-10 | Piping - Hydrotest Pack TP-051	5d	5d	05-Dec-24	10-Dec-24			66d
CON-PIP3030	Sub-System 64-10 | Piping - Reinstantment After TP-047	2d	2d	05-Dec-24	06-Dec-24			71d
CON-PIP3040	Sub-System 64-10 | Piping - Reinstantment After TP-051	2d	2d	11-Dec-24	12-Dec-24			66d
CON-PIP1790	Sub-System 64-10 | Piping - RFCC	0d	0d		12-Dec-24			66d
MH SUMMARY - Mechanical		99d	101d	22-Jul-24 A	18-Nov-24	22-Jun-24	19-Sep-24	103d
CON-MECH1200	MH SUMMARY - Mechanical Equipment - Installation - Lower Deck - Bess Battery	12d	11d	22-Jul-24 A	02-Aug-24 A	22-Jun-24	05-Jul-24	
CON-MECH1000	MH SUMMARY - Mechanical Equipment - Installation - Upper Deck - Fuell Cell	21d	27d	18-Sep-24 A	18-Oct-24 A	27-Aug-24	19-Sep-24	
Mechanical - Bess Battery		99d	101d	22-Jul-24 A	18-Nov-24			27d
CON-8570	BESS CPI - Delivery at yard	0d	0d	22-Jul-24 A				
CON-8571	Mechanical Equipment - Installation BESS container 1	4d	10d	23-Jul-24 A	02-Aug-24 A			
CON-8572	Mechanical Equipment - Installation BESS container 2	4d	10d	23-Jul-24 A	02-Aug-24 A			
CON-8573	Mechanical Equipment - Installation PCS container	4d	10d	23-Jul-24 A	02-Aug-24 A			
CON-8574	Mechanical Equipment - Exhaust units installation BESS container 1 (Vendor Responsability)	7d	5d	29-Jul-24 A	02-Aug-24 A			
CON-8575	Mechanical Equipment - Exhaust units installation BESS container 2 (Vendor Responsability)	7d	5d	29-Jul-24 A	02-Aug-24 A			
CON-8606	Mechanical Equipment - STATRON/FREQCON Activities BOP	19d	46d	25-Sep-24 A	18-Nov-24			27d
CON-8581	Mechanical Equipment - Installation of earthing cables (BESS 1 / BESS 2 /PCS)	6d	9d	23-Oct-24 A	02-Nov-24			27d
CON-8596	Mechanical Equipment - Start BESS Installation	0d	0d	23-Oct-24 A				
CON-8577	Mechanical Equipment - Installation of 400 VAC aux supply for PCS container	3d	5d	24-Oct-24 A	29-Oct-24			27d
CON-8580	Mechanical Equipment - Installation of 6.6 kV AC cables (PCS)	5d	8d	24-Oct-24 A	02-Nov-24			30d
CON-8576	Mechanical Equipment - Installation of 400 VAC aux supply for BESS containers	6d	7d	25-Oct-24 A	02-Nov-24			27d
CON-8578	Mechanical Equipment - Installation of DC cables between BESS containers and PCS	3d	5d	25-Oct-24 A	30-Oct-24			30d
CON-8582	Mechanical Equipment - Installation of CCS COMM cable(s) (PCS)	2d	7d	25-Oct-24 A	02-Nov-24			27d
CON-8583	Mechanical Equipment - Installation of CCS hard wired signal cables (PCS)	3d	8d	25-Oct-24 A	04-Nov-24			27d
CON-8579	Mechanical Equipment - Installation of COMM cables between BESS containers and PCS	3d	3d	30-Oct-24	02-Nov-24			27d
Mechanical		138d	468d	10-Jul-23 A	24-Jan-25	30-Jul-24	04-Dec-24	45d
CON-MECH1120	Mechanical Equipment - Installation - Lower Deck - Shelter For AC UPS & UPS System	15d	86d	29-Jul-24 A	07-Nov-24	02-Aug-24	20-Aug-24	66d
CON-MECH1130	Mechanical Equipment - Installation - Lower Deck - Shelter for HV Switchgear Room	15d	22d	29-Jul-24 A	23-Aug-24 A	06-Aug-24	23-Aug-24	
CON-MECH1140	Mechanical Equipment - Installation - Lower Deck - Shelter for LV Switchgear Room	15d	22d	29-Jul-24 A	23-Aug-24 A	09-Aug-24	27-Aug-24	
CON-MECH1150	Mechanical Equipment - Installation - Lower Deck - Shelter for Plant Instrument Room	15d	86d	29-Jul-24 A	07-Nov-24	13-Aug-24	30-Aug-24	66d
CON-MECH1090	Mechanical Equipment - Installation - Lower Deck - DC UPS Feeder Board	10d	10d	20-Aug-24 A	30-Aug-24 A	17-Aug-24	28-Aug-24	
CON-MECH1020	Mechanical Equipment - Installation - Vessel Rack - H2 Storage Vessel	20d	39d	30-Sep-24 A	14-Nov-24	12-Nov-24	04-Dec-24	63d
CON-MECH1070	Mechanical Equipment - Installation - Lower Deck - AC UPS for PAGA/FGS/EMCS	10d	1d	08-Oct-24 A	08-Oct-24 A	26-Aug-24	05-Sep-24	

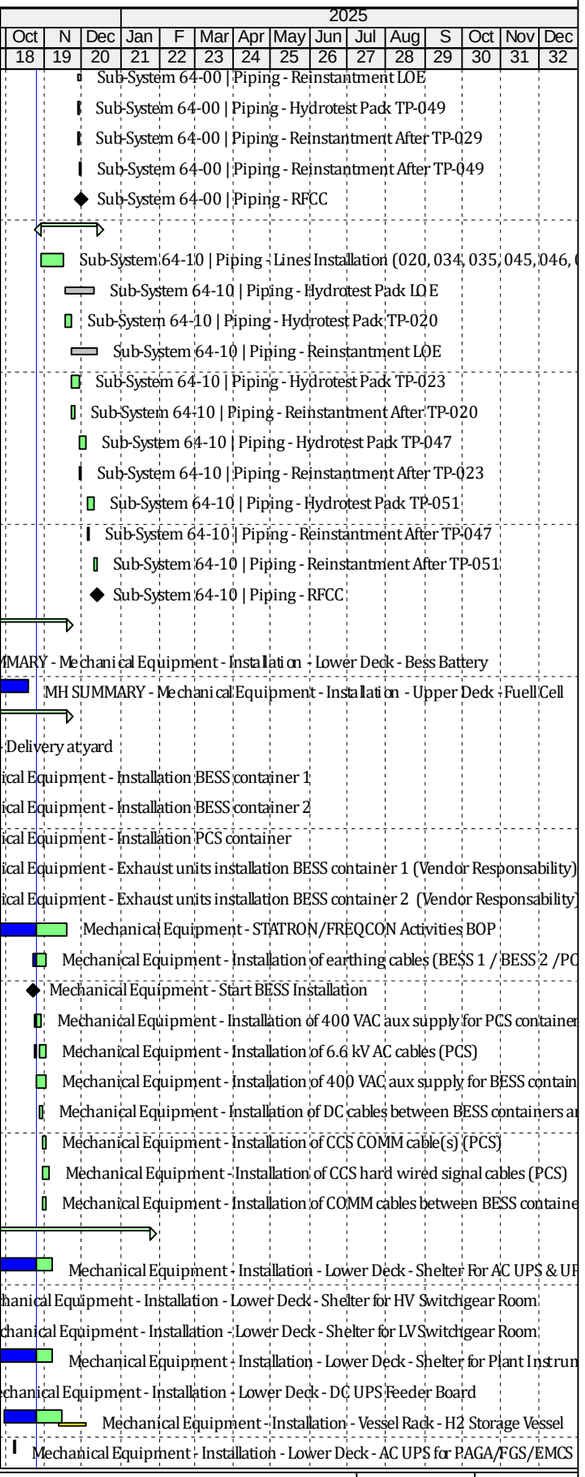

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-MECH1080	Mechanical Equipment - Installation - Lower Deck - AC UPS for CCS /SIS	22d	1d	08-Oct-24 A	08-Oct-24 A	05-Aug-24	16-Aug-24	
CON-MECH1100	Mechanical Equipment - Installation - Lower Deck - Waste Water Tank	10d	22d	12-Oct-24 A	07-Nov-24	04-Oct-24	15-Oct-24	68d
CON-MECH1160	Mechanical Equipment - Installation - Lower Deck - Automation Systems CCS-SIS-EMS	12d	19d	18-Oct-24 A	09-Nov-24	13-Sep-24	17-Oct-24	66d
CON-MECH1170	Mechanical Equipment - Installation - Upper Deck - Hydrogen Vent KO Drum	15d	15d	26-Oct-24	13-Nov-24	26-Oct-24	13-Nov-24	64d
CON-MECH1030	Mechanical Equipment - Installation - Lower Deck - Container 40' ISO for Water treatment system	15d	15d	02-Nov-24	19-Nov-24	30-Jul-24	16-Aug-24	72d
CON-MECH1050	Mechanical Equipment - Installation - Lower Deck - Instrument Air Package	10d	10d	02-Nov-24	13-Nov-24	26-Sep-24	07-Oct-24	71d
CON-MECH1110	Mechanical Equipment - Installation - Lower Deck - Instrument Air Reciever	10d	10d	02-Nov-24	13-Nov-24	18-Sep-24	28-Sep-24	79d
CON-MECH1210	Mechanical Equipment - Installation - Lower Deck - Water Treatment System	30d	30d	02-Nov-24	06-Dec-24	26-Aug-24	28-Sep-24	48d
CON-MECH1040	Mechanical Equipment - Installation - Upper Deck - Hydrogen Vent	18d	18d	30-Nov-24	20-Dec-24	06-Sep-24	26-Sep-24	48d
CON-MECH1010	Mechanical Equipment - Installation - Upper Deck - Electrolyser & Electrolyser Transformer	30d	30d	17-Dec-24	24-Jan-25	27-Aug-24	30-Sep-24	22d
CON-MECH1060	Mechanical Equipment - Installation - Upper Deck - Davit Crane	12d	12d	21-Dec-24	08-Jan-25	14-Sep-24	27-Sep-24	59d
Mechanical - Fuel Cell		19d	53d	18-Sep-24 A	09-Nov-24			82d
CON-8010	Fuel Cell CPI - Delivery at yard	0d	0d	18-Sep-24 A				
CON-8011	Mechanical Equipment - Preparation of fuel cell package	1d	3d	18-Sep-24 A	20-Sep-24 A			
CON-8012	Mechanical Equipment - Installation of containers and cooling skid	3d	3d	18-Sep-24 A	20-Sep-24 A			
CON-8013	Mechanical Equipment - Fuel cell system installation	15d	34d	07-Oct-24 A	09-Nov-24			82d
Mechanical - H2 Storage Vessel		21d	1d	10-Jul-23 A	10-Jul-23 A			
CON-2500	H2 storage vessels - Delivery at yard - DELETED	0d	0d	10-Jul-23 A				
CON-2501	Installation of H2 storage vessels -DELETED	21d	1d	10-Jul-23 A	10-Jul-23 A			
Mechanical - Water Treatment System		31d	1d	10-Jul-23 A	10-Jul-23 A			
CON-5000	Water treatment system - Delivery at yard - DELETED	0d	0d	10-Jul-23 A				
CON-5001	Installation Water treatment system - DELETED	31d	1d	10-Jul-23 A	10-Jul-23 A			
Electrical		187d	198d	22-Jul-24 A	15-Mar-25	27-Aug-24	03-Dec-24	6d
CON-EIT1550	Electrical Cables - Pulling & Dressing (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	50d	1d	23-Aug-24 A	23-Aug-24 A	18-Sep-24	15-Nov-24	
Lower Deck		119d	130d	29-Jul-24 A	31-Dec-24	27-Aug-24	21-Nov-24	68d
CON-EIT1190	Electrical Cable Trays - Installation - Lower Deck	27d	106d	29-Jul-24 A	30-Nov-24	27-Aug-24	26-Sep-24	41d
CON-EIT1200	Electrical Equipment - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	24d	1d	23-Aug-24 A	23-Aug-24 A	30-Aug-24	26-Sep-24	
CON-EIT1210	Electrical Junction Boxes - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	17d	1d	23-Aug-24 A	23-Aug-24 A	27-Sep-24	16-Oct-24	
CON-EIT1220	Electrical Cable Termination, Glanding & Connection - Installation - Lower Deck (DELETED AFTER REVISED SCI	35d	1d	23-Aug-24 A	23-Aug-24 A	11-Oct-24	21-Nov-24	
CON-EIT1230	Lighting & Small Power - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	21d	1d	23-Aug-24 A	23-Aug-24 A	27-Sep-24	21-Oct-24	
CON-EIT1240	Earthing - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	18d	1d	23-Aug-24 A	23-Aug-24 A	01-Oct-24	21-Oct-24	
CON-EIT1560	Electrical Heat Tracing - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	30-Sep-24	16-Oct-24	
CON-EIT1590	Navigation Aid - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	12d	1d	23-Aug-24 A	23-Aug-24 A	01-Oct-24	14-Oct-24	
CON-EIT8990	Electrical MCT - Installation - Lower Deck	27d	71d	07-Oct-24 A	31-Dec-24			59d
Upper Deck		115d	115d	19-Aug-24 A	04-Jan-25	10-Sep-24	03-Dec-24	65d
CON-EIT1250	Electrical Cable Trays - Installation - Upper Deck	27d	88d	19-Aug-24 A	30-Nov-24	10-Sep-24	10-Oct-24	45d
CON-EIT1260	Electrical Equipment - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	24d	1d	23-Aug-24 A	23-Aug-24 A	13-Sep-24	10-Oct-24	
CON-EIT1270	Electrical Junction Boxes - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	17d	1d	23-Aug-24 A	23-Aug-24 A	11-Oct-24	30-Oct-24	
CON-EIT1280	Electrical Cable Termination, Glanding & Connection - Installation - Upper Deck (DELETED AFTER REVISED SCI	35d	1d	23-Aug-24 A	23-Aug-24 A	23-Oct-24	03-Dec-24	
CON-EIT1290	Lighting & Small Power - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	21d	1d	23-Aug-24 A	23-Aug-24 A	11-Oct-24	05-Nov-24	
CON-EIT1300	Earthing - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	18d	1d	23-Aug-24 A	23-Aug-24 A	15-Oct-24	05-Nov-24	
CON-EIT1570	Electrical Heat Tracing - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	22-Oct-24	08-Nov-24	
CON-EIT1600	Navigation Aid - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	12d	1d	23-Aug-24 A	23-Aug-24 A	15-Oct-24	28-Oct-24	
CON-EIT9000	Electrical MCT - Installation - Upper Deck	27d	27d	02-Dec-24*	04-Jan-25			56d
Vessel Rack		83d	117d	23-Aug-24 A	11-Jan-25	11-Oct-24	29-Nov-24	60d
CON-EIT1320	Electrical Equipment - Installation - Vessel Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	15-Oct-24	31-Oct-24	

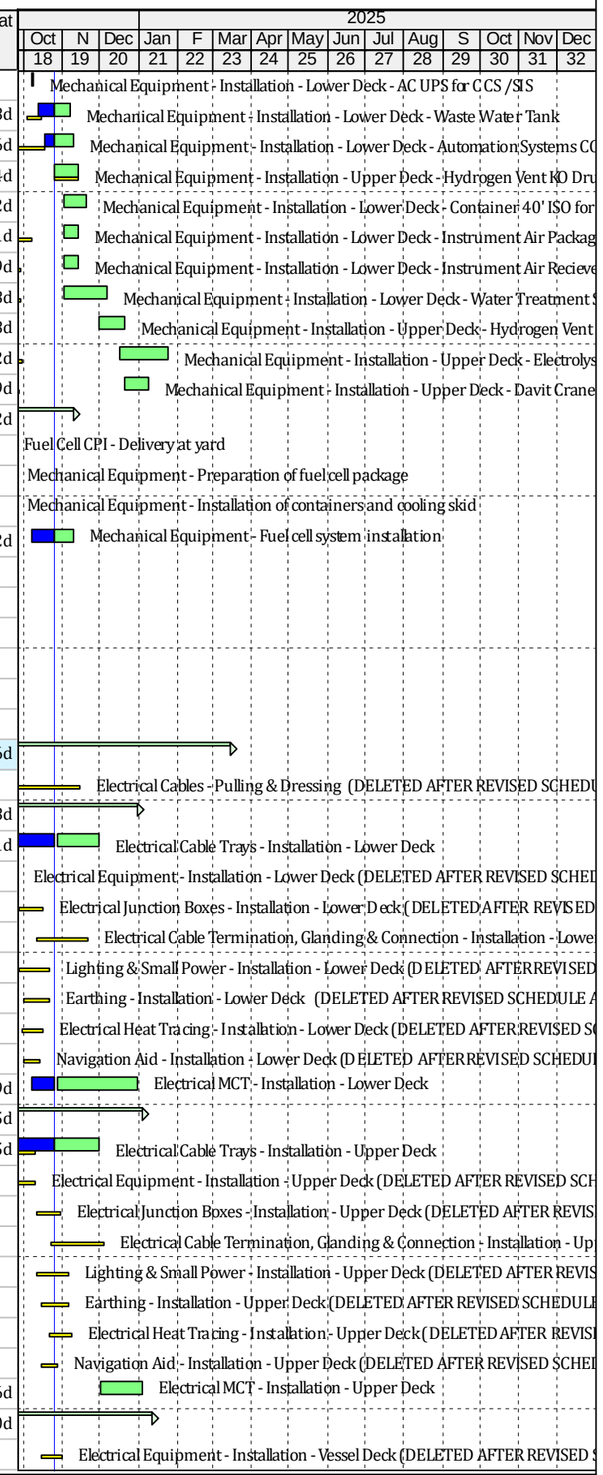

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT1330	Electrical Junction Boxes - Installation - Vessel Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	12d	1d	23-Aug-24 A	23-Aug-24 A	02-Nov-24	15-Nov-24	
CON-EIT1340	Electrical Cable Termination, Glanding & Connection - Installation - Vessel Deck (DELETED AFTER REVISED SCH	15d	1d	23-Aug-24 A	23-Aug-24 A	13-Nov-24	29-Nov-24	
CON-EIT1350	Lighting & Small Power - Installation - Vessel Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	02-Nov-24	19-Nov-24	
CON-EIT1360	Earthing - Installation - Vessel Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	12d	1d	23-Aug-24 A	23-Aug-24 A	06-Nov-24	19-Nov-24	
CON-EIT1580	Electrical Heat Tracing - Installation - Vessel Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	12d	1d	23-Aug-24 A	23-Aug-24 A	26-Oct-24	09-Nov-24	
CON-EIT1610	Navigation Aid - Installation - Vessel Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	6d	1d	23-Aug-24 A	23-Aug-24 A	06-Nov-24	12-Nov-24	
CON-EIT1310	Electrical Cable Trays - Installation - Vessel Deck/Transition Piece	18d	18d	18-Dec-24	11-Jan-25	11-Oct-24	31-Oct-24	31d
CON-EIT9010	Electrical MCT - Installation - Vessel Deck/Transition Piece	18d	18d	18-Dec-24*	11-Jan-25			51d
E.00 Sub-System 88-00 | Earthing		113d	118d	29-Jul-24 A	14-Dec-24			71d
CON-EIT1800	Sub-System 88-00 | Electrical - Equipment Arrival	0d	0d	29-Jul-24 A				
CON-EIT1790	Sub-System 88-00 | Electrical - Cable Pulling	3d	3d	30-Nov-24*	03-Dec-24			71d
CON-EIT1810	Sub-System 88-00 | Electrical - Cable Termination	2d	2d	04-Dec-24	05-Dec-24			71d
CON-EIT1820	Sub-System 88-00 | Electrical - Item Installation	4d	4d	06-Dec-24	10-Dec-24			71d
CON-EIT1830	Sub-System 88-00 | Electrical - Mechanical Completion	4d	4d	11-Dec-24	14-Dec-24			71d
CON-EIT1840	Sub-System 88-00 | Electrical - RFCC	0d	0d		14-Dec-24			71d
E.01 Sub-System 83-00 | 400 V Switchboard & Connection Box (SG-200N1)		58d	78d	07-Aug-24 A	07-Nov-24			41d
CON-EIT1395	Sub-System 83-00 | Electrical - Equipment Arrival	0d	0d	07-Aug-24 A				
CON-EIT1345	Sub-System 83-00 | Electrical - Cable Pulling	7d	47d	02-Sep-24 A	25-Oct-24 A			
CON-EIT1365	Sub-System 83-00 | Electrical - Item Installation	1d	47d	09-Sep-24 A	02-Nov-24			45d
CON-EIT1375	Sub-System 83-00 | Electrical - Mechanical Completion	4d	51d	09-Sep-24 A	07-Nov-24			41d
CON-EIT1355	Sub-System 83-00 | Electrical - Cable Termination	6d	42d	14-Sep-24 A	02-Nov-24			45d
CON-EIT1385	Sub-System 83-00 | Electrical - RFCC	0d	0d		07-Nov-24			41d
E.02 Sub-System 84-10 | AC 35 kVA UPS System (UP-200F3)		33d	48d	13-Sep-24 A	08-Nov-24			47d
CON-EIT1750	Sub-System 84-10 | Electrical - Item Installation	2d	25d	13-Sep-24 A	11-Oct-24 A			
CON-EIT1780	Sub-System 84-10 | Electrical - Equipment Arrival	0d	0d	13-Sep-24 A				
CON-EIT1760	Sub-System 84-10 | Electrical - Mechanical Completion	8d	40d	23-Sep-24 A	08-Nov-24			47d
CON-EIT1730	Sub-System 84-10 | Electrical - Cable Pulling	5d	29d	30-Sep-24 A	02-Nov-24			47d
CON-EIT1740	Sub-System 84-10 | Electrical - Cable Termination	3d	15d	16-Oct-24 A	02-Nov-24			52d
CON-EIT1770	Sub-System 84-10 | Electrical - RFCC	0d	0d		08-Nov-24			47d
E.03 Sub-System 84-20 | AC 15 kVA UPS System (UP-200F4)		33d	48d	13-Sep-24 A	08-Nov-24			79d
CON-EIT1880	Sub-System 84-20 | Electrical - Item Installation	2d	25d	13-Sep-24 A	11-Oct-24 A			
CON-EIT1860	Sub-System 84-20 | Electrical - Equipment Arrival	0d	0d	13-Sep-24 A				
CON-EIT1890	Sub-System 84-20 | Electrical - Mechanical Completion	8d	40d	23-Sep-24 A	08-Nov-24			79d
CON-EIT1850	Sub-System 84-20 | Electrical - Cable Pulling	5d	29d	30-Sep-24 A	02-Nov-24			79d
CON-EIT1870	Sub-System 84-20 | Electrical - Cable Termination	3d	15d	16-Oct-24 A	02-Nov-24			79d
CON-EIT1900	Sub-System 84-20 | Electrical - RFCC	0d	0d		08-Nov-24			79d
E.04 Sub-System 84-00 | DC 10 kVA UPS System (UP-200F1)		50d	76d	01-Aug-24 A	29-Oct-24			88d
CON-EIT1920	Sub-System 84-00 | Electrical - Equipment Arrival	0d	0d	01-Aug-24 A				
CON-EIT1940	Sub-System 84-00 | Electrical - Item Installation	2d	31d	30-Aug-24 A	04-Oct-24 A			
CON-EIT1910	Sub-System 84-00 | Electrical - Cable Pulling	5d	36d	18-Sep-24 A	29-Oct-24			88d
CON-EIT1950	Sub-System 84-00 | Electrical - Mechanical Completion	5d	31d	23-Sep-24 A	28-Oct-24			88d
CON-EIT1930	Sub-System 84-00 | Electrical - Cable Termination	2d	29d	26-Sep-24 A	29-Oct-24			88d
CON-EIT1960	Sub-System 84-00 | Electrical - RFCC	0d	0d		28-Oct-24			88d
E.05 Sub-System 82-00 | MV 6.6 kV Switchboard (SG-100D1)		61d	81d	07-Aug-24 A	11-Nov-24			81d
CON-EIT2000	Sub-System 82-00 | Electrical - Item Installation	1d	44d	07-Aug-24 A	27-Sep-24 A			
CON-EIT1980	Sub-System 82-00 | Electrical - Equipment Arrival	0d	0d	07-Aug-24 A				

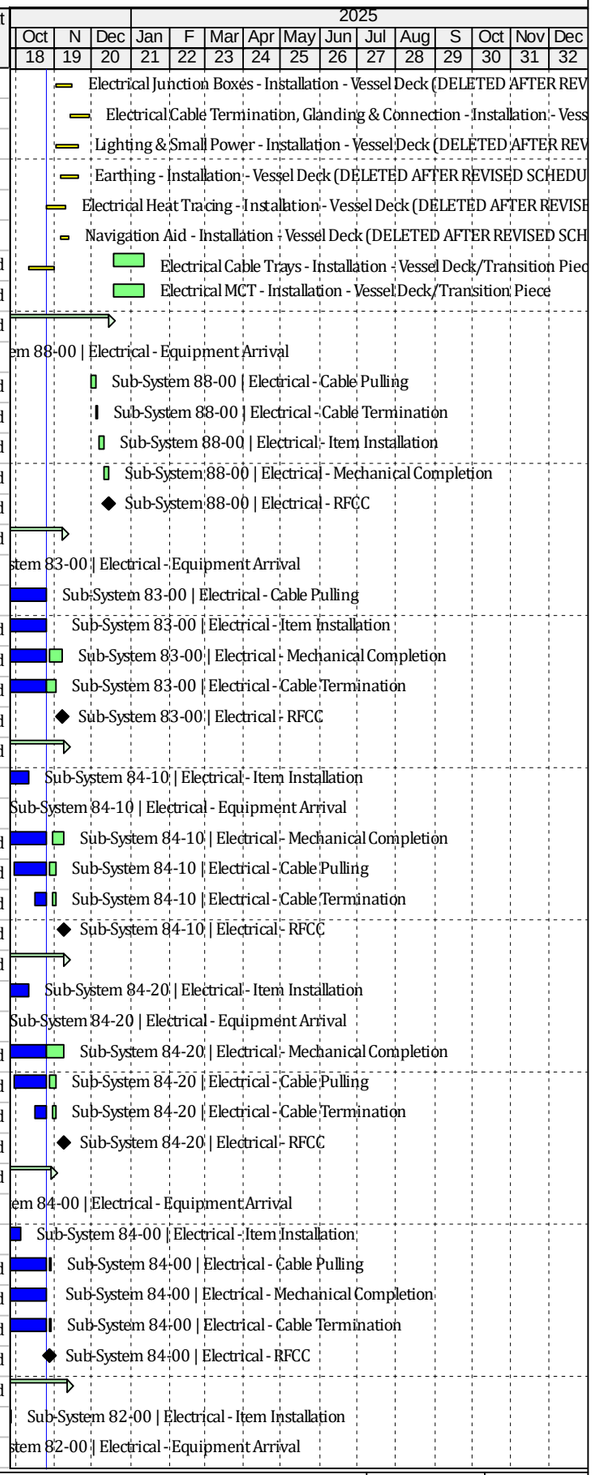

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT2010	Sub-System 82-00 | Electrical - Mechanical Completion	3d	54d	09-Sep-24 A	11-Nov-24			81d
CON-EIT1970	Sub-System 82-00 | Electrical - Cable Pulling	5d	21d	18-Sep-24 A	11-Oct-24 A			
CON-EIT1990	Sub-System 82-00 | Electrical - Cable Termination	3d	29d	26-Sep-24 A	29-Oct-24			81d
CON-EIT2020	Sub-System 82-00 | Electrical - RFCC	0d	0d		11-Nov-24			81d
E.06 Sub-System 82-40 | Power Transformer 1.6 MVA (TR-200DE1)		86d	89d	31-Jul-24 A	13-Nov-24			95d
CON-EIT2060	Sub-System 82-40 | Electrical - Item Installation	1d	38d	31-Jul-24 A	13-Sep-24 A			
CON-EIT2040	Sub-System 82-40 | Electrical - Equipment Arrival	0d	0d	31-Jul-24 A				
CON-EIT2070	Sub-System 82-40 | Electrical - Mechanical Completion	12d	56d	09-Sep-24 A	13-Nov-24			95d
CON-EIT2030	Sub-System 82-40 | Electrical - Cable Pulling	12d	30d	07-Oct-24 A	11-Nov-24			95d
CON-EIT2050	Sub-System 82-40 | Electrical - Cable Termination	7d	7d	06-Nov-24	13-Nov-24			95d
CON-EIT2080	Sub-System 82-40 | Electrical - RFCC	0d	0d		13-Nov-24			95d
E.08 Sub-System 81-10 | GIS 66 kV (HNA6-AFA70)		18d	95d	26-Sep-24 A	20-Jan-25			47d
CON-EIT2090	Sub-System 81-10 | Electrical - Cable Pulling	5d	92d	26-Sep-24 A	16-Jan-25			47d
CON-EIT2110	Sub-System 81-10 | Electrical - Cable Termination	12d	92d	26-Sep-24 A	16-Jan-25			47d
CON-EIT2120	Sub-System 81-10 | Electrical - Item Installation	2d	2d	15-Jan-25	16-Jan-25			47d
CON-EIT2100	Sub-System 81-10 | Electrical - Equipment Arrival	1d	1d	16-Jan-25	16-Jan-25			47d
CON-EIT2130	Sub-System 81-10 | Electrical - Mechanical Completion	3d	3d	17-Jan-25	20-Jan-25			47d
CON-EIT2140	Sub-System 81-10 | Electrical - RFCC	0d	0d		20-Jan-25			47d
E.09 Sub-System 83-20 | 400/230 V Switchboard (DP-200N1)		32d	36d	24-Sep-24 A	05-Nov-24			50d
CON-EIT2160	Sub-System 83-20 | Electrical - Equipment Arrival	0d	0d	24-Sep-24 A				
CON-EIT2180	Sub-System 83-20 | Electrical - Item Installation	1d	1d	26-Sep-24 A	26-Sep-24 A			
CON-EIT2190	Sub-System 83-20 | Electrical - Mechanical Completion	3d	31d	30-Sep-24 A	05-Nov-24			50d
CON-EIT2150	Sub-System 83-20 | Electrical - Cable Pulling	2d	20d	07-Oct-24 A	29-Oct-24			50d
CON-EIT2170	Sub-System 83-20 | Electrical - Cable Termination	1d	12d	12-Oct-24 A	25-Oct-24 A			
CON-EIT2200	Sub-System 83-20 | Electrical - RFCC	0d	0d		05-Nov-24			50d
E.10 Sub-System 80-00 | Hydrogen Fuel Cell Package (A-80000)		34d	37d	18-Sep-24 A	30-Oct-24			99d
CON-EIT2220	Sub-System 80-00 | Electrical - Equipment Arrival	0d	0d	18-Sep-24 A				
CON-EIT2210	Sub-System 80-00 | Electrical - Cable Pulling	1d	6d	19-Oct-24 A	25-Oct-24 A			
CON-EIT9050	Sub-System 80-00 | Electrical - Item Installation	2d	2d	26-Oct-24	28-Oct-24			99d
CON-EIT2230	Sub-System 80-00 | Electrical - Cable Termination	1d	1d	29-Oct-24	29-Oct-24			99d
CON-EIT2250	Sub-System 80-00 | Electrical - Mechanical Completion	1d	1d	30-Oct-24	30-Oct-24			99d
CON-EIT2260	Sub-System 80-00 | Electrical - RFCC	0d	0d		30-Oct-24			99d
E.11 Sub-System 85-00 | BESS Package (A-85000)		82d	93d	22-Jul-24 A	08-Nov-24			49d
CON-EIT2280	Sub-System 85-00 | Electrical - Equipment Arrival	0d	0d	22-Jul-24 A				
CON-EIT9060	Sub-System 85-00 | Electrical - Item Installation	2d	11d	22-Jul-24 A	02-Aug-24 A			
CON-EIT2310	Sub-System 85-00 | Electrical - Mechanical Completion	4d	40d	23-Sep-24 A	08-Nov-24			49d
CON-EIT2270	Sub-System 85-00 | Electrical - Cable Pulling	7d	25d	07-Oct-24 A	05-Nov-24			52d
CON-EIT2290	Sub-System 85-00 | Electrical - Cable Termination	2d	11d	17-Oct-24 A	29-Oct-24			57d
CON-EIT2320	Sub-System 85-00 | Electrical - RFCC	0d	0d		08-Nov-24			49d
E.12 Sub-System 72-00 | NAVAID		30d	38d	11-Oct-24 A	25-Nov-24			81d
CON-EIT2330	Sub-System 72-00 | Electrical - Cable Pulling	8d	22d	11-Oct-24 A	06-Nov-24			81d
CON-EIT2350	Sub-System 72-00 | Electrical - Cable Termination	4d	24d	16-Oct-24 A	13-Nov-24			91d
CON-EIT2340	Sub-System 72-00 | Electrical - Equipment Arrival	0d	0d	26-Oct-24				96d
CON-EIT2360	Sub-System 72-00 | Electrical - Item Installation	6d	6d	07-Nov-24	13-Nov-24			81d
CON-EIT2370	Sub-System 72-00 | Electrical - Mechanical Completion	10d	10d	14-Nov-24	25-Nov-24			81d
CON-EIT2380	Sub-System 72-00 | Electrical - RFCC	0d	0d		25-Nov-24			81d

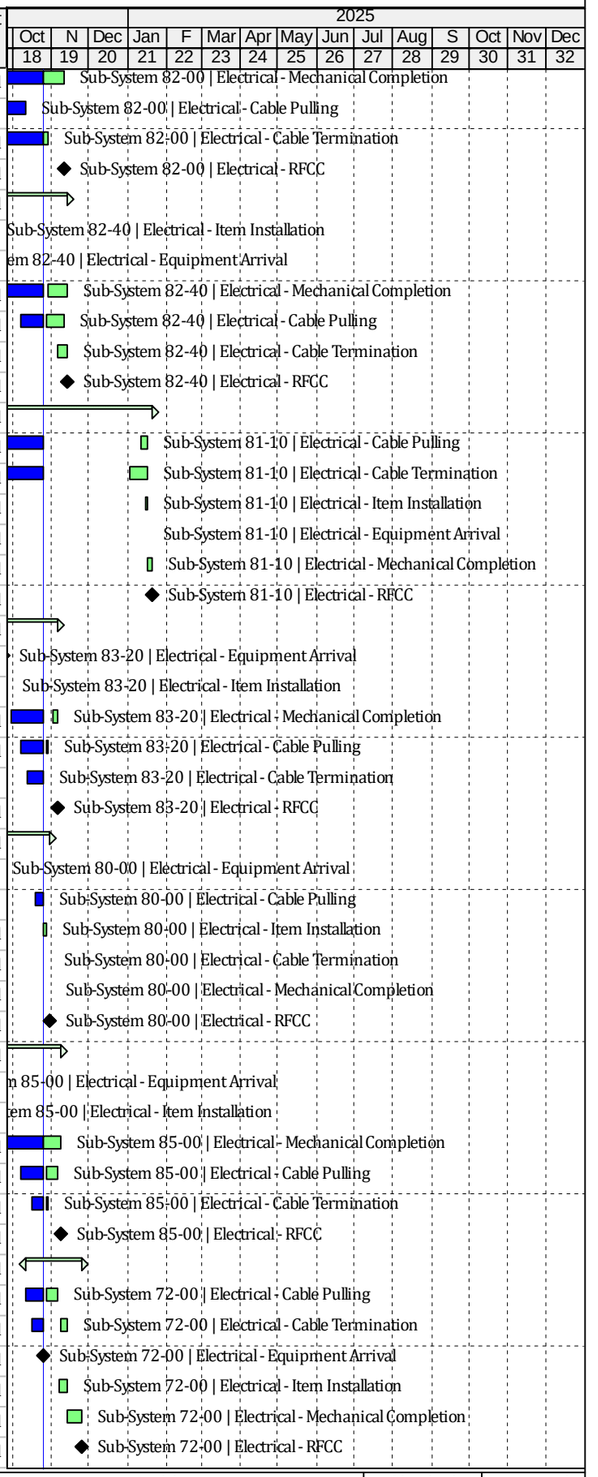


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
E.13 Sub-System 83-35 | Emergency Lighting		80d	87d	13-Sep-24 A	24-Dec-24			60d
CON-EIT2400	Sub-System 83-35 | Electrical - Equipment Arrival	0d	0d	13-Sep-24 A				
CON-EIT2420	Sub-System 83-35 | Electrical - Item Installation	25d	37d	30-Sep-24 A	12-Nov-24			66d
CON-EIT2390	Sub-System 83-35 | Electrical - Cable Pulling	10d	16d	21-Oct-24 A	08-Nov-24			69d
CON-EIT2410	Sub-System 83-35 | Electrical - Cable Termination	20d	25d	21-Oct-24 A	19-Nov-24			60d
CON-EIT2430	Sub-System 83-35 | Electrical - Mechanical Completion	30d	30d	20-Nov-24	24-Dec-24			60d
CON-EIT2440	Sub-System 83-35 | Electrical - RFCC	0d	0d		24-Dec-24			60d
E.14 Sub-System 83-40 | Normal Lighting		72d	79d	13-Sep-24 A	14-Dec-24			68d
CON-EIT2460	Sub-System 83-40 | Electrical - Equipment Arrival	0d	0d	13-Sep-24 A				
CON-EIT2480	Sub-System 83-40 | Electrical - Item Installation	18d	41d	30-Sep-24 A	16-Nov-24			68d
CON-EIT2450	Sub-System 83-40 | Electrical - Cable Pulling	11d	17d	21-Oct-24 A	09-Nov-24			74d
CON-EIT2470	Sub-System 83-40 | Electrical - Cable Termination	15d	23d	21-Oct-24 A	16-Nov-24			68d
CON-EIT2490	Sub-System 83-40 | Electrical - Mechanical Completion	24d	24d	18-Nov-24	14-Dec-24			68d
CON-EIT2500	Sub-System 83-40 | Electrical - RFCC	0d	0d		14-Dec-24			68d
E.15 Sub-System 83-55 | Power Sockets		76d	93d	30-Sep-24 A	21-Jan-25			43d
CON-EIT2540	Sub-System 83-55 | Electrical - Item Installation	5d	85d	30-Sep-24 A	11-Jan-25			43d
CON-EIT2520	Sub-System 83-55 | Electrical - Equipment Arrival	0d	0d	04-Oct-24 A				
CON-EIT2510	Sub-System 83-55 | Electrical - Cable Pulling	3d	73d	14-Oct-24 A	11-Jan-25			43d
CON-EIT2530	Sub-System 83-55 | Electrical - Cable Termination	5d	67d	21-Oct-24 A	11-Jan-25			43d
CON-EIT2550	Sub-System 83-55 | Electrical - Mechanical Completion	8d	8d	13-Jan-25	21-Jan-25			43d
CON-EIT2560	Sub-System 83-55 | Electrical - RFCC	0d	0d		21-Jan-25			43d
E.16 Sub-System 83-50 | WeldingSockets		53d	76d	30-Sep-24 A	30-Dec-24			42d
CON-EIT2600	Sub-System 83-50 | Electrical - Item Installation	5d	23d	30-Sep-24 A	25-Oct-24 A			
CON-EIT2580	Sub-System 83-50 | Electrical - Equipment Arrival	0d	0d	04-Oct-24 A				
CON-EIT2590	Sub-System 83-50 | Electrical - Cable Termination	5d	5d	26-Oct-24	31-Oct-24			84d
CON-EIT2570	Sub-System 83-50 | Electrical - Cable Pulling	3d	3d	18-Dec-24	20-Dec-24			42d
CON-EIT2610	Sub-System 83-50 | Electrical - Mechanical Completion	6d	6d	21-Dec-24	30-Dec-24			42d
CON-EIT2620	Sub-System 83-50 | Electrical - RFCC	0d	0d		30-Dec-24			42d
E.17 Sub-System 83-65 | Electrical Trace Heating		56d	84d	30-Sep-24 A	10-Jan-25			38d
CON-EIT2660	Sub-System 83-65 | Electrical - Item Installation	4d	70d	30-Sep-24 A	20-Dec-24			38d
CON-EIT2640	Sub-System 83-65 | Electrical - Equipment Arrival	0d	0d	02-Nov-24				77d
CON-EIT2630	Sub-System 83-65 | Electrical - Cable Pulling	3d	3d	18-Dec-24	20-Dec-24			38d
CON-EIT2650	Sub-System 83-65 | Electrical - Cable Termination	6d	6d	21-Dec-24	30-Dec-24			38d
CON-EIT2670	Sub-System 83-65 | Electrical - Mechanical Completion	8d	8d	31-Dec-24	10-Jan-25			38d
CON-EIT2680	Sub-System 83-65 | Electrical - RFCC	0d	0d		10-Jan-25			38d
E.18 Sub-System 83-75 | Temporary Diesel Generator		60d	60d	26-Oct-24	09-Jan-25			56d
CON-EIT2700	Sub-System 83-75 | Electrical - Equipment Arrival	0d	0d	26-Oct-24				100d
CON-EIT2690	Sub-System 83-75 | Electrical - Cable Pulling	3d	3d	18-Dec-24	20-Dec-24			56d
CON-EIT2720	Sub-System 83-75 | Electrical - Item Installation	4d	4d	21-Dec-24	27-Dec-24			56d
CON-EIT2710	Sub-System 83-75 | Electrical - Cable Termination	2d	2d	28-Dec-24	30-Dec-24			56d
CON-EIT2730	Sub-System 83-75 | Electrical - Mechanical Completion	7d	7d	31-Dec-24	09-Jan-25			56d
CON-EIT2740	Sub-System 83-75 | Electrical - RFCC	0d	0d		09-Jan-25			56d
E.19 Sub-System 81-20 | Power Transformer 7 MVA (TR-100AD1)		73d	95d	05-Aug-24 A	25-Nov-24			80d
CON-EIT2760	Sub-System 81-20 | Electrical - Equipment Arrival	0d	0d	05-Aug-24 A				
CON-EIT2780	Sub-System 81-20 | Electrical - Item Installation	1d	55d	07-Sep-24 A	11-Nov-24			80d
CON-EIT2790	Sub-System 81-20 | Electrical - Mechanical Completion	13d	66d	09-Sep-24 A	25-Nov-24			80d

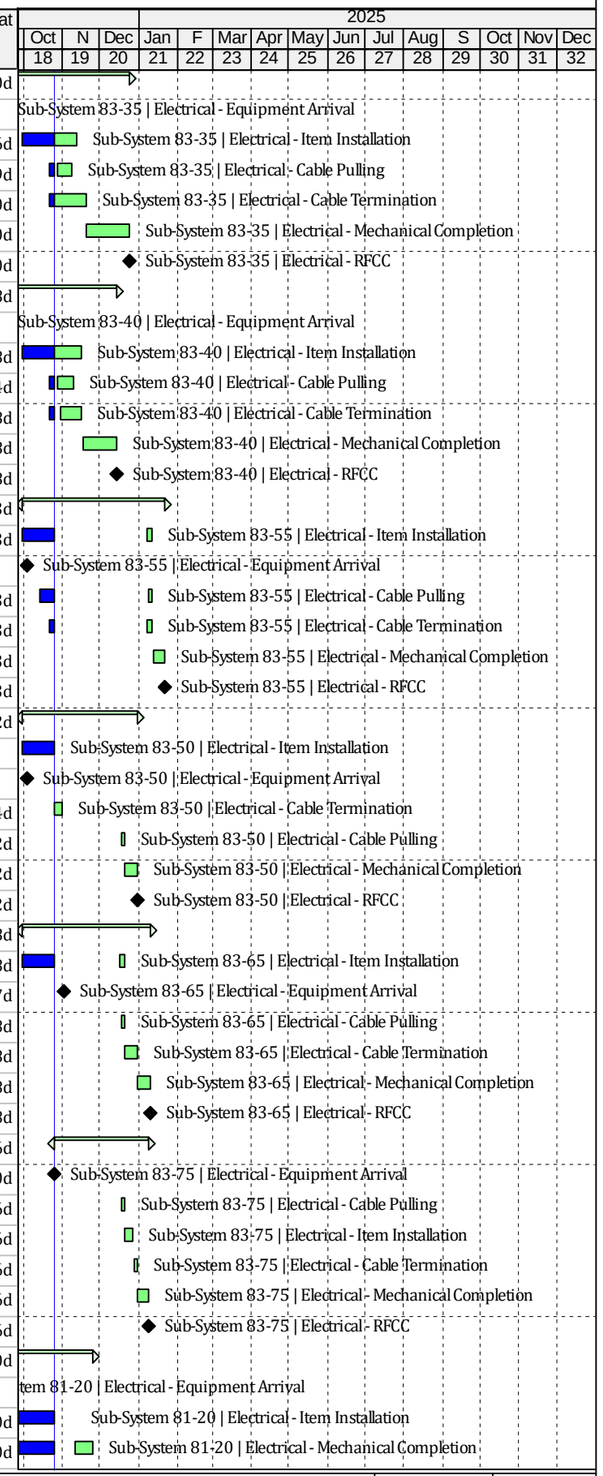

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT2750	Sub-System 81-20 | Electrical - Cable Pulling	7d	46d	18-Sep-24 A	11-Nov-24			80d
CON-EIT2770	Sub-System 81-20 | Electrical - Cable Termination	6d	39d	26-Sep-24 A	11-Nov-24			80d
CON-EIT2800	Sub-System 81-20 | Electrical - RFCC	0d	0d		25-Nov-24			80d
E.20 Sub-System 20-00 | Electrolyser Package (A-20000)		14d	14d	17-Dec-24	04-Jan-25			54d
CON-EIT2810	Sub-System 20-00 | Electrical - Cable Pulling	4d	4d	17-Dec-24	20-Dec-24			54d
CON-EIT2820	Sub-System 20-00 | Electrical - Equipment Arrival	0d	0d	17-Dec-24				54d
CON-EIT9070	Sub-System 20-00 | Electrical - Item Installation	5d	5d	21-Dec-24	28-Dec-24			54d
CON-EIT2830	Sub-System 20-00 | Electrical - Cable Termination	2d	2d	30-Dec-24	31-Dec-24			54d
CON-EIT2850	Sub-System 20-00 | Electrical - Mechanical Completion	3d	3d	02-Jan-25	04-Jan-25			54d
CON-EIT2860	Sub-System 20-00 | Electrical - RFCC	0d	0d		04-Jan-25			54d
E.21 Sub-System 82-30 | Power Transformer 1.25 MVA (TA30 FUEL CELL)		38d	41d	18-Sep-24 A	05-Nov-24			92d
CON-EIT2880	Sub-System 82-30 | Electrical - Equipment Arrival	0d	0d	18-Sep-24 A				
CON-EIT2870	Sub-System 82-30 | Electrical - Cable Pulling	3d	5d	07-Oct-24 A	11-Oct-24 A			
CON-EIT9080	Sub-System 82-30 | Electrical - Item Installation	5d	5d	26-Oct-24	31-Oct-24			92d
CON-EIT2890	Sub-System 82-30 | Electrical - Cable Termination	1d	1d	02-Nov-24	02-Nov-24			92d
CON-EIT2910	Sub-System 82-30 | Electrical - Mechanical Completion	2d	2d	04-Nov-24	05-Nov-24			92d
CON-EIT2920	Sub-System 82-30 | Electrical - RFCC	0d	0d		05-Nov-24			92d
E.22 Sub-System 82-10 | Power Transformer 1.25 MVA (1BT1 BESS)		80d	91d	22-Jul-24 A	06-Nov-24			96d
CON-EIT2940	Sub-System 82-10 | Electrical - Equipment Arrival	0d	0d	22-Jul-24 A				
CON-EIT2930	Sub-System 82-10 | Electrical - Cable Pulling	3d	2d	17-Oct-24 A	18-Oct-24 A			
CON-EIT9090	Sub-System 82-10 | Electrical - Item Installation	5d	5d	28-Oct-24	02-Nov-24			96d
CON-EIT2950	Sub-System 82-10 | Electrical - Cable Termination	1d	1d	04-Nov-24	04-Nov-24			96d
CON-EIT2970	Sub-System 82-10 | Electrical - Mechanical Completion	2d	2d	05-Nov-24	06-Nov-24			96d
CON-EIT2980	Sub-System 82-10 | Electrical - RFCC	0d	0d		06-Nov-24			96d
E.23 Sub-System 82-20 | Power Transformer 3.15 MVA (T4 ELECTROLYSER)		10d	10d	17-Dec-24	30-Dec-24			57d
CON-EIT2990	Sub-System 82-20 | Electrical - Cable Pulling	2d	2d	17-Dec-24	18-Dec-24			57d
CON-EIT3000	Sub-System 82-20 | Electrical - Equipment Arrival	0d	0d	17-Dec-24				57d
CON-EIT9100	Sub-System 82-20 | Electrical - Item Installation	5d	5d	19-Dec-24	24-Dec-24			57d
CON-EIT3010	Sub-System 82-20 | Electrical - Cable Termination	1d	1d	27-Dec-24	27-Dec-24			57d
CON-EIT3030	Sub-System 82-20 | Electrical - Mechanical Completion	2d	2d	28-Dec-24	30-Dec-24			57d
CON-EIT3040	Sub-System 82-20 | Electrical - RFCC	0d	0d		30-Dec-24			57d
E.24 Sub-System 82-50 | Solar PV Package Power Transformer 0.5 MVA (TR-200ED1)		34d	84d	29-Jul-24 A	05-Nov-24			102d
CON-EIT3080	Sub-System 82-50 | Electrical - Item Installation	1d	5d	29-Jul-24 A	02-Aug-24 A			
CON-EIT3060	Sub-System 82-50 | Electrical - Equipment Arrival	0d	0d	30-Jul-24 A				
CON-EIT3090	Sub-System 82-50 | Electrical - Mechanical Completion	5d	49d	09-Sep-24 A	05-Nov-24			102d
CON-EIT3050	Sub-System 82-50 | Electrical - Cable Pulling	7d	25d	07-Oct-24 A	05-Nov-24			102d
CON-EIT3070	Sub-System 82-50 | Electrical - Cable Termination	3d	3d	02-Nov-24	05-Nov-24			102d
CON-EIT3100	Sub-System 82-50 | Electrical - RFCC	0d	0d		05-Nov-24			102d
E.25 Sub-System 81-00 | 66 kV Subsea Cable		15d	15d	27-Feb-25	15-Mar-25			3d
CON-EIT3110	Sub-System 81-00 | Electrical - Cable Pulling	5d	5d	27-Feb-25	04-Mar-25			3d
CON-EIT3120	Sub-System 81-00 | Electrical - Equipment Arrival	0d	0d	27-Feb-25				3d
CON-EIT3140	Sub-System 81-00 | Electrical - Item Installation	4d	4d	05-Mar-25	08-Mar-25			3d
CON-EIT3130	Sub-System 81-00 | Electrical - Cable Termination	2d	2d	10-Mar-25	11-Mar-25			3d
CON-EIT3150	Sub-System 81-00 | Electrical - Mechanical Completion	4d	4d	12-Mar-25	15-Mar-25			3d
CON-EIT3160	Sub-System 81-00 | Electrical - RFCC	0d	0d		15-Mar-25			3d
M.01 Sub-System 90-02 | LV Switchgear Room B-200		133d	140d	26-Jul-24 A	11-Jan-25			56d

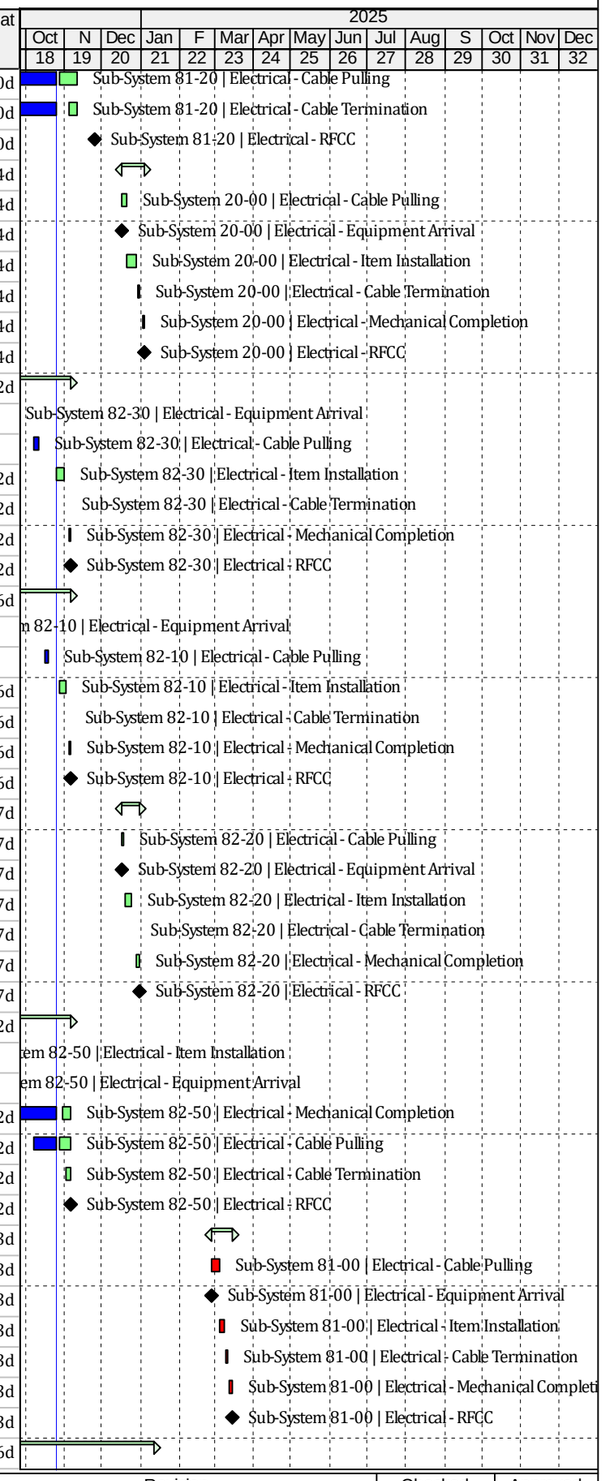

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT3180	Sub-System 90-02 | Electrical - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT3200	Sub-System 90-02 | Electrical - Item Installation (MCT)	7d	139d	27-Jul-24 A	11-Jan-25			56d
CON-EIT3170	Sub-System 90-02 | Electrical - Cable Pulling DELETED	3d	3d	12-Sep-24 A	14-Sep-24 A			
CON-EIT3190	Sub-System 90-02 | Electrical - Cable Termination DELETED	2d	1d	16-Sep-24 A	17-Sep-24 A			
CON-EIT3210	Sub-System 90-02 | Electrical - Mechanical Completion	3d	85d	30-Sep-24 A	11-Jan-25			56d
CON-EIT3220	Sub-System 90-02 | Electrical - RFCC	0d	0d		11-Jan-25			56d
M.02 Sub-System 90-03 | UPS System Equipment Room B-300		130d	129d	30-Jul-24 A	31-Dec-24			64d
CON-EIT3240	Sub-System 90-03 | Electrical - Equipment Arrival	0d	0d	30-Jul-24 A				
CON-EIT3260	Sub-System 90-03 | Electrical - Item Installation	1d	50d	31-Jul-24 A	27-Sep-24 A			
CON-EIT3230	Sub-System 90-03 | Electrical - Cable Pulling DELETED	3d	3d	12-Sep-24 A	14-Sep-24 A			
CON-EIT3250	Sub-System 90-03 | Electrical - Cable Termination DELETED	2d	1d	16-Sep-24 A	17-Sep-24 A			
CON-EIT3270	Sub-System 90-03 | Electrical - Mechanical Completion	2d	77d	30-Sep-24 A	31-Dec-24			64d
CON-EIT3280	Sub-System 90-03 | Electrical - RFCC	0d	0d		31-Dec-24			64d
M.03 Sub-System 90-01 | HV-MV Switchgear Room B-100		125d	132d	26-Jul-24 A	31-Dec-24			64d
CON-EIT3300	Sub-System 90-01 | Electrical - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT3320	Sub-System 90-01 | Electrical - Item Installation	9d	59d	27-Jul-24 A	04-Oct-24 A			
CON-EIT3290	Sub-System 90-01 | Electrical - Cable Pulling DELETED	3d	3d	12-Sep-24 A	14-Sep-24 A			
CON-EIT3310	Sub-System 90-01 | Electrical - Cable Termination DELETED	2d	1d	16-Sep-24 A	17-Sep-24 A			
CON-EIT3330	Sub-System 90-01 | Electrical - Mechanical Completion	5d	65d	14-Oct-24 A	31-Dec-24			64d
CON-EIT3340	Sub-System 90-01 | Electrical - RFCC	0d	0d		31-Dec-24			64d
M.04 Sub-System 90-04 | I&T System Equipment Room B-400		133d	134d	02-Aug-24 A	11-Jan-25			56d
CON-EIT3360	Sub-System 90-04 | Electrical - Equipment Arrival	0d	0d	02-Aug-24 A				
CON-EIT3380	Sub-System 90-04 | Electrical - Item Installation	5d	133d	03-Aug-24 A	11-Jan-25			56d
CON-EIT3350	Sub-System 90-04 | Electrical - Cable Pulling DELETED	3d	2d	12-Sep-24 A	14-Sep-24 A			
CON-EIT3370	Sub-System 90-04 | Electrical - Cable Termination DELETED	2d	1d	16-Sep-24 A	17-Sep-24 A			
CON-EIT3390	Sub-System 90-04 | Electrical - Mechanical Completion	2d	85d	30-Sep-24 A	11-Jan-25			56d
CON-EIT3400	Sub-System 90-04 | Electrical - RFCC	0d	0d		11-Jan-25			56d
H.01 Sub-System 77-20 | HVAC LV Switchgear Room B-200		74d	81d	26-Jul-24 A	29-Oct-24			117d
CON-EIT3420	Sub-System 77-20 | Electrical - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT3410	Sub-System 77-20 | Electrical - Cable Pulling	1d	28d	18-Sep-24 A	19-Oct-24 A			
CON-EIT3430	Sub-System 77-20 | Electrical - Cable Termination	1d	21d	26-Sep-24 A	19-Oct-24 A			
CON-EIT3440	Sub-System 77-20 | Electrical - Item Installation	1d	5d	30-Sep-24 A	04-Oct-24 A			
CON-EIT3450	Sub-System 77-20 | Electrical - Mechanical Completion	2d	20d	07-Oct-24 A	29-Oct-24			117d
CON-EIT3460	Sub-System 77-20 | Electrical - RFCC	0d	0d		29-Oct-24			117d
H.02 Sub-System 77-30 | HVAC UPS Equipment Room B-300		74d	79d	29-Jul-24 A	29-Oct-24			117d
CON-EIT3480	Sub-System 77-30 | Electrical - Equipment Arrival	0d	0d	29-Jul-24 A				
CON-EIT3470	Sub-System 77-30 | Electrical - Cable Pulling	2d	18d	30-Sep-24 A	19-Oct-24 A			
CON-EIT3490	Sub-System 77-30 | Electrical - Cable Termination	1d	18d	30-Sep-24 A	19-Oct-24 A			
CON-EIT3500	Sub-System 77-30 | Electrical - Item Installation	1d	5d	30-Sep-24 A	04-Oct-24 A			
CON-EIT3510	Sub-System 77-30 | Electrical - Mechanical Completion	2d	20d	07-Oct-24 A	29-Oct-24			117d
CON-EIT3520	Sub-System 77-30 | Electrical - RFCC	0d	0d		29-Oct-24			117d
H.03 Sub-System 77-10 | HVAC HV/MV Switchgear Room B-100		74d	81d	26-Jul-24 A	29-Oct-24			117d
CON-EIT3540	Sub-System 77-10 | Electrical - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT3530	Sub-System 77-10 | Electrical - Cable Pulling	3d	12d	30-Sep-24 A	12-Oct-24 A			
CON-EIT3560	Sub-System 77-10 | Electrical - Item Installation	1d	5d	30-Sep-24 A	04-Oct-24 A			
CON-EIT3550	Sub-System 77-10 | Electrical - Cable Termination	1d	11d	14-Oct-24 A	25-Oct-24 A			

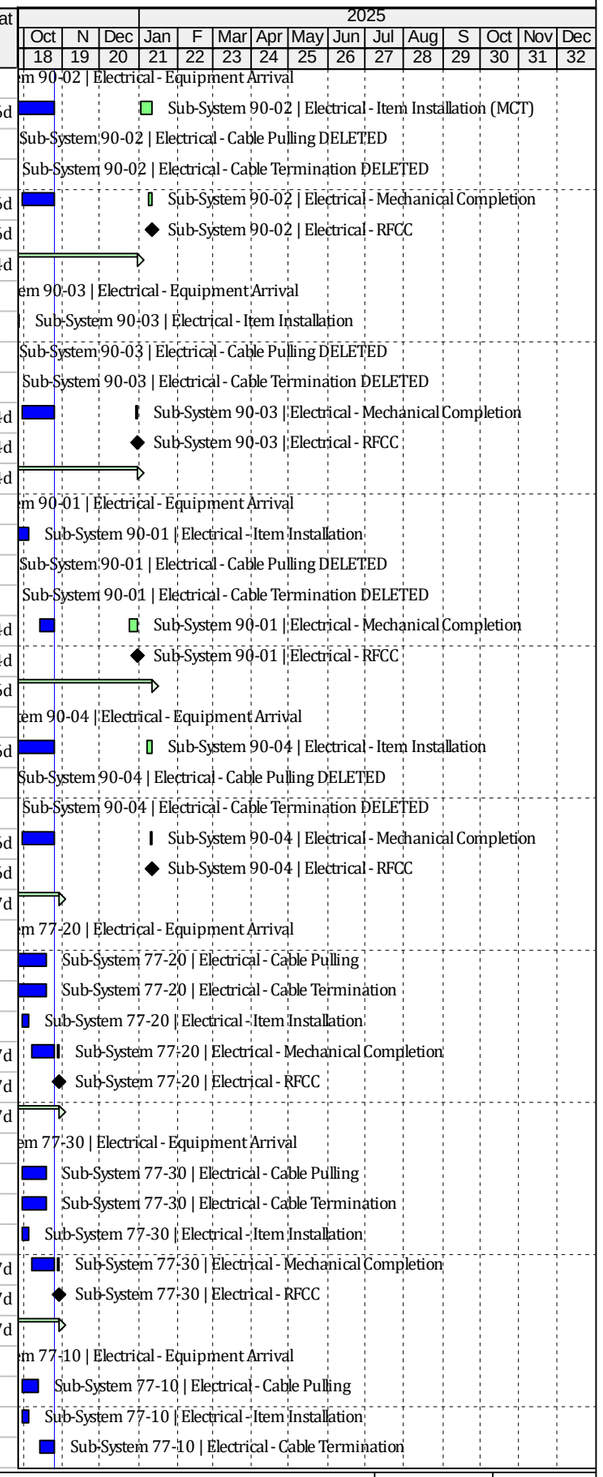

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT3570	Sub-System 77-10 | Electrical - Mechanical Completion	2d	13d	15-Oct-24 A	29-Oct-24			117d
CON-EIT3580	Sub-System 77-10 | Electrical - RFCC	0d	0d		29-Oct-24			117d
L04 Sub-System 77-40 | HVAC I&T Equipment Room B-400		74d	75d	02-Aug-24 A	29-Oct-24			117d
CON-EIT3600	Sub-System 77-40 | Electrical - Equipment Arrival	0d	0d	02-Aug-24 A				
CON-EIT3590	Sub-System 77-40 | Electrical - Cable Pulling	2d	17d	30-Sep-24 A	18-Oct-24 A			
CON-EIT3620	Sub-System 77-40 | Electrical - Item Installation	1d	5d	30-Sep-24 A	04-Oct-24 A			
CON-EIT3610	Sub-System 77-40 | Electrical - Cable Termination	1d	19d	07-Oct-24 A	28-Oct-24			118d
CON-EIT3630	Sub-System 77-40 | Electrical - Mechanical Completion	2d	14d	14-Oct-24 A	29-Oct-24			117d
CON-EIT3640	Sub-System 77-40 | Electrical - RFCC	0d	0d		29-Oct-24			117d
L01 Sub-System 87-10 | Process Control System (PCS)		13d	29d	30-Sep-24 A	02-Nov-24			86d
CON-EIT3650	Sub-System 87-10 | Electrical - Cable Pulling	3d	27d	30-Sep-24 A	30-Oct-24			86d
CON-EIT3670	Sub-System 87-10 | Electrical - Cable Termination	1d	11d	18-Oct-24 A	30-Oct-24			86d
CON-EIT3660	Sub-System 87-10 | Electrical - Equipment Arrival	0d	0d	18-Oct-24 A				
CON-EIT3690	Sub-System 87-10 | Electrical - Mechanical Completion	2d	2d	31-Oct-24	02-Nov-24			86d
CON-EIT3700	Sub-System 87-10 | Electrical - RFCC	0d	0d		02-Nov-24			86d
L02 Sub-System 79-00 | Emergency Shutdown Systems (SIS)		15d	27d	30-Sep-24 A	30-Oct-24			95d
CON-EIT3710	Sub-System 79-00 | Electrical - Cable Pulling	3d	12d	30-Sep-24 A	12-Oct-24 A			
CON-EIT3730	Sub-System 79-00 | Electrical - Cable Termination	1d	9d	18-Oct-24 A	28-Oct-24			95d
CON-EIT3720	Sub-System 79-00 | Electrical - Equipment Arrival	0d	0d	26-Oct-24				97d
CON-EIT3750	Sub-System 79-00 | Electrical - Mechanical Completion	2d	2d	29-Oct-24	30-Oct-24			95d
CON-EIT3760	Sub-System 79-00 | Electrical - RFCC	0d	0d		30-Oct-24			95d
L03 Sub-System 70-00 | F&G Control System		11d	29d	30-Sep-24 A	02-Nov-24			75d
CON-EIT3770	Sub-System 70-00 | Electrical - Cable Pulling	3d	27d	30-Sep-24 A	30-Oct-24			75d
CON-EIT3790	Sub-System 70-00 | Electrical - Cable Termination	1d	12d	17-Oct-24 A	30-Oct-24			75d
CON-EIT3780	Sub-System 70-00 | Electrical - Equipment Arrival	0d	0d	26-Oct-24				79d
CON-EIT3810	Sub-System 70-00 | Electrical - Mechanical Completion	2d	2d	31-Oct-24	02-Nov-24			75d
CON-EIT3820	Sub-System 70-00 | Electrical - RFCC	0d	0d		02-Nov-24			75d
L04 Sub-System 86-00 | Data Networks		14d	32d	30-Sep-24 A	06-Nov-24			72d
CON-EIT3830	Sub-System 86-00 | Electrical - Cable Pulling	5d	29d	30-Sep-24 A	02-Nov-24			72d
CON-EIT3850	Sub-System 86-00 | Electrical - Cable Termination	1d	14d	17-Oct-24 A	02-Nov-24			72d
CON-EIT3840	Sub-System 86-00 | Electrical - Equipment Arrival	0d	0d	26-Oct-24				78d
CON-EIT3870	Sub-System 86-00 | Electrical - Mechanical Completion	3d	3d	04-Nov-24	06-Nov-24			72d
CON-EIT3880	Sub-System 86-00 | Electrical - RFCC	0d	0d		06-Nov-24			72d
L05 Sub-System 87-00 | Power Distribution System (EMCS)		11d	29d	30-Sep-24 A	02-Nov-24			73d
CON-EIT3890	Sub-System 87-00 | Electrical - Cable Pulling	3d	27d	30-Sep-24 A	30-Oct-24			73d
CON-EIT3910	Sub-System 87-00 | Electrical - Cable Termination	1d	11d	18-Oct-24 A	30-Oct-24			73d
CON-EIT3900	Sub-System 87-00 | Electrical - Equipment Arrival	0d	0d	26-Oct-24				77d
CON-EIT3930	Sub-System 87-00 | Electrical - Mechanical Completion	2d	2d	31-Oct-24	02-Nov-24			73d
CON-EIT3940	Sub-System 87-00 | Electrical - RFCC	0d	0d		02-Nov-24			73d
M.05 Sub-System 63-00 | Instrument Air Package (A-63000)		11d	11d	02-Nov-24	14-Nov-24			78d
CON-EIT4370	Sub-System 63-00 | Electrical - Cable Pulling	3d	3d	02-Nov-24	05-Nov-24			78d
CON-EIT4380	Sub-System 63-00 | Electrical - Equipment Arrival	0d	0d	02-Nov-24				78d
CON-EIT9110	Sub-System 63-00 | Electrical - Item Installation	5d	5d	06-Nov-24	11-Nov-24			78d
CON-EIT4390	Sub-System 63-00 | Electrical - Cable Termination	1d	1d	12-Nov-24	12-Nov-24			78d
CON-EIT4410	Sub-System 63-00 | Electrical - Mechanical Completion	2d	2d	13-Nov-24	14-Nov-24			78d
CON-EIT4420	Sub-System 63-00 | Electrical - RFCC	0d	0d		14-Nov-24			78d

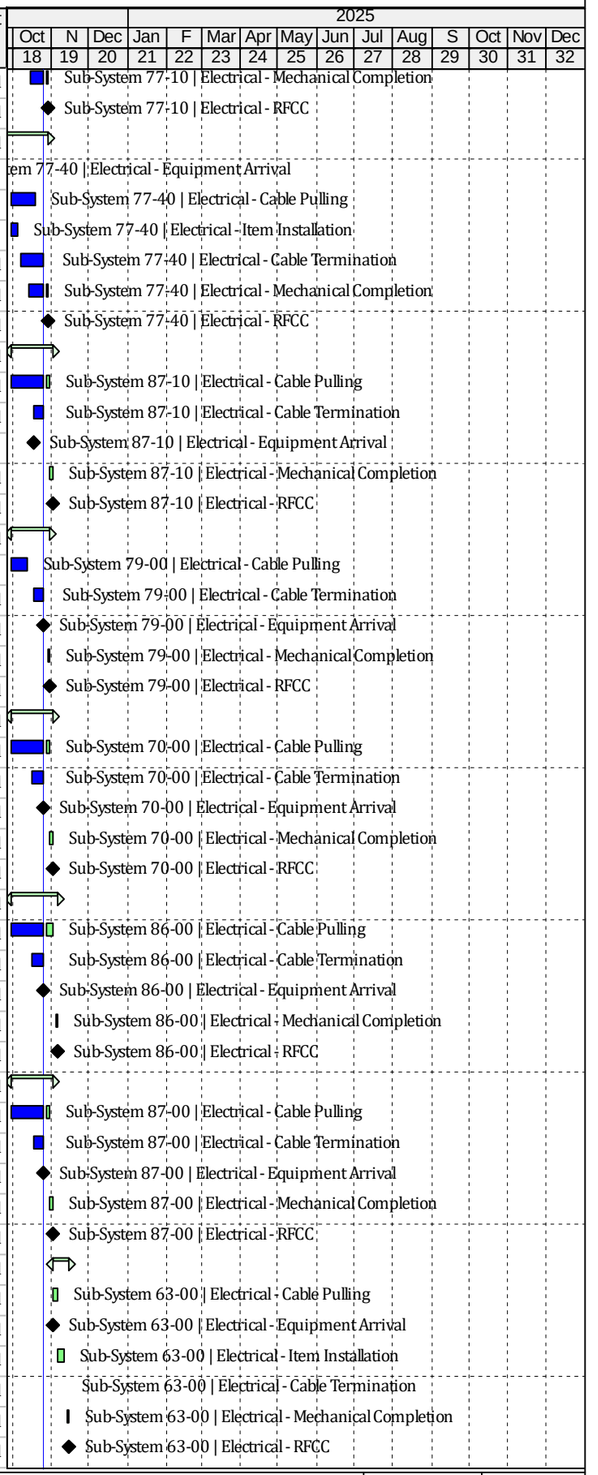

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
M.06 Sub-System 64-00 | Nitrogen Generator Package (U-6400)		10d	10d	04-Nov-24	14-Nov-24			82d
CON-EIT4430	Sub-System 64-00 | Electrical - Cable Pulling	2d	2d	04-Nov-24	05-Nov-24			82d
CON-EIT4440	Sub-System 64-00 | Electrical - Equipment Arrival	0d	0d	04-Nov-24				82d
CON-EIT9120	Sub-System 63-00 | Electrical - Item Installation	5d	5d	06-Nov-24	11-Nov-24			82d
CON-EIT4450	Sub-System 64-00 | Electrical - Cable Termination	1d	1d	12-Nov-24	12-Nov-24			82d
CON-EIT4470	Sub-System 64-00 | Electrical - Mechanical Completion	2d	2d	13-Nov-24	14-Nov-24			82d
CON-EIT4480	Sub-System 64-00 | Electrical - RFCC	0d	0d		14-Nov-24			82d
M.09 Sub-System 50-00 | Seawater Intake System (Lifting Pumps)		3d	56d	18-Oct-24 A	23-Dec-24			70d
CON-EIT4610	Sub-System 50-00 | Electrical - Cable Pulling	2d	54d	18-Oct-24 A	20-Dec-24			70d
CON-EIT4630	Sub-System 50-00 | Electrical - Cable Termination	1d	54d	18-Oct-24 A	20-Dec-24			70d
CON-EIT4650	Sub-System 50-00 | Electrical - Mechanical Completion	2d	2d	21-Dec-24	23-Dec-24			70d
CON-EIT4620	Sub-System 50-00 | Electrical - Equipment Arrival	0d	0d	21-Dec-24				70d
CON-EIT4660	Sub-System 50-00 | Electrical - RFCC	0d	0d		23-Dec-24			70d
M.10 Sub-System 50-10 | Water Desalination Package		4d	14d	21-Oct-24 A	06-Nov-24			96d
CON-EIT4690	Sub-System 50-10 | Electrical - Cable Termination	1d	12d	21-Oct-24 A	04-Nov-24			96d
CON-EIT4670	Sub-System 50-10 | Electrical - Cable Pulling	1d	1d	02-Nov-24	02-Nov-24			96d
CON-EIT4680	Sub-System 50-10 | Electrical - Equipment Arrival	0d	0d	02-Nov-24				96d
CON-EIT4700	Sub-System 50-10 | Electrical - Item Installation	1d	1d	04-Nov-24	04-Nov-24			96d
CON-EIT4710	Sub-System 50-10 | Electrical - Mechanical Completion	2d	2d	05-Nov-24	06-Nov-24			96d
CON-EIT4720	Sub-System 50-10 | Electrical - RFCC	0d	0d		06-Nov-24			96d
M.11 Sub-System 50-20 | Water Distribution Network		70d	70d	02-Nov-24	27-Jan-25			31d
CON-EIT4740	Sub-System 50-20 | Electrical - Equipment Arrival	0d	0d	02-Nov-24				85d
CON-EIT4730	Sub-System 50-20 | Electrical - Cable Pulling	3d	3d	09-Jan-25	11-Jan-25			31d
CON-EIT4760	Sub-System 50-20 | Electrical - Item Installation	4d	4d	13-Jan-25	16-Jan-25			31d
CON-EIT4750	Sub-System 50-20 | Electrical - Cable Termination	2d	2d	17-Jan-25	18-Jan-25			31d
CON-EIT4770	Sub-System 50-20 | Electrical - Mechanical Completion	7d	7d	20-Jan-25	27-Jan-25			31d
CON-EIT4780	Sub-System 50-20 | Electrical - RFCC	0d	0d		27-Jan-25			31d
M.14 Sub-System 99-00 | Crane		7d	7d	21-Dec-24	31-Dec-24			64d
CON-EIT4910	Sub-System 99-00 | Electrical - Cable Pulling	3d	3d	21-Dec-24	24-Dec-24			64d
CON-EIT4920	Sub-System 99-00 | Electrical - Equipment Arrival	0d	0d	21-Dec-24				64d
CON-EIT4940	Sub-System 99-00 | Electrical - Item Installation -	1d	1d	27-Dec-24	27-Dec-24			64d
CON-EIT4930	Sub-System 99-00 | Electrical - Cable Termination	1d	1d	28-Dec-24	28-Dec-24			64d
CON-EIT4950	Sub-System 99-00 | Electrical - Mechanical Completion	2d	2d	30-Dec-24	31-Dec-24			64d
CON-EIT4960	Sub-System 99-00 | Electrical - RFCC	0d	0d		31-Dec-24			64d
M.17 Sub-System 43-00 | Hydrogen Vent Header & Drum System		17d	17d	26-Oct-24	15-Nov-24			89d
CON-EIT5100	Sub-System 43-00 | Electrical - Equipment Arrival	0d	0d	26-Oct-24				90d
CON-EIT5090	Sub-System 43-00 | Electrical - Cable Pulling	3d	3d	28-Oct-24	30-Oct-24			89d
CON-EIT5120	Sub-System 43-00 | Electrical - Item Installation	4d	4d	31-Oct-24	05-Nov-24			89d
CON-EIT5110	Sub-System 43-00 | Electrical - Cable Termination	2d	2d	06-Nov-24	07-Nov-24			89d
CON-EIT5130	Sub-System 43-00 | Electrical - Mechanical Completion	7d	7d	08-Nov-24	15-Nov-24			89d
CON-EIT5140	Sub-System 43-00 | Electrical - RFCC	0d	0d		15-Nov-24			89d
Sub-System 87-20 | Process Control System (PCS) - Instrumentation		9d	23d	12-Oct-24 A	08-Nov-24			101d
CON-EIT8870	Sub-System 87-20 | Electrical - Cable Pulling - DELETED	3d	3d	12-Oct-24 A	15-Oct-24 A			
CON-EIT8880	Sub-System 87-20 | Electrical - Cable Termination - DELETED	2d	2d	16-Oct-24 A	17-Oct-24 A			
CON-EIT8890	Sub-System 87-20 | Electrical - Item Installation - DELETED	4d	11d	18-Oct-24 A	30-Oct-24			101d
CON-EIT8920	Sub-System 87-20 | Electrical - Equipment Arrival	0d	0d	18-Oct-24 A				

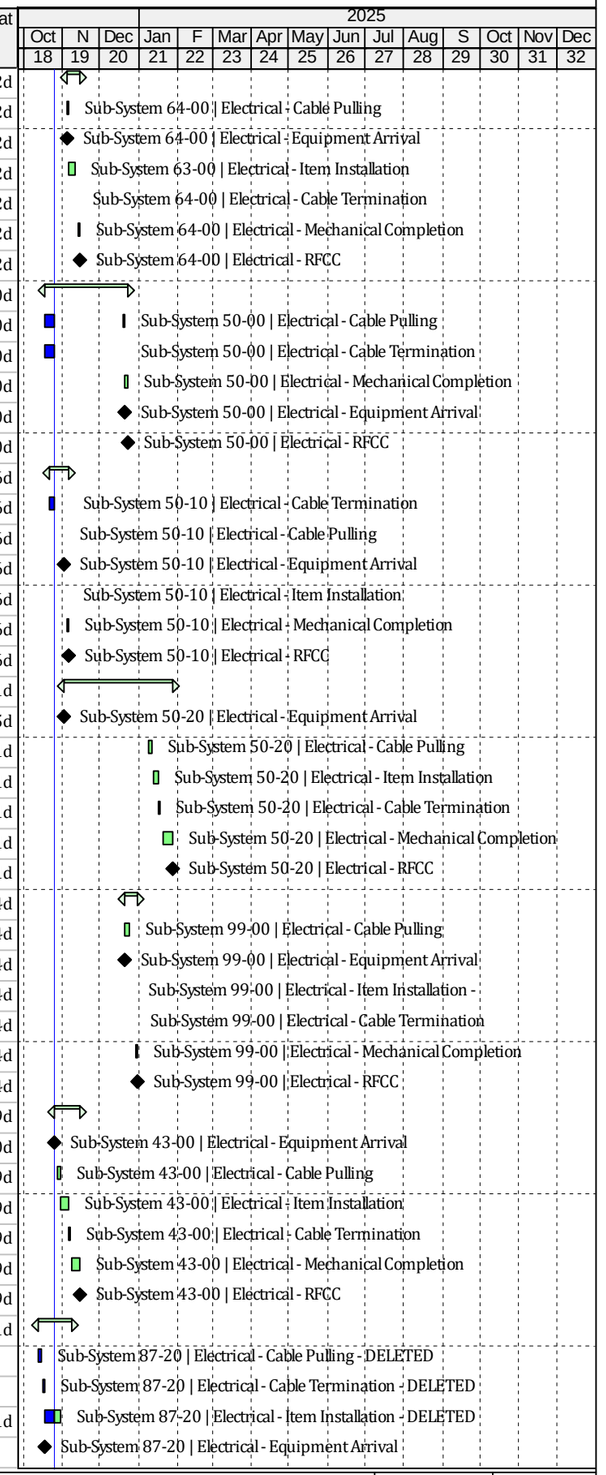

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT8900	Sub-System 87-20 | Electrical - Mechanical Completion	7d	7d	31-Oct-24	08-Nov-24			101d
CON-EIT8910	Sub-System 87-20 | Electrical - RFCC	0d	0d		08-Nov-24			101d
Sub-System 79-10 | Emergency Shutdown Systems (SIS) - Devices		11d	24d	12-Oct-24 A	09-Nov-24			100d
CON-EIT8930	Sub-System 79-10 | Electrical - Cable Pulling - DELETED	3d	3d	12-Oct-24 A	15-Oct-24 A			
CON-EIT8940	Sub-System 79-10 | Electrical - Cable Termination - DELETED	2d	2d	16-Oct-24 A	17-Oct-24 A			
CON-EIT8980	Sub-System 79-10 | Electrical - Equipment Arrival	0d	0d	18-Oct-24 A				
CON-EIT8950	Sub-System 79-10 | Electrical - Item Installation	4d	10d	21-Oct-24 A	31-Oct-24			100d
CON-EIT8960	Sub-System 79-10 | Electrical - Mechanical Completion	7d	7d	02-Nov-24	09-Nov-24			100d
CON-EIT8970	Sub-System 79-10 | Electrical - RFCC	0d	0d		09-Nov-24			100d
Instrumentation		152d	151d	22-Jul-24 A	20-Jan-25	27-Aug-24	03-Dec-24	236d
CON-EIT1620	Instrument & Control Cables - Pulling & Dressing (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	40d	1d	23-Aug-24 A	23-Aug-24 A	25-Sep-24	11-Nov-24	
Lower Deck		122d	113d	19-Aug-24 A	31-Dec-24	27-Aug-24	03-Dec-24	68d
CON-EIT1370	Instrument & Control Cable Trays - Installation - Lower Deck	27d	86d	19-Aug-24 A	27-Nov-24	27-Aug-24	26-Sep-24	46d
CON-EIT1380	Instrument & Control Equipment - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2	24d	1d	23-Aug-24 A	23-Aug-24 A	13-Sep-24	10-Oct-24	
CON-EIT1390	Instrument & Control Junction Boxes - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUS	17d	1d	23-Aug-24 A	23-Aug-24 A	27-Sep-24	16-Oct-24	
CON-EIT1400	Instrument & Control Cable Termination, Glanding & Connection - Installation - Lower Deck (DELETED AFTER I	11d	1d	23-Aug-24 A	23-Aug-24 A	12-Oct-24	22-Nov-24	
CON-EIT1410	Instrument & F&G Devices - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	21d	1d	23-Aug-24 A	23-Aug-24 A	09-Nov-24	03-Dec-24	
CON-EIT9020	Instrument & Control MCT - Installation - Lower Deck	27d	71d	07-Oct-24 A	31-Dec-24			61d
CON-EIT1420	Tubing - Installation - Lower Deck	18d	18d	20-Nov-24	10-Dec-24	15-Oct-24	05-Nov-24	77d
Upper Deck		136d	133d	29-Jul-24 A	04-Jan-25	10-Sep-24	03-Dec-24	65d
CON-EIT1430	Instrument & Control Cable Trays - Installation - Upper Deck	27d	89d	29-Jul-24 A	11-Nov-24	10-Sep-24	10-Oct-24	77d
CON-EIT1440	Instrument & Control Equipment - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2	22d	1d	23-Aug-24 A	23-Aug-24 A	13-Sep-24	10-Oct-24	
CON-EIT1450	Instrument & Control Junction Boxes - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUS	17d	1d	23-Aug-24 A	23-Aug-24 A	11-Oct-24	30-Oct-24	
CON-EIT1460	Instrument & Control Cable Termination, Glanding & Connection - Installation - Upper Deck (DELETED AFTER I	35d	1d	23-Aug-24 A	23-Aug-24 A	23-Oct-24	03-Dec-24	
CON-EIT1470	Instrument & F&G Devices - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	21d	1d	23-Aug-24 A	23-Aug-24 A	09-Nov-24	03-Dec-24	
CON-EIT1480	Tubing - Installation - Upper Deck	18d	18d	20-Nov-24	10-Dec-24	06-Nov-24	26-Nov-24	77d
CON-EIT9030	Instrument & Control MCT - Installation - Upper Deck	27d	27d	02-Dec-24*	04-Jan-25			58d
Vessel Rack		88d	124d	29-Jul-24 A	21-Dec-24	11-Oct-24	03-Dec-24	74d
CON-EIT1490	Instrument & Control Cable Trays - Installation - Vessel Rack/Transition Piece	18d	90d	29-Jul-24 A	12-Nov-24	11-Oct-24	31-Oct-24	71d
CON-EIT1500	Instrument & Control Equipment - Installation - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST 2(	15d	1d	23-Aug-24 A	23-Aug-24 A	15-Oct-24	31-Oct-24	
CON-EIT1510	Instrument & Control Junction Boxes - Installation - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST	12d	1d	23-Aug-24 A	23-Aug-24 A	02-Nov-24	15-Nov-24	
CON-EIT1520	Instrument & Control Cable Termination, Glanding & Connection - Installation - Vessel Rack (DELETED AFTER R	15d	1d	23-Aug-24 A	23-Aug-24 A	13-Nov-24	29-Nov-24	
CON-EIT1530	Instrument & F&G Devices - Installation - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	16-Nov-24	03-Dec-24	
CON-EIT1540	Tubing - Installation - Vessel Rack	12d	12d	20-Nov-24	03-Dec-24	06-Nov-24	19-Nov-24	83d
CON-EIT9040	Instrument & Control MCT - Installation - Vessel Rack/Transition Piece	18d	18d	02-Dec-24*	21-Dec-24			67d
E.01 Sub-System 83-00 | 400 V Switchboard & Connection Box (SG-200N1)		50d	69d	07-Aug-24 A	26-Oct-24			50d
CON-EIT5310	Sub-System 83-00 | Instrumental - Equipment Arrival	0d	0d	07-Aug-24 A				
CON-EIT5210	Sub-System 83-00 | Instrumental - Cable Pulling	1d	11d	07-Oct-24 A	18-Oct-24 A			
CON-EIT5240	Sub-System 83-00 | Instrumental - Mechanical Completion	1d	6d	21-Oct-24 A	26-Oct-24			50d
CON-EIT5220	Sub-System 83-00 | Instrumental - Cable Termination	1d	1d	26-Oct-24	26-Oct-24			50d
CON-EIT5250	Sub-System 83-00 | Instrumental - RFCC	0d	0d		26-Oct-24			50d
E.02 Sub-System 84-10 | AC 35 kVA UPS System (UP-200F3)		15d	17d	10-Oct-24 A	29-Oct-24			55d
CON-EIT5320	Sub-System 84-10 | Instrumental - Equipment Arrival	0d	0d	10-Oct-24 A				
CON-EIT5260	Sub-System 84-10 | Instrumental - Cable Pulling	2d	6d	12-Oct-24 A	18-Oct-24 A			
CON-EIT5270	Sub-System 84-10 | Instrumental - Cable Termination	1d	1d	26-Oct-24	26-Oct-24			55d
CON-EIT5290	Sub-System 84-10 | Instrumental - Mechanical Completion	2d	2d	28-Oct-24	29-Oct-24			55d

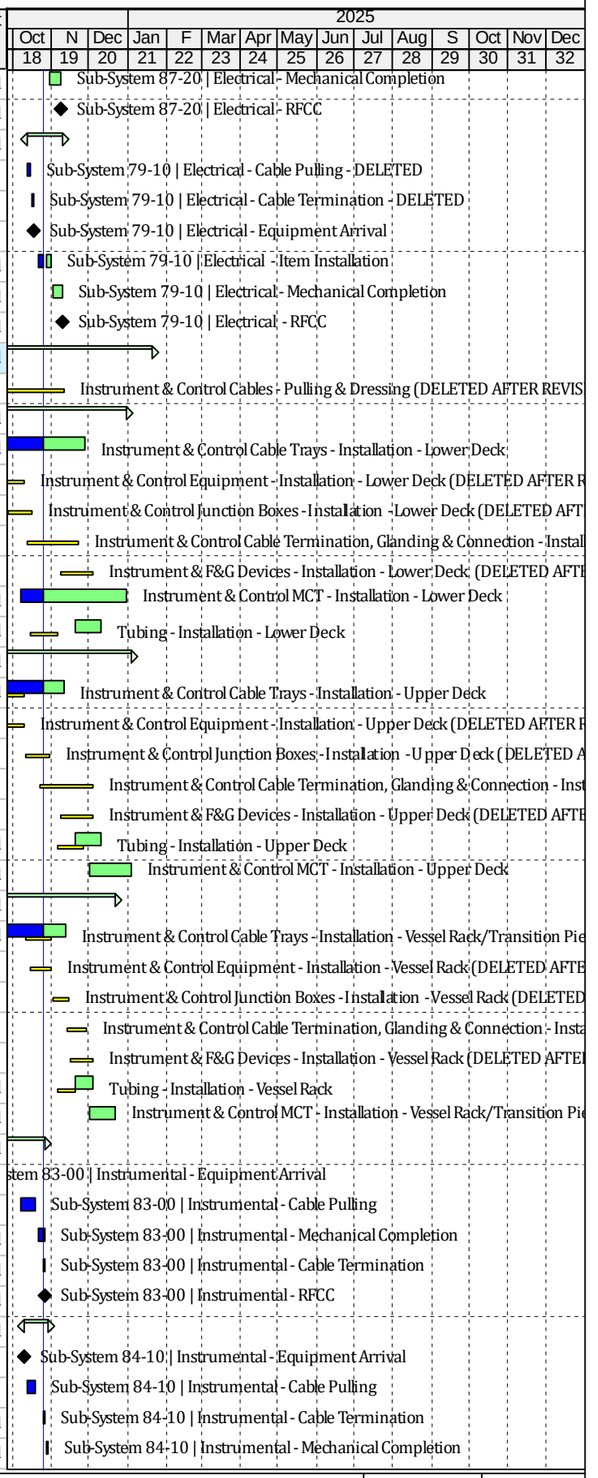

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT5300	Sub-System 84-10 | Instrumental - RFCC	0d	0d		29-Oct-24			55d
E.03 Sub-System 84-20 | AC 15 kVA UPS System (UP-200F4)		16d	20d	07-Oct-24 A	29-Oct-24			87d
CON-EIT5390	Sub-System 84-20 | Instrumental - Cable Pulling	2d	11d	07-Oct-24 A	18-Oct-24 A			
CON-EIT5440	Sub-System 84-20 | Instrumental - Equipment Arrival	0d	0d	08-Oct-24 A				
CON-EIT5400	Sub-System 84-20 | Instrumental - Cable Termination	1d	1d	26-Oct-24	26-Oct-24			87d
CON-EIT5420	Sub-System 84-20 | Instrumental - Mechanical Completion	2d	2d	28-Oct-24	29-Oct-24			87d
CON-EIT5430	Sub-System 84-20 | Instrumental - RFCC	0d	0d		29-Oct-24			87d
E.04 Sub-System 84-00 | DC 10 kVA UPS System (UP-200F1)		44d	75d	01-Aug-24 A	28-Oct-24			88d
CON-EIT5500	Sub-System 84-00 | Instrumental - Equipment Arrival	0d	0d	01-Aug-24 A				
CON-EIT5450	Sub-System 84-00 | Instrumental - Cable Pulling	7d	27d	18-Sep-24 A	18-Oct-24 A			
CON-EIT5460	Sub-System 84-00 | Instrumental - Cable Termination	1d	1d	26-Oct-24	26-Oct-24			88d
CON-EIT5480	Sub-System 84-00 | Instrumental - Mechanical Completion	1d	1d	28-Oct-24	28-Oct-24			88d
CON-EIT5490	Sub-System 84-00 | Instrumental - RFCC	0d	0d		28-Oct-24			88d
E.05 Sub-System 82-00 | MV 6.6 kV Switchboard (SG-100D1)		45d	71d	07-Aug-24 A	29-Oct-24			91d
CON-EIT5560	Sub-System 82-00 | Instrumental - Equipment Arrival	0d	0d	07-Aug-24 A				
CON-EIT5510	Sub-System 82-00 | Instrumental - Cable Pulling	4d	27d	18-Sep-24 A	18-Oct-24 A			
CON-EIT5520	Sub-System 82-00 | Instrumental - Cable Termination	1d	27d	26-Sep-24 A	26-Oct-24			91d
CON-EIT5540	Sub-System 82-00 | Instrumental - Mechanical Completion	2d	2d	28-Oct-24	29-Oct-24			91d
CON-EIT5550	Sub-System 82-00 | Instrumental - RFCC	0d	0d		29-Oct-24			91d
E.06 Sub-System 82-40 | Power Transformer 1.6 MVA (TR-200DE1)		84d	87d	31-Jul-24 A	11-Nov-24			97d
CON-EIT5620	Sub-System 82-40 | Instrumental - Equipment Arrival	0d	0d	31-Jul-24 A				
CON-EIT5590	Sub-System 82-40 | Instrumental - Item Installation	4d	33d	01-Aug-24 A	09-Sep-24 A			
CON-EIT5570	Sub-System 82-40 | Instrumental - Cable Pulling - DELETED	8d	8d	31-Aug-24 A	09-Sep-24 A			
CON-EIT5580	Sub-System 82-40 | Instrumental - Cable Termination - DELETED	5d	5d	11-Sep-24 A	16-Sep-24 A			
CON-EIT5600	Sub-System 82-40 | Instrumental - Mechanical Completion	12d	12d	28-Oct-24	11-Nov-24			97d
CON-EIT5610	Sub-System 82-40 | Instrumental - RFCC	0d	0d		11-Nov-24			97d
E.08 Sub-System 81-10 | GIS 66 kV (HNA6-AFA70)		4d	4d	16-Jan-25	20-Jan-25			47d
CON-EIT5630	Sub-System 81-10 | Instrumental - Cable Pulling	2d	2d	16-Jan-25	17-Jan-25			47d
CON-EIT5680	Sub-System 81-10 | Instrumental - Equipment Arrival	0d	0d	16-Jan-25				47d
CON-EIT5640	Sub-System 81-10 | Instrumental - Cable Termination	1d	1d	18-Jan-25	18-Jan-25			47d
CON-EIT5660	Sub-System 81-10 | Instrumental - Mechanical Completion	1d	1d	20-Jan-25	20-Jan-25			47d
CON-EIT5670	Sub-System 81-10 | Instrumental - RFCC	0d	0d		20-Jan-25			47d
E.09 Sub-System 83-20 | 400/230 V Switchboard (DP-200N1)		36d	40d	24-Sep-24 A	09-Nov-24			46d
CON-EIT5740	Sub-System 83-20 | Instrumental - Equipment Arrival	0d	0d	24-Sep-24 A				
CON-EIT5690	Sub-System 83-20 | Instrumental - Cable Pulling - DELETED, NO INSTRUMENTAL SCOPE	8d	8d	28-Sep-24 A	07-Oct-24 A			
CON-EIT5710	Sub-System 83-20 | Instrumental - Item Installation - DELETED, NO INSTRUMENTAL SCOPE	4d	4d	08-Oct-24 A	11-Oct-24 A			
CON-EIT5700	Sub-System 83-20 | Instrumental - Cable Termination - DELETED, NO INSTRUMENTAL SCOPE	5d	6d	21-Oct-24 A	28-Oct-24			46d
CON-EIT5720	Sub-System 83-20 | Instrumental - Mechanical Completion	12d	12d	26-Oct-24	09-Nov-24			46d
CON-EIT5730	Sub-System 83-20 | Instrumental - RFCC	0d	0d		09-Nov-24			46d
E.10 Sub-System 80-00 | Hydrogen Fuel Cell Package (A-80000)		19d	36d	18-Sep-24 A	29-Oct-24			100d
CON-EIT5800	Sub-System 80-00 | Instrumental - Equipment Arrival	0d	0d	18-Sep-24 A				
CON-EIT5750	Sub-System 80-00 | Instrumental - Cable Pulling	1d	11d	07-Oct-24 A	18-Oct-24 A			
CON-EIT5760	Sub-System 80-00 | Instrumental - Cable Termination	1d	1d	26-Oct-24	26-Oct-24			100d
CON-EIT5780	Sub-System 80-00 | Instrumental - Mechanical Completion	2d	2d	28-Oct-24	29-Oct-24			100d
CON-EIT5790	Sub-System 80-00 | Instrumental - RFCC	0d	0d		29-Oct-24			100d
E.11 Sub-System 85-00 | BESS Package (A-85000)		74d	85d	22-Jul-24 A	29-Oct-24			57d

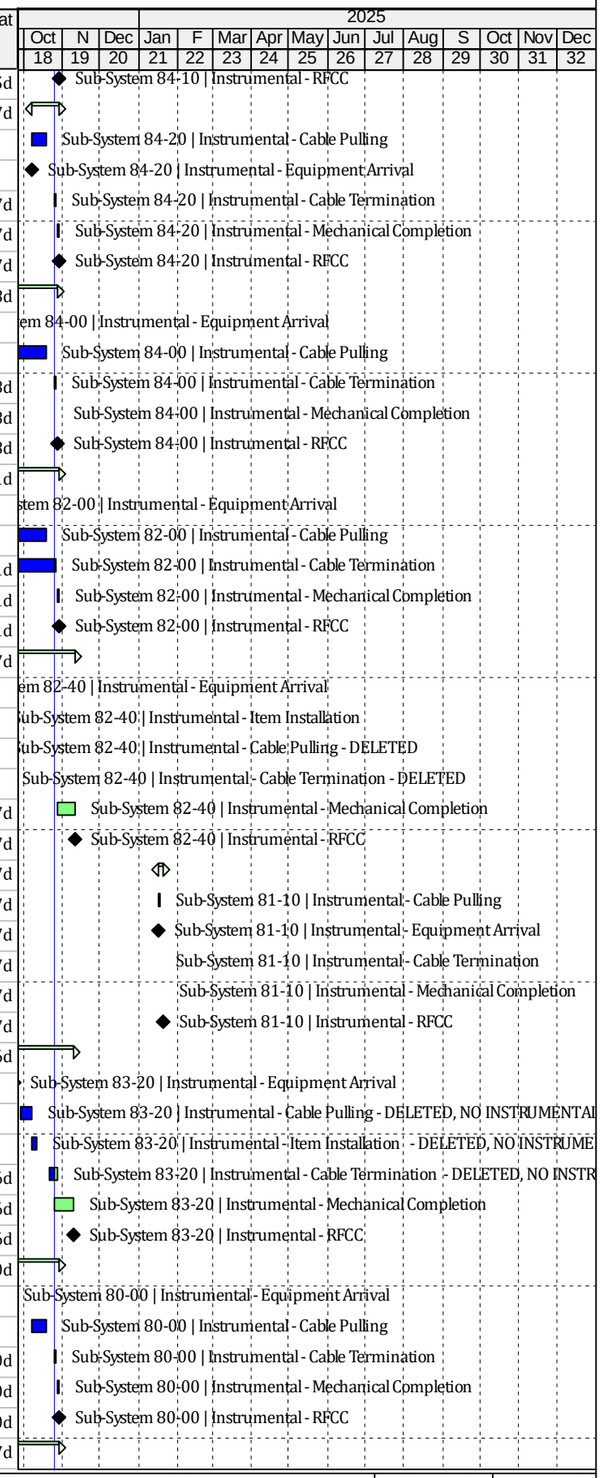

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT5860	Sub-System 85-00 | Instrumental - Equipment Arrival	0d	0d	22-Jul-24 A				
CON-EIT5810	Sub-System 85-00 | Instrumental - Cable Pulling	1d	7d	12-Oct-24 A	19-Oct-24 A			
CON-EIT5820	Sub-System 85-00 | Instrumental - Cable Termination	1d	1d	26-Oct-24	26-Oct-24			57d
CON-EIT5840	Sub-System 85-00 | Instrumental - Mechanical Completion	2d	2d	28-Oct-24	29-Oct-24			57d
CON-EIT5850	Sub-System 85-00 | Instrumental - RFCC	0d	0d		29-Oct-24			57d
E.12 Sub-System 72-00 | NAVAID		21d	8d	21-Oct-24 A	29-Oct-24			103d
CON-EIT5870	Sub-System 72-00 | Instrumental - Cable Pulling	1d	5d	21-Oct-24 A	25-Oct-24 A			
CON-EIT5880	Sub-System 72-00 | Instrumental - Cable Termination	1d	1d	26-Oct-24	26-Oct-24			103d
CON-EIT5920	Sub-System 72-00 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				104d
CON-EIT5900	Sub-System 72-00 | Instrumental - Mechanical Completion	2d	2d	28-Oct-24	29-Oct-24			103d
CON-EIT5910	Sub-System 72-00 | Instrumental - RFCC	0d	0d		29-Oct-24			103d
E.19 Sub-System 81-20 | Power Transformer 7 MVA (TR-100AD1)		73d	95d	05-Aug-24 A	25-Nov-24			80d
CON-EIT6340	Sub-System 81-20 | Instrumental - Equipment Arrival	0d	0d	05-Aug-24 A				
CON-EIT6310	Sub-System 81-20 | Instrumental - Item Installation	4d	29d	06-Aug-24 A	09-Sep-24 A			
CON-EIT6290	Sub-System 81-20 | Instrumental - Cable Pulling	8d	8d	26-Oct-24	05-Nov-24			80d
CON-EIT6300	Sub-System 81-20 | Instrumental - Cable Termination	5d	5d	06-Nov-24	11-Nov-24			80d
CON-EIT6320	Sub-System 81-20 | Instrumental - Mechanical Completion	12d	12d	12-Nov-24	25-Nov-24			80d
CON-EIT6330	Sub-System 81-20 | Instrumental - RFCC	0d	0d		25-Nov-24			80d
E.20 Sub-System 20-00 | Electrolyser Package (A-20000)		5d	5d	17-Dec-24	21-Dec-24			63d
CON-EIT6350	Sub-System 20-00 | Instrumental - Cable Pulling	2d	2d	17-Dec-24	18-Dec-24			63d
CON-EIT6400	Sub-System 20-00 | Instrumental - Equipment Arrival	0d	0d	17-Dec-24				63d
CON-EIT6360	Sub-System 20-00 | Instrumental - Cable Termination	1d	1d	19-Dec-24	19-Dec-24			63d
CON-EIT6380	Sub-System 20-00 | Instrumental - Mechanical Completion	2d	2d	20-Dec-24	21-Dec-24			63d
CON-EIT6390	Sub-System 20-00 | Instrumental - RFCC	0d	0d		21-Dec-24			63d
M.01 Sub-System 90-02 | LV Switchgear Room B-200		89d	92d	26-Jul-24 A	12-Nov-24			104d
CON-EIT6760	Sub-System 90-02 | Instrumental - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT6710	Sub-System 90-02 | Instrumental - Cable Pulling - DELETED	8d	8d	31-Aug-24 A	09-Sep-24 A			
CON-EIT6720	Sub-System 90-02 | Instrumental - Cable Termination DELETED	5d	5d	11-Sep-24 A	16-Sep-24 A			
CON-EIT6740	Sub-System 90-02 | Instrumental - Mechanical Completion	3d	36d	30-Sep-24 A	12-Nov-24			104d
CON-EIT6730	Sub-System 90-02 | Instrumental - Item Installation (MCT)	4d	26d	11-Oct-24 A	12-Nov-24			104d
CON-EIT6750	Sub-System 90-02 | Instrumental - RFCC	0d	0d		12-Nov-24			104d
M.02 Sub-System 90-03 | UPS System Equipment Room B-300		89d	90d	29-Jul-24 A	12-Nov-24			104d
CON-EIT6820	Sub-System 90-03 | Instrumental - Equipment Arrival	0d	0d	29-Jul-24 A				
CON-EIT6770	Sub-System 90-03 | Instrumental - Cable Pulling DELETED	8d	8d	31-Aug-24 A	09-Sep-24 A			
CON-EIT6780	Sub-System 90-03 | Instrumental - Cable Termination DELETED	5d	5d	11-Sep-24 A	16-Sep-24 A			
CON-EIT6800	Sub-System 90-03 | Instrumental - Mechanical Completion	3d	36d	30-Sep-24 A	12-Nov-24			104d
CON-EIT6790	Sub-System 90-03 | Instrumental - Item Installation (MCT)	4d	18d	21-Oct-24 A	12-Nov-24			104d
CON-EIT6810	Sub-System 90-03 | Instrumental - RFCC	0d	0d		12-Nov-24			104d
M.03 Sub-System 90-01 | HV-MV Switchgear Room B-100		89d	92d	26-Jul-24 A	12-Nov-24			104d
CON-EIT6880	Sub-System 90-01 | Instrumental - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT6830	Sub-System 90-01 | Instrumental - Cable Pulling DELETED	8d	8d	31-Aug-24 A	09-Sep-24 A			
CON-EIT6840	Sub-System 90-01 | Instrumental - Cable Termination DELETED	5d	5d	11-Sep-24 A	16-Sep-24 A			
CON-EIT6860	Sub-System 90-01 | Instrumental - Mechanical Completion	3d	24d	14-Oct-24 A	12-Nov-24			104d
CON-EIT6850	Sub-System 90-01 | Instrumental - Item Installation (MCT)	4d	18d	21-Oct-24 A	12-Nov-24			104d
CON-EIT6870	Sub-System 90-01 | Instrumental - RFCC	0d	0d		12-Nov-24			104d
M.04 Sub-System 90-04 | I&T System Equipment Room B-400		89d	86d	02-Aug-24 A	12-Nov-24			104d

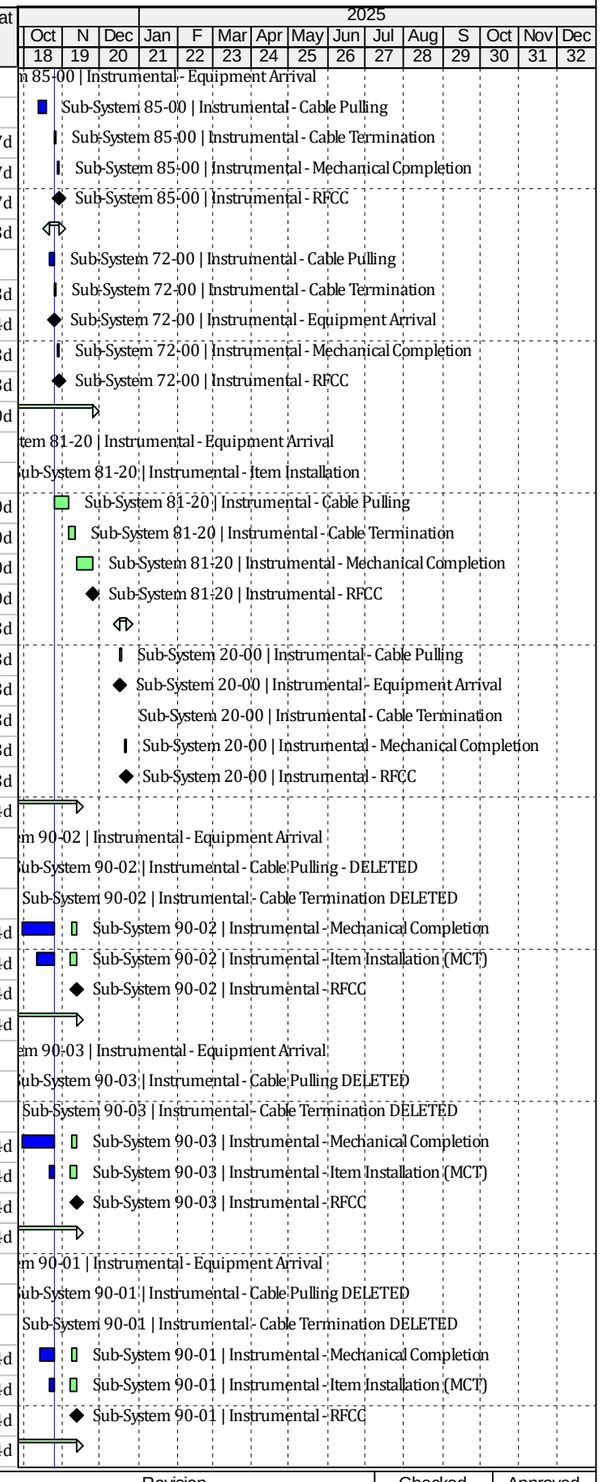

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT6940	Sub-System 90-04 | Instrumental - Equipment Arrival	0d	0d	02-Aug-24 A				
CON-EIT6890	Sub-System 90-04 | Instrumental - Cable Pulling DELETED	8d	8d	31-Aug-24 A	09-Sep-24 A			
CON-EIT6900	Sub-System 90-04 | Instrumental - Cable Termination DELETED	5d	5d	11-Sep-24 A	16-Sep-24 A			
CON-EIT6920	Sub-System 90-04 | Instrumental - Mechanical Completion	3d	37d	30-Sep-24 A	12-Nov-24			104d
CON-EIT6910	Sub-System 90-04 | Instrumental - Item Installation (MCT)	4d	27d	11-Oct-24 A	12-Nov-24			104d
CON-EIT6930	Sub-System 90-04 | Instrumental - RFCC	0d	0d		12-Nov-24			104d
H.01 Sub-System 77-20 | HVAC LV Switchgear Room B-200		78d	85d	26-Jul-24 A	04-Nov-24			113d
CON-EIT7000	Sub-System 77-20 | Instrumental - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT6950	Sub-System 77-20 | Instrumental - Cable Pulling	5d	17d	28-Sep-24 A	17-Oct-24 A			
CON-EIT6960	Sub-System 77-20 | Instrumental - Cable Termination	4d	21d	07-Oct-24 A	30-Oct-24			116d
CON-EIT6980	Sub-System 77-20 | Instrumental - Mechanical Completion	7d	24d	07-Oct-24 A	04-Nov-24			113d
CON-EIT6990	Sub-System 77-20 | Instrumental - RFCC	0d	0d		04-Nov-24			113d
H.02 Sub-System 77-30 | HVAC UPS Equipment Room B-300		82d	87d	29-Jul-24 A	08-Nov-24			109d
CON-EIT7060	Sub-System 77-30 | Instrumental - Equipment Arrival	0d	0d	29-Jul-24 A				
CON-EIT7010	Sub-System 77-30 | Instrumental - Cable Pulling	5d	17d	28-Sep-24 A	17-Oct-24 A			
CON-EIT7020	Sub-System 77-30 | Instrumental - Cable Termination	3d	26d	30-Sep-24 A	29-Oct-24			117d
CON-EIT9130	Sub-System 77-30 | Instrumental - Item Installation	4d	5d	30-Sep-24 A	04-Oct-24 A			
CON-EIT7040	Sub-System 77-30 | Instrumental - Mechanical Completion	11d	28d	07-Oct-24 A	08-Nov-24			109d
CON-EIT7050	Sub-System 77-30 | Instrumental - RFCC	0d	0d		08-Nov-24			109d
H.03 Sub-System 77-10 | HVAC HV/MV Switchgear Room B-100		80d	85d	26-Jul-24 A	04-Nov-24			113d
CON-EIT7120	Sub-System 77-10 | Instrumental - Equipment Arrival	0d	0d	26-Jul-24 A				
CON-EIT7070	Sub-System 77-10 | Instrumental - Cable Pulling	10d	17d	30-Sep-24 A	18-Oct-24 A			
CON-EIT7080	Sub-System 77-10 | Instrumental - Cable Termination	4d	27d	30-Sep-24 A	30-Oct-24			116d
CON-EIT9140	Sub-System 77-10 | Instrumental - Item Installation	3d	5d	30-Sep-24 A	04-Oct-24 A			
CON-EIT7100	Sub-System 77-10 | Instrumental - Mechanical Completion	7d	18d	14-Oct-24 A	04-Nov-24			113d
CON-EIT7110	Sub-System 77-10 | Instrumental - RFCC	0d	0d		04-Nov-24			113d
H.04 Sub-System 77-40 | HVAC I&T Equipment Room B-400		85d	84d	02-Aug-24 A	09-Nov-24			108d
CON-EIT7180	Sub-System 77-40 | Instrumental - Equipment Arrival	0d	0d	02-Aug-24 A				
CON-EIT7130	Sub-System 77-40 | Instrumental - Cable Pulling	2d	25d	30-Sep-24 A	28-Oct-24			108d
CON-EIT7140	Sub-System 77-40 | Instrumental - Cable Termination	2d	25d	30-Sep-24 A	28-Oct-24			113d
CON-EIT9150	Sub-System 77-40 | Instrumental - Item Installation	5d	5d	30-Sep-24 A	04-Oct-24 A			
CON-EIT7160	Sub-System 77-40 | Instrumental - Mechanical Completion	12d	23d	14-Oct-24 A	09-Nov-24			108d
CON-EIT7170	Sub-System 77-40 | Instrumental - RFCC	0d	0d		09-Nov-24			108d
L.01 Sub-System 87-10 | Process Control System (PCS)		22d	65d	09-Sep-24 A	23-Nov-24			68d
CON-EIT7210	Sub-System 87-10 | Instrumental - Item Installation	1d	53d	09-Sep-24 A	09-Nov-24			68d
CON-EIT9160	Sub-System 87-10 | Instrumental - Cable Pulling	12d	23d	14-Oct-24 A	09-Nov-24			68d
CON-EIT9170	Sub-System 87-10 | Instrumental - Cable Termination	8d	23d	14-Oct-24 A	09-Nov-24			68d
CON-EIT7240	Sub-System 87-10 | Instrumental - Equipment Arrival	0d	0d	18-Oct-24 A				
CON-EIT7220	Sub-System 87-10 | Instrumental - Mechanical Completion	12d	12d	11-Nov-24	23-Nov-24			68d
CON-EIT7230	Sub-System 87-10 | Instrumental - RFCC	0d	0d		23-Nov-24			68d
L.02 Sub-System 79-00 | Emergency Shutdown Systems (SIS)		15d	15d	26-Oct-24	13-Nov-24			84d
CON-EIT7300	Sub-System 79-00 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				84d
CON-EIT9180	Sub-System 79-00 | Instrumental - Cable Pulling	5d	5d	26-Oct-24	31-Oct-24			84d
CON-EIT7270	Sub-System 79-00 | Instrumental - Item Installation	1d	1d	02-Nov-24	02-Nov-24			84d
CON-EIT9190	Sub-System 79-00 | Instrumental - Cable Termination	2d	2d	04-Nov-24	05-Nov-24			84d
CON-EIT7280	Sub-System 79-00 | Instrumental - Mechanical Completion	7d	7d	06-Nov-24	13-Nov-24			84d

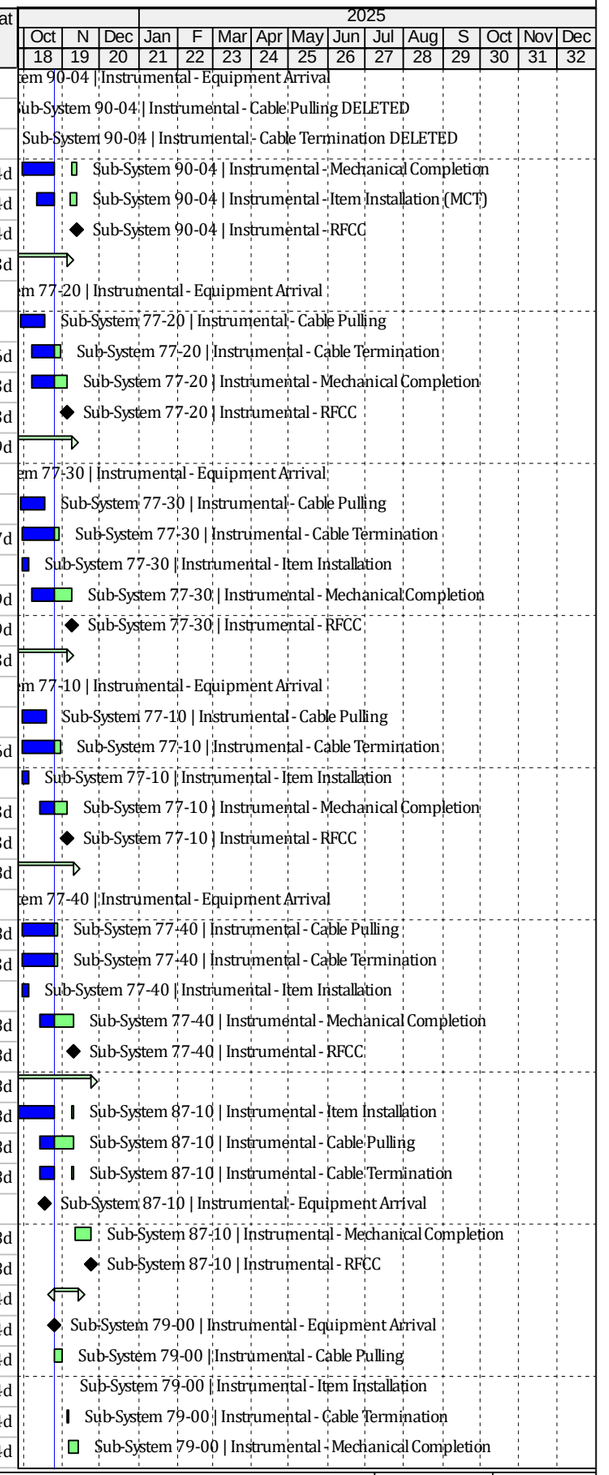


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT7290	Sub-System 79-00 | Instrumental - RFCC	0d	0d		13-Nov-24			84d
L03 Sub-System 70-00 | F&G Control System		20d	64d	05-Sep-24 A	19-Nov-24			61d
CON-EIT7330	Sub-System 70-00 | Instrumental - Item Installation	10d	59d	05-Sep-24 A	13-Nov-24			61d
CON-EIT7360	Sub-System 70-00 | Instrumental - Equipment Arrival	0d	0d	18-Oct-24 A				
CON-EIT9200	Sub-System 70-00 | Instrumental - Cable Pulling	15d	20d	21-Oct-24 A	13-Nov-24			61d
CON-EIT9210	Sub-System 70-00 | Instrumental - Cable Termination	5d	20d	21-Oct-24 A	13-Nov-24			61d
CON-EIT7340	Sub-System 70-00 | Instrumental - Mechanical Completion	15d	15d	02-Nov-24	19-Nov-24			61d
CON-EIT7350	Sub-System 70-00 | Instrumental - RFCC	0d	0d		19-Nov-24			61d
L04 Sub-System 86-00 | Data Networks		18d	18d	26-Oct-24	16-Nov-24			63d
CON-EIT7370	Sub-System 86-00 | Instrumental - Cable Pulling	11d	11d	26-Oct-24	08-Nov-24			63d
CON-EIT7420	Sub-System 86-00 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				63d
CON-EIT7390	Sub-System 86-00 | Instrumental - Item Installation	1d	1d	09-Nov-24	09-Nov-24			63d
CON-EIT7380	Sub-System 86-00 | Instrumental - Cable Termination	3d	3d	11-Nov-24	13-Nov-24			63d
CON-EIT7400	Sub-System 86-00 | Instrumental - Mechanical Completion	3d	3d	14-Nov-24	16-Nov-24			63d
CON-EIT7410	Sub-System 86-00 | Instrumental - RFCC	0d	0d		16-Nov-24			63d
L05 Sub-System 87-00 | Power Distribution System (EMCS)		2d	2d	26-Oct-24	28-Oct-24			77d
CON-EIT7450	Sub-System 87-00 | Instrumental - Item Installation	1d	1d	26-Oct-24	26-Oct-24			77d
CON-EIT7480	Sub-System 87-00 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				77d
CON-EIT7460	Sub-System 87-00 | Instrumental - Mechanical Completion	1d	1d	28-Oct-24	28-Oct-24			77d
CON-EIT7470	Sub-System 87-00 | Instrumental - RFCC	0d	0d		28-Oct-24			77d
L06 Sub-System 70-10/11 | F&G H2 GAS INDOOR LOW /UPPER		84d	68d	05-Oct-24 A	24-Dec-24			255d
CON-EIT7490	Sub-System 70-10/11 | Instrumental - Cable Pulling	66d	56d	05-Oct-24 A	10-Dec-24			66d
CON-EIT7500	Sub-System 70-10/11 | Instrumental - Cable Termination	78d	68d	05-Oct-24 A	24-Dec-24			255d
CON-EIT7520	Sub-System 70-10/11 | Instrumental - Mechanical Completion	75d	65d	05-Oct-24 A	20-Dec-24			69d
CON-EIT7540	Sub-System 70-10/11 | Instrumental - Equipment Arrival	0d	0d	05-Oct-24 A				
CON-EIT7510	Sub-System 70-10/11 | Instrumental - Item Installation	84d	67d	07-Oct-24 A	24-Dec-24			255d
CON-EIT7530	Sub-System 70-10/11 | Instrumental - RFCC	0d	0d		25-Oct-24			93d
L07 Sub-System 70-14/15 | F&G FLAME INDOOR LOW/UPPER		84d	74d	28-Sep-24 A	24-Dec-24			66d
CON-EIT7550	Sub-System 70-14/15 | Instrumental - Cable Pulling	78d	74d	28-Sep-24 A	24-Dec-24			66d
CON-EIT7560	Sub-System 70-14/15 | Instrumental - Cable Termination	78d	74d	28-Sep-24 A	24-Dec-24			66d
CON-EIT7570	Sub-System 70-14/15 | Instrumental - Item Installation	78d	74d	28-Sep-24 A	24-Dec-24			66d
CON-EIT7580	Sub-System 70-14/15 | Instrumental - Mechanical Completion	78d	74d	28-Sep-24 A	24-Dec-24			66d
CON-EIT7600	Sub-System 70-14/15 | Instrumental - Equipment Arrival	0d	0d	28-Sep-24 A				
CON-EIT7590	Sub-System 70-14/15 | Instrumental - RFCC	0d	0d		25-Oct-24			98d
L08 Sub-System 70-18/19 | F&G SMOKE INDOOR LOW/UPPER		81d	64d	07-Oct-24 A	20-Dec-24			258d
CON-EIT7610	Sub-System 70-18/19 | Instrumental - Cable Pulling	75d	64d	07-Oct-24 A	20-Dec-24			69d
CON-EIT7620	Sub-System 70-18/19 | Instrumental - Cable Termination	75d	64d	07-Oct-24 A	20-Dec-24			69d
CON-EIT7630	Sub-System 70-18/19 | Instrumental - Item Installation	4d	64d	07-Oct-24 A	20-Dec-24			258d
CON-EIT7640	Sub-System 70-18/19 | Instrumental - Mechanical Completion	75d	64d	07-Oct-24 A	20-Dec-24			69d
CON-EIT7660	Sub-System 70-18/19 | Instrumental - Equipment Arrival	0d	0d	07-Oct-24 A				
CON-EIT7650	Sub-System 70-18/19 | Instrumental - RFCC	0d	0d		25-Oct-24			102d
L09 Sub-System 70-21/22 | F&G H2 GAS OUTDOOR LOW/UPPER		81d	71d	28-Sep-24 A	20-Dec-24			258d
CON-EIT7670	Sub-System 70-21/22 | Instrumental - Cable Pulling	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7680	Sub-System 70-21/22 | Instrumental - Cable Termination	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7700	Sub-System 70-21/22 | Instrumental - Mechanical Completion	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7720	Sub-System 70-21/22 | Instrumental - Equipment Arrival	0d	0d	28-Sep-24 A				

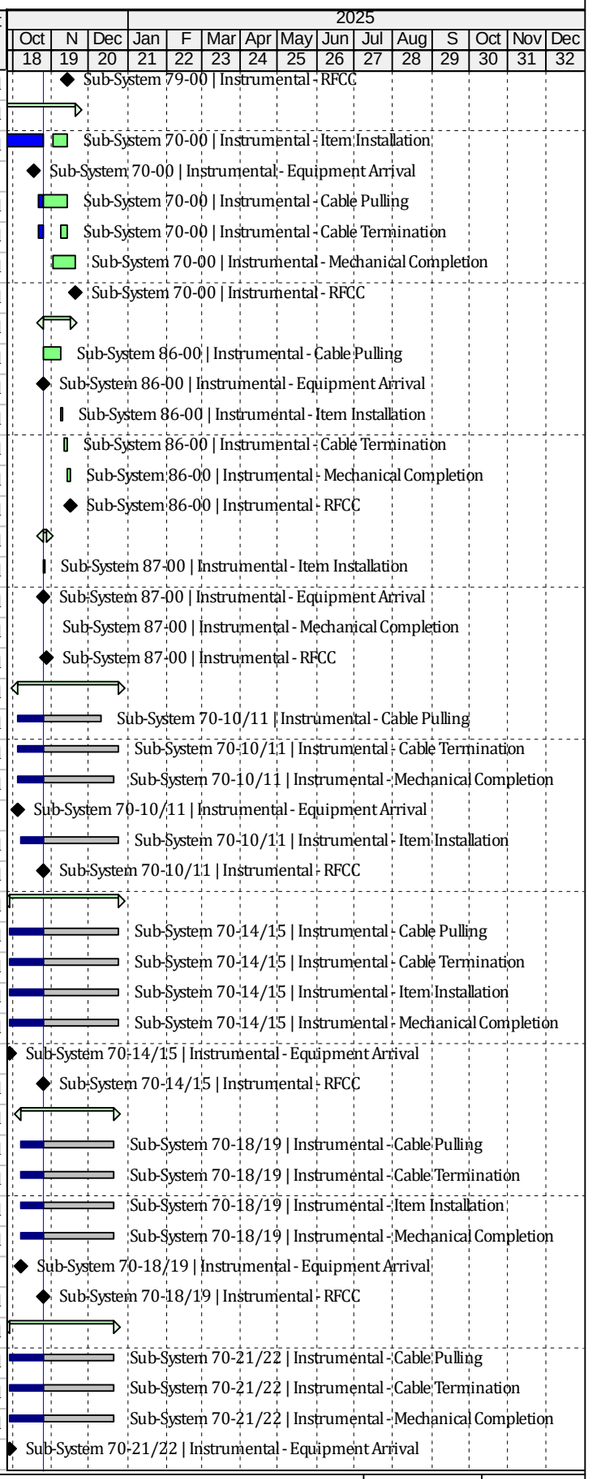

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT7690	Sub-System 70-21/22 | Instrumental - Item Installation	4d	64d	07-Oct-24 A	20-Dec-24			258d
CON-EIT7710	Sub-System 70-21/22 | Instrumental - RFCC	0d	0d		25-Oct-24			107d
L10 Sub-System 70-26/27 | F&G FLAME OUTDOOR LOW/UPPER		81d	71d	28-Sep-24 A	20-Dec-24			258d
CON-EIT7730	Sub-System 70-26/27 | Instrumental - Cable Pulling	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7740	Sub-System 70-26/27 | Instrumental - Cable Termination	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7760	Sub-System 70-26/27 | Instrumental - Mechanical Completion	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7780	Sub-System 70-26/27 | Instrumental - Equipment Arrival	0d	0d	28-Sep-24 A				
CON-EIT7750	Sub-System 70-26/27 | Instrumental - Item Installation	71d	62d	07-Oct-24 A	18-Dec-24			260d
CON-EIT7770	Sub-System 70-26/27 | Instrumental - RFCC	0d	0d		25-Oct-24			111d
L11 Sub-System 70-28/29 | F&G SMOKE OUTDOOR LOW/UPPER		81d	71d	28-Sep-24 A	20-Dec-24			258d
CON-EIT7790	Sub-System 70-28/29 | Instrumental - Cable Pulling	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7800	Sub-System 70-28/29 | Instrumental - Cable Termination	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7820	Sub-System 70-28/29 | Instrumental - Mechanical Completion	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7840	Sub-System 70-28/29 | Instrumental - Equipment Arrival	0d	0d	28-Sep-24 A				
CON-EIT7810	Sub-System 70-28/29 | Instrumental - Item Installation	4d	64d	07-Oct-24 A	20-Dec-24			258d
CON-EIT7830	Sub-System 70-28/29 | Instrumental - RFCC	0d	0d		25-Oct-24			114d
L12 Sub-System 70-31| F&G MCP BEACON/SOUNDER		81d	71d	28-Sep-24 A	20-Dec-24			258d
CON-EIT7850	Sub-System 70-31 | Instrumental - Cable Pulling	75d	71d	28-Sep-24 A	20-Dec-24			71d
CON-EIT7860	Sub-System 70-31 | Instrumental - Cable Termination	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7880	Sub-System 70-31 | Instrumental - Mechanical Completion	75d	71d	28-Sep-24 A	20-Dec-24			69d
CON-EIT7900	Sub-System 70-31 | Instrumental - Equipment Arrival	0d	0d	28-Sep-24 A				
CON-EIT7870	Sub-System 70-31 | Instrumental - Item Installation	4d	64d	07-Oct-24 A	20-Dec-24			258d
CON-EIT7890	Sub-System 70-31 | Instrumental - RFCC	0d	0d		25-Oct-24			118d
Sub-System 70-10| F&G Devices FZ-01 (Fuel Cell Area)		47d	72d	27-Sep-24 A	20-Dec-24			69d
CON-EIT9220	Sub-System 70-10 | Instrumental - Equipment Arrival	0d	0d	27-Sep-24 A				
CON-EIT9230	Sub-System 70-10 | Instrumental - Cable Pulling	3d	3d	07-Dec-24	10-Dec-24			66d
CON-EIT9240	Sub-System 70-10 | Instrumental - Item Installation	2d	2d	11-Dec-24	12-Dec-24			66d
CON-EIT9250	Sub-System 70-10 | Instrumental - Cable Termination	2d	2d	13-Dec-24	14-Dec-24			66d
CON-EIT9260	Sub-System 70-10 | Instrumental - Mechanical Completion	4d	4d	17-Dec-24	20-Dec-24			69d
CON-EIT9270	Sub-System 70-10 | Instrumental - RFCC	0d	0d		20-Dec-24			69d
Sub-System 70-11| F&G Devices FZ-02 (Hydrogen Storage Area)		40d	65d	27-Sep-24 A	12-Dec-24			76d
CON-EIT9280	Sub-System 70-11 | Instrumental - Equipment Arrival	0d	0d	27-Sep-24 A				
CON-EIT9290	Sub-System 70-11 | Instrumental - Cable Pulling	8d	8d	21-Nov-24	29-Nov-24			66d
CON-EIT9300	Sub-System 70-11 | Instrumental - Item Installation	3d	3d	30-Nov-24	03-Dec-24			66d
CON-EIT9310	Sub-System 70-11 | Instrumental - Cable Termination	3d	3d	04-Dec-24	06-Dec-24			66d
CON-EIT9320	Sub-System 70-11 | Instrumental - Mechanical Completion	5d	5d	07-Dec-24	12-Dec-24			76d
CON-EIT9330	Sub-System 70-11 | Instrumental - RFCC	0d	0d		12-Dec-24			76d
Sub-System 70-12| F&G Devices FZ-03 (Electrolyser Area)		36d	61d	27-Sep-24 A	07-Dec-24			80d
CON-EIT9340	Sub-System 70-12 | Instrumental - Equipment Arrival	0d	0d	27-Sep-24 A				
CON-EIT9350	Sub-System 70-12 | Instrumental - Cable Pulling	4d	4d	21-Nov-24	25-Nov-24			80d
CON-EIT9360	Sub-System 70-12 | Instrumental - Item Installation	3d	3d	26-Nov-24	28-Nov-24			80d
CON-EIT9370	Sub-System 70-12 | Instrumental - Cable Termination	3d	3d	29-Nov-24	02-Dec-24			80d
CON-EIT9380	Sub-System 70-12 | Instrumental - Mechanical Completion	4d	4d	04-Dec-24	07-Dec-24			80d
CON-EIT9390	Sub-System 70-12 | Instrumental - RFCC	0d	0d		07-Dec-24			80d
Sub-System 70-13| F&G Devices FZ-04 (B-200 LV Switchgear Room)		18d	39d	27-Sep-24 A	12-Nov-24			102d
CON-EIT9400	Sub-System 70-13 | Instrumental - Equipment Arrival	0d	0d	27-Sep-24 A				

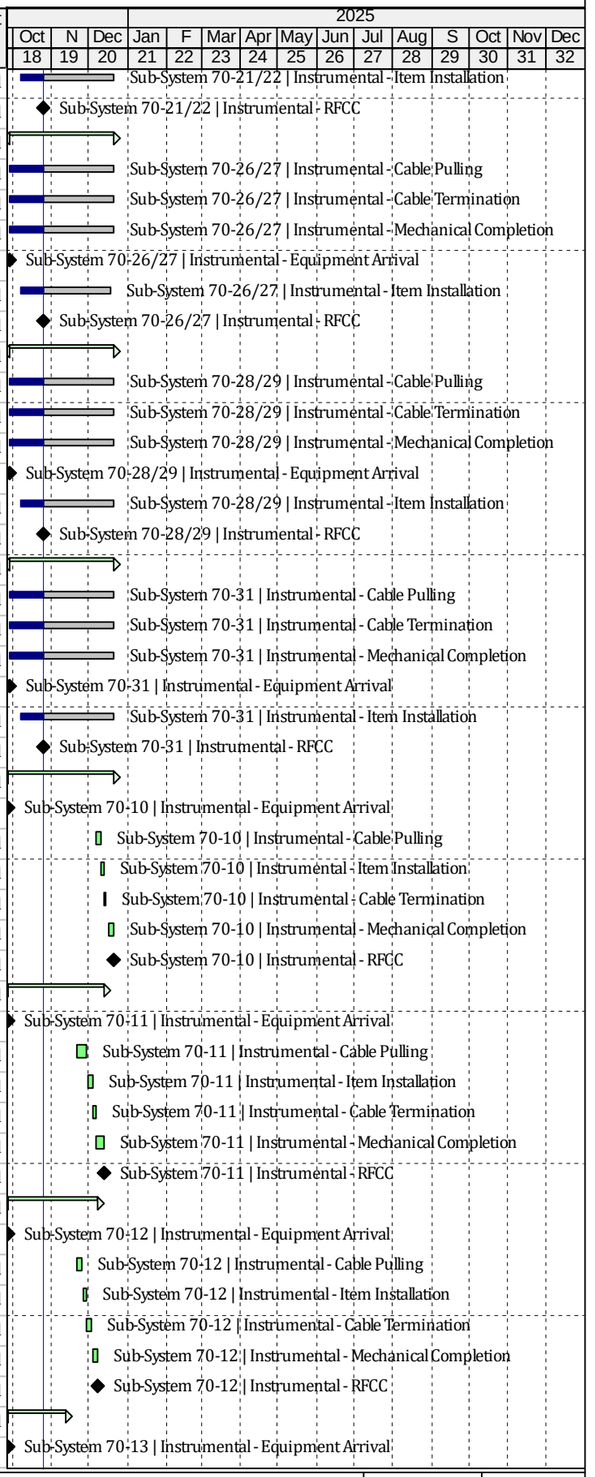

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT9420	Sub-System 70-13 | Instrumental - Item Installation	4d	18d	11-Oct-24 A	31-Oct-24			66d
CON-EIT9410	Sub-System 70-13 | Instrumental - Cable Pulling	5d	14d	16-Oct-24 A	31-Oct-24			66d
CON-EIT9430	Sub-System 70-13 | Instrumental - Cable Termination	3d	12d	18-Oct-24 A	31-Oct-24			66d
CON-EIT9440	Sub-System 70-13 | Instrumental - Mechanical Completion	9d	9d	02-Nov-24	12-Nov-24			102d
CON-EIT9450	Sub-System 70-13 | Instrumental - RFCC	0d	0d		12-Nov-24			102d
Sub-System 70-14| F&G Devices FZ-04 (B-300 UPS & Batteries Switchroom)		7d	32d	27-Sep-24 A	04-Nov-24			109d
CON-EIT9460	Sub-System 70-14 | Instrumental - Equipment Arrival	0d	0d	27-Sep-24 A				
CON-EIT9470	Sub-System 70-14 | Instrumental - Cable Pulling	2d	7d	11-Oct-24 A	18-Oct-24 A			
CON-EIT9480	Sub-System 70-14 | Instrumental - Item Installation	2d	2d	11-Oct-24 A	12-Oct-24 A			
CON-EIT9490	Sub-System 70-14 | Instrumental - Cable Termination	2d	9d	18-Oct-24 A	28-Oct-24			69d
CON-EIT9500	Sub-System 70-14 | Instrumental - Mechanical Completion	5d	5d	29-Oct-24	04-Nov-24			109d
CON-EIT9510	Sub-System 70-14 | Instrumental - RFCC	0d	0d		04-Nov-24			109d
Sub-System 70-15| F&G Devices FZ-04 (B-400 I&T Equipment Room)		17d	17d	26-Oct-24	15-Nov-24			99d
CON-EIT9520	Sub-System 70-15 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				71d
CON-EIT9530	Sub-System 70-15 | Instrumental - Cable Pulling	2d	2d	02-Nov-24	04-Nov-24			66d
CON-EIT9540	Sub-System 70-15 | Instrumental - Item Installation	3d	3d	05-Nov-24	07-Nov-24			66d
CON-EIT9550	Sub-System 70-15 | Instrumental - Cable Termination	2d	2d	08-Nov-24	09-Nov-24			66d
CON-EIT9560	Sub-System 70-15 | Instrumental - Mechanical Completion	5d	5d	11-Nov-24	15-Nov-24			99d
CON-EIT9570	Sub-System 70-15 | Instrumental - RFCC	0d	0d		15-Nov-24			99d
Sub-System 70-16| F&G Devices FZ-05 (Bess Area)		45d	51d	27-Sep-24 A	26-Nov-24			90d
CON-EIT9580	Sub-System 70-16 | Instrumental - Equipment Arrival	0d	0d	27-Sep-24 A				
CON-EIT9600	Sub-System 70-16 | Instrumental - Item Installation	3d	25d	18-Oct-24 A	16-Nov-24			66d
CON-EIT9590	Sub-System 70-16 | Instrumental - Cable Pulling	6d	6d	11-Nov-24	16-Nov-24			66d
CON-EIT9610	Sub-System 70-16 | Instrumental - Cable Termination	3d	3d	18-Nov-24	20-Nov-24			66d
CON-EIT9620	Sub-System 70-16 | Instrumental - Mechanical Completion	7d	7d	19-Nov-24	26-Nov-24			90d
CON-EIT9630	Sub-System 70-16 | Instrumental - RFCC	0d	0d		26-Nov-24			90d
Sub-System 70-17| F&G Devices FZ-06 (B-100 HV/MV Switchroom Area)		36d	45d	27-Sep-24 A	19-Nov-24			96d
CON-EIT9640	Sub-System 70-17 | Instrumental - Equipment Arrival	0d	0d	27-Sep-24 A				
CON-EIT9660	Sub-System 70-17 | Instrumental - Item Installation	3d	25d	11-Oct-24 A	09-Nov-24			66d
CON-EIT9650	Sub-System 70-17 | Instrumental - Cable Pulling	5d	22d	15-Oct-24 A	09-Nov-24			66d
CON-EIT9670	Sub-System 70-17 | Instrumental - Cable Termination	3d	21d	16-Oct-24 A	09-Nov-24			66d
CON-EIT9680	Sub-System 70-17 | Instrumental - Mechanical Completion	8d	8d	11-Nov-24	19-Nov-24			96d
CON-EIT9690	Sub-System 70-17 | Instrumental - RFCC	0d	0d		19-Nov-24			96d
Sub-System 70-18| F&G Devices FZ-07 (Transition Piece Area)		50d	50d	26-Oct-24	24-Dec-24			66d
CON-EIT9700	Sub-System 70-18 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				108d
CON-EIT9710	Sub-System 70-18 | Instrumental - Cable Pulling	1d	1d	16-Dec-24	16-Dec-24			66d
CON-EIT9720	Sub-System 70-18 | Instrumental - Item Installation	1d	1d	17-Dec-24	17-Dec-24			66d
CON-EIT9730	Sub-System 70-18 | Instrumental - Cable Termination	1d	1d	18-Dec-24	18-Dec-24			66d
CON-EIT9740	Sub-System 70-18 | Instrumental - Mechanical Completion	2d	2d	23-Dec-24	24-Dec-24			66d
CON-EIT9750	Sub-System 70-18 | Instrumental - RFCC	0d	0d		24-Dec-24			66d
M.05 Sub-System 63-00 | Instrument Air Package (A-63000)		2d	2d	02-Nov-24	04-Nov-24			87d
CON-EIT7910	Sub-System 63-00 | Instrumental - Cable Pulling	1d	1d	02-Nov-24	02-Nov-24			87d
CON-EIT7960	Sub-System 63-00 | Instrumental - Equipment Arrival	0d	0d	02-Nov-24				87d
CON-EIT7940	Sub-System 63-00 | Instrumental - Mechanical Completion	1d	1d	04-Nov-24	04-Nov-24			87d
CON-EIT7950	Sub-System 63-00 | Instrumental - RFCC	0d	0d		04-Nov-24			87d
M.06 Sub-System 64-00 | Nitrogen Generator Package (U-6400)		4d	4d	04-Nov-24	07-Nov-24			88d

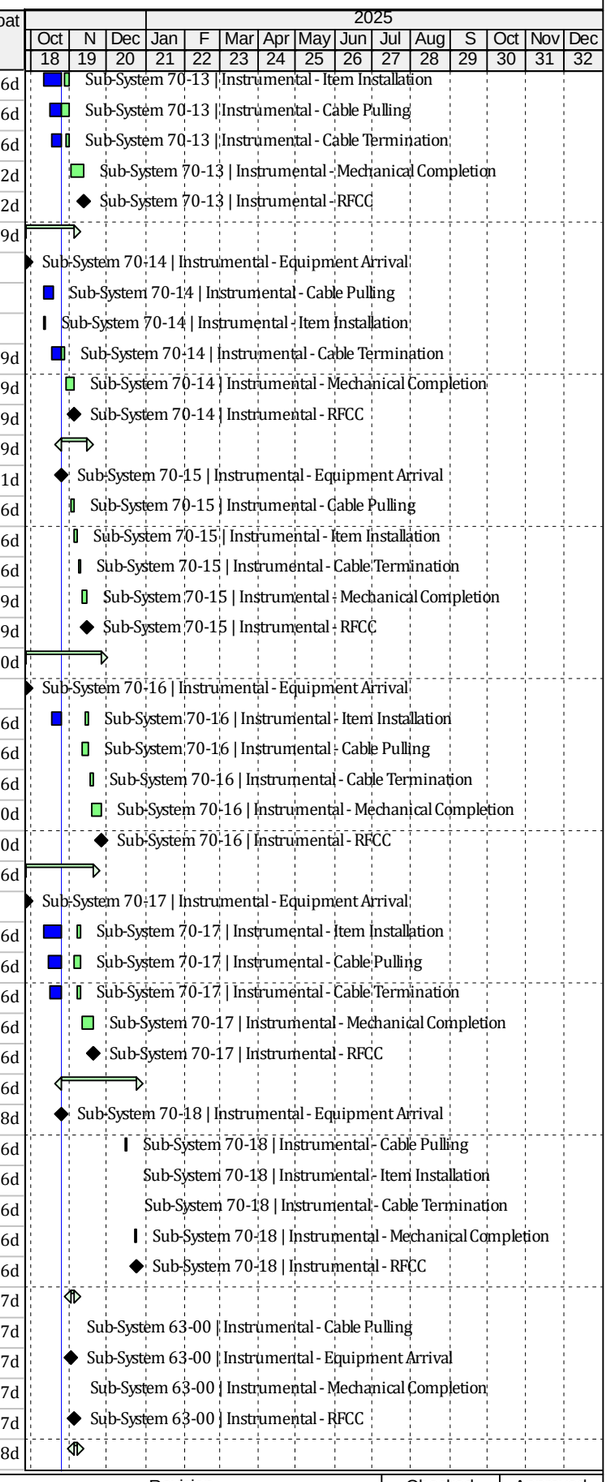

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT7970	Sub-System 64-00 | Instrumental - Cable Pulling	2d	2d	04-Nov-24	05-Nov-24			88d
CON-EIT8020	Sub-System 64-00 | Instrumental - Equipment Arrival	0d	0d	04-Nov-24				88d
CON-EIT7980	Sub-System 64-00 | Instrumental - Cable Termination	1d	1d	06-Nov-24	06-Nov-24			88d
CON-EIT8000	Sub-System 64-00 | Instrumental - Mechanical Completion	1d	1d	07-Nov-24	07-Nov-24			88d
CON-EIT8010	Sub-System 64-00 | Instrumental - RFCC	0d	0d		07-Nov-24			88d
M.07 Sub-System 63-30 | Instrument Air Network		19d	25d	07-Oct-24 A	05-Nov-24			91d
CON-EIT8060	Sub-System 63-30 | Instrumental - Mechanical Completion	8d	25d	07-Oct-24 A	05-Nov-24			91d
CON-EIT8030	Sub-System 63-30 | Instrumental - Cable Pulling	1d	1d	26-Oct-24	26-Oct-24			96d
CON-EIT8080	Sub-System 63-30 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				96d
CON-EIT8050	Sub-System 63-30 | Instrumental - Item Installation	1d	1d	28-Oct-24	28-Oct-24			96d
CON-EIT8040	Sub-System 63-30 | Instrumental - Cable Termination	1d	1d	29-Oct-24	29-Oct-24			96d
CON-EIT8070	Sub-System 63-30 | Instrumental - RFCC	0d	0d		05-Nov-24			91d
M.08 Sub-System 64-10 | Nitrogen Distribution Network		57d	54d	07-Oct-24 A	09-Dec-24			69d
CON-EIT8120	Sub-System 64-10 | Instrumental - Mechanical Completion	37d	54d	07-Oct-24 A	09-Dec-24			69d
CON-EIT8090	Sub-System 64-10 | Instrumental - Cable Pulling	9d	9d	04-Nov-24	13-Nov-24			74d
CON-EIT8140	Sub-System 64-10 | Instrumental - Equipment Arrival	0d	0d	04-Nov-24				74d
CON-EIT8110	Sub-System 64-10 | Instrumental - Item Installation	10d	10d	14-Nov-24	25-Nov-24			74d
CON-EIT8100	Sub-System 64-10 | Instrumental - Cable Termination	7d	7d	26-Nov-24	03-Dec-24			74d
CON-EIT8130	Sub-System 64-10 | Instrumental - RFCC	0d	0d		09-Dec-24			69d
M.09 Sub-System 50-00 | Seawater Intake System (Lifting Pumps)		27d	82d	30-Sep-24 A	08-Jan-25			60d
CON-EIT8180	Sub-System 50-00 | Instrumental - Mechanical Completion	15d	82d	30-Sep-24 A	08-Jan-25			60d
CON-EIT8150	Sub-System 50-00 | Instrumental - Cable Pulling	5d	5d	21-Dec-24	28-Dec-24			60d
CON-EIT8200	Sub-System 50-00 | Instrumental - Equipment Arrival	0d	0d	21-Dec-24				60d
CON-EIT8170	Sub-System 50-00 | Instrumental - Item Installation	4d	4d	30-Dec-24	03-Jan-25			60d
CON-EIT8160	Sub-System 50-00 | Instrumental - Cable Termination	3d	3d	04-Jan-25	08-Jan-25			60d
CON-EIT8190	Sub-System 50-00 | Instrumental - RFCC	0d	0d		08-Jan-25			60d
M.10 Sub-System 50-10 | Water Desalination Package & Distribution		7d	7d	02-Nov-24	09-Nov-24			93d
CON-EIT8210	Sub-System 50-10 | Instrumental - Cable Pulling	2d	2d	02-Nov-24	04-Nov-24			93d
CON-EIT8260	Sub-System 50-10 | Instrumental - Equipment Arrival	0d	0d	02-Nov-24				93d
CON-EIT8220	Sub-System 50-10 | Instrumental - Cable Termination	3d	3d	05-Nov-24	07-Nov-24			93d
CON-EIT8240	Sub-System 50-10 | Instrumental - Mechanical Completion	2d	2d	08-Nov-24	09-Nov-24			93d
CON-EIT8250	Sub-System 50-10 | Instrumental - RFCC	0d	0d		09-Nov-24			93d
M.11 Sub-System 50-20 | Water Desalination Package & Distribution		30d	30d	02-Nov-24	06-Dec-24			71d
CON-EIT8320	Sub-System 50-11 | Instrumental - Equipment Arrival	0d	0d	02-Nov-24				72d
CON-EIT8270	Sub-System 50-11 | Instrumental - Cable Pulling	8d	8d	02-Nov-24	12-Nov-24			71d
CON-EIT8290	Sub-System 50-11 | Instrumental - Item Installation	4d	4d	12-Nov-24	16-Nov-24			71d
CON-EIT8280	Sub-System 50-11 | Instrumental - Cable Termination	5d	5d	16-Nov-24	22-Nov-24			71d
CON-EIT8300	Sub-System 50-11 | Instrumental - Mechanical Completion	12d	12d	22-Nov-24	06-Dec-24			71d
CON-EIT8310	Sub-System 50-11 | Instrumental - RFCC	0d	0d		06-Dec-24			71d
M.12 Sub-System 55-00 | Waste Water Disposal		67d	69d	09-Aug-24 A	29-Oct-24			109d
CON-EIT8380	Sub-System 55-00 | Instrumental - Equipment Arrival	0d	0d	09-Aug-24 A				
CON-EIT8360	Sub-System 55-00 | Instrumental - Mechanical Completion	2d	26d	30-Sep-24 A	29-Oct-24			109d
CON-EIT8330	Sub-System 55-00 | Instrumental - Cable Pulling	1d	1d	26-Oct-24	26-Oct-24			109d
CON-EIT8340	Sub-System 55-00 | Instrumental - Cable Termination	1d	1d	28-Oct-24	28-Oct-24			109d
CON-EIT8350	Sub-System 55-00 | Instrumental - Item Installation	1d	1d	29-Oct-24	29-Oct-24			109d
CON-EIT8370	Sub-System 55-00 | Instrumental - RFCC	0d	0d		29-Oct-24			109d

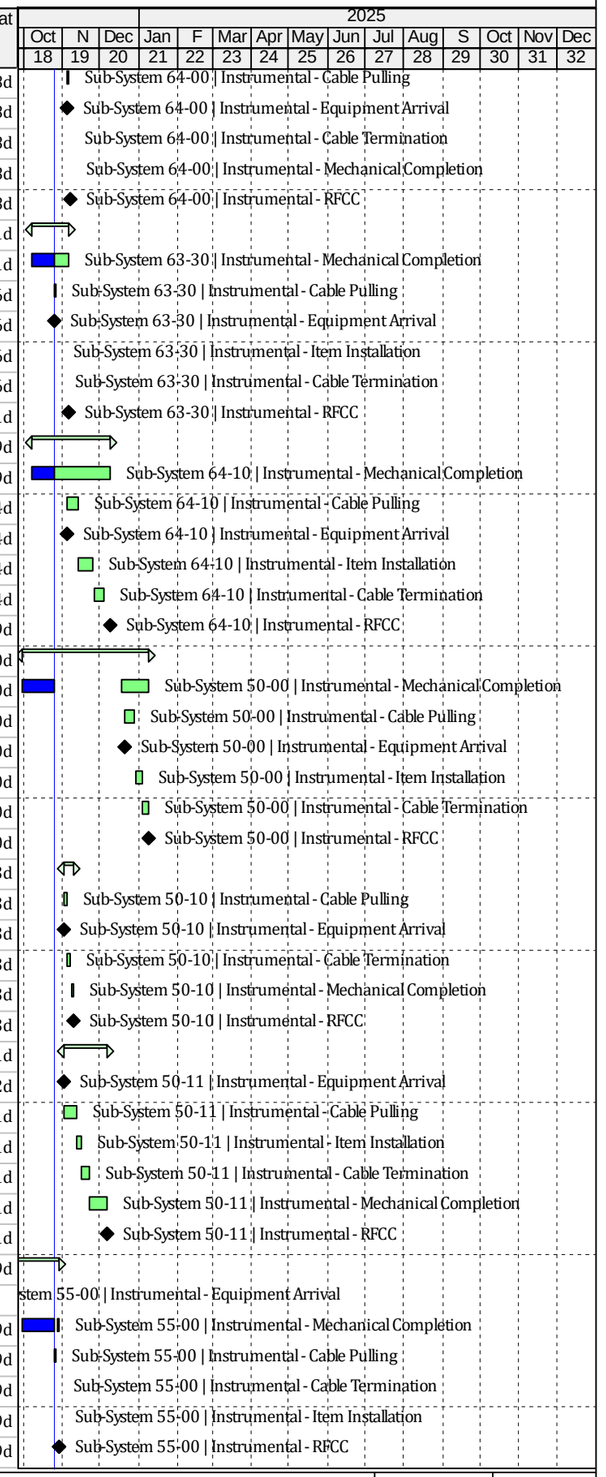

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
M.13 Sub-System 55-01 | WasteWater Brine Discharge System		14d	27d	30-Sep-24 A	30-Oct-24			110d
CON-EIT8420	Sub-System 55-01 | Instrumental - Mechanical Completion	4d	27d	30-Sep-24 A	30-Oct-24			110d
CON-EIT8390	Sub-System 55-01 | Instrumental - Cable Pulling	1d	1d	26-Oct-24	26-Oct-24			111d
CON-EIT8440	Sub-System 55-01 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				111d
CON-EIT8410	Sub-System 55-01 | Instrumental - Item Installation	1d	1d	28-Oct-24	28-Oct-24			111d
CON-EIT8400	Sub-System 55-01 | Instrumental - Cable Termination	1d	1d	29-Oct-24	29-Oct-24			111d
CON-EIT8430	Sub-System 55-01 | Instrumental - RFCC	0d	0d		30-Oct-24			110d
M.14 Sub-System 99-00 | Crane		18d	18d	21-Dec-24	15-Jan-25			53d
CON-EIT8450	Sub-System 99-00 | Instrumental - Cable Pulling	8d	8d	21-Dec-24	02-Jan-25			53d
CON-EIT8500	Sub-System 99-00 | Instrumental - Equipment Arrival	0d	0d	21-Dec-24				53d
CON-EIT8470	Sub-System 99-00 | Instrumental - Item Installation	4d	4d	03-Jan-25	08-Jan-25			53d
CON-EIT8460	Sub-System 99-00 | Instrumental - Cable Termination	5d	5d	09-Jan-25	14-Jan-25			53d
CON-EIT8480	Sub-System 99-00 | Instrumental - Mechanical Completion	1d	1d	15-Jan-25	15-Jan-25			53d
CON-EIT8490	Sub-System 99-00 | Instrumental - RFCC	0d	0d		15-Jan-25			53d
M.15 Sub-System 25-08 | Hydrogen Storage Vessels Header (Outlet)		31d	63d	30-Sep-24 A	13-Dec-24			73d
CON-EIT8540	Sub-System 25-08 | Instrumental - Mechanical Completion	15d	63d	30-Sep-24 A	13-Dec-24			73d
CON-EIT8560	Sub-System 25-08 | Instrumental - Equipment Arrival	0d	0d	08-Nov-24				77d
CON-EIT8510	Sub-System 25-08 | Instrumental - Cable Pulling	12d	12d	12-Nov-24	26-Nov-24			73d
CON-EIT8530	Sub-System 25-08 | Instrumental - Item Installation	8d	8d	26-Nov-24	05-Dec-24			73d
CON-EIT8520	Sub-System 25-08 | Instrumental - Cable Termination	7d	7d	05-Dec-24	13-Dec-24			73d
CON-EIT8550	Sub-System 25-08 | Instrumental - RFCC	0d	0d		13-Dec-24			73d
M.16 Sub-System 25-01/06 | Hydrogen Storage Vessels		46d	70d	30-Sep-24 A	20-Dec-24			70d
CON-EIT8600	Sub-System 25-01/06 | Instrumental - Mechanical Completion	20d	70d	30-Sep-24 A	20-Dec-24			70d
CON-EIT8570	Sub-System 25-01/06 | Instrumental - Cable Pulling	20d	20d	08-Nov-24	30-Nov-24			70d
CON-EIT8620	Sub-System 25-01/06 | Instrumental - Equipment Arrival	0d	0d	08-Nov-24				70d
CON-EIT8580	Sub-System 25-01/06 | Instrumental - Cable Termination	13d	13d	02-Dec-24	16-Dec-24			70d
CON-EIT8590	Sub-System 25-01/06 | Instrumental - Item Installation	4d	4d	17-Dec-24	20-Dec-24			70d
CON-EIT8610	Sub-System 25-01/06 | Instrumental - RFCC	0d	0d		20-Dec-24			70d
M.17 Sub-System 43-00 | Hydrogen Vent Header & Drum System		81d	74d	30-Sep-24 A	27-Dec-24			55d
CON-EIT8660	Sub-System 43-00 | Instrumental - Mechanical Completion	30d	74d	30-Sep-24 A	27-Dec-24			55d
CON-EIT8630	Sub-System 43-00 | Instrumental - Cable Pulling	4d	4d	26-Oct-24	30-Oct-24			86d
CON-EIT8680	Sub-System 43-00 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				86d
CON-EIT8640	Sub-System 43-00 | Instrumental - Cable Termination	2d	2d	31-Oct-24	02-Nov-24			86d
CON-EIT8650	Sub-System 43-00 | Instrumental - Item Installation	14d	14d	10-Dec-24	27-Dec-24			55d
CON-EIT8670	Sub-System 43-00 | Instrumental - RFCC	0d	0d		27-Dec-24			55d
M.18 Sub-System 25-07 | Hydrogen Storage Vessels Header (Intlet)		28d	48d	30-Sep-24 A	26-Nov-24			87d
CON-EIT8720	Sub-System 25-07 | Instrumental - Mechanical Completion	23d	48d	30-Sep-24 A	26-Nov-24			87d
CON-EIT8690	Sub-System 25-07 | Instrumental - Cable Pulling	6d	6d	08-Nov-24	14-Nov-24			87d
CON-EIT8740	Sub-System 25-07 | Instrumental - Equipment Arrival	0d	0d	08-Nov-24				87d
CON-EIT8700	Sub-System 25-07 | Instrumental - Cable Termination	4d	4d	15-Nov-24	19-Nov-24			87d
CON-EIT8710	Sub-System 25-07 | Instrumental - Item Installation	6d	6d	20-Nov-24	26-Nov-24			87d
CON-EIT8730	Sub-System 25-07 | Instrumental - RFCC	0d	0d		26-Nov-24			87d
Sub-System 87-20 | Process Control System (PCS) - Instrumentation		26d	26d	26-Oct-24	26-Nov-24			86d
CON-EIT8750	Sub-System 87-20 | Instrumental - Cable Pulling	8d	8d	26-Oct-24	05-Nov-24			86d
CON-EIT8760	Sub-System 87-20 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				86d
CON-EIT8770	Sub-System 87-20 | Instrumental - Cable Termination	5d	5d	06-Nov-24	11-Nov-24			86d

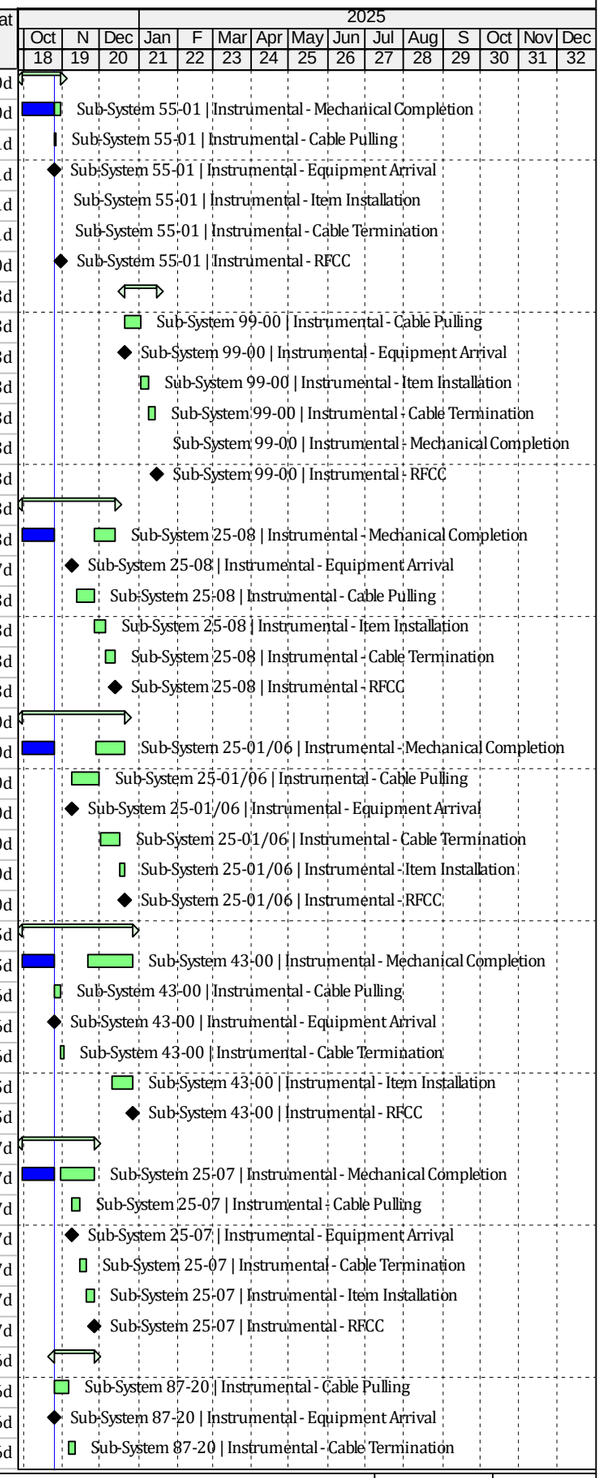

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT8780	Sub-System 87-20 | Instrumental - Item Installation	4d	4d	12-Nov-24	15-Nov-24			86d
CON-EIT8790	Sub-System 87-20 | Instrumental - Mechanical Completion	9d	9d	16-Nov-24	26-Nov-24			86d
CON-EIT8800	Sub-System 87-20 | Instrumental - RFCC	0d	0d		26-Nov-24			86d
Sub-System 79-10 | Emergency Shutdown Systems (SIS) - Devices		25d	25d	26-Oct-24	25-Nov-24			87d
CON-EIT8810	Sub-System 79-10 | Instrumental - Cable Pulling	5d	5d	26-Oct-24	31-Oct-24			87d
CON-EIT8820	Sub-System 79-10 | Instrumental - Equipment Arrival	0d	0d	26-Oct-24				87d
CON-EIT8830	Sub-System 79-10 | Instrumental - Cable Termination	5d	5d	02-Nov-24	07-Nov-24			87d
CON-EIT8840	Sub-System 79-10 | Instrumental - Item Installation	5d	5d	08-Nov-24	13-Nov-24			87d
CON-EIT8850	Sub-System 79-10 | Instrumental - Mechanical Completion	10d	10d	14-Nov-24	25-Nov-24			87d
CON-EIT8860	Sub-System 79-10 | Instrumental - RFCC	0d	0d		25-Nov-24			87d
Telecommunication		57d	1d	23-Aug-24 A	23-Aug-24 A	03-Oct-24	19-Nov-24	
CON-EIT1640	Telecomm Cable Pulling - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	20d	1d	23-Aug-24 A	23-Aug-24 A	21-Oct-24	13-Nov-24	
Lower Deck		40d	1d	23-Aug-24 A	23-Aug-24 A	03-Oct-24	19-Nov-24	
CON-EIT1040	Telecomm Cable Trays - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	03-Oct-24	19-Oct-24	
CON-EIT1650	Telecomm Equipment - Installation - Lower Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	6d	1d	23-Aug-24 A	23-Aug-24 A	12-Oct-24	05-Nov-24	
CON-EIT1660	Telecomm Termination, Glanding & Connection - Installation - Lower Deck (DELETED AFTER REVISED SCHEDU	15d	1d	23-Aug-24 A	23-Aug-24 A	02-Nov-24	19-Nov-24	
Upper Deck		57d	1d	23-Aug-24 A	23-Aug-24 A	11-Oct-24	19-Nov-24	
CON-EIT1670	Telecomm Cable Trays - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	11-Oct-24	28-Oct-24	
CON-EIT1680	Telecomm Equipment - Installation - Upper Deck (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	20d	1d	23-Aug-24 A	23-Aug-24 A	12-Oct-24	05-Nov-24	
CON-EIT1690	Telecomm Termination, Glanding & Connection - Installation - Upper Deck (DELETED AFTER REVISED SCHEDU	15d	1d	23-Aug-24 A	23-Aug-24 A	02-Nov-24	19-Nov-24	
Vessel Rack		40d	1d	23-Aug-24 A	23-Aug-24 A	12-Oct-24	19-Nov-24	
CON-EIT1700	Telecomm Cable Trays - Installation - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	02-Nov-24	19-Nov-24	
CON-EIT1710	Telecomm Equipment - Installation - Vessel Rack (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	12-Oct-24	29-Oct-24	
CON-EIT1720	Telecomm Termination, Glanding & Connection - Installation - Vessel Rack (DELETED AFTER REVISED SCHEDU	15d	1d	23-Aug-24 A	23-Aug-24 A	02-Nov-24	19-Nov-24	
Safety		24d	24d	10-Feb-25	08-Mar-25	12-Oct-24	18-Nov-24	12d
CON-SAF1000	Safety Equipment - Installation - Lower Deck	12d	12d	10-Feb-25	22-Feb-25	12-Oct-24	29-Oct-24	4d
CON-SAF1010	Safety Equipment - Installation - Upper Deck	12d	12d	24-Feb-25	08-Mar-25	25-Oct-24	12-Nov-24	12d
CON-SAF1020	Safety Equipment - Installation - Vessel Rack	12d	12d	24-Feb-25	08-Mar-25	31-Oct-24	18-Nov-24	12d
Key Package Integration		233d	475d	10-Jul-23 A	01-Feb-25	18-Sep-24	03-Apr-25	121d
CON-8021	Transformer Main 66/6.6kV installation - DELETED	20d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8121	Transformer Aux. 6.6/0.4kV installation - DELETED	20d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8221	Transformer 0,4/6,6kV 630kVA installation - DELETED	20d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8226	LV Switchboard installation - DELETED	25d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8500	Shelter arrival at site AC UPS - DELETED	0d	0d		10-Jul-23 A			
CON-8510	UPS arrival at site - DELETED	0d	0d		10-Jul-23 A			
CON-8520	Battery bank arrival at site - DELETED	0d	0d		10-Jul-23 A			
CON-8530	AC & DC UPS installation - DELETED	25d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8130	Shelter HV Switchgear arrival at site - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8131	MV Switchboard arrival at site - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8132	MV Switchboard installation - DELETED	25d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8030	GIS Arrival at site - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8031	GIS installation - DELETED	14d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8710	Shelter Plant Instrument arrival at site - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8711	ICSS arrival at site - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8712	ICSS installation - DELETED	13d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8620	Telecomm arrival at site - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			

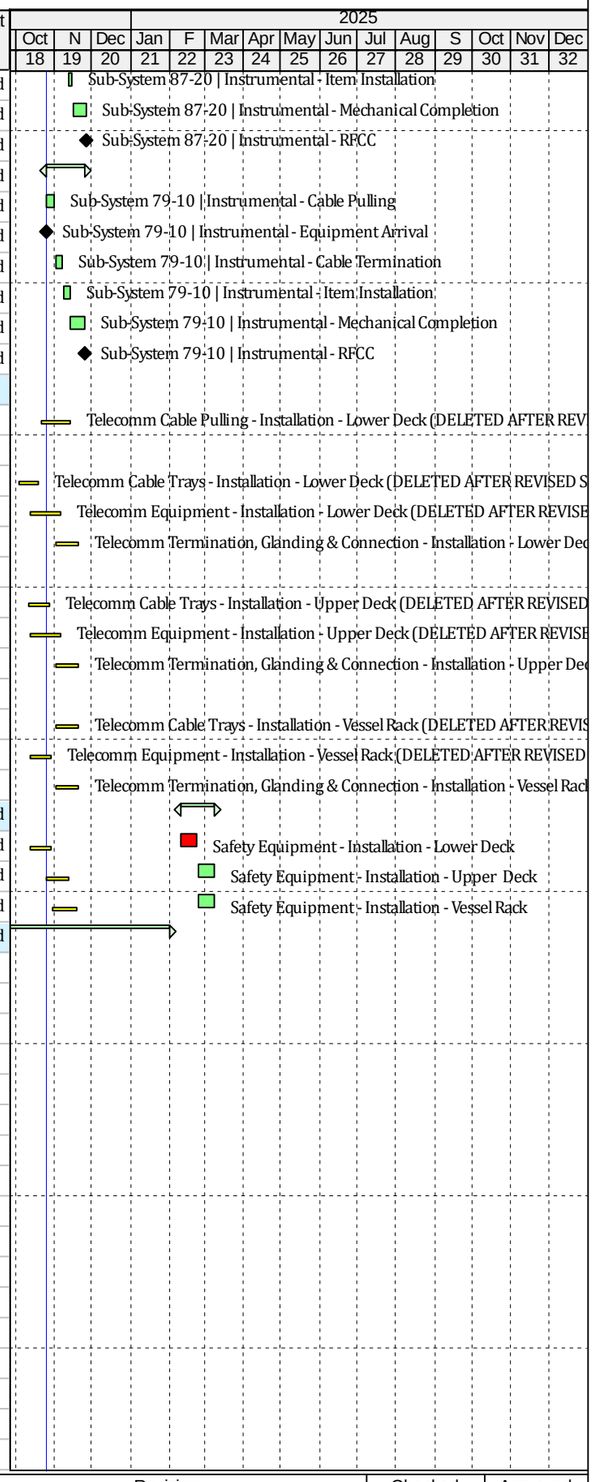

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-8621	Telecomm installation - DELETED	25d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8720	F&G - SIS - PCS arrival at site - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8721	F&G - SIS - PCS installation - DELETED	20d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8020	Transformer Main 66/6.6kV arrival at site - DELETED	0d	0d		10-Jul-23 A			
CON-8120	Transformer Aux. 6.6/0.4kV arrival at site - DELETED	0d	0d		10-Jul-23 A			
CON-8220	Transformer 0,4/6,6kV 630kVA arrival at site - DELETED	0d	0d		10-Jul-23 A			
CON-8224	Shelter arrival at site - DELETED	0d	0d		10-Jul-23 A			
CON-8225	LV Switchboard arrival at site - DELETED	0d	0d		10-Jul-23 A			
CON-EIT1160	Key Package Integration - Aux Transformer 6.6kV / 0.4kV - Installation	17d	5d	29-Jul-24 A	02-Aug-24 A	30-Oct-24	05-Nov-24	
CON-EIT1630	Key Package Integration - LV Transformer 0.4kV / 6.6kV- Installation	17d	5d	29-Jul-24 A	02-Aug-24 A	30-Oct-24	05-Nov-24	
CON-EIT1130	Key Package Integration - MV Switchgear 6.6kV - Installation	12d	10d	20-Aug-24 A	30-Aug-24 A	25-Sep-24	08-Oct-24	
CON-EIT1140	Key Package Integration - LV Switchgear 0.4kV - Installation	20d	4d	20-Aug-24 A	23-Aug-24 A	18-Sep-24	01-Oct-24	
CON-EIT1110	Construction Completion - Post Equipment Installation (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	30d	1d	23-Aug-24 A	23-Aug-24 A	14-Feb-25	20-Mar-25	
CON-EIT1120	Key Package Integration - GIS & Main Transformer - Mechanical Completion (DELETED AFTER REVISED SCHEI	12d	1d	23-Aug-24 A	23-Aug-24 A	21-Mar-25	03-Apr-25	
CON-EIT1170	Key Package Integration - Electrical Completion Works (DELETED AFTERREVISED SCHEDULE AUGUST 2024)	23d	1d	23-Aug-24 A	23-Aug-24 A	17-Oct-24	13-Nov-24	
CON-EIT1180	Key Package Integration - Mechanical Completion (Electrical) (DELETED AFTER REVISED SCHEDULE AUGUST	15d	1d	23-Aug-24 A	23-Aug-24 A	05-Nov-24	21-Nov-24	
CON-EIT1100	Key Package Integration - Main Transformer 66kV / 6,6kV Installation	17d	17d	26-Oct-24	15-Nov-24	08-Feb-25	13-Feb-25	75d
CON-EIT1090	Key Package Integration - HV Switchgear 66kV - GIS - Installation	10d	10d	22-Jan-25	01-Feb-25	03-Feb-25	13-Feb-25	36d
Mechanical Completion		172d	173d	23-Aug-24 A	18-Mar-25	11-Sep-24	28-Dec-24	91d
CON-FIN0904	Finalization - Electrical Mechanical Completion (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	60d	1d	23-Aug-24 A	23-Aug-24 A	28-Sep-24	07-Dec-24	
CON-FIN0902	Finalization - Equipment & Piping Mechanical Completion (DELETED AFTER REVISED SCHEDULE AUGUST 2(	60d	1d	23-Aug-24 A	23-Aug-24 A	28-Sep-24	07-Dec-24	
CON-FIN0906	Finalization - Instrumentation & Telecomm Mechanical Completion (DELETED AFTER REVISED SCHEDULE AU	60d	1d	23-Aug-24 A	23-Aug-24 A	17-Oct-24	28-Dec-24	
CON-FIN1100	Finalization - PRE-COMM - Leak Testing (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	10d	1d	23-Aug-24 A	23-Aug-24 A	27-Nov-24	07-Dec-24	
CON-FIN0900	Finalization - Structural Mechanical Completion - Build (Arch+Struc+MCT+Cable Tray)	60d	60d	09-Dec-24	20-Feb-25	11-Sep-24	20-Nov-24	26d
CON-FIN0910	Finalization - Painting and Insulation Mechanical Completion	40d	40d	31-Jan-25	18-Mar-25			4d
CON-FIN0920	Finalization - Safety Mechanical Completion	20d	20d	24-Feb-25	18-Mar-25			4d
Mechanical Completion - Transformer 0,4/6,6kV 630kVA		15d	15d	26-Oct-24	09-Nov-24			120d
CON-8222	Mechanical Completion - Transformer 0,4/6,6kV 630kVA	12d	12d	26-Oct-24	06-Nov-24			120d
CON-8223	RFCC Transformer 0,4/6,6kV 630kVA	3d	3d	07-Nov-24	09-Nov-24			120d
Mechanical Completion - Transformer Aux. 6.6/0.4kV		15d	15d	26-Oct-24	09-Nov-24			120d
CON-8122	Mechanical Completion - Transformer Aux. 6.6/0.4kV	12d	12d	26-Oct-24	06-Nov-24			120d
CON-8123	RFCC Transformer Aux. 6.6/0.4kV	3d	3d	07-Nov-24	09-Nov-24			120d
Mechanical Completion - Transformer Main 66/6.6kV		15d	15d	16-Nov-24	30-Nov-24			93d
CON-8022	Mechanical Completion - Transformer Main 66/6.6kV	12d	12d	16-Nov-24	27-Nov-24			93d
CON-8023	RFCC Transformer Main 66/6.6kV	3d	3d	28-Nov-24	30-Nov-24			93d
Mechanical Completion - BESS Without Batteries		13d	13d	05-Nov-24	19-Nov-24			26d
CON-8584	Mechanical Completion of all AUX installed BESS equipment (w/o batteries)	12d	12d	05-Nov-24	16-Nov-24			31d
CON-8585	Partial RFCC	2d	2d	18-Nov-24	19-Nov-24			26d
Mechanical Completion - AC & DC UPS		10d	10d	26-Oct-24	04-Nov-24			64d
CON-8540	Mechanical Completion - AC & DC UPS	7d	7d	26-Oct-24	01-Nov-24			64d
CON-8550	RFCC AC & DC UPS	3d	3d	02-Nov-24	04-Nov-24			64d
Mechanical Completion - BESS with Batteries		54d	54d	20-Nov-24	26-Jan-25			28d
CON-8587	Precommissioning of the system without batteries	14d	14d	20-Nov-24	05-Dec-24			26d
CON-8586	Installation of battery modules in BESS container 1	12d	12d	06-Dec-24	19-Dec-24			26d
CON-8588	Installation of battery modules in BESS container 2	9d	9d	20-Dec-24	02-Jan-25			26d
CON-8589	Mechanical completion - batteries	23d	23d	03-Jan-25	25-Jan-25			32d

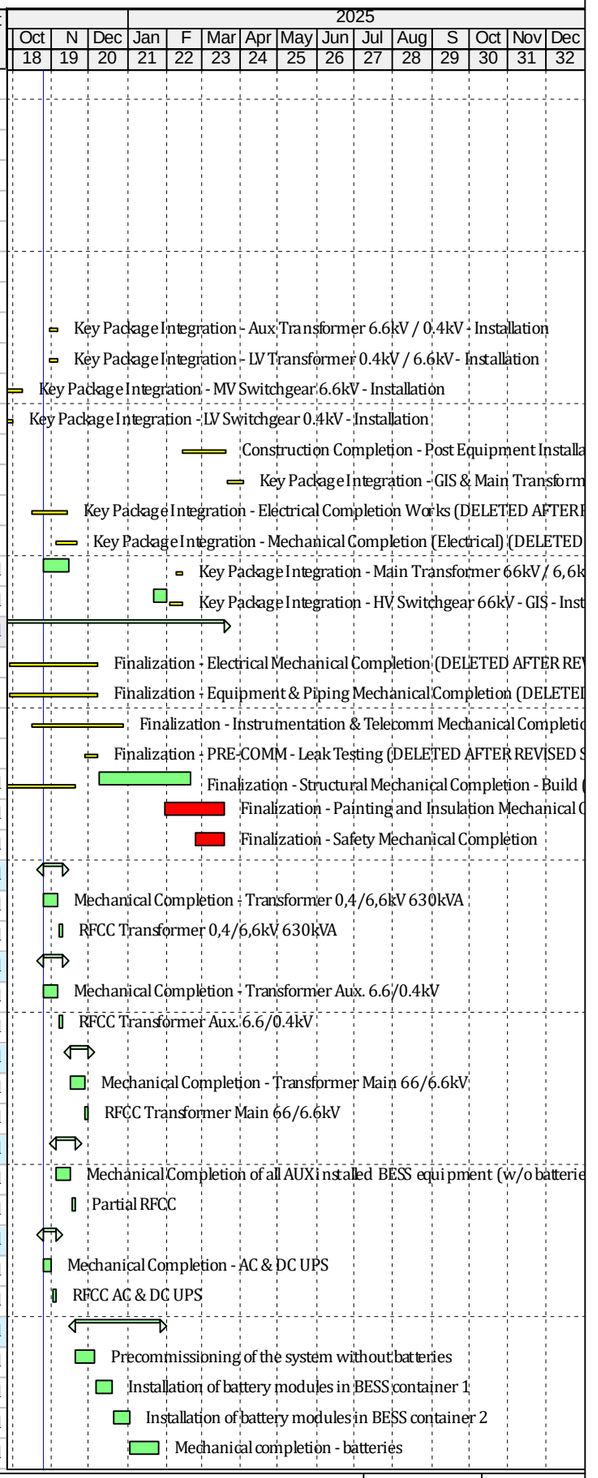

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-8590	Complete RFCC - BESS	1d	1d	26-Jan-25	26-Jan-25			32d
Mechanical Completion - LV Switchboard 400V		10d	54d	09-Sep-24 A	01-Nov-24			50d
CON-8227	Mechanical Completion - LV Switchboard	7d	54d	09-Sep-24 A	01-Nov-24			50d
CON-8228	RFCC LV Switchboard	3d	42d	21-Sep-24 A	01-Nov-24			50d
Mechanical Completion - HV/MV Switchboard 66kV/6.6kV		9d	9d	26-Oct-24	03-Nov-24			105d
CON-8133	Mechanical Completion - MV Switchboard	6d	6d	26-Oct-24	31-Oct-24			105d
CON-8134	RFCC MV Switchboard	3d	3d	01-Nov-24	03-Nov-24			105d
Mechanical Completion - F&G - SIS -PCS		15d	15d	28-Oct-24	11-Nov-24			81d
CON-8722	Mechanical Completion - F&G - SIS - PCS	12d	12d	28-Oct-24	08-Nov-24			81d
CON-8723	RFCC F&G - SIS - PCS	3d	3d	09-Nov-24	11-Nov-24			81d
Mechanical Completion - Fuel Cell System		15d	15d	10-Nov-24	24-Nov-24			96d
CON-8014	Mechanical Completion - Fuel cell system	12d	12d	10-Nov-24	21-Nov-24			96d
CON-8015	RFCC Fuel cell system	3d	3d	22-Nov-24	24-Nov-24			96d
Mechanical Completion - ICSS		9d	9d	26-Oct-24	03-Nov-24			89d
CON-8713	Mechanical Completion - ICSS	6d	6d	26-Oct-24	31-Oct-24			89d
CON-8714	RFCC ICSS	3d	3d	01-Nov-24	03-Nov-24			89d
Mechanical Completion - Small Power Sockets		18d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8212	Mechanical Completion - Small Power Sockets (DELETED AFTER REVISED SCHED ULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8213	RFCC Small Power Sockets (DELETED AFTER REVISED SCH EDULE AUGUST 2024)	3d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - Telecomm		9d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8622	Mechanical Completion - Telecomm (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	6d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8623	RFCC Telecomm (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	3d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - H2 Storage Vessels		16d	16d	15-Nov-24	30-Nov-24			107d
CON-2502	Mechanical Completion - H2 storage vessels	12d	12d	15-Nov-24	26-Nov-24			107d
CON-2503	RFCC H2 storage vessels	3d	3d	28-Nov-24	30-Nov-24			107d
Mechanical Completion - Lighting Fixtures		15d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8202	Mechanical Completion - Lighting Fixtures (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	12d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8203	RFCC Lighting Fixtures (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	3d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - Trace Heating		15d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8232	Mechanical Completion - Trace Heating (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	12d	1d	23-Aug-24 A	23-Aug-24 A			
CON-8233	RFCC Trace Heating (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	3d	1d	23-Aug-24 A	23-Aug-24 A			
Mechanical Completion - Water treatment system		15d	15d	25-Nov-24	09-Dec-24			84d
CON-5002	Mechanical Completion - Water treatment system	12d	12d	25-Nov-24	06-Dec-24			84d
CON-5003	RFCC Water treatment system	3d	3d	07-Dec-24	09-Dec-24			84d
Mechanical Completion - GIS		9d	9d	02-Feb-25	10-Feb-25			148d
CON-8032	Mechanical Completion - GIS	6d	6d	02-Feb-25	07-Feb-25			148d
CON-8033	RFCC GIS	3d	3d	08-Feb-25	10-Feb-25			148d
Finalization		35d	35d	01-Apr-25	16-May-25	01-Apr-25	16-May-25	2d
CON-FIN1010	Finalization - Barge Arrival at Yard	0d	0d	01-Apr-25*		01-Apr-25		0d
CON-FIN1020	Finalization - Topside - Erection Lower Grillage on Barge	20d	20d	07-Apr-25	03-May-25	04-Apr-25	30-Apr-25	2d
CON-FIN1090	Finalization - Transition Piece - Erection Lower Grillage on Barge	12d	12d	16-Apr-25	03-May-25	14-Apr-25	30-Apr-25	5d
CON-FIN1030	Finalization - Topside Weighing	2d	2d	29-Apr-25	30-Apr-25	02-May-25	03-May-25	4d
CON-FIN1070	Finalization - Transition Piece Weighing	2d	2d	02-May-25	03-May-25	05-May-25	06-May-25	5d
CON-FIN1040	Finalization - Topside Ready for Load-Out	0d	0d	05-May-25		05-May-25		2d
CON-FIN1060	Finalization - Topside Ready for Sail-Away	0d	0d	16-May-25*		16-May-25		2d
Onshore Commissioning & Integrated Testing		326d	545d	10-Jul-23 A	29-Apr-25	07-Dec-24	02-May-25	155d

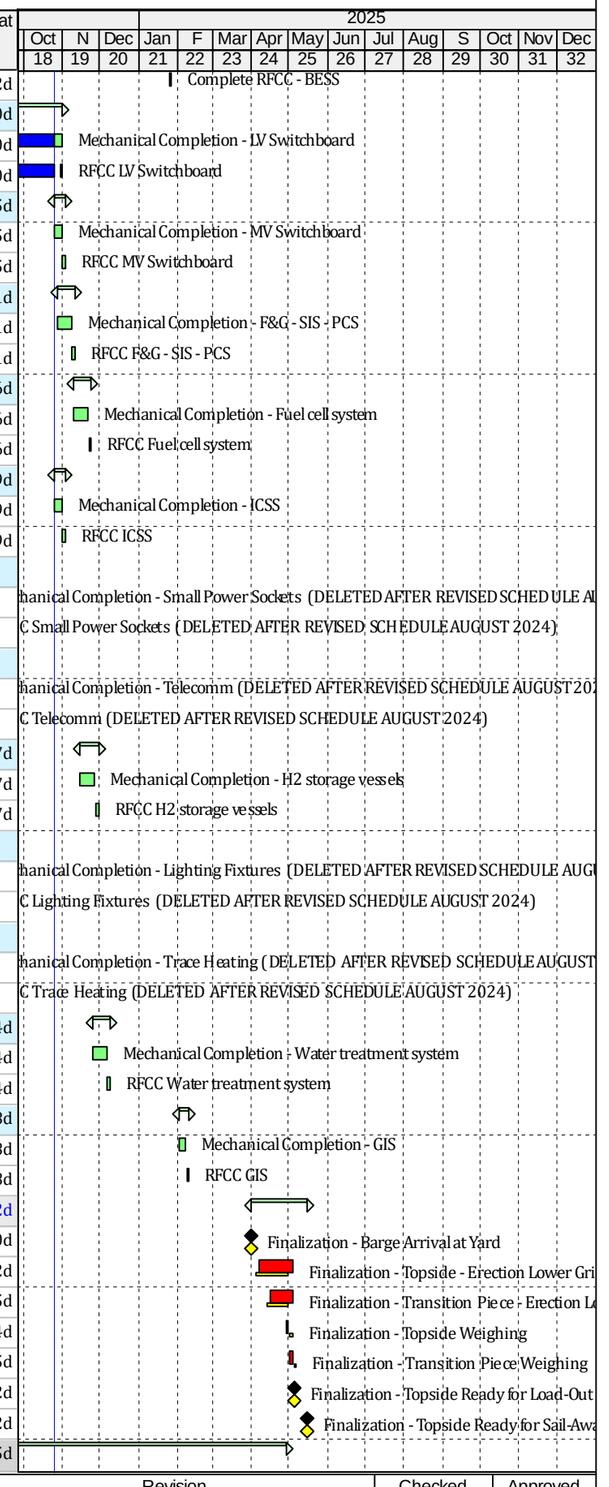

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Construction		252d	292d	10-Jul-23 A	26-Apr-24 A			
Structure		130d	292d	10-Jul-23 A	26-Apr-24 A			
CON-STR3020	Painting UDN - DELETED	20d	1d	10-Jul-23 A	10-Jul-23 A			
CON-STR3030	Painting UDS - DELETED	20d	1d	10-Jul-23 A	10-Jul-23 A			
CON-STR3040	Welding LDS to LDN - DELETED	21d	1d	10-Jul-23 A	10-Jul-23 A			
CON-STR3050	Welding UDS to UDN - DELETED	21d	1d	10-Jul-23 A	10-Jul-23 A			
CON-STR3060	Lifting lower deck to final erection position - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-STR3080	Preparation for lifting of the upper deck - DELETED	6d	1d	10-Jul-23 A	10-Jul-23 A			
CON-STR3090	Lifting of the upper deck - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-STR3000	Painting LDS - DELETED	19d	19d	18-Mar-24 A	05-Apr-24 A			
CON-STR3010	Painting LDN - DELETED	21d	21d	06-Apr-24 A	26-Apr-24 A			
Lighting Fixtures		50d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8200	Lighting Fixtures - Delivery atyard - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8201	Installation of Lighting Fixtures - DELETED	49d	1d	10-Jul-23 A	10-Jul-23 A			
Trace Heating		67d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8230	Trace Heating - Delivery at yard - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8231	Installation of Trace Heating - DELETED	66d	1d	10-Jul-23 A	10-Jul-23 A			
Small Power Sockets		21d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8210	Small Power Sockets - Delivery at yard - DELETED	1d	1d	10-Jul-23 A	10-Jul-23 A			
CON-8211	Installation of Small Power Sockets - DELETED	20d	1d	10-Jul-23 A	10-Jul-23 A			
Onshore Commissioning (Systems/Subsystems)		134d	149d	20-Sep-24 A	19-Mar-25	02-Apr-25	02-Apr-25	4d
Commissioning - Milestones		134d	145d	25-Sep-24 A	19-Mar-25	02-Apr-25	02-Apr-25	4d
COMM-ON-8200	TEMPORARY YARD POWER SUPPLIES 400V/230VAC	1d	1d	25-Sep-24 A	25-Sep-24 A			
COMM-ON-8220	E1 Reached	0d	0d		25-Sep-24 A			
COMM-ON-8201	TEMPORARY YARD POWER SUPPLY 6.6 kVAC	2d	2d	04-Nov-24	05-Nov-24			105d
COMM-ON-8221	E2 Reached	0d	0d		05-Nov-24			105d
COMM-ON-9174	E7 Reached	0d	0d		15-Nov-24			54d
COMM-ON-9044	E3 Reached	0d	0d		19-Nov-24			52d
COMM-ON-9074	E4 Reached	0d	0d		19-Nov-24			91d
COMM-ON-9394	E8 Reached	0d	0d		19-Nov-24			74d
COMM-ON-9104	E5 Reached	0d	0d		20-Nov-24			91d
COMM-ON-9134	E6 Reached	0d	0d		27-Nov-24			91d
COMM-ON-9884	I1 Reached	0d	0d		04-Dec-24			77d
COMM-ON-9894	I2 Reached	0d	0d		14-Dec-24			76d
COMM-ON2000	Onshore Commissioning Completed	0d	0d	19-Mar-25		02-Apr-25		4d
Commissioning - Electrical Systems and Subsystems		110d	123d	20-Sep-24 A	18-Mar-25			3d
E.00 Sub-System 88-00 | Earthing		7d	7d	16-Dec-24	24-Dec-24			59d
E.00 Sub-System 88-00 | Pre-Commissioning		4d	4d	16-Dec-24	19-Dec-24			59d
COMM-ON-10194	Earthing - Sub-System SS 88-00 Pre-Commissioning	4d	4d	16-Dec-24	19-Dec-24			59d
E.00 Sub-System 88-00 | Commissioning-1		3d	3d	20-Dec-24	24-Dec-24			59d
COMM-ON-10204	Earthing - Sub-System SS 88-00 Commissioning	3d	3d	20-Dec-24	24-Dec-24			59d
E.01 Sub-System 83-00 | 400 V Switchboard & Connection Box (SG-200N1)		41d	53d	23-Sep-24 A	05-Dec-24			72d
E.01 Sub-System 83-00 | Pre-Commissioning		5d	33d	23-Sep-24 A	07-Nov-24			34d
COMM-ON-3000	LV 400V SWBD SG-200N1 - Sub-System SS 83-00 Pre-Commissioning	5d	33d	23-Sep-24 A	07-Nov-24			34d
E.01 Sub-System 83-00 | Commissioning		20d	20d	08-Nov-24	05-Dec-24			72d
COMM-ON-9014	LV 400V SWBD SG-200N1 - Sub-System SS 83-00 Commissioning w/0.4Kv	5d	5d	08-Nov-24	14-Nov-24			34d

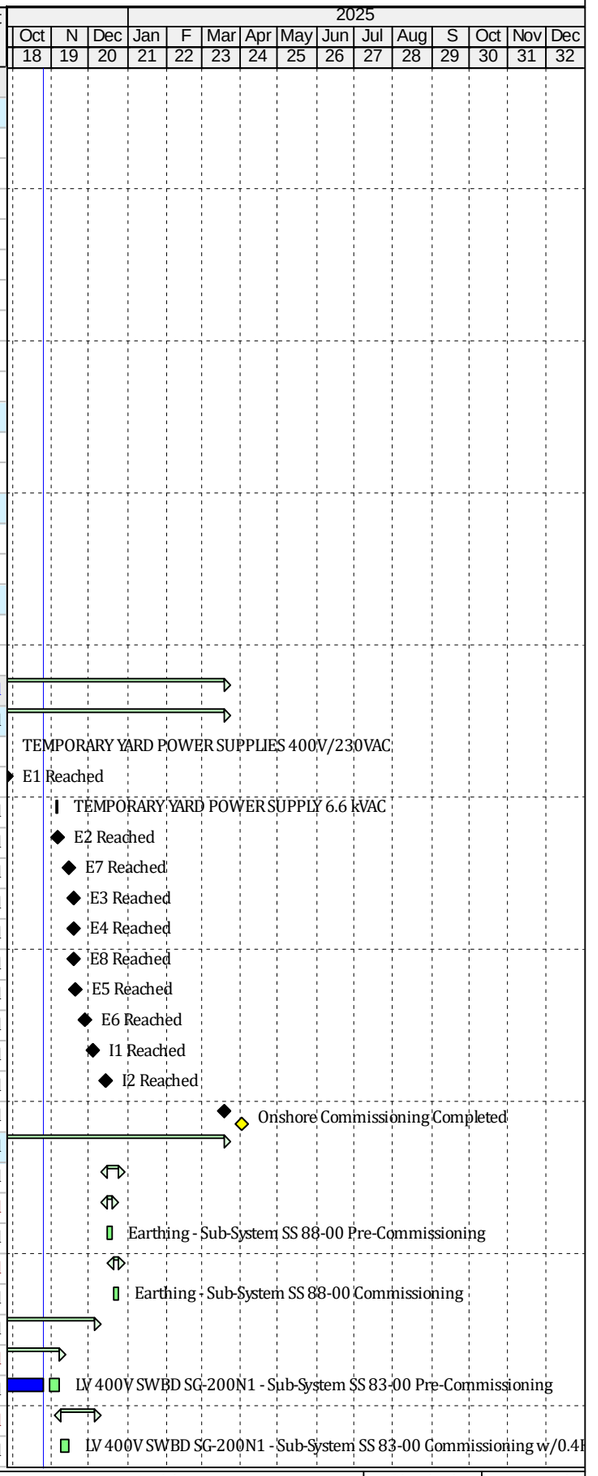

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON-9164	LV 400V SWBD SG-200N1 - Sub-System SS 83-00 Final Commissioning w/6.6Kv	2d	2d	04-Dec-24	05-Dec-24			72d
E.02 Sub-System 84-10 | AC 35 kVA UPS System (UP-200F3)		14d	40d	20-Sep-24 A	18-Nov-24			34d
E.02 Sub-System 84-10 | Pre-Commissioning		3d	38d	20-Sep-24 A	14-Nov-24			34d
COMM-ON-9024	UPS AC 35KVA UP-200F3 - Sub-System SS 84-10 Pre-Commissioning	3d	38d	20-Sep-24 A	14-Nov-24			34d
E.02 Sub-System 84-10 | Commissioning		2d	2d	15-Nov-24	18-Nov-24			34d
COMM-ON-9034	UPS AC 35KVA UP-200F3 - Sub-System SS 84-10 Commissioning	2d	2d	15-Nov-24	18-Nov-24			34d
E.03 Sub-System 84-20 | AC 15 kVA UPS System (UP-200F4)		14d	40d	20-Sep-24 A	18-Nov-24			61d
E.03 Sub-System 84-20 | Pre-Commissioning		3d	38d	20-Sep-24 A	14-Nov-24			61d
COMM-ON-9054	UPS AC 15KVA UP-200F4 - Sub-System 84-20 Pre-Commissioning	3d	38d	20-Sep-24 A	14-Nov-24			61d
E.03 Sub-System 84-20 | Commissioning		2d	2d	15-Nov-24	18-Nov-24			61d
COMM-ON-9064	UPS AC 15KVA UP-200F4 - Sub-System 84-20 Commissioning	2d	2d	15-Nov-24	18-Nov-24			61d
E.04 Sub-System 84-00 | DC 10 kVA UPS System (UP-200F1)		15d	41d	20-Sep-24 A	19-Nov-24			61d
E.04 Sub-System 84-00 | Pre-Commissioning		4d	38d	20-Sep-24 A	14-Nov-24			61d
COMM-ON-9084	UPS DC 10kVA UP-200F1 - Sub-System 84-00 Pre-Commissioning	4d	38d	20-Sep-24 A	14-Nov-24			61d
E.04 Sub-System 84-00 | Commissioning		3d	3d	15-Nov-24	19-Nov-24			61d
COMM-ON-9094	UPS DC 10kVA UP-200F1 - Sub-System 84-00 Commissioning	3d	3d	15-Nov-24	19-Nov-24			61d
E.05 Sub-System 82-00 | MV 6.6 kV Switchboard (SG-100D1)		5d	5d	20-Nov-24	26-Nov-24			61d
E.05 Sub-System 82-00 | Pre-Commissioning		3d	3d	20-Nov-24	22-Nov-24			61d
COMM-ON-9114	MV 6,6 kV SWBD SG-A00D1 - Sub-System 82-00 Pre-Commissioning	3d	3d	20-Nov-24	22-Nov-24			61d
E.05 Sub-System 82-00 | Commissioning		2d	2d	25-Nov-24	26-Nov-24			61d
COMM-ON-9124	MV 6,6 kV SWBD SG-A00D1 - Sub-System 82-00 Commissioning	2d	2d	25-Nov-24	26-Nov-24			61d
E.06 Sub-System 82-40 | Power Transformer 1.6 MVA (TR-200DE1)		5d	5d	27-Nov-24	03-Dec-24			69d
E.06 Sub-System 82-40 | Pre-Commissioning		3d	3d	27-Nov-24	29-Nov-24			69d
COMM-ON-9144	TRANS. 1,6 MVA TR-200DE1 - Sub-System 82-40 Pre-Commissioning	3d	3d	27-Nov-24	29-Nov-24			69d
E.06 Sub-System 82-40 | Commissioning		2d	2d	02-Dec-24	03-Dec-24			69d
COMM-ON-9154	TRANS. 1,6 MVA TR-200DE1 - Sub-System 82-40 Commissioning	2d	2d	02-Dec-24	03-Dec-24			69d
E.08 Sub-System 81-10 | GIS 66 kV (HNA6-AFA70)		5d	5d	03-Feb-25	07-Feb-25			30d
E.08 Sub-System 81-10 | Pre-Commissioning		5d	5d	03-Feb-25	07-Feb-25			30d
COMM-ON-9184	GIS 66 kV HNA6-AFA70 - Sub-System 81-10 Pre-Commissioning	5d	5d	03-Feb-25	07-Feb-25			30d
E.09 Sub-System 83-20 | 400/230 V Switchboard (DP-200N1)		10d	35d	30-Sep-24 A	18-Nov-24			34d
E.09 Sub-System 83-20 | Pre-Commissioning		3d	33d	30-Sep-24 A	14-Nov-24			34d
COMM-ON-9194	400/230 VAC SWBD DP-200N1 - Sub-System 83-20 Pre-Commissioning	3d	33d	30-Sep-24 A	14-Nov-24			34d
E.09 Sub-System 83-20 | Commissioning		2d	2d	15-Nov-24	18-Nov-24			34d
COMM-ON-9204	400/230 VAC SWBD DP-200N1 - Sub-System 83-20 Commissioning	2d	2d	15-Nov-24	18-Nov-24			34d
E.10 Sub-System 80-00 | Hydrogen Fuel Cell Package (A-80000)		31d	61d	30-Sep-24 A	24-Dec-24			51d
E.10 Sub-System 80-00 | Pre-Commissioning		29d	59d	30-Sep-24 A	20-Dec-24			51d
COMM-ON-9214	FUEL CELL A-80000 (PACKAGE) - Sub-System 80-00 Pre-Commissioning H2 ABSENT	3d	39d	30-Sep-24 A	22-Nov-24			66d
COMM-ON-10234	FUEL CELL A-80000 (PACKAGE) - Sub-System 80-00 Pre-Commissioning TEMP H2	5d	5d	16-Dec-24	20-Dec-24			51d
E.10 Sub-System 80-00 | Commissioning		22d	22d	25-Nov-24	24-Dec-24			51d
COMM-ON-9224	FUEL CELL A-80000 (PACKAGE) - Sub-System 80-00 Commissioning H2 ABSENT	2d	2d	25-Nov-24	26-Nov-24			69d
COMM-ON-10244	FUEL CELL A-80000 (PACKAGE) - Sub-System 80-00 Commissioning TEMP H2	2d	2d	23-Dec-24	24-Dec-24			51d
E.11 Sub-System 85-00 | BESS Package (A-85000)		62d	102d	20-Sep-24 A	17-Feb-25			24d
E.11 Sub-System 85-00 | Pre-Commissioning		54d	94d	20-Sep-24 A	05-Feb-25			24d
COMM-ON-9234	BESS A-85000 (PACKAGE) - w/o batteries - Sub-System 85-00 Pre-Commissioning	4d	42d	20-Sep-24 A	19-Nov-24			33d
COMM-ON-10214	BESS A-85000 (PACKAGE) - with batteries - Sub-System 85-00 Pre-Commissioning	8d	8d	27-Jan-25	05-Feb-25			24d
E.11 Sub-System 85-00 | Commissioning		60d	60d	20-Nov-24	17-Feb-25			24d

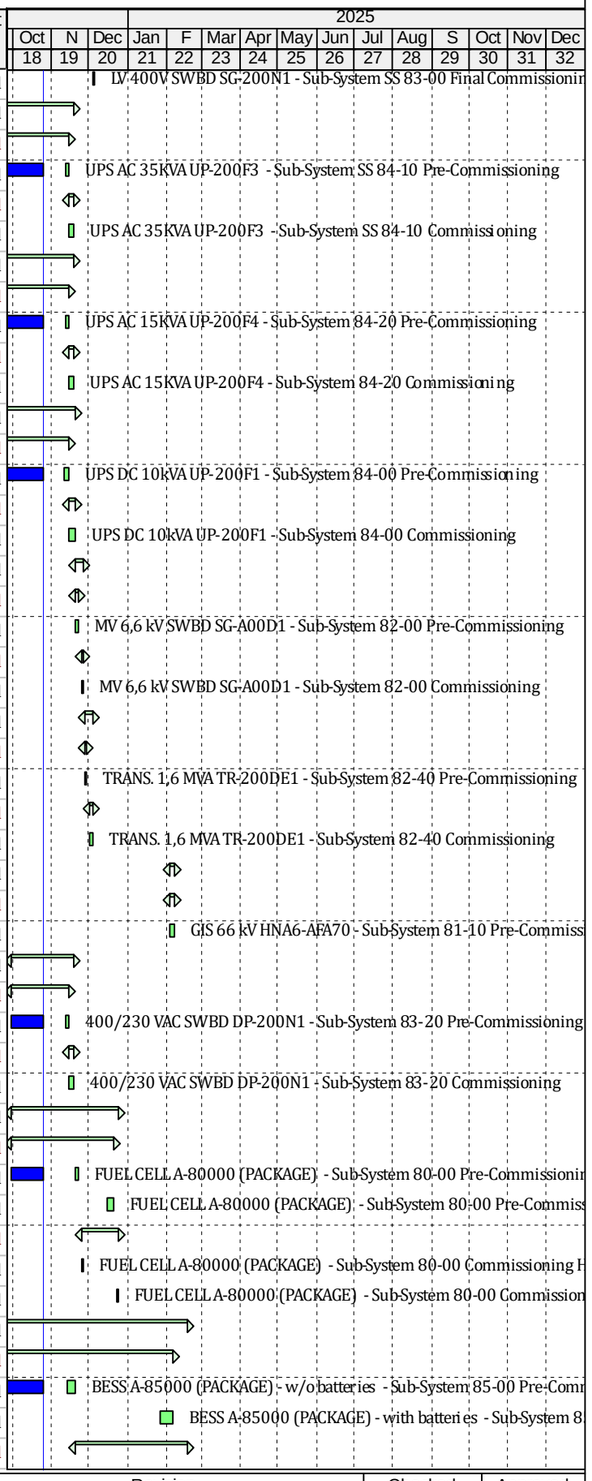

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON-9244	BESS A-85000 (PACKAGE) - w/o batteries - Sub-System 85-00 Commissioning	4d	4d	20-Nov-24	25-Nov-24			64d
COMM-ON-10224	BESS A-85000 (PACKAGE) - with batteries - Sub-System 85-00 Commissioning	8d	8d	06-Feb-25	17-Feb-25			24d
E.12 Sub-System 72-00 | NAVAID		8d	43d	30-Sep-24 A	28-Nov-24			67d
E.12 Sub-System 72-00 | Pre-Commissioning		4d	40d	30-Sep-24 A	25-Nov-24			67d
COMM-ON-9254	NAVAID - Sub-System 72-00 Pre-Commissioning	4d	40d	30-Sep-24 A	25-Nov-24			67d
E.12 Sub-System 72-00 | Commissioning		3d	3d	26-Nov-24	28-Nov-24			67d
COMM-ON-9264	NAVAID - Sub-System 72-00 Commissioning	3d	3d	26-Nov-24	28-Nov-24			67d
E.13 Sub-System 83-35 | Emergency Lighting		10d	10d	27-Dec-24	13-Jan-25			49d
E.13 Sub-System 83-35 | Pre-Commissioning		5d	5d	27-Dec-24	03-Jan-25			49d
COMM-ON-9274	EMERGENCY LIGHTING - Sub-System 83-35 Pre-Commissioning	5d	5d	27-Dec-24	03-Jan-25			49d
E.13 Sub-System 83-35 | Commissioning		5d	5d	07-Jan-25	13-Jan-25			49d
COMM-ON-9284	EMERGENCY LIGHTING - Sub-System 83-35 Commissioning	5d	5d	07-Jan-25	13-Jan-25			49d
E.14 Sub-System 83-40 | Normal Lighting		10d	10d	16-Dec-24	31-Dec-24			56d
E.14 Sub-System 83-40 | Pre-Commissioning		5d	5d	16-Dec-24	20-Dec-24			56d
COMM-ON-9294	NORMAL LIGHTING - Sub-System 83-40 Pre-Commissioning	5d	5d	16-Dec-24	20-Dec-24			56d
E.14 Sub-System 83-40 | Commissioning		5d	5d	23-Dec-24	31-Dec-24			56d
COMM-ON-9304	NORMAL LIGHTING - Sub-System 83-40 Commissioning	5d	5d	23-Dec-24	31-Dec-24			56d
E.15 Sub-System 83-55 | Power Sockets		7d	7d	22-Jan-25	30-Jan-25			36d
E.15 Sub-System 83-55 | Pre-Commissioning		4d	4d	22-Jan-25	27-Jan-25			36d
COMM-ON-9314	POWER SOCKETS - Sub-System 83-55 Pre-Commissioning	4d	4d	22-Jan-25	27-Jan-25			36d
E.15 Sub-System 83-55 | Commissioning		3d	3d	28-Jan-25	30-Jan-25			36d
COMM-ON-9324	POWER SOCKETS - Sub-System 83-55 Commissioning	3d	3d	28-Jan-25	30-Jan-25			36d
E.16 Sub-System 83-50 | WeldingSockets		9d	61d	07-Oct-24 A	03-Jan-25			35d
E.16 Sub-System 83-50 | Pre-Commissioning		3d	58d	07-Oct-24 A	30-Dec-24			35d
COMM-ON-9334	WELDING SOCKETS - Sub-System 83-50 Precommissioning	3d	58d	07-Oct-24 A	30-Dec-24			35d
E.16 Sub-System 83-50 | Commissioning		3d	3d	31-Dec-24	03-Jan-25			35d
COMM-ON-9344	WELDING SOCKETS - Sub-System 83-50 Commissioning	3d	3d	31-Dec-24	03-Jan-25			35d
E.17 Sub-System 83-65 | Electrical Trace Heating		9d	75d	30-Sep-24 A	17-Jan-25			31d
E.17 Sub-System 83-65 | Pre-Commissioning		6d	70d	30-Sep-24 A	10-Jan-25			31d
COMM-ON-9354	ELECTRICAL TRACE HEATING - Sub-System 83-65 Pre-Commissioning	6d	70d	30-Sep-24 A	10-Jan-25			31d
E.17 Sub-System 83-65 | Commissioning		5d	5d	13-Jan-25	17-Jan-25			31d
COMM-ON-9364	ELECTRICAL TRACE HEATING - Sub-System 83-65 Commissioning	5d	5d	13-Jan-25	17-Jan-25			31d
E.18 Sub-System 83-75 | Temporary Diesel Generator		5d	5d	10-Jan-25	16-Jan-25			46d
E.18 Sub-System 83-75 | Pre-Commissioning		3d	3d	10-Jan-25	14-Jan-25			46d
COMM-ON-9374	TEMP. DIESEL GENERATOR - Sub-System 83-75 Pre-Commissioning	3d	3d	10-Jan-25	14-Jan-25			46d
E.18 Sub-System 83-75 | Commissioning		2d	2d	15-Jan-25	16-Jan-25			46d
COMM-ON-9384	TEMP. DIESEL GENERATOR - Sub-System 83-75 Commissioning	2d	2d	15-Jan-25	16-Jan-25			46d
E.19 Sub-System 81-20 | Power Transformer 7 MVA (TR-100AD1)		5d	5d	20-Jan-25	24-Jan-25			31d
E.19 Sub-System 81-20 | Pre-Commissioning		5d	5d	20-Jan-25	24-Jan-25			31d
COMM-ON-9404	TRANS. 7,0 MVA TR-100AD1 - Sub-System 81-20 Pre-Commissioning	5d	5d	20-Jan-25	24-Jan-25			31d
E.20 Sub-System 20-00 | Electrolyser Package (A-20000)		14d	84d	14-Oct-24 A	13-Feb-25			26d
E.20 Sub-System 20-00 | Pre-Commissioning		3d	79d	14-Oct-24 A	06-Feb-25			26d
COMM-ON-9414	ELECTROLYZER PACKAGE (H2 ABSENT) - Sub-System 20-00 Pre-Commissioning	2d	70d	14-Oct-24 A	24-Jan-25			31d
COMM-ON-10254	ELECTROLYZER PACKAGE (H2 PRODUCED) - Sub-System 20-00 Pre-Commissioning	3d	3d	04-Feb-25	06-Feb-25			26d
E.20 Sub-System 20-00 | Commissioning		14d	14d	27-Jan-25	13-Feb-25			26d
COMM-ON-9424	ELECTROLYZER PACKAGE (H2 ABSENT) - Sub-System 20-00 Commissioning	1d	1d	27-Jan-25	27-Jan-25			31d

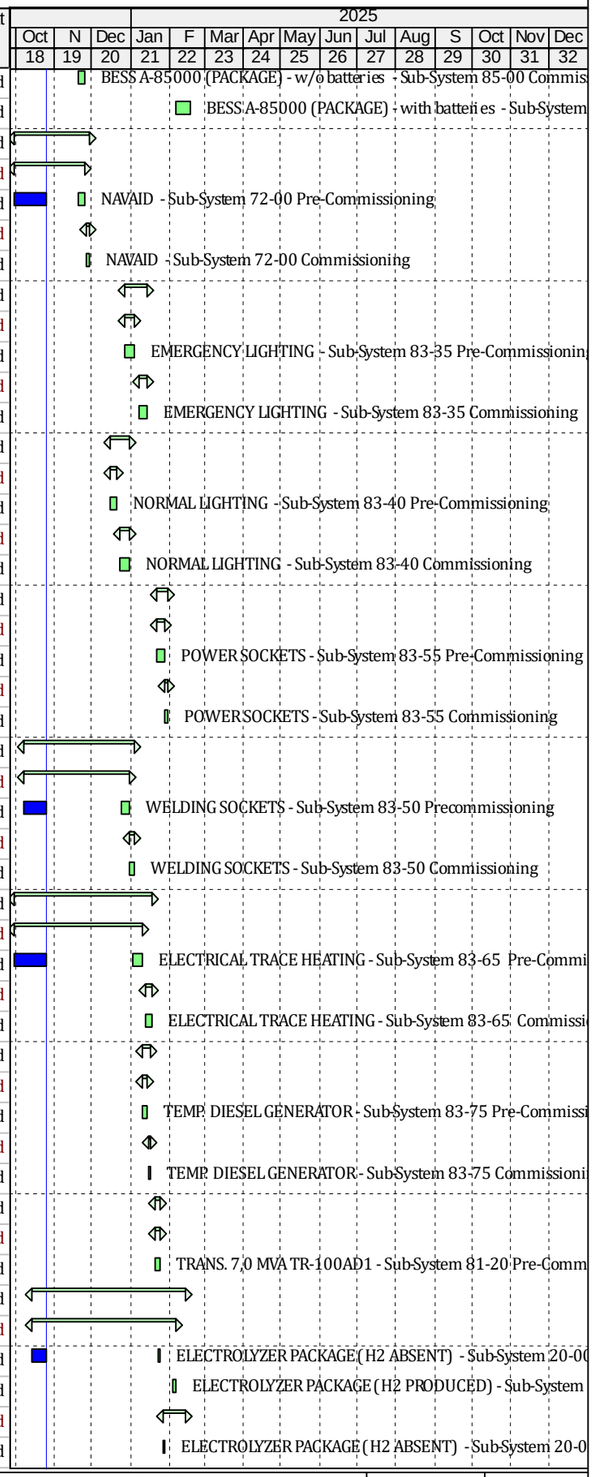

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON-10264	ELECTROLYZER PACKAGE (H2 PRODUCED) - Sub-System 20-00 Commissioning	5d	5d	07-Feb-25	13-Feb-25			26d
E.21 Sub-System 82-30 | Power Transformer 1.25 MVA (TA30 FUEL CELL)		4d	4d	27-Nov-24	02-Dec-24			61d
E.21 Sub-System 82-30 | Pre-Commissioning		2d	2d	27-Nov-24	28-Nov-24			61d
COMM-ON-9434	TRANS. 1,25 MVA (F.C.) TA30 (H2 ABSENT) - Sub-System 82-30 Pre-Commissioning	2d	2d	27-Nov-24	28-Nov-24			61d
E.21 Sub-System 82-30 | Commissioning		2d	2d	29-Nov-24	02-Dec-24			61d
COMM-ON-9444	TRANS. 1,25 MVA (F.C.) TA30 (H2 ABSENT) - Sub-System 82-30 Commissioning	2d	2d	29-Nov-24	02-Dec-24			61d
E.22 Sub-System 82-10 | Power Transformer 1.25 MVA (18T1 BESS)		4d	4d	03-Dec-24	06-Dec-24			61d
E.22 Sub-System 82-10 | Pre-Commissioning		2d	2d	03-Dec-24	04-Dec-24			61d
COMM-ON-9454	TRANS. 1,25 MVA (BESS) 1BT1 - Sub-System 82-10 Pre-Commissioning	2d	2d	03-Dec-24	04-Dec-24			61d
E.22 Sub-System 82-10 | Commissioning		2d	2d	05-Dec-24	06-Dec-24			61d
COMM-ON-9464	TRANS. 1,25 MVA (BESS) 1BT1 - Sub-System 82-10 Commissioning	2d	2d	05-Dec-24	06-Dec-24			61d
E.23 Sub-System 82-20 | Power Transformer 3.15 MVA (T4 ELECTROLYSER)		10d	10d	31-Dec-24	15-Jan-25			47d
E.23 Sub-System 82-20 | Pre-Commissioning		5d	5d	31-Dec-24	08-Jan-25			47d
COMM-ON-9474	TRANS. 3,15 MVA (ELECTROL.) T4 (H2 ABSENT) - Sub-System 82-20 Pre-Commissioning	5d	5d	31-Dec-24	08-Jan-25			47d
E.23 Sub-System 82-20 | Commissioning		5d	5d	09-Jan-25	15-Jan-25			47d
COMM-ON-9484	TRANS. 3,15 MVA (ELECTROL.) T4 (H2 ABSENT) - Sub-System 82-20 Commissioning	5d	5d	09-Jan-25	15-Jan-25			47d
E.24 Sub-System 82-50 | Solar PV Package Power Transformer 0.5 MVA (TR-200ED1)		10d	10d	27-Nov-24	10-Dec-24			69d
E.24 Sub-System 82-50 | Pre-Commissioning		5d	5d	27-Nov-24	03-Dec-24			69d
COMM-ON-9494	TRANS. 0,50 MVA (SOLAR) TR-200ED1 - Sub-System 82-50 Pre-Commissioning	5d	5d	27-Nov-24	03-Dec-24			69d
E.24 Sub-System 82-50 | Commissioning		5d	5d	04-Dec-24	10-Dec-24			69d
COMM-ON-9504	TRANS. 0,50 MVA (SOLAR) TR-200ED1 - Sub-System 82-50 Commissioning	5d	5d	04-Dec-24	10-Dec-24			69d
E.25 Sub-System 81-00 | 66 kV Subsea Cable - NEEDED FOR OFFSHORE		2d	2d	17-Mar-25	18-Mar-25			3d
E.25 Sub-System 81-00 | Pre-Commissioning		2d	2d	17-Mar-25	18-Mar-25			3d
COMM-ON-9514	66 kV SUBSEA CABLE - Sub-System 81-00 Pre-Commissioning - NEEDED FOR OFFSHORE	2d	2d	17-Mar-25	18-Mar-25			3d
Commissioning - Structural and HVAC Systems		65d	79d	20-Sep-24 A	15-Jan-25			47d
M.01 Sub-System 90-02 | LV Switchgear Room B-200 (Internal Services)		3d	3d	13-Jan-25	15-Jan-25			47d
M.01 Sub-System 90-02 | Pre-Commissioning		3d	3d	13-Jan-25	15-Jan-25			47d
COMM-ON-9524	LV SWITCHGEAR ROOM B-200 - Sub-System 90-02 Pre-Commissioning DELETED	3d	3d	13-Jan-25	15-Jan-25			47d
M.02 Sub-System 90-03 | UPS System Equipment Room B-300 (Internal Services)		3d	3d	02-Jan-25	07-Jan-25			53d
M.02 Sub-System 90-03 | Pre-Commissioning		3d	3d	02-Jan-25	07-Jan-25			53d
COMM-ON-9534	UPS SYSTEMS ROOM B-300 - Sub-System 90-03 Pre-Commissioning DELETED	3d	3d	02-Jan-25	07-Jan-25			53d
M.03 Sub-System 90-01 | HV-MV Switchgear Room B-100 (Internal Services)		3d	3d	02-Jan-25	07-Jan-25			53d
M.03 Sub-System 90-01 | Pre-Commissioning		3d	3d	02-Jan-25	07-Jan-25			53d
COMM-ON-9544	HV/MV SWGR ROOM B-100 - Sub-System 90-01 Pre-Commissioning DELETED	3d	3d	02-Jan-25	07-Jan-25			53d
M.04 Sub-System 90-04 | I&T System Equipment Room B-400 (Internal Services)		3d	3d	13-Jan-25	15-Jan-25			47d
M.04 Sub-System 90-04 | Pre-Commissioning		3d	3d	13-Jan-25	15-Jan-25			47d
COMM-ON-9554	I&T SYSTEMS ROOM B-400 - Sub-System 90-04 Pre-Commissioning DELETED	3d	3d	13-Jan-25	15-Jan-25			47d
H.01 Sub-System 77-20 | HVAC LV Switchgear Room B-200		26d	40d	20-Sep-24 A	15-Nov-24			86d
H.01 Sub-System 77-20 | Pre-Commissioning		2d	39d	20-Sep-24 A	14-Nov-24			86d
COMM-ON-9564	HVAC ROOM B-200 - Sub-System 77-20 Pre-Commissioning	2d	39d	20-Sep-24 A	14-Nov-24			86d
H.01 Sub-System 77-20 | Commissioning		1d	1d	15-Nov-24	15-Nov-24			86d
COMM-ON-9574	HVAC ROOM B-200 - Sub-System 77-20 Commissioning	1d	1d	15-Nov-24	15-Nov-24			86d
H.02 Sub-System 77-30 | HVAC UPS Equipment Room B-300		25d	40d	20-Sep-24 A	15-Nov-24			86d
H.02 Sub-System 77-30 | Pre-Commissioning		2d	39d	20-Sep-24 A	14-Nov-24			86d
COMM-ON-9584	HVAC ROOM B-300 - Sub-System 77-30 Pre-Commissioning	2d	39d	20-Sep-24 A	14-Nov-24			86d
H.02 Sub-System 77-30 | Commissioning		1d	1d	15-Nov-24	15-Nov-24			86d

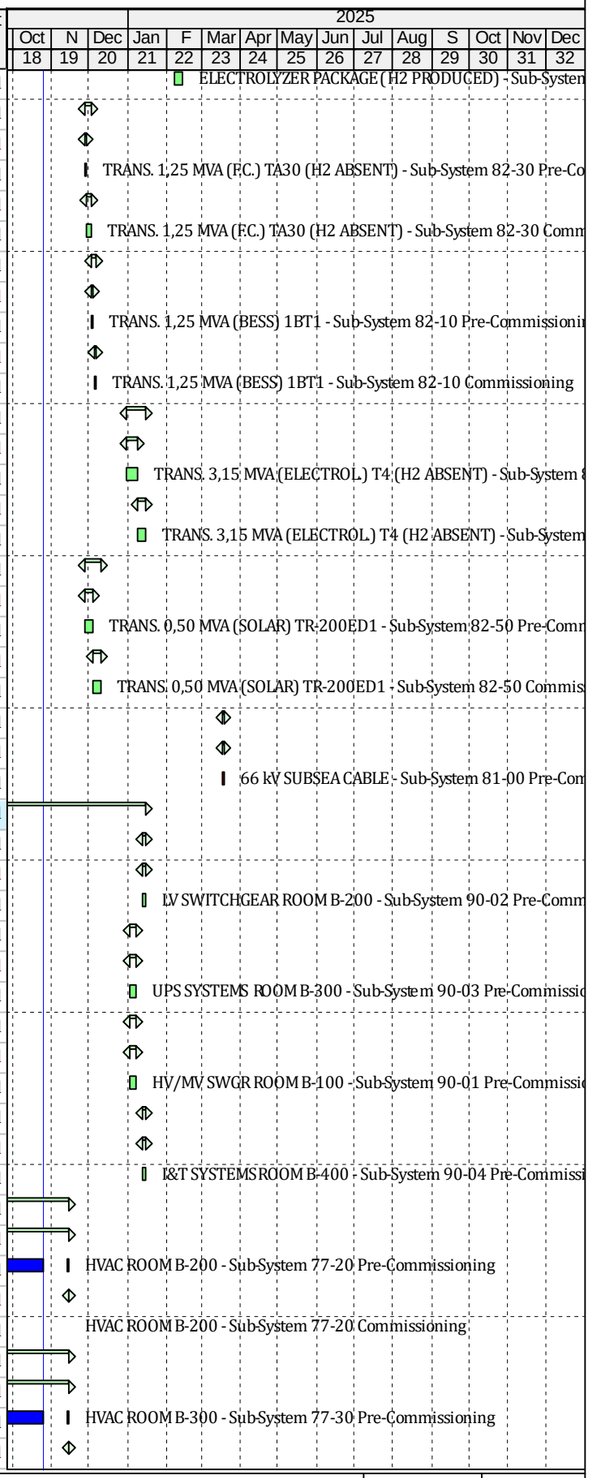


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON-9594	HVAC ROOM B-300 - Sub-System 77-30 Commissioning	1d	1d	15-Nov-24	15-Nov-24			86d
H.03 Sub-System 77-10 | HVAC HV/MV Switchgear Room B-100		24d	40d	20-Sep-24 A	15-Nov-24			86d
H.03 Sub-System 77-10 | Pre-Commissioning		2d	39d	20-Sep-24 A	14-Nov-24			86d
COMM-ON-9604	HVAC ROOM B-100 - Sub-System 77-10 Pre-Commissioning	2d	39d	20-Sep-24 A	14-Nov-24			86d
H.03 Sub-System 77-10 | Commissioning		1d	1d	15-Nov-24	15-Nov-24			86d
COMM-ON-9614	HVAC ROOM B-100 - Sub-System 77-10 Commissioning	1d	1d	15-Nov-24	15-Nov-24			86d
H.04 Sub-System 77-40 | HVAC I&T Equipment Room B-400		7d	34d	30-Sep-24 A	15-Nov-24			86d
H.04 Sub-System 77-40 | Pre-Commissioning		2d	33d	30-Sep-24 A	14-Nov-24			86d
COMM-ON-9624	HVAC ROOM B-400 - Sub-System 77-40 Pre-Commissioning	2d	33d	30-Sep-24 A	14-Nov-24			86d
H.04 Sub-System 77-40 | Commissioning		1d	1d	15-Nov-24	15-Nov-24			86d
COMM-ON-9634	HVAC ROOM B-400 - Sub-System 77-40 Commissioning	1d	1d	15-Nov-24	15-Nov-24			86d
Commissioning - CCS and EMCS Systems		54d	54d	05-Nov-24	10-Jan-25			61d
L01 Sub-System 87-10 | Process Control System (PCS)		25d	25d	25-Nov-24	31-Dec-24			56d
I.01 Sub-System 87-10 | Pre-Commissioning		20d	20d	25-Nov-24	20-Dec-24			56d
COMM-ON-9644	PCS - Sub-System 87-10 Pre-Commissioning	20d	20d	25-Nov-24	20-Dec-24			56d
I.01 Sub-System 87-10 | Commissioning		5d	5d	23-Dec-24	31-Dec-24			56d
COMM-ON-9654	PCS - Sub-System 87-10 Commissioning	5d	5d	23-Dec-24	31-Dec-24			56d
Sub-System 87-20 | Process Control System (PCS) - Instrumentation		10d	10d	27-Nov-24	07-Dec-24			86d
Sub-System 87-20 | Pre-Commissioning		5d	5d	27-Nov-24	02-Dec-24			86d
COMM-ON-9655	FIELD INSTRUMENTS AND DEVICES EQUIPMENT PKGS - Sub-System 87-20 Pre-Commissioning	5d	5d	27-Nov-24	02-Dec-24			86d
Sub-System 87-20 | Commissioning		5d	5d	03-Dec-24	07-Dec-24			86d
COMM-ON-9656	FIELD INSTRUMENTS AND DEVICES EQUIPMENT PKGS - Sub-System 87-20 Commissioning	5d	5d	03-Dec-24	07-Dec-24			86d
L02 Sub-System 79-00 | Emergency Shutdown Systems (SIS)		11d	11d	19-Nov-24	03-Dec-24			66d
I.02 Sub-System 79-00 | Pre-Commissioning		6d	6d	19-Nov-24	26-Nov-24			66d
COMM-ON-9664	SIS - Sub-System 79-00 Pre-Commissioning	6d	6d	19-Nov-24	26-Nov-24			66d
I.02 Sub-System 79-00 | Commissioning		5d	5d	27-Nov-24	03-Dec-24			66d
COMM-ON-9674	SIS - Sub-System 79-00 Commissioning	5d	5d	27-Nov-24	03-Dec-24			66d
Sub-System 79-10 | Emergency Shutdown Systems (SIS) - Devices		10d	10d	04-Dec-24	14-Dec-24			80d
Sub-System 79-10 | Pre-Commissioning		5d	5d	04-Dec-24	09-Dec-24			80d
COMM-ON-9657	SIS PUSHBUTTONS SHUTDOWN VALVES - Sub-System 79-10 Pre-Commissioning	5d	5d	04-Dec-24	09-Dec-24			80d
Sub-System 79-10 | Commissioning		5d	5d	10-Dec-24	14-Dec-24			80d
COMM-ON-9658	SIS PUSHBUTTONS SHUTDOWN VALVES - Sub-System 79-10 Commissioning	5d	5d	10-Dec-24	14-Dec-24			80d
L03 Sub-System 70-00 | F&G Control System		10d	10d	20-Nov-24	03-Dec-24			50d
I.03 Sub-System 70-00 | Pre-Commissioning		5d	5d	20-Nov-24	26-Nov-24			50d
COMM-ON-9684	F&G - Sub-System 70-00 Pre-Commissioning	5d	5d	20-Nov-24	26-Nov-24			50d
I.03 Sub-System 70-00 | Commissioning		5d	5d	27-Nov-24	03-Dec-24			50d
COMM-ON-9694	F&G - Sub-System 70-00 Commissioning	5d	5d	27-Nov-24	03-Dec-24			50d
L04 Sub-System 86-00 | Data Networks		11d	11d	19-Nov-24	03-Dec-24			51d
I.04 Sub-System 86-00 | Pre-Commissioning		6d	6d	19-Nov-24	26-Nov-24			51d
COMM-ON-9704	DATA NETWORKS- Sub-System 86-00 Pre-Commissioning	6d	6d	19-Nov-24	26-Nov-24			51d
I.04 Sub-System 86-00 | Commissioning		5d	5d	27-Nov-24	03-Dec-24			51d
COMM-ON-9714	DATA NETWORKS- Sub-System 86-00 Commissioning	5d	5d	27-Nov-24	03-Dec-24			51d
L05 Sub-System 87-00 | Power Distribution System (EMCS)		19d	19d	19-Nov-24	13-Dec-24			50d
I.05 Sub-System 87-00 | Pre-Commissioning		10d	10d	19-Nov-24	02-Dec-24			50d
COMM-ON-9724	EMCS - Sub-System 87-00 Pre-Commissioning	10d	10d	19-Nov-24	02-Dec-24			50d
I.05 Sub-System 87-00 | Commissioning		9d	9d	03-Dec-24	13-Dec-24			50d

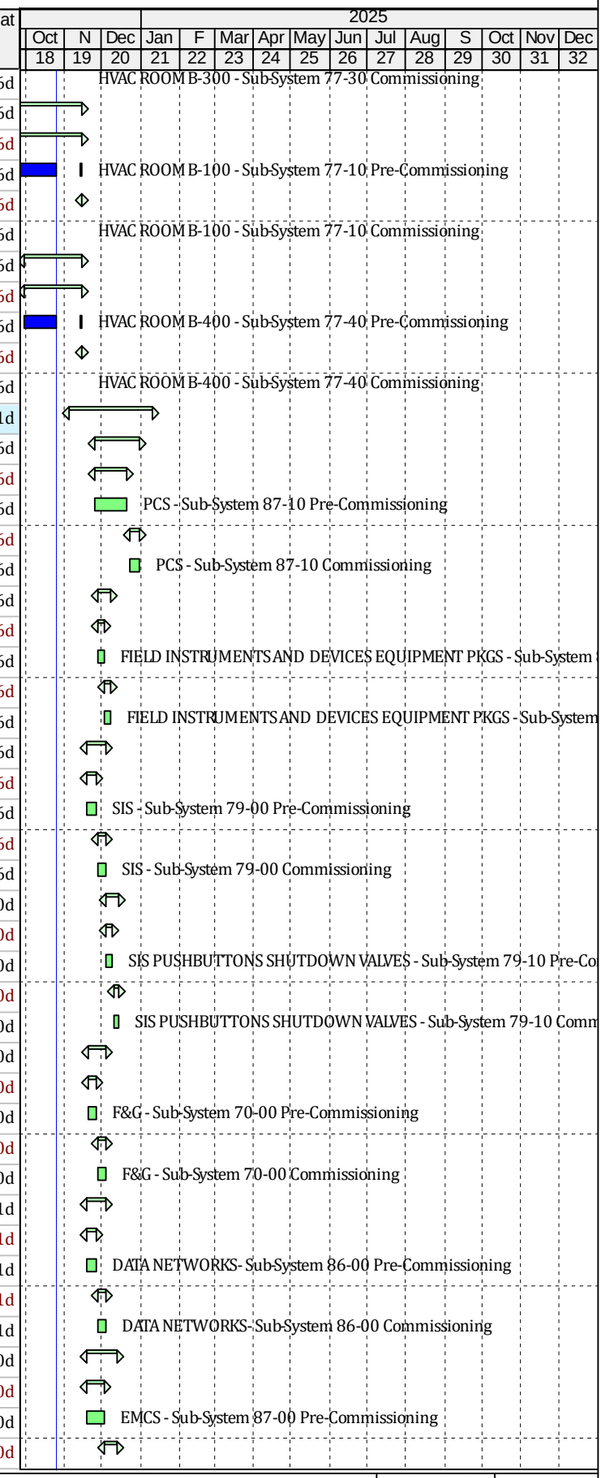

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON-9734	EMCS - Sub-System 87-00 Commissioning	9d	9d	03-Dec-24	13-Dec-24			50d
L06 Sub-System 70-10/11 | F&G H2 GAS INDOOR LOW /UPPER		4d	4d	04-Dec-24	09-Dec-24			50d
I.06 Sub-System 70-10/11 | Pre-Commissioning		2d	2d	04-Dec-24	05-Dec-24			50d
COMM-ON-9744	F&G H2 GAS INDOOR LOW/UPPER - Sub-System 70-10/11 Pre-Commissioning	2d	2d	04-Dec-24	05-Dec-24			50d
I.06 Sub-System 70-10/11 | Commissioning		2d	2d	06-Dec-24	09-Dec-24			50d
COMM-ON-9754	F&G H2 GAS INDOOR LOW/UPPER - Sub-System 70-10/11 Commissioning	2d	2d	06-Dec-24	09-Dec-24			50d
L07 Sub-System 70-14/15 | F&G FLAME INDOOR LOW/UPPER		4d	4d	10-Dec-24	13-Dec-24			50d
I.07 Sub-System 70-14/15 | Pre-Commissioning		2d	2d	10-Dec-24	11-Dec-24			50d
COMM-ON-9764	F&G FLAME INDOOR LOW/UPPER - Sub-System 70-14/15 Pre-Commissioning	2d	2d	10-Dec-24	11-Dec-24			50d
I.07 Sub-System 70-14/15 | Commissioning		2d	2d	12-Dec-24	13-Dec-24			50d
COMM-ON-9774	F&G FLAME INDOOR LOW/UPPER - Sub-System 70-14/15 Commissioning	2d	2d	12-Dec-24	13-Dec-24			50d
L08 Sub-System 70-18/19 | F&G SMOKE INDOOR LOW/UPPER		4d	4d	16-Dec-24	19-Dec-24			50d
I.08 Sub-System 70-18/19 | Pre-Commissioning		2d	2d	16-Dec-24	17-Dec-24			50d
COMM-ON-9784	F&G SMOKE INDOOR LOW/UPPER - Sub-System 70-18/19 Pre-Commissioning	2d	2d	16-Dec-24	17-Dec-24			50d
I.08 Sub-System 70-18/19 | Commissioning		2d	2d	18-Dec-24	19-Dec-24			50d
COMM-ON-9794	F&G SMOKE INDOOR LOW/UPPER - Sub-System 70-18/19 Commissioning	2d	2d	18-Dec-24	19-Dec-24			50d
L09 Sub-System 70-21/22 | F&G H2 GAS OUTDOOR LOW/UPPER		3d	3d	20-Dec-24	24-Dec-24			50d
I.09 Sub-System 70-21/22 | Pre-Commissioning		2d	2d	20-Dec-24	23-Dec-24			50d
COMM-ON-9804	F&G H2 GAS OUTDOOR LOW/UPPER - Sub-System 70-21/22 Pre-Commissioning	2d	2d	20-Dec-24	23-Dec-24			50d
I.09 Sub-System 70-21/22 | Commissioning		1d	1d	24-Dec-24	24-Dec-24			50d
COMM-ON-9814	F&G H2 GAS OUTDOOR LOW/UPPER - Sub-System 70-21/22 Commissioning	1d	1d	24-Dec-24	24-Dec-24			50d
L10 Sub-System 70-26/27 | F&G FLAME OUTDOOR LOW/UPPER		3d	3d	27-Dec-24	31-Dec-24			50d
I.10 Sub-System 70-26/27 | Pre-Commissioning		2d	2d	27-Dec-24	30-Dec-24			50d
COMM-ON-9824	F&G FLAME OUTDOOR LOW/UPPER - Sub-System 70-26/27 Pre-Commissioning	2d	2d	27-Dec-24	30-Dec-24			50d
I.10 Sub-System 70-26/27 | Commissioning		1d	1d	31-Dec-24	31-Dec-24			50d
COMM-ON-9834	F&G FLAME OUTDOOR LOW/UPPER - Sub-System 70-26/27 Commissioning	1d	1d	31-Dec-24	31-Dec-24			50d
L11 Sub-System 70-28/29 | F&G SMOKE OUTDOOR LOW/UPPER		3d	3d	02-Jan-25	07-Jan-25			50d
I.11 Sub-System 70-28/29 | Pre-Commissioning		2d	2d	02-Jan-25	03-Jan-25			50d
COMM-ON-9844	F&G SMOKE OUTDOOR LOW/UPPER - Sub-System 70-28/29 Pre-Commissioning	2d	2d	02-Jan-25	03-Jan-25			50d
I.11 Sub-System 70-28/29 | Commissioning		1d	1d	07-Jan-25	07-Jan-25			50d
COMM-ON-9854	F&G SMOKE OUTDOOR LOW/UPPER - Sub-System 70-28/29 Commissioning	1d	1d	07-Jan-25	07-Jan-25			50d
L12 Sub-System 70-31| F&G MCP BEACON/SOUNDER		3d	3d	08-Jan-25	10-Jan-25			50d
I.12 Sub-System 70-31| Pre-Commissioning		2d	2d	08-Jan-25	09-Jan-25			50d
COMM-ON-9864	F&G MCP BEACON/SOUNDER - Sub-System 70-31 Pre-Commissioning	2d	2d	08-Jan-25	09-Jan-25			50d
I.12 Sub-System 70-31| Commissioning		1d	1d	10-Jan-25	10-Jan-25			50d
COMM-ON-9874	F&G MCP BEACON/SOUNDER - Sub-System 70-31 Commissioning	1d	1d	10-Jan-25	10-Jan-25			50d
Sub-System 70-10 | F&G Devices FZ-01 (Fuel Cell Area)		5d	5d	23-Dec-24	31-Dec-24			56d
COMM-ON-10294	F&G Devices FZ-01 (Fuel Cell Area) - Sub-System 70-10 Precommissioning and Commissioning	5d	5d	23-Dec-24	31-Dec-24			56d
Sub-System 70-11 | F&G Devices FZ-02 (Hydrogen Storage Area)		5d	5d	13-Dec-24	19-Dec-24			62d
COMM-ON-10304	F&G Devices FZ-02 (Hydrogen Storage Area) - Sub-System 70-11 Precommissioning and Commissioning	5d	5d	13-Dec-24	19-Dec-24			62d
Sub-System 70-12| F&G Devices FZ-03 (Electrolyser Area)		5d	5d	09-Dec-24	13-Dec-24			66d
COMM-ON-10314	F&G Devices FZ-03 (Electrolyser Area) - Sub-System 70-12 Precommissioning and Commissioning	5d	5d	09-Dec-24	13-Dec-24			66d
Sub-System 70-13 | F&G Devices FZ-04 (B-200 LV Switchgear Room)		5d	5d	13-Nov-24	19-Nov-24			84d
COMM-ON-10324	F&G Devices FZ-04 (B-200 LV Switchgear Room) - Sub-System 70-13 Precommissioning and Commissioning	5d	5d	13-Nov-24	19-Nov-24			84d
Sub-System 70-14 | F&G Devices FZ-04 (B-300 UPS & Batteries Switchroom)		5d	5d	05-Nov-24	11-Nov-24			90d
COMM-ON-10334	F&G Devices FZ-04 (B-300 UPS & Batteries Switchroom) - Sub-System 70-14 Precommissioning and Commissi	5d	5d	05-Nov-24	11-Nov-24			90d

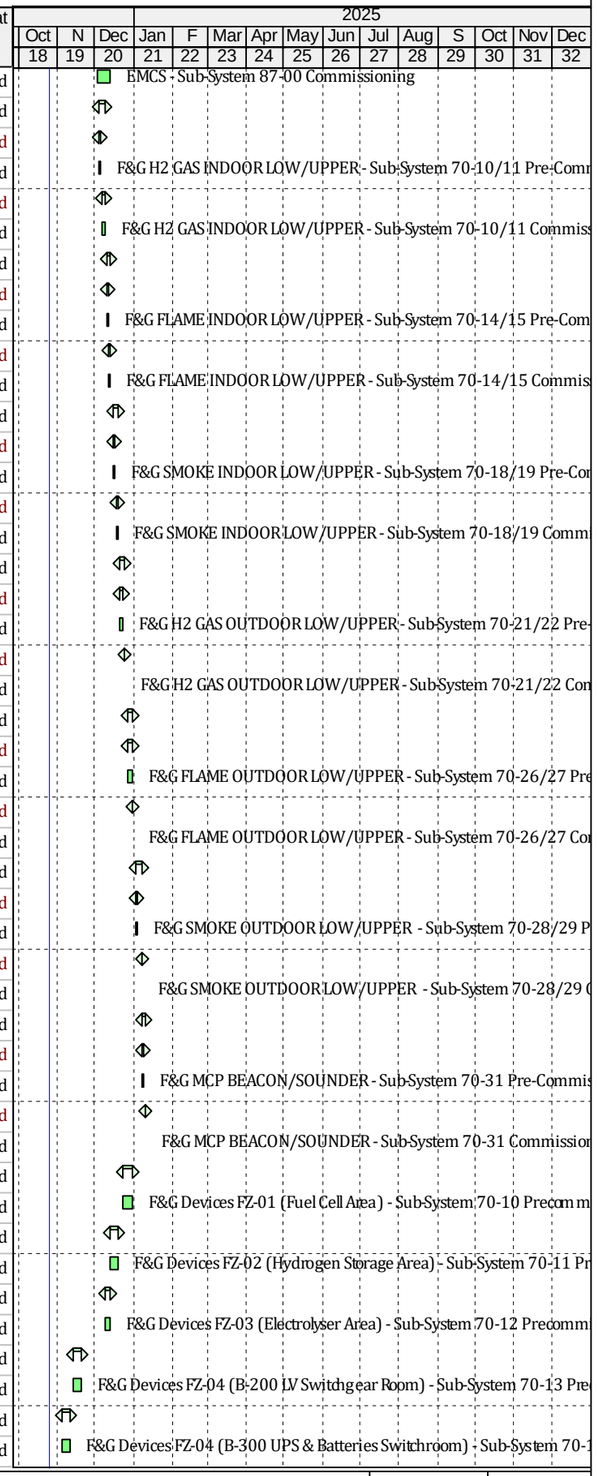

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

CROSSWIND


HOLLANDSE KUST NOORD WIND PARK Project

BASE LOAD POWER HUB

Contract No. CW-I-WP4-2023-05

ROSETTI MARINO

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Sub-System 70-15 | F&G Devices FZ-04 (B-400 I&T Equipment Room)		5d	5d	18-Nov-24	22-Nov-24			81d
COMM-ON-10344	F&G Devices FZ-04 (B-200 LV Switchgear Room) - Sub-System 70-15 Precommissioning and Commissioning	5d	5d	18-Nov-24	22-Nov-24			81d
Sub-System 70-16 | F&G Devices FZ-05 (Bess Area)		5d	5d	27-Nov-24	03-Dec-24			74d
COMM-ON-10354	F&G Devices FZ-05 (Bess Area) - Sub-System 70-16 Precommissioning and Commissioning	5d	5d	27-Nov-24	03-Dec-24			74d
Sub-System 70-17 | F&G Devices FZ-06 (B-100 HV/MV Switchroom Area)		5d	5d	20-Nov-24	26-Nov-24			79d
COMM-ON-10364	F&G Devices FZ-06 (B-100 HV/MV Switchroom Area) - Sub-System 70-17 Precommissioning and Commissioni	5d	5d	20-Nov-24	26-Nov-24			79d
Sub-System 70-18 | F&G Devices FZ-07 (Transition Piece Area)		5d	5d	27-Dec-24	03-Jan-25			54d
COMM-ON-10374	F&G Devices FZ-07 (Transition Piece) - Sub-System 70-18 Precommissioning and Commissioning	5d	5d	27-Dec-24	03-Jan-25			54d
Commissioning - Utility Systems		61d	102d	30-Sep-24 A	25-Feb-25			18d
M.05 Sub-System 63-00 | Instrument Air Package (A-63000)		13d	54d	30-Sep-24 A	13-Dec-24			51d
M.05 Sub-System 63-00 | Pre-Commissioning		8d	46d	30-Sep-24 A	03-Dec-24			51d
COMM-ON-9904	INSTRUMENT AIR PACKAGE A-63000 - Sub-System 63-00 Pre-Commissioning	8d	46d	30-Sep-24 A	03-Dec-24			51d
M.05 Sub-System 63-00 | Commissioning		8d	8d	04-Dec-24	13-Dec-24			51d
COMM-ON-9914	INSTRUMENT AIR PACKAGE A-63000 - Sub-System 63-00 Commissioning	8d	8d	04-Dec-24	13-Dec-24			51d
M.06 Sub-System 64-00 | Nitrogen Generator Package (U-6400)		5d	5d	27-Nov-24	03-Dec-24			59d
M.06 Sub-System 64-00 | Pre-Commissioning		3d	3d	27-Nov-24	29-Nov-24			59d
COMM-ON-9944	N2 GENERATOR PACKAGE A-64000 - Sub-System 64-00 Pre-Commissioning	3d	3d	27-Nov-24	29-Nov-24			59d
M.06 Sub-System 64-00 | Commissioning		2d	2d	02-Dec-24	03-Dec-24			59d
COMM-ON-9954	N2 GENERATOR PACKAGE A-64000 - Sub-System 64-00 Commissioning	2d	2d	02-Dec-24	03-Dec-24			59d
M.07 Sub-System 63-30 | Instrument Air Network		11d	11d	03-Dec-24	17-Dec-24			56d
M.07 Sub-System 63-30 | Pre-Commissioning		6d	6d	03-Dec-24	10-Dec-24			56d
COMM-ON-9924	INSTRUMENT AIR NETWORK - Sub-System 63-30 Pre-Commissioning	6d	6d	03-Dec-24	10-Dec-24			56d
M.07 Sub-System 63-30 | Commissioning		5d	5d	11-Dec-24	17-Dec-24			56d
COMM-ON-9934	INSTRUMENT AIR NETWORK - Sub-System 63-30 Commissioning	5d	5d	11-Dec-24	17-Dec-24			56d
M.08 Sub-System 64-10 | Nitrogen Distribution Network		5d	5d	13-Dec-24	19-Dec-24			54d
M.08 Sub-System 64-10 | Pre-Commissioning		3d	3d	13-Dec-24	17-Dec-24			54d
COMM-ON-9964	N2 NETWORK - Sub-System 64-10 Pre-Commissioning	3d	3d	13-Dec-24	17-Dec-24			54d
M.08 Sub-System 64-10 | Commissioning		2d	2d	18-Dec-24	19-Dec-24			54d
COMM-ON-9974	N2 NETWORK - Sub-System 64-10 Commissioning	2d	2d	18-Dec-24	19-Dec-24			54d
M.09 Sub-System 50-00 | Seawater Intake System (Lifting Pumps)		14d	72d	30-Sep-24 A	14-Jan-25			48d
M.09 Sub-System 50-00 | Pre-Commissioning		3d	70d	30-Sep-24 A	10-Jan-25			48d
COMM-ON-9984	SEAWATER INTAKE SYSTEM - Sub-System 50-00 Pre-Commissioning	3d	70d	30-Sep-24 A	10-Jan-25			48d
M.09 Sub-System 50-00 | PCommissioning		2d	2d	13-Jan-25	14-Jan-25			48d
COMM-ON-9994	SEAWATER INTAKE SYSTEM - Sub-System 50-00 Commissioning OFF-SHORE	2d	2d	13-Jan-25	14-Jan-25			48d
M.10 Sub-System 50-10 | Water Desalination Package & Distribution		30d	79d	30-Sep-24 A	23-Jan-25			33d
M.10 Sub-System 50-10 | Pre-Commissioning		5d	50d	30-Sep-24 A	09-Dec-24			56d
COMM-ON-10004	WATER DESALIN. PACKAGE - Sub-System 50-10 Pre-Commissioning	5d	50d	30-Sep-24 A	09-Dec-24			56d
M.10 Sub-System 50-10 | Commissioning		6d	6d	16-Jan-25	23-Jan-25			33d
COMM-ON-10014	WATER DESALIN. PACKAGE - Sub-System 50-10 Commissioning	6d	6d	16-Jan-25	23-Jan-25			33d
M.11 Sub-System 50-20 | Water Desalination Package & Distribution		5d	5d	28-Jan-25	03-Feb-25			26d
M.11 Sub-System 50-20 | Pre-Commissioning		3d	3d	28-Jan-25	30-Jan-25			26d
COMM-ON-10024	WATER DIST. NETWORK - Sub-System 50-20 Pre-Commissioning	3d	3d	28-Jan-25	30-Jan-25			26d
M.11 Sub-System 50-20 | Commissioning		2d	2d	31-Jan-25	03-Feb-25			26d
COMM-ON-10034	WATER DIST. NETWORK - Sub-System 50-20 Commissioning	2d	2d	31-Jan-25	03-Feb-25			26d
M.12 Sub-System 55-00 | Waste Water Disposal		8d	8d	14-Feb-25	25-Feb-25			18d
M.12 Sub-System 50-10 | Pre-Commissioning		4d	4d	14-Feb-25	19-Feb-25			18d

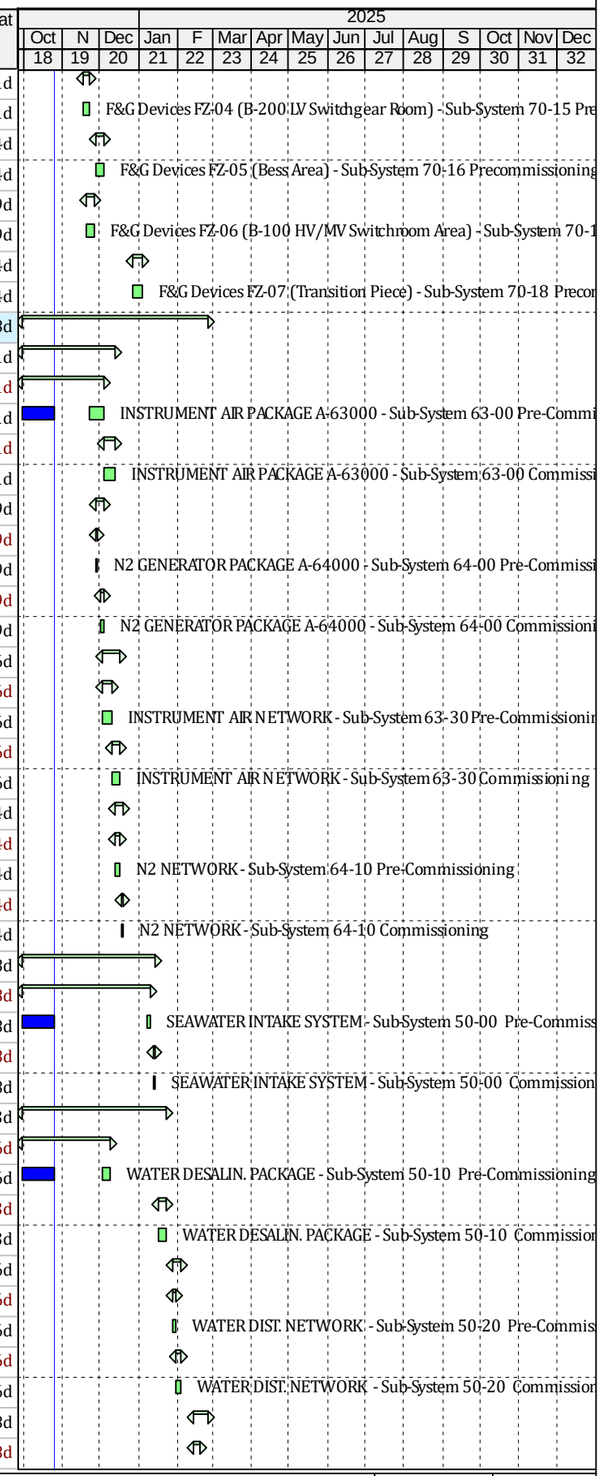

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Data Date: 25-Oct-24

CROSSWIND BLPH EPCI

Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON-10044	WATER DISPOSAL NETWORK - Sub-System 55-00 Pre-Commissioning	4d	4d	14-Feb-25	19-Feb-25			18d
M.12 Sub-System 50-10 | Commissioning		4d	4d	20-Feb-25	25-Feb-25			18d
COMM-ON-10054	WATER DISPOSAL NETWORK - Sub-System 55-00 Commissioning	4d	4d	20-Feb-25	25-Feb-25			18d
M.13 Sub-System 55-01 | WasteWater Brine Discharge System		6d	6d	13-Feb-25	20-Feb-25			21d
M.13 Sub-System 55-01 | Pre-Commissioning		3d	3d	13-Feb-25	17-Feb-25			21d
COMM-ON-10055	BRINE DISCHARGE SYSTEM - Sub-System 55-01 Pre-Commissioning	3d	3d	13-Feb-25	17-Feb-25			21d
M.13 Sub-System 55-01 | Commissioning		3d	3d	18-Feb-25	20-Feb-25			21d
COMM-ON-10056	BRINE DISCHARGE SYSTEM - Sub-System 55-01 Commissioning	3d	3d	18-Feb-25	20-Feb-25			21d
M.14 Sub-System 99-00 | Crane		3d	76d	30-Sep-24 A	20-Jan-25			44d
M.14 Sub-System 99-00 | Pre-Commissioning		3d	73d	30-Sep-24 A	15-Jan-25			44d
COMM-ON-10064	CRANE - Sub-System 99-00 Pre-Commissioning	3d	73d	30-Sep-24 A	15-Jan-25			44d
M.14 Sub-System 99-00 | Commissioning		3d	3d	16-Jan-25	20-Jan-25			44d
COMM-ON-10074	CRANE - Sub-System 99-00 Commissioning	3d	3d	16-Jan-25	20-Jan-25			44d
Commissioning - Process and Process Support Systems		23d	23d	17-Dec-24	16-Jan-25			55d
M.15 Sub-System 25-08 | Hydrogen Storage Vessels Header (Outlet)		7d	7d	08-Jan-25	16-Jan-25			55d
M.15 Sub-System 25-80 | Pre-Commissioning		4d	4d	08-Jan-25	13-Jan-25			55d
COMM-ON-10274	Leak Test - H2 Storage Systems	0d	0d		08-Jan-25			53d
COMM-ON-10284	Leak Test - H2 Vent System	0d	0d		08-Jan-25			53d
COMM-ON-10084	H2 STORAGE HEAD. OUTLET - Sub-System 25-08 Pre-Commissioning	3d	3d	09-Jan-25	13-Jan-25			46d
M.15 Sub-System 25-80 | Commissioning		3d	3d	14-Jan-25	16-Jan-25			46d
COMM-ON-10094	H2 STORAGE HEAD. OUTLET - Sub-System 25-08 Commissioning	3d	3d	14-Jan-25	16-Jan-25			46d
M.16 Sub-System 25-01/06 | Hydrogen Storage Vessels		4d	4d	31-Dec-24	07-Jan-25			53d
M.16 Sub-System 25-01/06| Pre-Commissioning		2d	2d	31-Dec-24	02-Jan-25			53d
COMM-ON-10104	H2 STORAGE VESSELS -Sub-System 25-01/06 Pre-Commissioning	2d	2d	31-Dec-24	02-Jan-25			53d
M.16 Sub-System 25-01/06| Commissioning		2d	2d	03-Jan-25	07-Jan-25			53d
COMM-ON-10114	H2 STORAGE VESSELS -Sub-System 25-01/06 Commissioning	2d	2d	03-Jan-25	07-Jan-25			53d
M.17 Sub-System 43-00 | Hydrogen Vent Header & Drum System		5d	5d	30-Dec-24	07-Jan-25			45d
M.17 Sub-System 43-00 | Pre-Commissioning		3d	3d	30-Dec-24	02-Jan-25			45d
COMM-ON-10124	H2 VENT HEADER & DRUM SYSTEM - Sub-System 43-00 Pre-Commissioning	3d	3d	30-Dec-24	02-Jan-25			45d
M.17 Sub-System 43-00 | Commissioning		2d	2d	03-Jan-25	07-Jan-25			45d
COMM-ON-10134	H2 VENT HEADER & DRUM SYSTEM - Sub-System 43-00 Commissioning	2d	2d	03-Jan-25	07-Jan-25			45d
M.18 Sub-System 25-07 | Hydrogen Storage Vessels Header (Intlet)		7d	7d	17-Dec-24	27-Dec-24			58d
M.18 Sub-System 25-01/06 | Pre-Commissioning		4d	4d	17-Dec-24	20-Dec-24			58d
COMM-ON-10144	H2 STORAGE HEAD. INLET - Sub-System 25-07 Pre-Commissioning	4d	4d	17-Dec-24	20-Dec-24			58d
M.18 Sub-System 25-01/06 | Commissioning		3d	3d	23-Dec-24	27-Dec-24			58d
COMM-ON-10154	H2 STORAGE HEAD. INLET - Sub-System 25-07 Commissioning	3d	3d	23-Dec-24	27-Dec-24			58d
Onshore Commissioning - MH SUMMARY/Baseline		226d	54d	21-Jun-24 A	23-Aug-24 A	07-Dec-24	01-Apr-25	
COMM-ON1000	First Energization / with Temporary Power (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	0d	0d	23-Aug-24 A		07-Dec-24		
COMM-ON1010	MH SUMMARY - UPS (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	13d	1d	23-Aug-24 A	23-Aug-24 A	10-Dec-24	30-Dec-24	
COMM-ON1020	MH SUMMARY - 400V Switchboard & Trafo (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	25d	1d	23-Aug-24 A	23-Aug-24 A	24-Dec-24	31-Jan-25	
COMM-ON1030	MH SUMMARY - JB for Temporary Supply (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	5d	1d	23-Aug-24 A	23-Aug-24 A	31-Dec-24	08-Jan-25	
COMM-ON1100	MH SUMMARY - 6.6kV Switchboard & Trafo (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	13d	1d	23-Aug-24 A	23-Aug-24 A	09-Jan-25	27-Jan-25	
COMM-ON1180	MH SUMMARY - 66kV Switchboard (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	13d	1d	23-Aug-24 A	23-Aug-24 A	28-Jan-25	13-Feb-25	
COMM-ON1280	MH SUMMARY - Lighting (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	8d	1d	23-Aug-24 A	23-Aug-24 A	14-Feb-25	25-Feb-25	
COMM-ON1360	MH SUMMARY - Trace Heating (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	8d	1d	23-Aug-24 A	23-Aug-24 A	26-Feb-25	07-Mar-25	
COMM-ON1300	MH SUMMARY - HVAC (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	19d	1d	23-Aug-24 A	23-Aug-24 A	14-Feb-25	12-Mar-25	

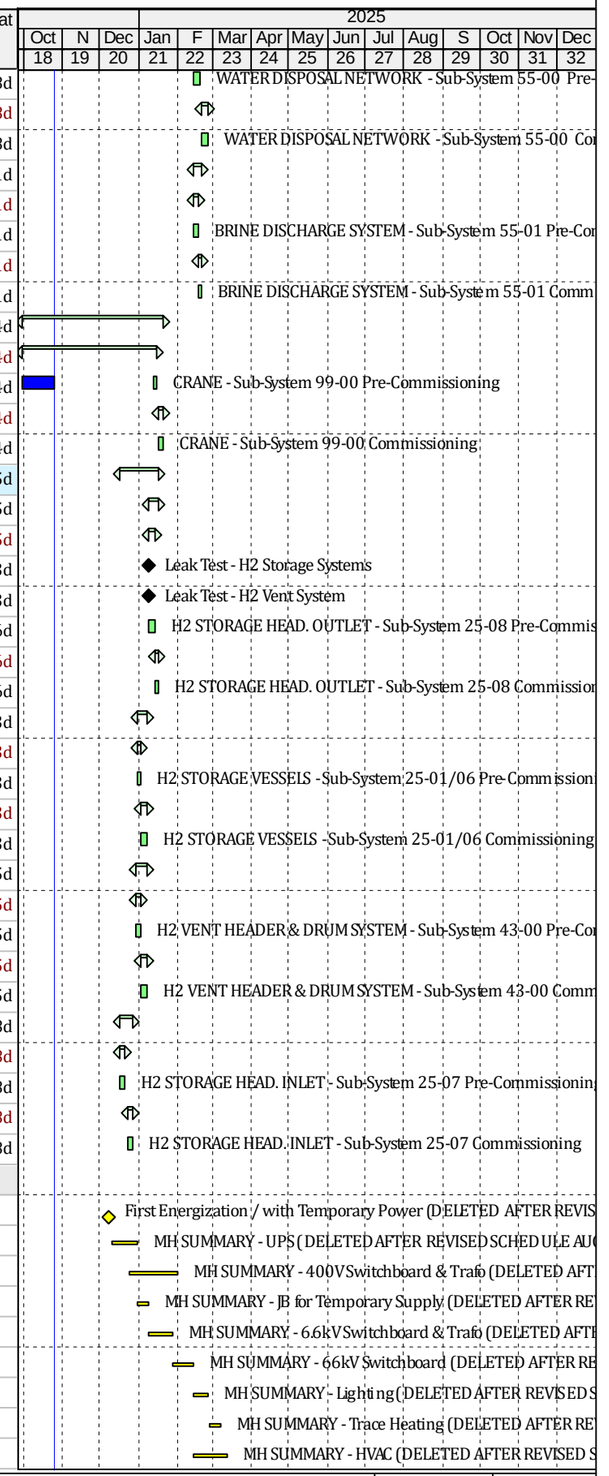

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON1380	MH SUMMARY - Cathodic Protection (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	4d	1d	23-Aug-24 A	23-Aug-24 A	10-Mar-25	13-Mar-25	
COMM-ON1400	MH SUMMARY - Crane (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	4d	1d	23-Aug-24 A	23-Aug-24 A	14-Mar-25	19-Mar-25	
COMM-ON1120	MH SUMMARY - TELECOMM - FO PANELS (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	7d	1d	23-Aug-24 A	23-Aug-24 A	29-Jan-25	06-Feb-25	
COMM-ON1320	MH SUMMARY - TELECOMM- ACCESS CONTROL (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	9d	1d	23-Aug-24 A	23-Aug-24 A	17-Mar-25	27-Mar-25	
COMM-ON1050	MH SUMMARY - Servers / EWS /OWS (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	10d	1d	23-Aug-24 A	23-Aug-24 A	31-Dec-24	15-Jan-25	
COMM-ON1060	MH SUMMARY - CCS (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	50d	1d	23-Aug-24 A	23-Aug-24 A	09-Jan-25	19-Mar-25	
COMM-ON1190	MH SUMMARY - F&G Devices (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	13d	1d	23-Aug-24 A	23-Aug-24 A	28-Jan-25	13-Feb-25	
COMM-ON1330	MH SUMMARY - SIS & F&G (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	13d	1d	23-Aug-24 A	23-Aug-24 A	19-Feb-25	07-Mar-25	
COMM-ON1200	MH SUMMARY - BESS (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	15d	1d	23-Aug-24 A	23-Aug-24 A	30-Jan-25	19-Feb-25	
COMM-ON1270	MH SUMMARY - PV System (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	13d	1d	23-Aug-24 A	23-Aug-24 A	20-Feb-25	10-Mar-25	
COMM-ON1350	MH SUMMARY - Fuel Cell (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	8d	1d	23-Aug-24 A	23-Aug-24 A	11-Mar-25	20-Mar-25	
COMM-ON1130	WATER DISPOSAL (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	7d	1d	23-Aug-24 A	23-Aug-24 A	24-Jan-25	03-Feb-25	
COMM-ON1390	MH SUMMARY - Electrolyzer (No H2 Production) (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	3d	1d	23-Aug-24 A	23-Aug-24 A	21-Mar-25	25-Mar-25	
COMM-ON1410	MH SUMMARY - C&E TEST (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	6d	1d	23-Aug-24 A	23-Aug-24 A	20-Mar-25	27-Mar-25	
COMM-ON1420	MH SUMMARY - Electrolyzer (With H2 Production) (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	3d	1d	23-Aug-24 A	23-Aug-24 A	28-Mar-25	01-Apr-25	
MH SUMMARY - TLC Sequence		29d	1d	23-Aug-24 A	23-Aug-24 A	31-Dec-24	14-Mar-25	
COMM-ON1040	MH SUMMARY - Telecomm - Network - (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	19d	1d	23-Aug-24 A	23-Aug-24 A	31-Dec-24	28-Jan-25	
COMM-ON1150	MH SUMMARY - Telecomm - PAGA - (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	8d	1d	23-Aug-24 A	23-Aug-24 A	07-Feb-25	18-Feb-25	
COMM-ON1230	MH SUMMARY - Telecomm - Telephones - (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	9d	1d	23-Aug-24 A	23-Aug-24 A	19-Feb-25	03-Mar-25	
COMM-ON1250	MH SUMMARY - Telecomm - Intrusive Detection - (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	9d	1d	23-Aug-24 A	23-Aug-24 A	04-Mar-25	14-Mar-25	
MH SUMMARY - Electrolyzer Sequence		58d	1d	23-Aug-24 A	23-Aug-24 A	09-Jan-25	31-Mar-25	
COMM-ON1070	MH SUMMARY - Compressed Air (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	5d	1d	23-Aug-24 A	23-Aug-24 A	09-Jan-25	15-Jan-25	
COMM-ON1090	MH SUMMARY - Nitrogen (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	6d	1d	23-Aug-24 A	23-Aug-24 A	16-Jan-25	23-Jan-25	
COMM-ON1160	MH SUMMARY - Waste Water (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	7d	1d	23-Aug-24 A	23-Aug-24 A	04-Feb-25	12-Feb-25	
COMM-ON1210	MH SUMMARY - Deionized Water (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	6d	1d	23-Aug-24 A	23-Aug-24 A	13-Feb-25	20-Feb-25	
COMM-ON1080	MH SUMMARY - Sea Water Lifting Pumps (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	6d	1d	23-Aug-24 A	23-Aug-24 A	09-Jan-25	16-Jan-25	
COMM-ON1110	MH SUMMARY - Sea Water Filters & Tank (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	8d	1d	23-Aug-24 A	23-Aug-24 A	17-Jan-25	28-Jan-25	
COMM-ON1140	MH SUMMARY - Electrochlorinator (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	9d	1d	23-Aug-24 A	23-Aug-24 A	29-Jan-25	10-Feb-25	
COMM-ON1220	MH SUMMARY - Fresh Water (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	10d	1d	23-Aug-24 A	23-Aug-24 A	11-Feb-25	24-Feb-25	
COMM-ON1240	MH SUMMARY - Desalinizator (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	25d	1d	23-Aug-24 A	23-Aug-24 A	25-Feb-25	31-Mar-25	
COMM-ON1260	MH SUMMARY - Oxygen Vent (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	5d	1d	23-Aug-24 A	23-Aug-24 A	28-Feb-25	06-Mar-25	
COMM-ON1310	MH SUMMARY - H2 Vent (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	5d	1d	23-Aug-24 A	23-Aug-24 A	07-Mar-25	13-Mar-25	
COMM-ON1340	MH SUMMARY - H2 Manifold (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	4d	1d	23-Aug-24 A	23-Aug-24 A	14-Mar-25	19-Mar-25	
COMM-ON1370	MH SUMMARY - H2 Vessels (DELETED AFTER REVISED SCHEDULE AUGUST 2024)	4d	1d	23-Aug-24 A	23-Aug-24 A	20-Mar-25	25-Mar-25	
Commissioning - OLD		224d	9d	21-Jun-24 A	01-Jul-24 A			
Electrical Systems and Subsystems - OLD		263d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8210	LV 400V SWBD SG-200N1 - Sub-System 83-00 DELETED	10d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8550	UPS AC 35KVA UP-200F3 - Sub-System 84-10 -DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8551	UPS AC 15KVA UP-200F4 - Sub-System 84-20 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8540	UPS DC 10kVA UP-200F1 - Sub-System 84-00 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8120	MV 6,6 kV SWBD SG-A00D1 - Sub-System 82-00 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8121	TRANS. 1,6 MVA TR-200DE1 - Sub-System 82-40 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8211	LV 400V SWBD SG-200N1 Final - Sub-System 83-00 DELETED	2d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8125	TRANS. 1,25 MVA (F.C.) TA30 (H2 ABSENT) - Sub-System 82-30 DELETED	4d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8123	TRANS. 1,25 MVA (BESS) 1BT1 - Sub-System 82-10 DELETED	4d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8124	TRANS. 3,15 MVA (ELECTROL.) T4 (H2 ABSENT) - Sub-System 82-20 DELETED	10d	1d	21-Jun-24 A	21-Jun-24 A			

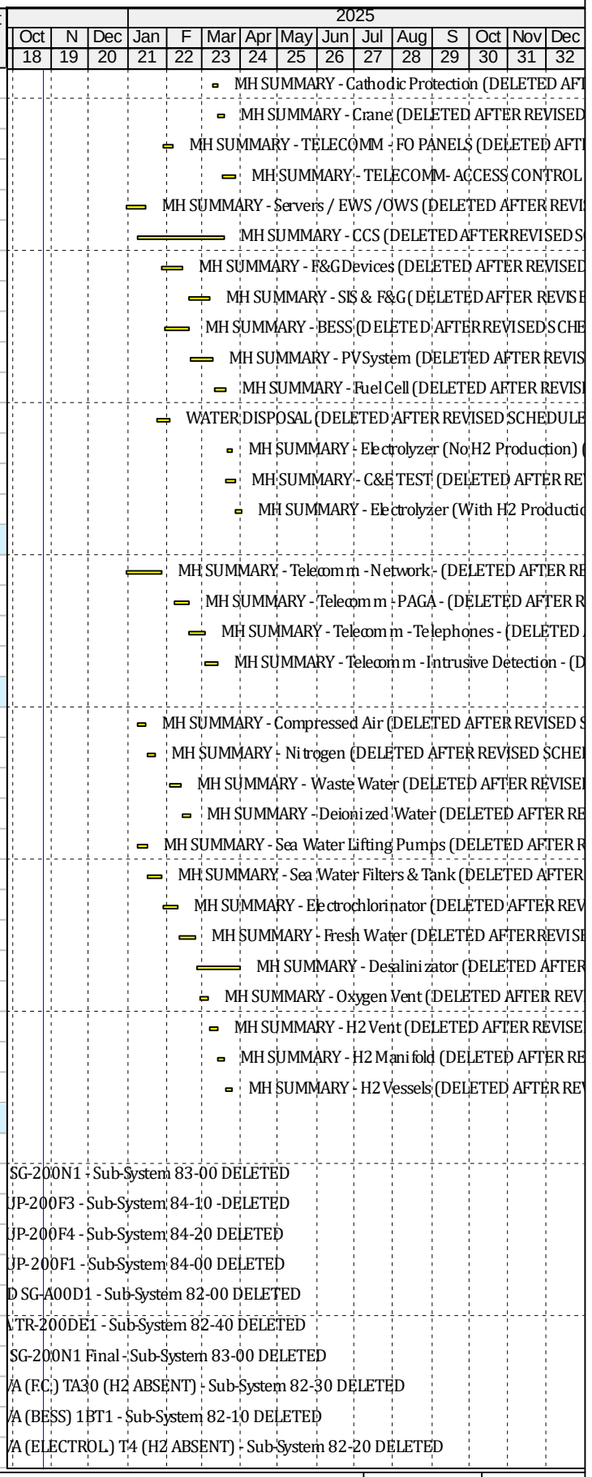

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR


Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
COMM-ON-8127	TRANS. 0,50 MVA (SOLAR) TR-200ED1 - Sub-System 82-50 DELETED	14d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8212	400/230 VAC SWBD DP-200N1 - Sub-System 83-20 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8213	EMERGENCY LIGHTING - Sub-System 83-35 DELETED	10d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8214	NORMAL LIGHTING - Sub-System 83-35 DELETED	10d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8410	TEMP. DIESEL GENERATOR - Sub-System 83-75 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8218	ELECTRICAL TRACE HEATING - Sub-System 83-65 DELETED	15d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8215	WELDING SOCKETS - Sub-System 83-50 DELETED	6d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8216	POWER SOCKETS - Sub-System 83-55 DELETED	7d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8670	NAVAID - Sub-System 72-00 DELETED	7d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8500	BESS A-85000 (PACKAGE) - w/o batteries - Sub-System 85-00 DELETED	8d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8000	FUEL CELL A-80000 (PACKAGE) - Sub-System 80-00 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8501	BESS A-85000 (PACKAGE) DELETED	20d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-2000	ELECTROLYZER PACKAGE (H2 ABSENT) - Sub-System 20-00 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-2010	ELECTROLYZER PACKAGE (H2 PRODUCING) DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8021	GIS 66 kV HNA6-AFA70 - Sub-System 81-10 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8022	TRANS. 7,0 MVA TR-100AD1 - Sub-System 81-20 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8020	66 kV SUBSEA CABLE - Sub-System 81-00 DELETED	2d	1d	21-Jun-24 A	21-Jun-24 A			
Structural and HVAC Systems - OLD		18d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7722	HVAC ROOM B-200 - Sub-System 77-20 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-9002	LV SWITCHGEAR ROOM B-200 - Sub-System 90-02 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7723	HVAC ROOM B-300 - Sub-System 77-30 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-9003	UPS SYSTEMS ROOM B-300 - Sub-System 90-03 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7721	HVAC ROOM B-100 - Sub-System 77-10 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-9001	HV/MV SWGR ROOM B-100 - Sub-System 90-01 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7724	HVAC ROOM B-400 - Sub-System 77-40 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-9004	I&T SYSTEMS ROOM B-400 - Sub-System 90-04 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
Process and Process Support Systems - OLD		8d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-2520	H2 STORAGE HEAD. OUTLET - Sub-System 25-08 DELETED	6d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-2500	H2 STORAGE VESSELS - Sub-System 25-01 DELETED	4d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-4300	H2 VENT HEADER & DRUM SYSTEM - Sub-System 43-00 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-4400	O2 VENT SYSTEM D ELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-2510	H2 STORAGE HEAD. INLET DELETED	7d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-2530	H2 STORAGE HEAD. INLET - Sub-System 25-07 DELETED	7d	1d	21-Jun-24 A	21-Jun-24 A			
CCS and EMCS Systems - OLD		165d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8710	PCS - Sub-System 87-10 DELETED	15d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8730	SIS - Sub-System 79-00 DELETED	15d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8740	F&G - Sub-System 70-00 DELETED	10d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7010	F&G H2 GAS INDOOR LOW/UPPER - Sub-System 70-10/11 DELETED	4d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7011	F&G FLAME INDOOR LOW/UPPER - Sub-System 70-14/15 DELETED	4d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7012	F&G SMOKE INDOOR LOW/UPPER - Sub-System 70-18/19 DELETED	4d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7013	F&G MCP BEACON/SOUNDER - Sub-System 70-31 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7014	F&G FLAME OUTDOOR LOW/UPPER - Sub-System 70-26/27 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7016	F&G H2 GAS OUTDOOR LOW/UPPER - Sub-System 70-21/22 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7017	F&G SMOKE OUTDOOR LOW/UPPER - Sub-System 70-28/29 DELETED	3d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8620	DATA NETWORKS- Sub-System 86-00 DELETED	15d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-8770	EMCS - Sub-System 87-00 DELETED	25d	1d	21-Jun-24 A	21-Jun-24 A			

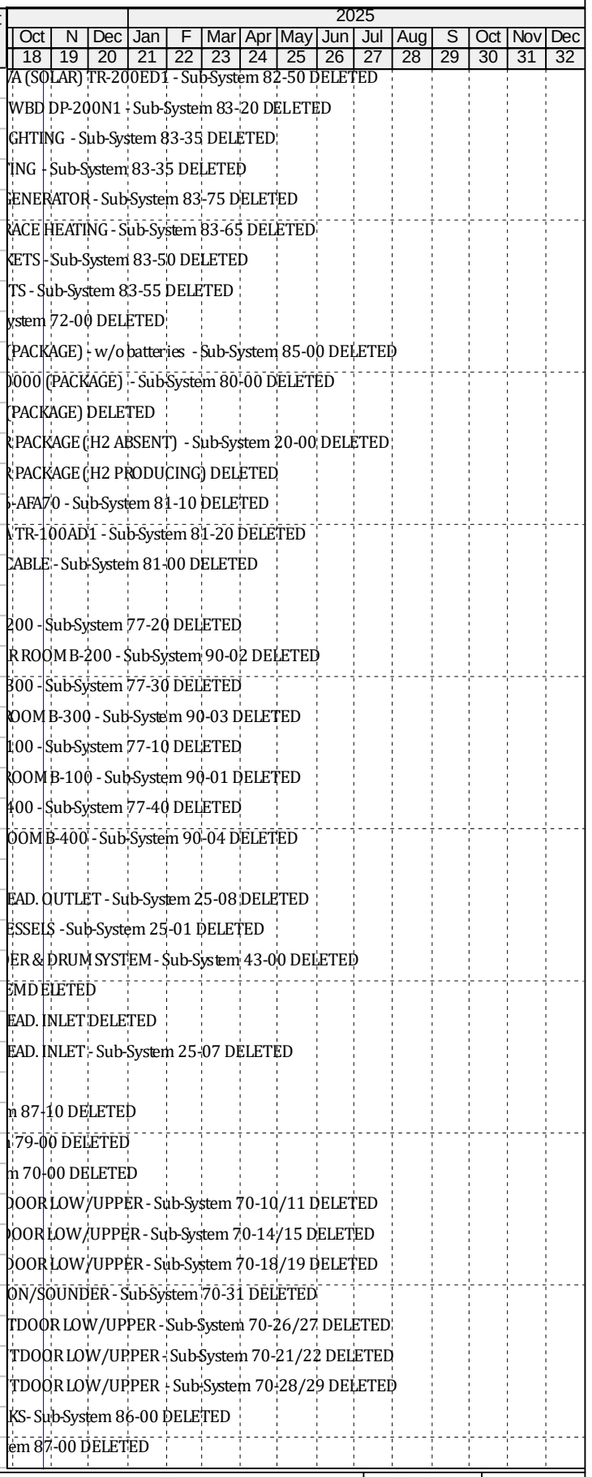

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Utility Systems - OLD		189d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-6300	INSTRUMENT AIR PACKAGE A-63000 - Sub-System 63-00 DELETED	20d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-6330	INSTRUMENT AIR NETWORK - Sub-System 63-30 DELETED	15d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-6400	N2 GENERATOR PACKAGE A-64000 - Sub-System 64-00 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-6410	N2 NETWORK - Sub-System 64-10 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-5000	SEAWATER INTAKE SYSTEM - Sub-System 50-00 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-5010	WATER DESALIN. PACKAGE - Sub-System 50-10 DELETED	13d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-5020	WATER DIST. NETWORK - Sub-System 50-20 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-5500	WATER DISPOSAL NETWORK - Sub-System 55-00 DELETED	8d	1d	21-Jun-24 A	21-Jun-24 A			
COMM-ON-7310	CRANE - Sub-System 99-00 DELETED	5d	1d	21-Jun-24 A	21-Jun-24 A			
DELETED		209d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT2240	Sub-System 80-00 | Electrical - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT2300	Sub-System 85-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT2840	Sub-System 20-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT2900	Sub-System 82-30 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT2960	Sub-System 82-10 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3020	Sub-System 82-20 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3680	Sub-System 87-10 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3740	Sub-System 79-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3800	Sub-System 70-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3860	Sub-System 86-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3920	Sub-System 87-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3950	Sub-System 70-10/11 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3970	Sub-System 70-10/11 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3980	Sub-System 70-10/11 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3990	Sub-System 70-10/11 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT3960	Sub-System 70-10/11 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4010	Sub-System 70-14/15 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4030	Sub-System 70-14/15 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4040	Sub-System 70-14/15 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4050	Sub-System 70-14/15 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4020	Sub-System 70-14/15 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4070	Sub-System 70-18/19 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4090	Sub-System 70-18/19 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4100	Sub-System 70-18/19 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4110	Sub-System 70-18/19 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4080	Sub-System 70-18/19 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4130	Sub-System 70-21/22 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4150	Sub-System 70-21/22 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4160	Sub-System 70-21/22 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4170	Sub-System 70-21/22 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4140	Sub-System 70-21/22 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4190	Sub-System 70-26/27 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4210	Sub-System 70-26/27 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4220	Sub-System 70-26/27 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4230	Sub-System 70-26/27 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			

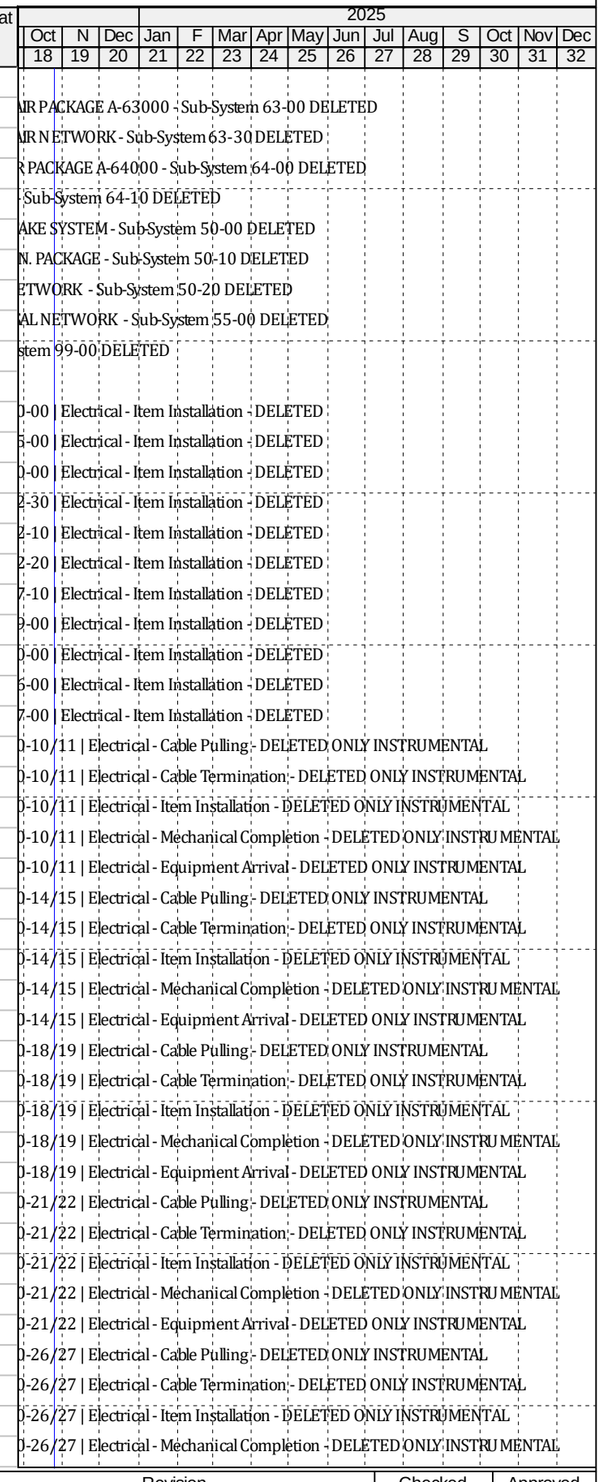


Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT4200	Sub-System 70-26/27 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4250	Sub-System 70-28/29 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4270	Sub-System 70-28/29 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4280	Sub-System 70-28/29 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4290	Sub-System 70-28/29 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4260	Sub-System 70-28/29 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4310	Sub-System 70-31 | Electrical - Cable Pulling - RFCC - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4330	Sub-System 70-31 | Electrical - Cable Termination - RFCC - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4340	Sub-System 70-31 | Electrical - Item Installation - RFCC - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4350	Sub-System 70-31 | Electrical - Mechanical Completion - RFCC - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4320	Sub-System 70-31 | Electrical - Equipment Arrival - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4400	Sub-System 63-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4460	Sub-System 64-00 | Electrical - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4490	Sub-System 63-30 | Electrical - Cable Pulling - RFCC - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4510	Sub-System 63-30 | Electrical - Cable Termination - RFCC - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4520	Sub-System 63-30 | Electrical - Item Installation - RFCC - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4530	Sub-System 63-30 | Electrical - Mechanical Completion - RFCC - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4500	Sub-System 63-30 | Electrical - Equipment Arrival - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4550	Sub-System 64-10 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4570	Sub-System 64-10 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4580	Sub-System 64-10 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4590	Sub-System 64-10 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4560	Sub-System 64-10 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4640	Sub-System 50-00 | Electrical - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4790	Sub-System 55-00 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4810	Sub-System 55-00 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4820	Sub-System 55-00 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4830	Sub-System 55-00 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4800	Sub-System 55-00 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4850	Sub-System 55-01 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4870	Sub-System 55-01 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4880	Sub-System 55-01 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4890	Sub-System 55-01 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4860	Sub-System 55-01 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT4970	Sub-System 25-08 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4990	Sub-System 25-08 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5000	Sub-System 25-08 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5010	Sub-System 25-08 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4980	Sub-System 25-08 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT5030	Sub-System 25-01/06 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5050	Sub-System 25-01/06 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5060	Sub-System 25-01/06 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5070	Sub-System 25-01/06 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5040	Sub-System 25-01/06 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT5150	Sub-System 25-07 | Electrical - Cable Pulling - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5170	Sub-System 25-07 | Electrical - Cable Termination - DELETED ONLY INSTRUMENTAL	2d	1d	01-Jul-24 A	01-Jul-24 A			

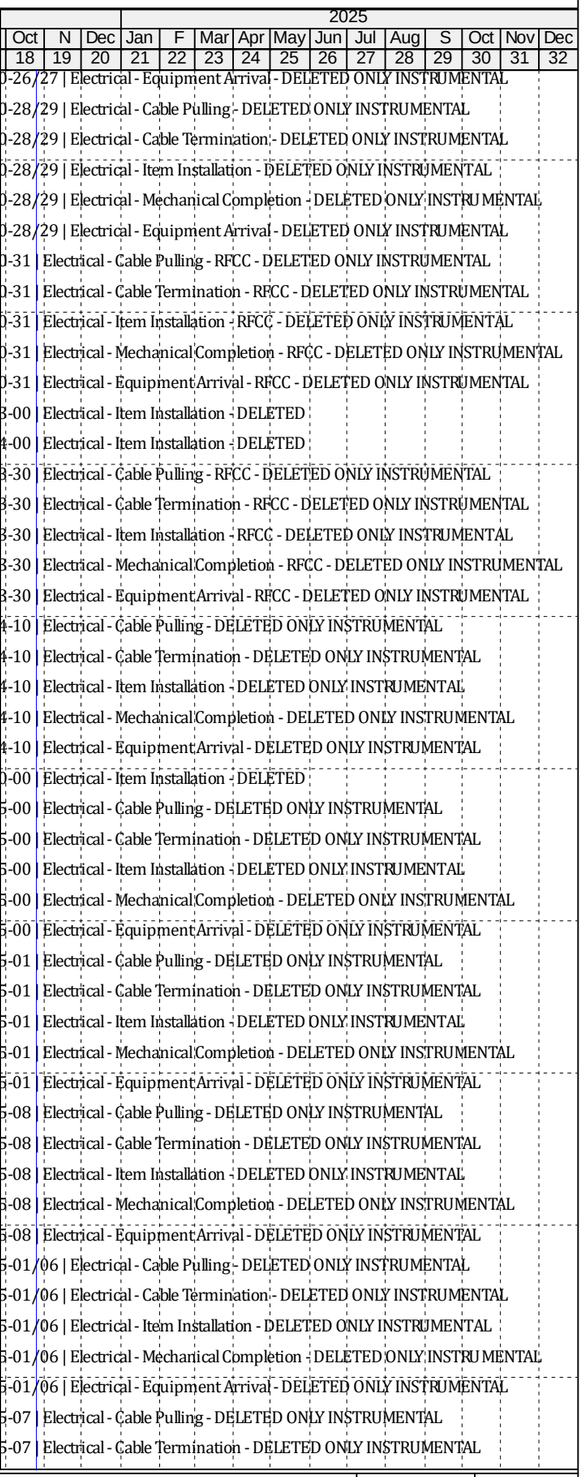

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT5180	Sub-System 25-07 | Electrical - Item Installation - DELETED ONLY INSTRUMENTAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5190	Sub-System 25-07 | Electrical - Mechanical Completion - DELETED ONLY INSTRUMENTAL	3d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5160	Sub-System 25-07 | Electrical - Equipment Arrival - DELETED ONLY INSTRUMENTAL	0d	0d	01-Jul-24 A				
CON-EIT5230	Sub-System 83-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5280	Sub-System 84-10 | Instrumental - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5330	Sub-System 88-00 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5340	Sub-System 88-00 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	1d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5350	Sub-System 88-00 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	1d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5360	Sub-System 88-00 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	1d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5380	Sub-System 88-00 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT5410	Sub-System 84-20 | Instrumental - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5470	Sub-System 84-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5530	Sub-System 82-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5650	Sub-System 81-10 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5770	Sub-System 80-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5830	Sub-System 85-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5890	Sub-System 72-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5930	Sub-System 83-35 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5940	Sub-System 83-35 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5950	Sub-System 83-35 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5960	Sub-System 83-35 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT5980	Sub-System 83-35 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT5990	Sub-System 83-40 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6000	Sub-System 83-40 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6010	Sub-System 83-40 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6020	Sub-System 83-40 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6040	Sub-System 83-40 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6050	Sub-System 83-55 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6060	Sub-System 83-55 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6070	Sub-System 83-55 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6080	Sub-System 83-55 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6100	Sub-System 83-55 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6110	Sub-System 83-50 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6120	Sub-System 83-50 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6130	Sub-System 83-50 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6140	Sub-System 83-50 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6160	Sub-System 83-50 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6170	Sub-System 83-65 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6180	Sub-System 83-65 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6190	Sub-System 83-65 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6200	Sub-System 83-65 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6220	Sub-System 83-65 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6230	Sub-System 83-75 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6240	Sub-System 83-75 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6250	Sub-System 83-75 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6260	Sub-System 83-75 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			

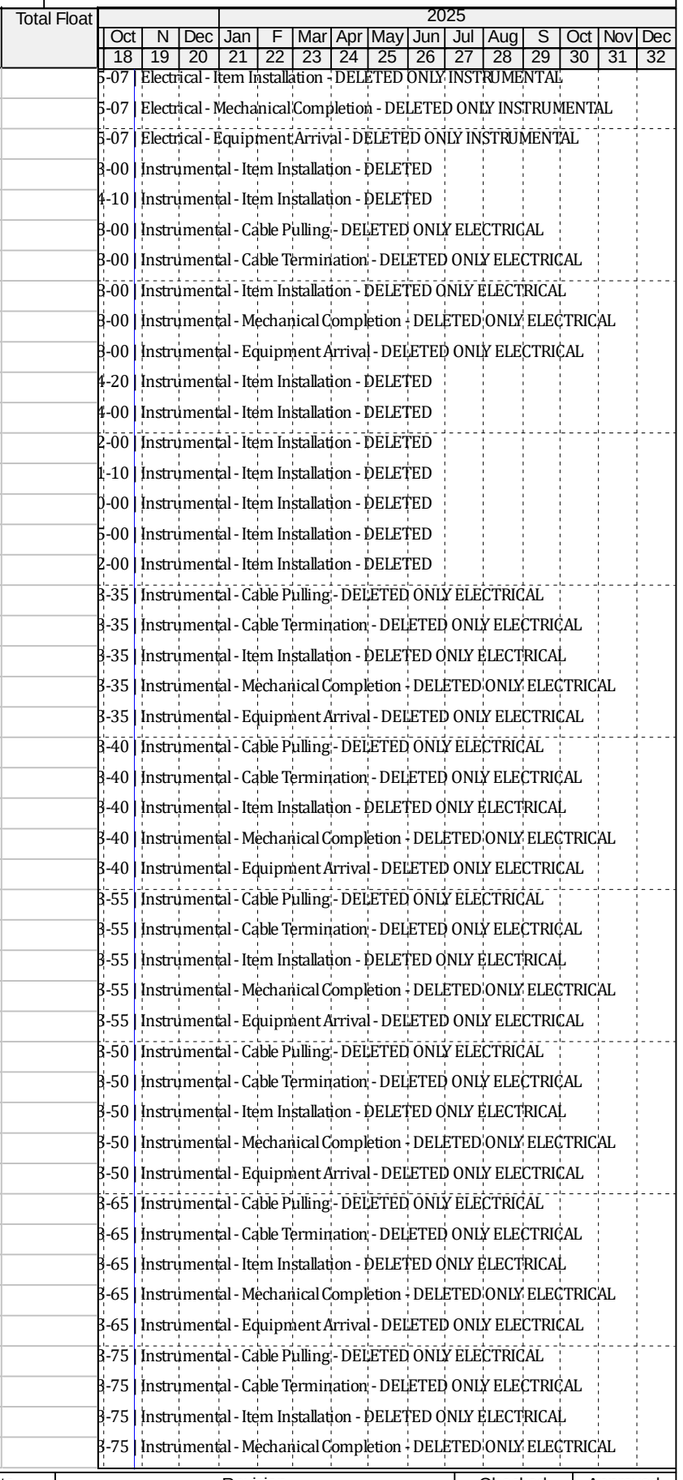

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT6280	Sub-System 83-75 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6370	Sub-System 20-00 | Instrumental - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6410	Sub-System 82-30 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6420	Sub-System 82-30 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6430	Sub-System 82-30 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6440	Sub-System 82-30 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6460	Sub-System 82-30 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6470	Sub-System 82-10 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6480	Sub-System 82-10 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6490	Sub-System 82-10 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6500	Sub-System 82-10 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6520	Sub-System 82-10 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6530	Sub-System 82-20 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6540	Sub-System 82-20 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6550	Sub-System 82-20 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6560	Sub-System 82-20 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6580	Sub-System 82-20 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6590	Sub-System 82-50 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6600	Sub-System 82-50 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6610	Sub-System 82-50 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6620	Sub-System 82-50 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6640	Sub-System 82-50 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6650	Sub-System 81-00 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL	8d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6660	Sub-System 81-00 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6670	Sub-System 81-00 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL	4d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6680	Sub-System 81-00 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL	5d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT6700	Sub-System 81-00 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL	0d	0d	01-Jul-24 A				
CON-EIT6970	Sub-System 77-20 | Instrumental - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7030	Sub-System 77-30 | Instrumental - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7090	Sub-System 77-10 | Instrumental - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7150	Sub-System 77-40 | Instrumental - Item Installation - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7190	Sub-System 87-10 | Instrumental - Cable Pulling - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7200	Sub-System 87-10 | Instrumental - Cable Termination - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7250	Sub-System 79-00 | Instrumental - Cable Pulling - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7260	Sub-System 79-00 | Instrumental - Cable Termination - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7310	Sub-System 70-00 | Instrumental - Cable Pulling - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7320	Sub-System 70-00 | Instrumental - Cable Termination - DELETED	0d	1d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7430	Sub-System 87-00 | Instrumental - Cable Pulling - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7440	Sub-System 87-00 | Instrumental - Cable Termination - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7920	Sub-System 63-00 | Instrumental - Cable Termination - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7930	Sub-System 63-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT7990	Sub-System 64-00 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT8230	Sub-System 50-10 | Instrumental - Item Installation - DELETED	0d	0d	01-Jul-24 A	01-Jul-24 A			
CON-EIT4000	Sub-System 70-10/11 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4060	Sub-System 70-14/15 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4120	Sub-System 70-18/19 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			

2025


Oct	N	Dec	Jan	F	Mar	Apr	May	Jun	Jul	Aug	S	Oct	Nov	Dec
18	19	20	21	22	23	24	25	26	27	28	29	30	31	32

3-75 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL
0-00 | Instrumental - Item Installation - DELETED
2-30 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL
2-30 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL
2-30 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL
2-30 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL
2-30 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL
2-10 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL
2-10 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL
2-10 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL
2-10 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL
2-10 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL
2-20 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL
2-20 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL
2-20 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL
2-20 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL
2-20 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL
2-50 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL
2-50 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL
2-50 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL
2-50 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL
2-50 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL
1-00 | Instrumental - Cable Pulling - DELETED ONLY ELECTRICAL
1-00 | Instrumental - Cable Termination - DELETED ONLY ELECTRICAL
1-00 | Instrumental - Item Installation - DELETED ONLY ELECTRICAL
1-00 | Instrumental - Mechanical Completion - DELETED ONLY ELECTRICAL
1-00 | Instrumental - Equipment Arrival - DELETED ONLY ELECTRICAL
7-20 | Instrumental - Item Installation - DELETED
7-30 | Instrumental - Item Installation - DELETED
7-10 | Instrumental - Item Installation - DELETED
7-40 | Instrumental - Item Installation - DELETED
7-10 | Instrumental - Cable Pulling - DELETED
7-10 | Instrumental - Cable Termination - DELETED
9-00 | Instrumental - Cable Pulling - DELETED
9-00 | Instrumental - Cable Termination - DELETED
0-00 | Instrumental - Cable Pulling - DELETED
0-00 | Instrumental - Cable Termination - DELETED
7-00 | Instrumental - Cable Pulling - DELETED
7-00 | Instrumental - Cable Termination - DELETED
3-00 | Instrumental - Cable Termination - DELETED
3-00 | Instrumental - Item Installation - DELETED
4-00 | Instrumental - Item Installation - DELETED
0-10 | Instrumental - Item Installation - DELETED
0-10/11 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL
0-14/15 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL
0-18/19 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
CON-EIT4180	Sub-System 70-21/22 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4240	Sub-System 70-26/27 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4300	Sub-System 70-28/29 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4360	Sub-System 70-31 | Electrical - RFCC - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4540	Sub-System 63-30 | Electrical - RFCC - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4600	Sub-System 64-10 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4840	Sub-System 55-00 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT4900	Sub-System 55-01 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT5020	Sub-System 25-08 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT5080	Sub-System 25-01/06 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT5200	Sub-System 25-07 | Electrical - RFCC - DELETED ONLY INSTRUMENTAL	0d	0d		01-Jul-24 A			
CON-EIT5370	Sub-System 88-00 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT5970	Sub-System 83-35 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6030	Sub-System 83-40 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6090	Sub-System 83-55 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6150	Sub-System 83-50 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6210	Sub-System 83-65 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6270	Sub-System 83-75 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6450	Sub-System 82-30 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6510	Sub-System 82-10 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6570	Sub-System 82-20 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6630	Sub-System 82-50 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
CON-EIT6690	Sub-System 81-00 | Instrumental - RFCC - DELETED ONLY ELECTRICAL	0d	0d		01-Jul-24 A			
Onshore Testing		32d	32d	19-Mar-25	29-Apr-25	14-Mar-25	02-May-25	155d
Preparatory Works		8d	8d	19-Mar-25	31-Mar-25	14-Mar-25	02-Apr-25	3d
COMM-ON2020	Removal of all the temporary equipment	8d	8d	19-Mar-25	28-Mar-25	14-Mar-25	25-Mar-25	3d
COMM-ON2030	Arrangement of all the firefighting equipment	5d	5d	24-Mar-25	28-Mar-25	19-Mar-25	25-Mar-25	3d
COMM-ON2040	Fencing of the area around the test	3d	3d	26-Mar-25	28-Mar-25	21-Mar-25	25-Mar-25	3d
COMM-ON2050	Ready For Onshore Integrated Testing	0d	0d	31-Mar-25		02-Apr-25		3d
Integrated Test		22d	22d	31-Mar-25	29-Apr-25	02-Apr-25	02-May-25	155d
COMM-ON1430	Mode 1 - Charging (WF + Solar Farm)	3d	3d	31-Mar-25	02-Apr-25	02-Apr-25	04-Apr-25	3d
COMM-ON1440	Mode 2 - Hot Stand-By Mode	1d	1d	03-Apr-25	03-Apr-25	07-Apr-25	07-Apr-25	3d
COMM-ON1450	Mode 3 - Discharging Mode	2d	2d	04-Apr-25	07-Apr-25	08-Apr-25	09-Apr-25	3d
COMM-ON1460	Mode 1 - Charging - (To Test the Emergency Mode)	2d	2d	08-Apr-25	09-Apr-25	10-Apr-25	11-Apr-25	3d
COMM-ON1470	Mode 4 - Cold Stand-By Mode	1d	1d	10-Apr-25	10-Apr-25	14-Apr-25	14-Apr-25	3d
COMM-ON1480	Mode 6 - Maintenance Access Mode	1d	1d	11-Apr-25	11-Apr-25	15-Apr-25	15-Apr-25	3d
COMM-ON1490	Mode 4A - Emergancy Mode (By Mean Of the Load Bank)	3d	3d	14-Apr-25	16-Apr-25	16-Apr-25	18-Apr-25	3d
COMM-ON1500	Mode 5 - Black Out (Included Black-Start)	1d	1d	17-Apr-25	17-Apr-25	22-Apr-25	22-Apr-25	3d
COMM-ON1510	Reliability Run Test	5d	5d	18-Apr-25	25-Apr-25	23-Apr-25	29-Apr-25	3d
COMM-ON1520	Mode 1 - Charging (To Recharge the BESS)	1d	1d	28-Apr-25	28-Apr-25	30-Apr-25	30-Apr-25	3d
COMM-ON2010	Onshore Integrated Test Completed	0d	0d	29-Apr-25		02-May-25		155d
Transpotation and Installation		10d	10d	05-May-25	15-May-25	05-May-25	15-May-25	2d
CON-FIN1050	Finalization - Load-Out & Sea-Fastening	10d	10d	05-May-25	15-May-25	05-May-25	15-May-25	2d
CON-FIN1080	Finalization - Transition Piece Load-Out & Sea-Fastening	7d	7d	05-May-25	12-May-25	07-May-25	14-May-25	5d
Installation at Project Site		63d	63d	22-Apr-25	24-Jun-25	22-Apr-25	25-Jun-25	38d

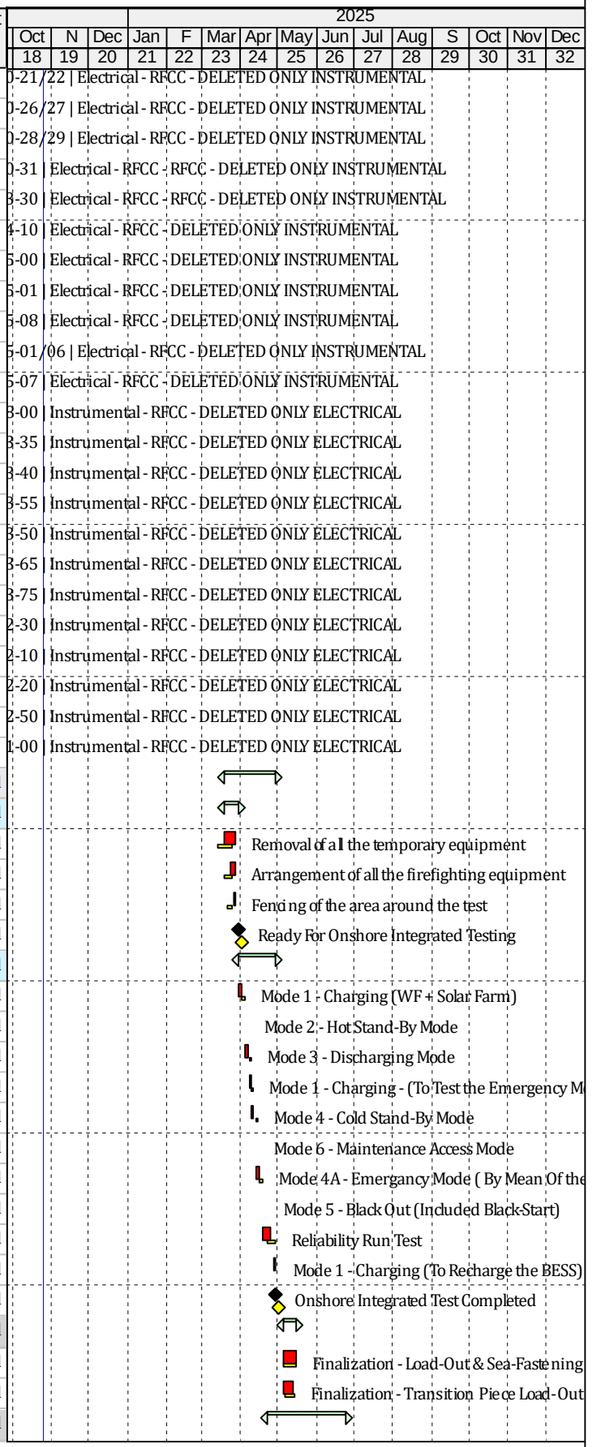

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

CROSSWIND


HOLLANDSE KUST NOORD WIND PARK Project

BASE LOAD POWER HUB

Contract No. CW-I-WP4-2023-05

ROSETTI MARINO

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Mob/Demob Vessel		63d	63d	22-Apr-25	24-Jun-25	22-Apr-25	25-Jun-25	38d
HVL Gulliver		8d	8d	13-Jun-25	21-Jun-25	13-Jun-25	22-Jun-25	41d
T&I1020	Preparation of Equipment	2d	2d	13-Jun-25	15-Jun-25	13-Jun-25	15-Jun-25	45d
T&I1040	Mobilisation to Site	1d	1d	15-Jun-25	16-Jun-25	15-Jun-25	16-Jun-25	2d
T&I1050	Demobilisation to Flushing	1d	1d	19-Jun-25	20-Jun-25	20-Jun-25	21-Jun-25	41d
T&I1080	Clearance of Equipment	1d	1d	20-Jun-25	21-Jun-25	21-Jun-25	22-Jun-25	41d
Cargo Barge BLPH		63d	63d	22-Apr-25	24-Jun-25	22-Apr-25	25-Jun-25	38d
T&I1090	In Survey Transport Barge	1d	1d	22-Apr-25	23-Apr-25	22-Apr-25	23-Apr-25	3d
T&I1100	Mobilisation to Fabrication Yard	1d	1d	23-Apr-25	24-Apr-25	23-Apr-25	24-Apr-25	3d
T&I1000	Topside Transportation	30d	30d	16-May-25	15-Jun-25	16-May-25	15-Jun-25	3d
T&I1160	Mobilisation to Site	30d	30d	16-May-25	15-Jun-25	16-May-25	15-Jun-25	2d
T&I1170	Demobilisation of Barge to Owner	1d	1d	18-Jun-25	19-Jun-25	19-Jun-25	20-Jun-25	38d
T&I1180	Clean Barge at Barge Owner incl. Out Survey	5d	5d	19-Jun-25	24-Jun-25	20-Jun-25	25-Jun-25	38d
Installation Vessel + Support Vessel		56d	56d	24-Apr-25	19-Jun-25	24-Apr-25	20-Jun-25	2d
HLV Offshore Execution Works		1d	1d	15-Jun-25	16-Jun-25	15-Jun-25	16-Jun-25	2d
T&I1540	Pre-Installation Survey - (Monopile & IAC) - Activitiy to be verified	1d	1d	15-Jun-25	16-Jun-25	15-Jun-25	16-Jun-25	2d
T&I1510	HLV Arrival at Site	0d	0d	16-Jun-25		16-Jun-25		2d
T&I1520	Transposrt Barge Arrival at Site	0d	0d	16-Jun-25		16-Jun-25		2d
T&I1530	Anchor HLV on Site	0d	0d	16-Jun-25	16-Jun-25	16-Jun-25	16-Jun-25	2d
BLPH Transition Piece (TP) Installation		1d	1d	16-Jun-25	17-Jun-25	16-Jun-25	17-Jun-25	2d
T&I1230	Moor Cargo Barge on Stern HLV	0d	0d	16-Jun-25	16-Jun-25	16-Jun-25	16-Jun-25	2d
T&I1320	Prepare and Connect Rigging to TP	0d	0d	16-Jun-25	16-Jun-25	16-Jun-25	16-Jun-25	2d
T&I1330	Cut Seafastening and Ballast HLV	0d	0d	16-Jun-25	16-Jun-25	16-Jun-25	16-Jun-25	2d
T&I1340	Lift TP	0d	0d	16-Jun-25	16-Jun-25	16-Jun-25	16-Jun-25	2d
T&I1350	Position TP onto MP Foundation, Secure TP to MP	0d	0d	16-Jun-25	16-Jun-25	16-Jun-25	16-Jun-25	2d
T&I1360	Recover Rigging	0d	0d	16-Jun-25	16-Jun-25	16-Jun-25	16-Jun-25	2d
T&I1370	Boiling Connection MP - TP	1d	1d	16-Jun-25	17-Jun-25	16-Jun-25	17-Jun-25	2d
BLPH Caissons Installation		1d	1d	17-Jun-25	18-Jun-25	17-Jun-25	18-Jun-25	2d
T&I1400	Moor Cargo Barge to Stern HLV	0d	0d	17-Jun-25	17-Jun-25	17-Jun-25	17-Jun-25	2d
T&I1410	Prepare and Connect Rigging to Caissons	0d	0d	17-Jun-25	17-Jun-25	17-Jun-25	17-Jun-25	2d
T&I1420	Cut Seafastening and Ballast HLV	0d	0d	17-Jun-25	17-Jun-25	17-Jun-25	17-Jun-25	2d
T&I1430	Lift Caissons	0d	0d	17-Jun-25	17-Jun-25	17-Jun-25	17-Jun-25	2d
T&I1440	Postioning Caissons to BLPH Foundation	1d	1d	17-Jun-25	18-Jun-25	17-Jun-25	18-Jun-25	2d
T&I1450	Recover Rigging	0d	0d	18-Jun-25	18-Jun-25	18-Jun-25	18-Jun-25	2d
BLPH Topside (TS) Installation		56d	56d	24-Apr-25	19-Jun-25	24-Apr-25	20-Jun-25	2d
T&I1110	Installation of Grillage, Load-Out Caissons, TP and TS incl. Seafastening	21d	21d	24-Apr-25	15-May-25	24-Apr-25	15-May-25	3d
T&I1070	Prepare and Connect Rigging to TS	0d	0d	18-Jun-25	18-Jun-25	18-Jun-25	18-Jun-25	2d
T&I1120	Cut Seafastening and Ballast HLV	0d	0d	18-Jun-25	18-Jun-25	18-Jun-25	18-Jun-25	2d
T&I1130	Lift TS	0d	0d	18-Jun-25	18-Jun-25	19-Jun-25	19-Jun-25	2d
T&I1140	Position TS on TP	0d	0d	18-Jun-25	18-Jun-25	19-Jun-25	19-Jun-25	2d
T&I1150	Recover Rigging TS	0d	0d	18-Jun-25	18-Jun-25	19-Jun-25	19-Jun-25	2d
T&I1240	Store Rigging Equipment	0d	0d	18-Jun-25	18-Jun-25	19-Jun-25	19-Jun-25	2d
T&I1250	Welding Works TS to TP	1d	1d	18-Jun-25	19-Jun-25	19-Jun-25	20-Jun-25	2d
T&I1260	Retieve Anchors	0d	0d	19-Jun-25	19-Jun-25	20-Jun-25	20-Jun-25	2d
T&I1270	Leave Site	0d	0d	19-Jun-25	19-Jun-25	20-Jun-25	20-Jun-25	2d
Offshore Hook-Up, Commissioning and Start-Up		41d	41d	19-Jun-25	30-Jul-25	21-Jun-25	01-Aug-25	2d

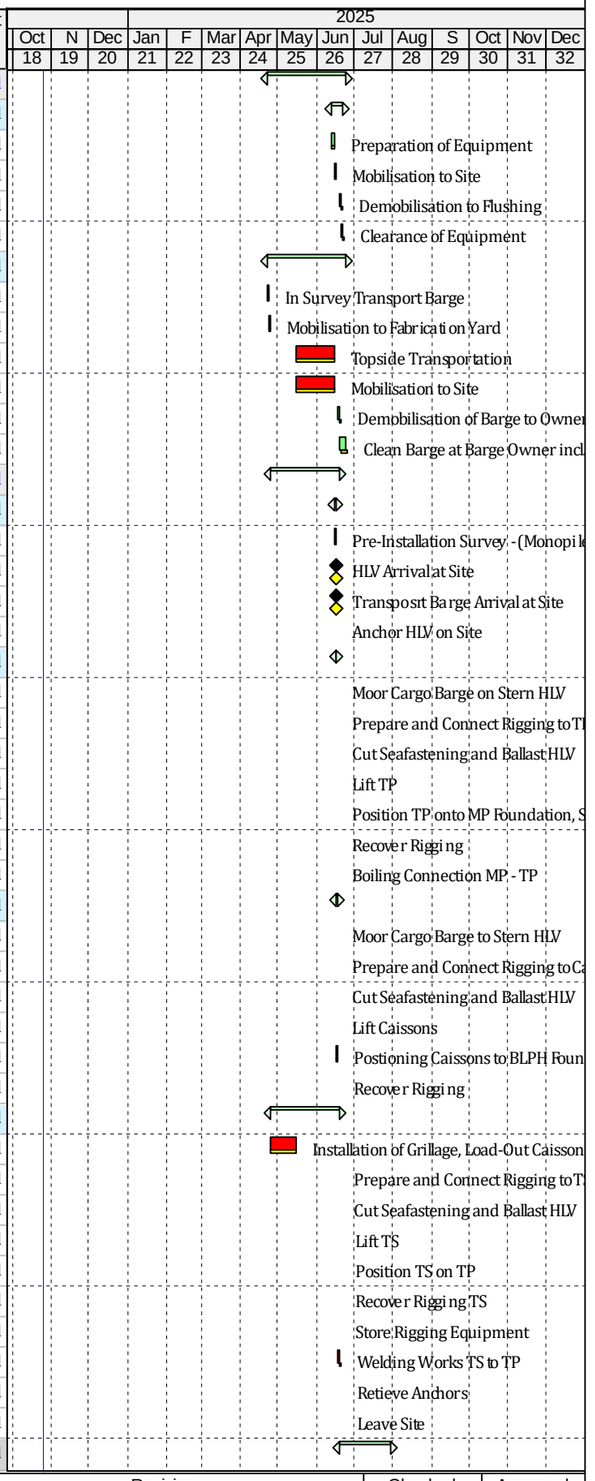

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary


Data Date: 25-Oct-24

CROSSWIND BLPH EPCI

Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR

Activity ID	Activity Name	Original Duration	At Completion Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float
Hook-Up Activities		25d	25d	19-Jun-25	13-Jul-25	21-Jun-25	15-Jul-25	6d
COMM-OFF1000	Offshore Campaign Start	0d	0d	19-Jun-25		21-Jun-25		2d
COMM-OFF1020	FO Cable Termination Completed	0d	0d		28-Jun-25		30-Jun-25	2d
COMM-OFF1060	66kV Power Cable Termination Completed	0d	0d		03-Jul-25		05-Jul-25	5d
COMM-OFF1080	PV Power Cable Termination Completed	0d	0d		08-Jul-25		10-Jul-25	5d
COMM-OFF1090	Sea Water Pump & Caisson HU Completion	0d	0d		08-Jul-25		10-Jul-25	5d
COMM-OFF1150	Water Disposal Sump Caisson HU Completion	0d	0d		13-Jul-25		15-Jul-25	6d
COMM-OFF1160	Cathodic Protection HU Completed	0d	0d		13-Jul-25		15-Jul-25	6d
Offshore Commissioning		40d	40d	20-Jun-25	30-Jul-25	22-Jun-25	01-Aug-25	2d
Offshore Campaign		40d	40d	20-Jun-25	30-Jul-25	22-Jun-25	01-Aug-25	2d
COMM-OFF1010	HUB Power-Up by Mean of Temporary Generator Connected to the JB	20d	20d	20-Jun-25	09-Jul-25	22-Jun-25	11-Jul-25	4d
COMM-OFF1030	FO Panel Commissioning	2d	2d	30-Jun-25	01-Jul-25	02-Jul-25	03-Jul-25	2d
COMM-OFF1040	Network Integration	2d	2d	02-Jul-25	03-Jul-25	04-Jul-25	05-Jul-25	2d
COMM-OFF1050	CCS Integration	3d	3d	04-Jul-25	06-Jul-25	06-Jul-25	08-Jul-25	2d
COMM-OFF1070	66kV Switchboard Commissioning	6d	6d	07-Jul-25	12-Jul-25	09-Jul-25	14-Jul-25	2d
COMM-OFF1110	Sea Water Pump Commissioning	3d	3d	10-Jul-25	12-Jul-25	12-Jul-25	14-Jul-25	4d
COMM-OFF1100	HUB Energization from the 66kV Switchboard	2d	2d	13-Jul-25	14-Jul-25	15-Jul-25	16-Jul-25	2d
COMM-OFF1130	Desalinator Start-Up	2d	2d	13-Jul-25	14-Jul-25	15-Jul-25	16-Jul-25	4d
COMM-OFF1170	Cathodic Protection Commissioning	3d	3d	14-Jul-25	16-Jul-25	16-Jul-25	18-Jul-25	6d
COMM-OFF1120	Bess Offshore re-test	2d	2d	15-Jul-25	16-Jul-25	17-Jul-25	18-Jul-25	2d
COMM-OFF1180	Electrolizer Offshore re-test	4d	4d	15-Jul-25	18-Jul-25	17-Jul-25	20-Jul-25	4d
COMM-OFF1140	PV Commissioning	4d	4d	17-Jul-25	20-Jul-25	19-Jul-25	22-Jul-25	2d
COMM-OFF1190	Fuel Cell Offshore re-test (H2 Produced by Electrolizer)	2d	2d	21-Jul-25	22-Jul-25	23-Jul-25	24-Jul-25	2d
COMM-OFF2100	Offshore Integrated Test Completed	0d	0d	30-Jul-25		01-Aug-25		2d
Start-Up		7d	7d	23-Jul-25	29-Jul-25	25-Jul-25	31-Jul-25	2d
COMM-OFF1200	Start-Up & Handover	7d	7d	23-Jul-25	29-Jul-25	25-Jul-25	31-Jul-25	2d
Variation Orders		180d	189d	15-Apr-24 A	25-Nov-24			97d
Variation Orders		180d	189d	15-Apr-24 A	25-Nov-24			97d
VO-CON-STR1000	VO xx - Davit Crane - Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Bracings	5d	27d	15-Apr-24 A	17-May-24 A			
VO-CON-STR1010	VO xx - Davit Crane - Steel Structure - Assembly - Lower Deck - (Primary & Secondary Steel) - Block 1	5d	127d	15-Apr-24 A	12-Sep-24 A			
VO-CON-STR1020	VO xx - Davit Crane -Steel Structure - Painting - Lower Deck - Block 1	5d	169d	15-Apr-24 A	31-Oct-24			26d
VO-CON-STR1040	VO xx - Davit Crane - Steel Structure - Pre-Fabrication - Lower Deck - Block 1 - Legs	25d	29d	27-May-24 A	28-Jun-24 A			
VO-CON-PIP1050	VO xx - Piping Drainage - Painting	5d	11d	08-Jul-24 A	19-Jul-24 A			
VO-CON-PIP1060	VO xx - Piping Drainage - Line Installation (128 to 149)	15d	106d	11-Jul-24 A	13-Nov-24			97d
VO-CON-STR1030	VO xx - Davit Crane - Steel Structure - Erection - Lower Deck - Block 1 - Welding	15d	15d	02-Nov-24	19-Nov-24			26d
VO-CON-PIP1070	VO xx - Piping Drainage - Hydrotest Pack	5d	5d	14-Nov-24	19-Nov-24			97d
VO-CON-PIP1080	VO xx - Piping Drainage - Reinstaintment	5d	5d	20-Nov-24	25-Nov-24			97d

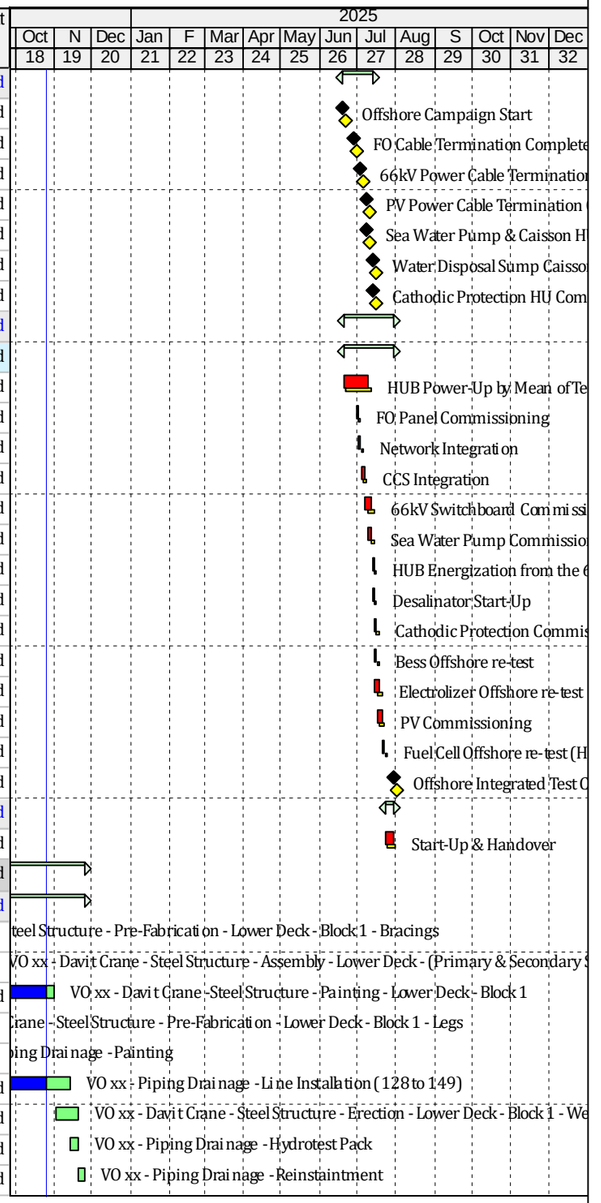

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Notification Mechanism
Critical Remaining Work
Baseline Milestone
Milestone
summary

Data Date: 25-Oct-24

CROSSWIND BLPH EPCI
Level 4 Project Baseline Schedule

Date	Revision	Checked	Approved
16-Aug-23	Lvl.4 Preliminary Project Baseline Schedule	SS	MR
06-Oct-23	Lvl.4 Project Baseline Schedule	SS	MR
06-Sep-24	Lvl.4 Project Baseline Schedule - cut-off 30.08.2024	FF	MR
04-Oct-24	Lvl.4 Project Baseline Schedule - cut-off 27.09.2024	FF	MR
04-Nov-24	Lvl.4 Project Baseline Schedule - cut-off 25.10.2024	FF	MR
