Base Load Power Hub (BLPH)

INSTRUMENT AIR PACKAGE A-63000
HANDLING, PRESERVATION AND PACKAGING PROCEDURE

Document Number: 1724000428-QC-PRO-00031

ROSETTI MARINO	
1	NO COMMENTS - APPROVED - WORK MAY PROCEED
2	MINOR COMMENTS - REVISE AND RESUBMIT - WORK MAY PROCEED
3	MAJOR COMMENTS – REJECTED – DO NOT PROCEED
4	APPROVAL NOT REQUIRED
NOTE: Approval doesn't relieve the supplier from mandatory compliance with contractual documents and specifications. Comments made do not imply acceptance of any cost or delivery impact.	
Sign	Date
M. Bh	04/02/2025

Document Class: 3

Rev.	Date	Description	Prepared	Reviewed	Approved
02	03/02/2025	Issue for Information (IFI)	GT	MC	TM
01	02/01/2025	Issue for Information (IFI)	GT	MC	TM
00	02/10/2024	Issue for Information (IFI)	GT	MC	TM

COES

This document undergoes an issuance cycle within EDMS Fusionlive". Its distribution is electronically controlled. Once printed shall be considered as "NOT CONTROLLED" copy

Revision / Change Log

Rev.	Description
00	Issue for Information (IFI)
01	Issue for Information (IFI)
02	Issue for Information (IFI)

HOLDS LIST

No.	Description
1	
2	
3	
4	

Table of contents

1 INTRODUCTION 5

1.1 PROJECT OVERVIEW 5

1.1.1 Project Location 5

1.1.2 Project Concept 6

2 DOCUMENT SCOPE 8

2.1 REFERENCES 8

2.2 DEFINITIONS AND ABBREVIATIONS 8

3 HANDLING, PRESERVATION AND PACKING PROCEDURE 9

3.1 SCOPE 9

This document undergoes an issuance cycle within EDMS Fusionlive". Its distribution is electronically controlled. Once printed shall be considered as "NOT CONTROLLED" copy

List of Figures

Figure 1 HOLLANDSE KUST NOORD WIND PARK Location Map 5

Figure 2 - Wind Park Details 6

Figure 3 – BLPH Concept 6

List of tables

Table 1 - Reference Documents 8

Table 2 - Definitions and Abbreviations 8

List of Attachments

None

1 INTRODUCTION

1.1 PROJECT OVERVIEW

Crosswind, a Shell and Eneco joint venture, was awarded the tender to develop the offshore Hollandse Kust Noord (HKN) wind farm, located 18.5km off the coast of Netherlands near the town of Egmond aan Zee. The consortium plans to have HKN operational in 2023 with an installed capacity of 759MW generating at least 3.3TWh per year. This is sufficient renewable power to supply more than 1 million Dutch households with green electricity.

Offshore wind farms produce intermittent electricity and balancing these dips and peaks and integrating this electricity into the national energy system requires new technologies. For this reason, the offshore wind farm will include several new technologies that could be implemented at full-scale in the future. The new technologies being explored include a floating solar park, a short-duration battery storage as well as long-term storage via green hydrogen produced by water electrolysis and subsequently consumed in a fuel cell. The combination of these individual measures, herein referred to as the Base Load Power Hub (BLPH) will ensure a continuous power supply regardless of the wind situation.

1.1.1 Project Location

The Hollandse Kust Noord (HKN) wind farm is located 18.5km off the coast of the Netherlands near the town of Egmond aan Zee.

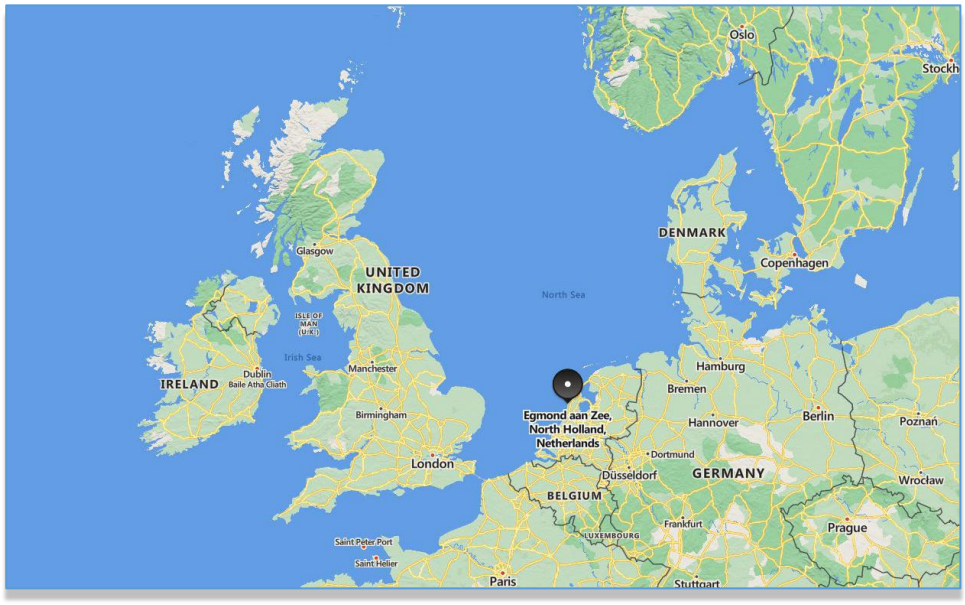


Figure 1 HOLLANDSE KUST NOORD WIND PARK Location Map



Figure 2 - Wind Park Details

The wind farm will consist of No. 69 x 11.5MW wind turbine generators each to be installed on a dedicated monopile structure. A 70th monopile located on coordinates E 590719.1, N 5841602.3 is reserved for installing the platform accommodating the BLPH. The monopile structure was designed and installed by Van Oord Offshore Wind (VooW) and therefore not part of the BLPH scope.

1.1.2 Project Concept

All components included in the BLPH will be integrated onshore on a topsides and installed in an offshore location within the boundaries of the HKN wind farm. At its simplest, the BLPH will store energy during periods of high electricity generation from renewable sources (a wind turbine generator and the floating solar PV farm) and release it during periods of low generation. In practice. It is expected that the energy stored will supplement generation from renewable sources to ensure that at least 1.0MW of power is exported to the electrical grid regardless of wind/solar availability.

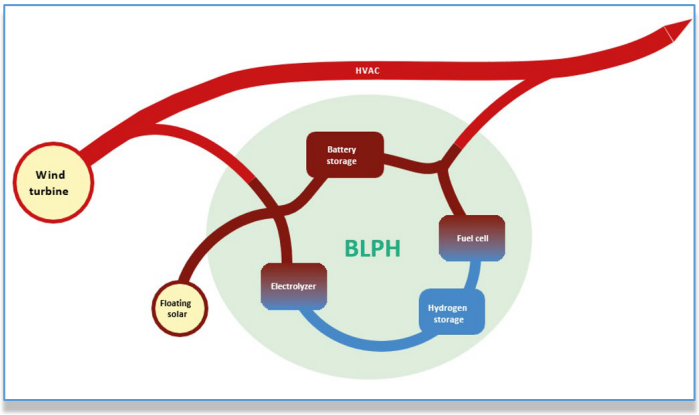


Figure 3 – BLPH Concept

Electricity in the BLPH will be stored in the form of electrons in a battery energy storage system (BESS) as well as converted into green hydrogen via water electrolysis. When the power output from the connecting wind turbine drops to below 1 MWe, the BLPH will return its stored energy to supplement the remaining power output. This will be by discharging the BESS, while stored hydrogen will be converted back into electricity using a fuel cell to extend the discharge duration.

The purpose of the BLPH s to function as a testbed for the integration of energy storage technologies with renewable generation. It is expected that equipment installed on the BLPH will operate as Normally Unmanned Installation for at least two (2) years with no or minimal maintenance and it will have its own independent control room with the ability to communicate with Crosswind's control room.

This document undergoes an issuance cycle within EDMS Fusionlive". Its distribution is electronically controlled. Once printed shall be considered as "NOT CONTROLLED" copy

2 DOCUMENT SCOPE

This document identifies any electrical equipment to be fed with its main characteristics.

2.1 REFERENCES

Doc. No.	Description
1724000428-PR-PID-00019	PACKAGE P&ID
1724000428-MAC-DA-00005	CERTIFIED PACKAGE GENERAL ARRANGEMENT AND DIMENSIONAL OUTLINE DRAWINGS (INCLUDING : NAMEPLATE, BASEFRAME, FOUNDATION LOADS, NOZZLES LOADS, NOZZLES LIST, BATTERY LIMITS, CoG)
1724000428-MAC-DD-00006	EQUIPMENT SECTIONAL DRAWING WITH BILL OF MATERIAL

Table 1 - Reference Documents

2.2 DEFINITIONS AND ABBREVIATIONS

COMPANY or Client (CPY):	Crosswind
CONTRACTOR (CTR):	ROSETTI MARINO S.p.A.
PROJECT:	HOLLANDSE KUST NOORD WIND PARK Project

Table 2 - Definitions and Abbreviations

3 HANDLING, PRESERVATION AND PACKING PROCEDURE

3.1 SCOPE

The instrument air package will be delivered fully assembled, protected with a heat shrinkable film suitable for road transportation.

The instrument air receiver will be delivered fully assembled (in terms of installed instruments and valves), of a wooden pallet protected with a heat shrinkable film suitable for road transportation.

Any exposed equipment that may be damaged by slings and lifting equipment during transportation and installation shall be protected or removed.

The equipment can be handled with furnished no.4 lifting lugs; welded on main baseframe.

Every 3 months check the conditions of the packing: if damaged proceed with replacing

Keep closed all battery limit connections with blind flanges or plugs (supplied with the package), to avoid that humidity, dust or atmospheric pollution enter into the component of the package.

Keep closed all vent and drain valves and all electrical connections.

In case of prolonged storage, every month it is suggested to carry out site inspection as per following checklist:

1. Check that all manual vent and drain valves are closed.
2. Check that all blind flanges (if any) are closed and correctly tightened: install the flanges and tighten the stud bolts, if necessary.
3. Check that all terminal boxes are closed and that the internal is clean from sand or dust and that no dew is detected: clean, close of replace them, if necessary.
4. Check that all instruments, valves are not damaged: replace them, if necessary.
5. Check that all tubing is properly connected: tighten compression fittings, if necessary.

This document undergoes an issuance cycle within EDMS Fusionlive". Its distribution is electronically controlled. Once printed shall be considered as "NOT CONTROLLED" copy
